

Proposed Change Orders for June 2025
 BG #21-072 New Stanton Elementary School
 Powell County Board of Education

<u>CO #</u>	<u>Contractor's Name</u>	<u>Fees</u>	<u>Amount</u>
CO #2-1	Hinkle Contracting Company	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #4-3	Mason Structure, Inc.	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #6-1	Dixie Roofing, Inc.	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #7-2	Grayhawk, LLC	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #8-1	Elliott Contracting	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #12-1	C & T Design & Equipment	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #13-1	Irwin Installation	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #14-1	Marting Flooring Company	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #17-1	Twin Lakes Fire Service	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #18-3	Central Kentucky Sheet Metal	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00

CO #19-5	Rimar Electric, LLC	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #20-1	Facility Commissioning	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #21-7	Rising Sun Developing Company	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00
CO #22-2	Rosa Mosaic & Tile	CO Cost	\$0.00
		AE Fee	\$0.00
		CM Fee	\$0.00

Background/Rationale- 1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days. 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days. Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

CO #7-3	Grayhawk, LLC	CO Cost	\$1,350.00
		AE Fee	\$72.90
		CM Fee	\$25.65

Background/Rationale- PR #15-Change to aCapella clouds in lieu of Serenda Clouds.

Suggested Motion- Motion to approve CO #7-3 issued to Grayhawk, LLC in the amount of \$1,448.55 in accordance to PR #15-Change to aCapella clouds in lieu of Serenda Clouds.

CO #21-6	Rising Sun Developing Company	CO Cost	-\$2,850.00	Credit
		AE Fee	\$0.00	
		CM Fee	<u>\$0.00</u>	

Background/Rationale- PR #12-Delete paint on ceilings in IDF and Mechanical Rooms

Suggested Motion- Motion to approve CO #21-6 issued to Rising Sun Developing Company for a credit in the amount of -\$2,850.00 in accordance with PR #12-delete pain on ceilings in IDF and Mechanical Rooms.

CO #21-8	Rising Sun Developing Company	CO Cost	\$7,033.40
		AE Fee	\$379.80
		CM Fee	\$133.63

Background/Rationale- PR #14-Change the locking functions to BWST 45H/T14HVIB for the following doors: 135, 155, 191, 116A, 120A, 175A, and 177A.

Suggested Motion- Motion to approve CO #21-8 issued to Rising Sun_Developing Company in the amount of \$7546.83 in accordance with PR #14 to change the locking function to Bwst 45H7T14HVIB for the following doors: 135, 155, 191, 116A, 120A, 175A, and 177A.

FACPAC Contract Change Order

Supplemental Information Form (Ref#

62490)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Hinkle Contracting Company, LLC, 0002, Asphalt Paving

Type: CM Bid Package

Proposed

Change Order Number02-01

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency Balance

Contract Change Requested By Construction Manager

Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner

No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

Change Order Supplemental Information Form Signature Page (Online Form Ref# 62490)

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 02-01
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 HINKLE CONTRACTING COMPANY LLC

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #02 ASPHALT PAVING

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	878,344.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	878,344.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	878,344.00

The Contract Time will be adjusted by 93 days.

The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

HINKLE CONTRACTING COMPANY LLC

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24	2	3	4																	
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24	3	4																		
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24	4																			
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24	5																			
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24	6																			
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24	7	8	9	10	11	12														
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24	8	9	10	11	12															
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24	9	10																		
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24	10	11																		
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24	11	12																		
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24	13	14																		
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24	14	15																		
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24	15	16																		
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24	16	17																		
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24	17	18																		
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24	18	19	20	21	22	23	24	25	26	27	28	29	30	31						
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24	19	20																		
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24	20	21	22	23	24	25	26	27	28	29	30	31								
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24	21	22																		
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24	22	23	24	25	26	27	28	29	30	31										
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24	23	24																		
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24	24	25	26	27	28	29	30	31												
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24	25	26	27	28	29	30	31													
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24	26	27	28	29	30	31														
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24	27	28	29	30	31															
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24	28	29	30	31																
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24	29	30	31																	
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24	30	31																		
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24	31	32																		
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25	32	33																		
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25	33																			
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr													
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																					
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																					
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																					
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																					
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																					
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																					
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																					
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																					
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																					
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																					
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																					
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																					
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																					
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																					
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																					
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																					
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																					
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																					
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																					
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																					
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																					
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																					
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																					
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																					
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																					
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																					
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																					
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																					
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																					
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																					
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																					
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																					
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																					
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																					

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

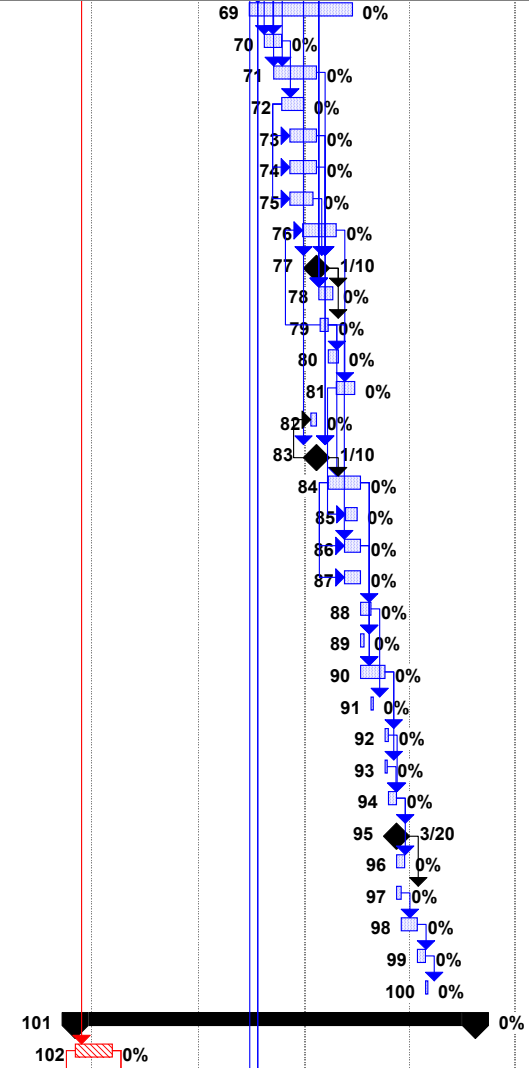

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

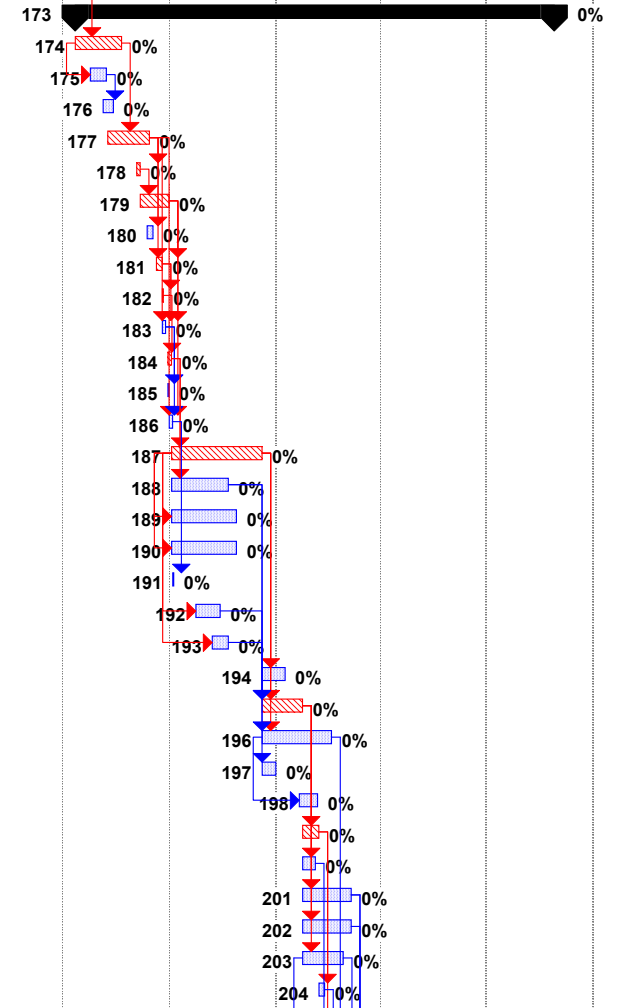

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone





STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																								
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																								
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																								
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																								
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																								
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																								
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																								
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																								
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																								
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																								
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																								
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																								
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																								
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																								
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																								
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																								
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																								
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																								
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																								
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																								
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																								
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																								
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																								
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																								
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																								
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																								
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																								
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																								
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																								
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																								
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																								
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																								
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																								
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																								
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																								
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																								
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																								
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																								
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																								
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																								
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																								
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																								
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																								
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																								
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																								
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																								
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																								
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																								
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																								
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																								
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																								
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																								
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																								
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																								
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																								
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																								
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																								
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																								
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																								
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																								
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																								
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																								
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																								
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																								
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

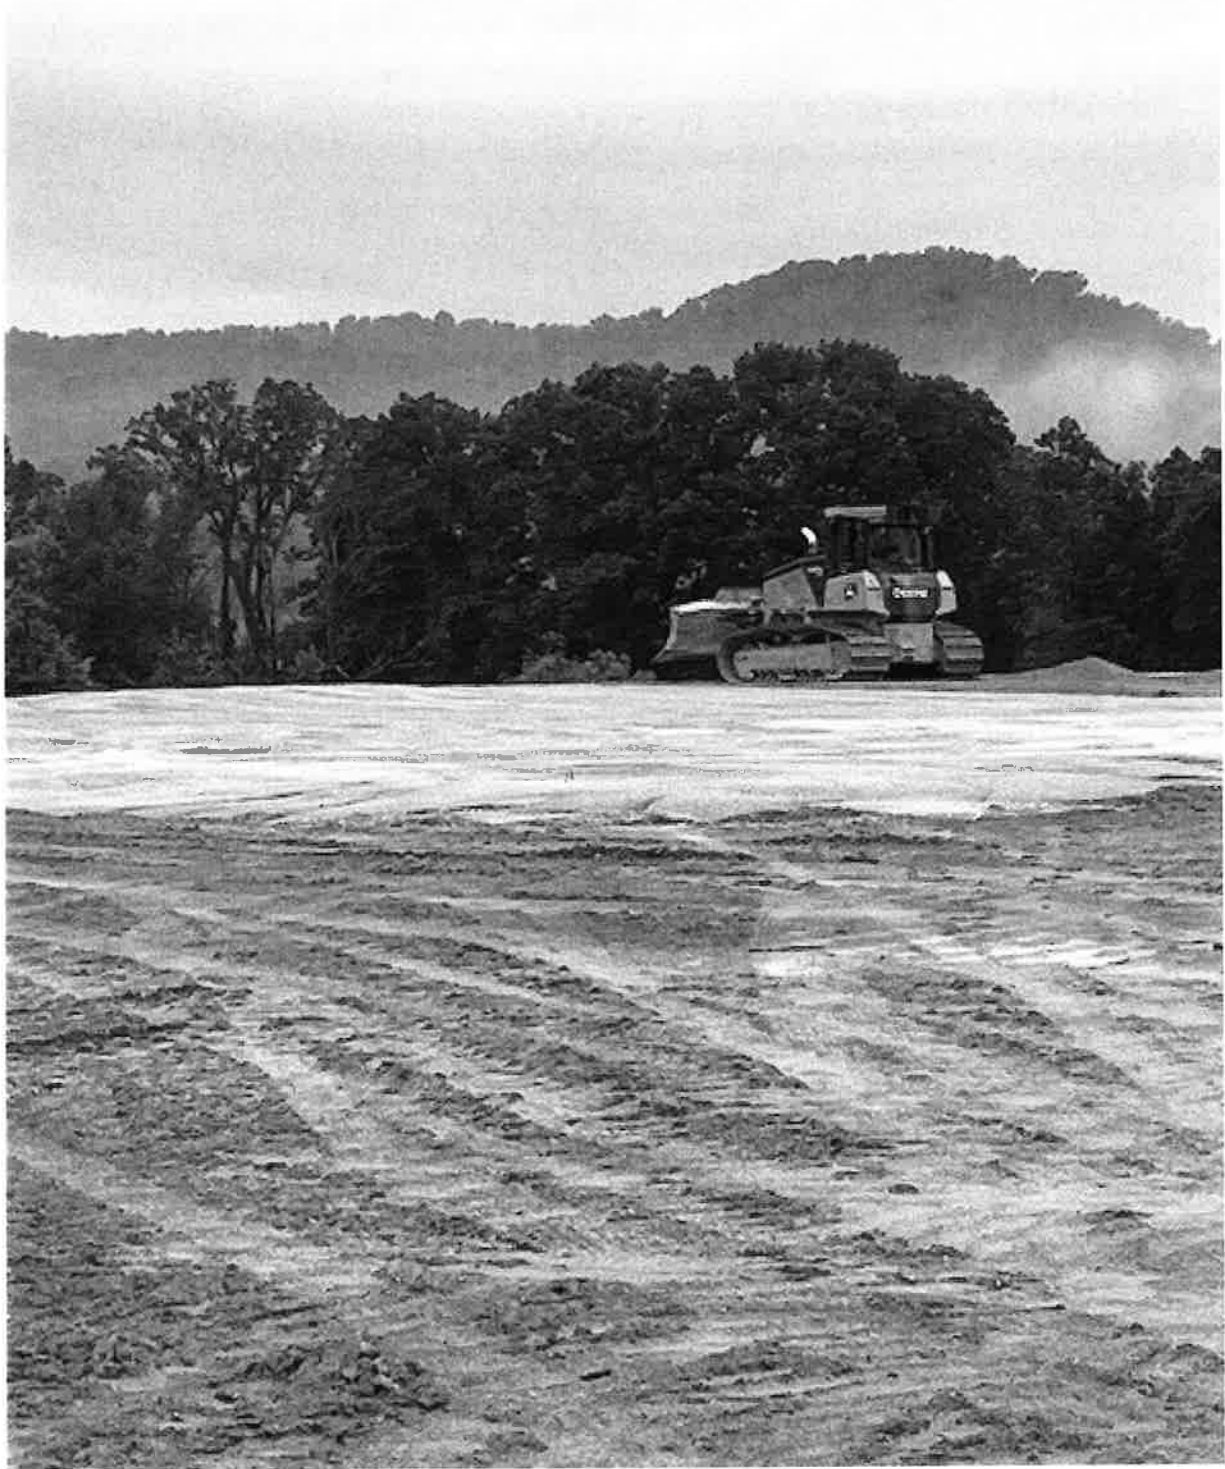



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM

CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

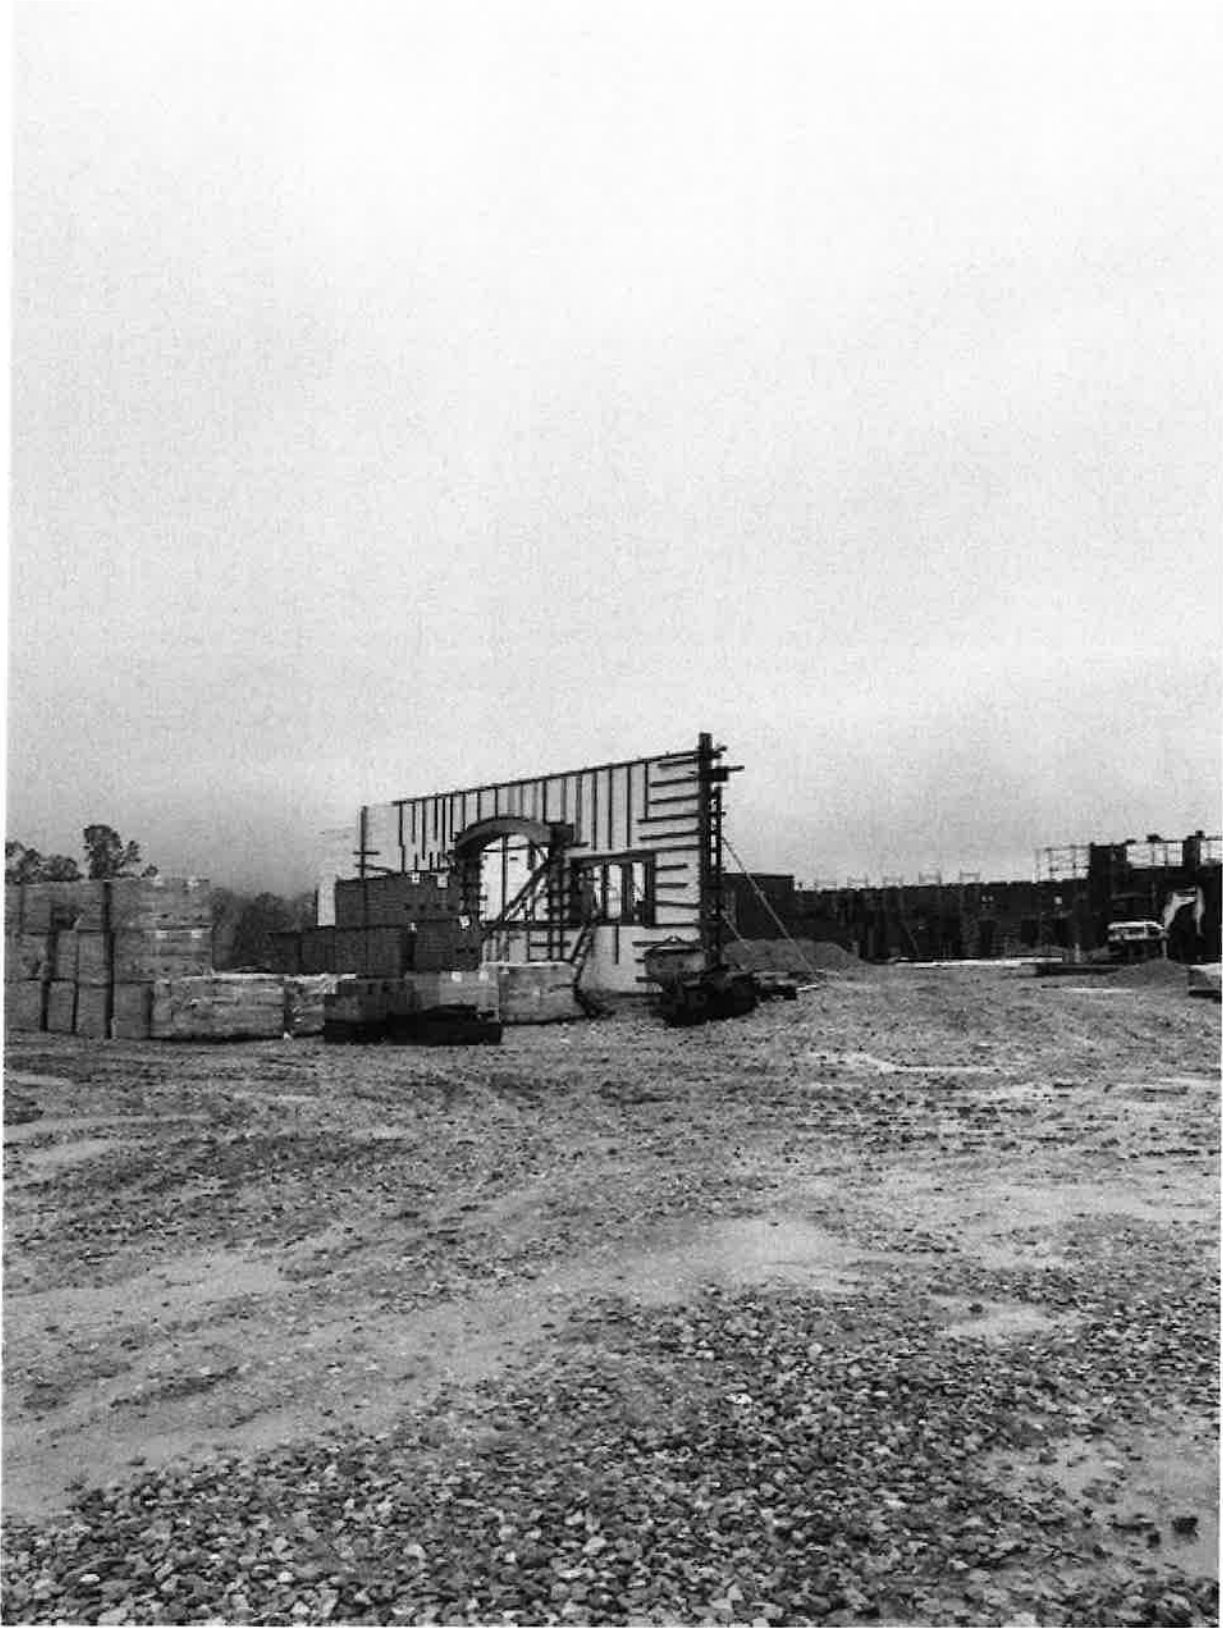



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM



File

Daily Report 2024...
Michael Graf





Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM

File
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael GrafFile
12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM

File
12/16/2024 2:01 PM
Michael GrafFile
12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM


Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM

File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

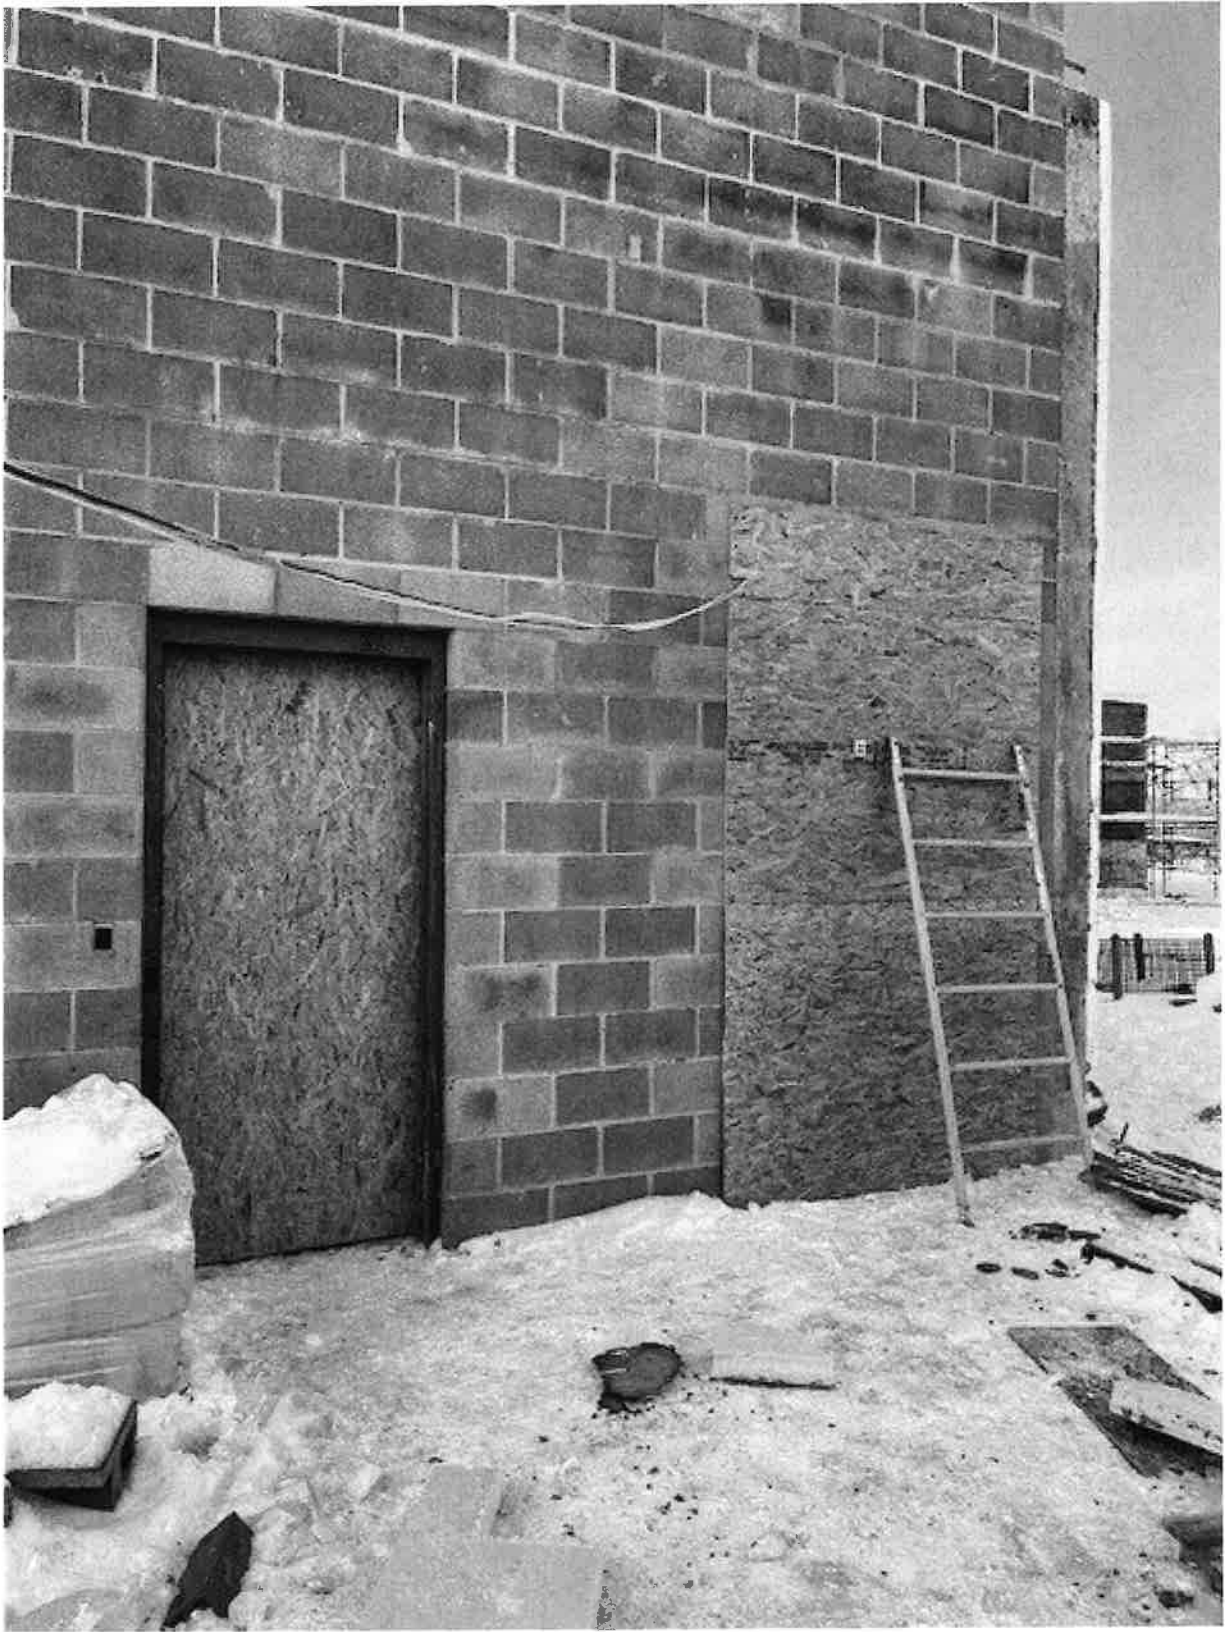



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM

File
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael Graf


Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.

Michael Graf on 1/14/2025 03:13 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

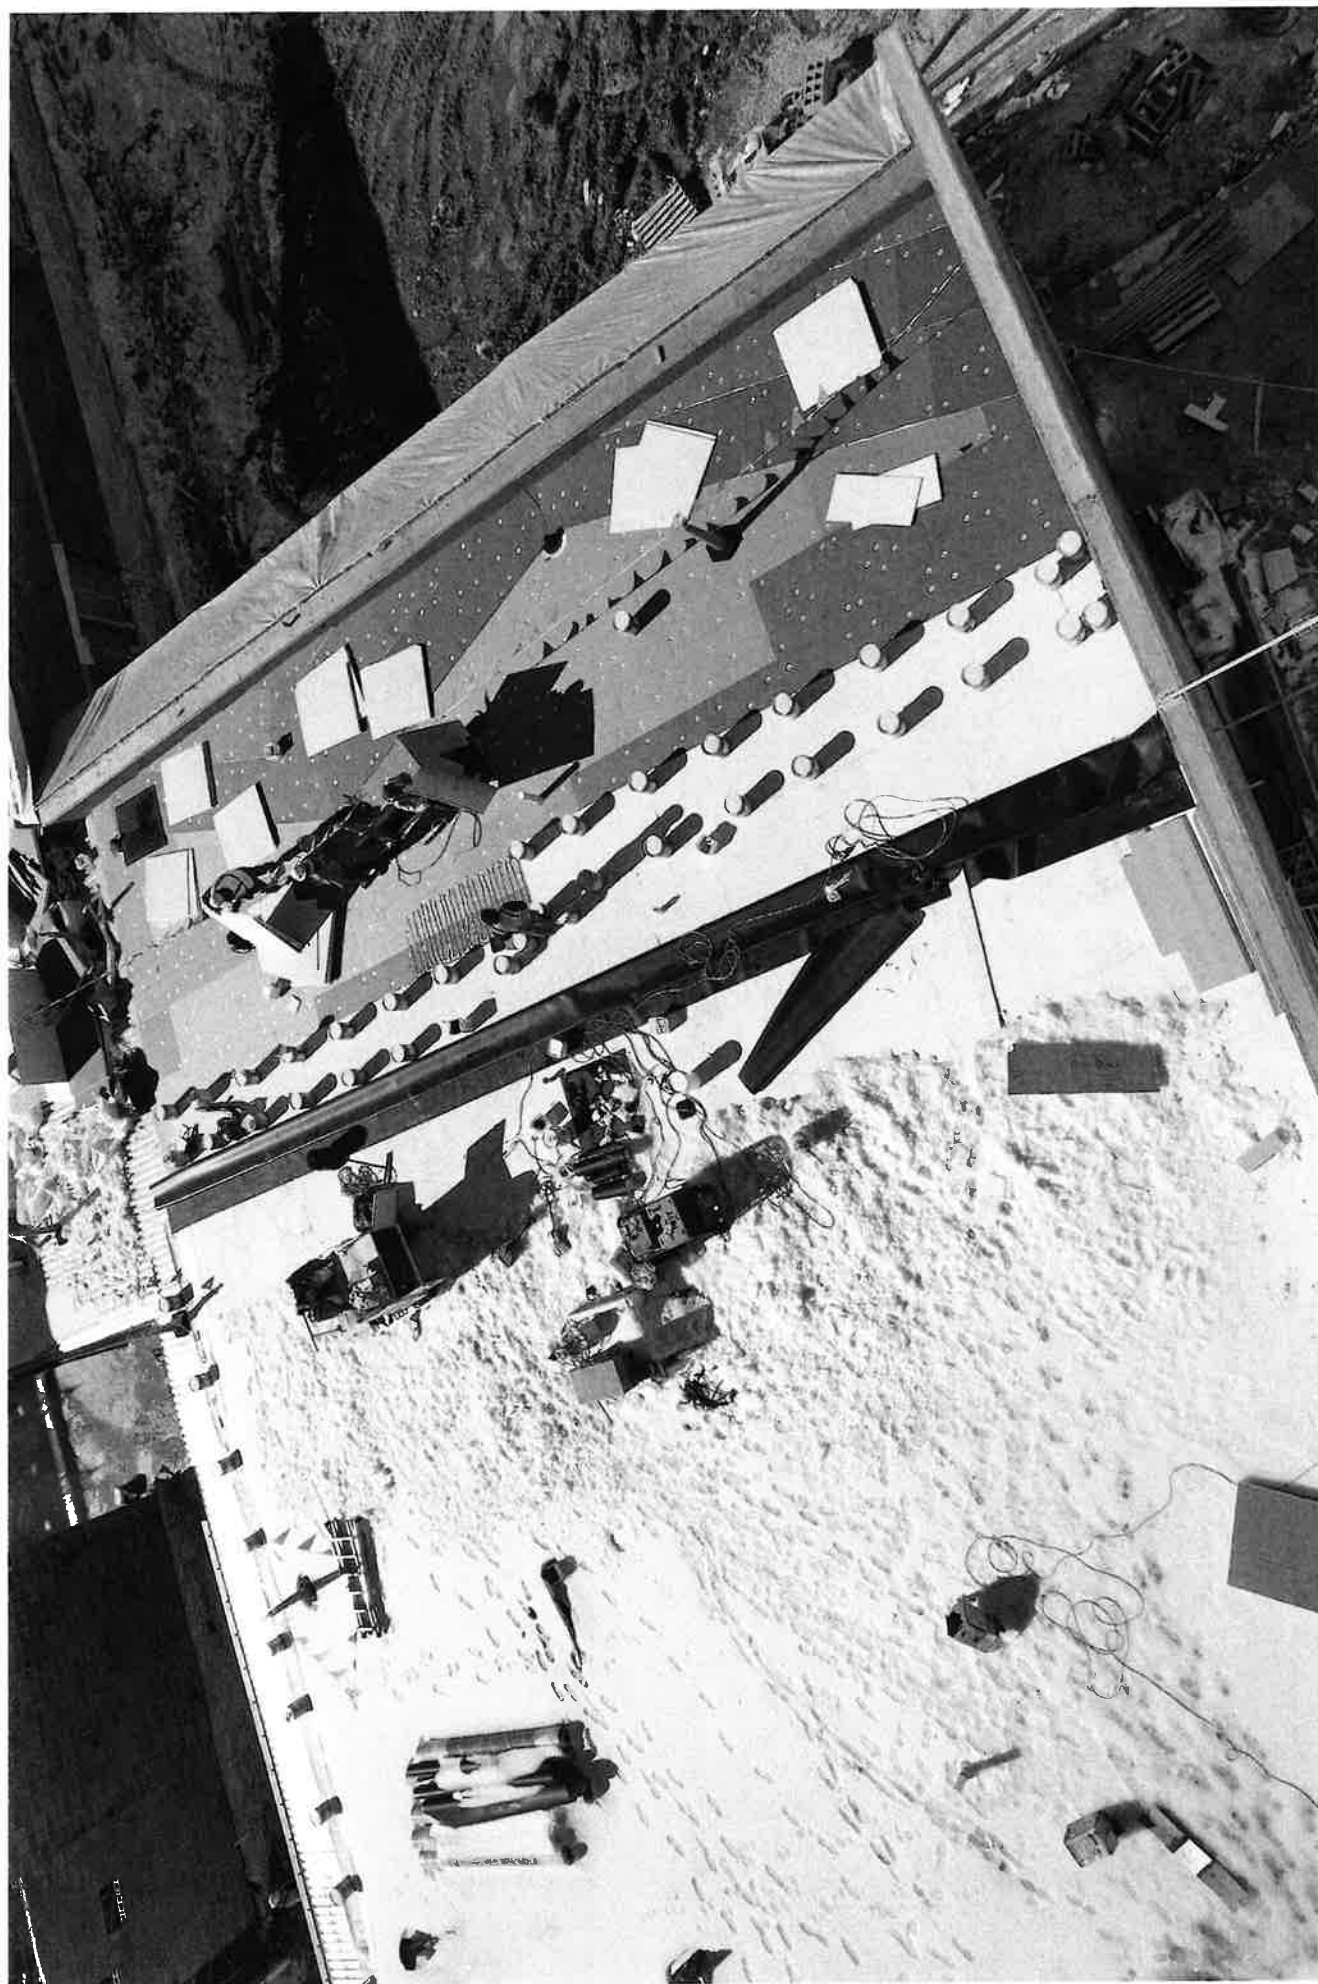



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf

Michael Graf on 1/23/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM

File
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.


Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontals/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62493)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Mason Structure Inc., 0004, Masonry

Type: CM Bid Package

Proposed

Change Order Number04-03

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency

Balance

Contract Change Requested ByConstruction Manager

Contract Change Reason CodeTime Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner

No cost from Contractors

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote		
Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62493)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 04-03
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 MASON STRUCTURE, INC.

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #04 MASONRY

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	1,476,430.00
Net change by previously authorized Change Orders	-2,390.96
The Contract Sum prior to this Change Order was	1,474,039.04
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	1,474,039.04

The Contract Time will be adjusted by 93 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

MASON STRUCTURE, INC.

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																				
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

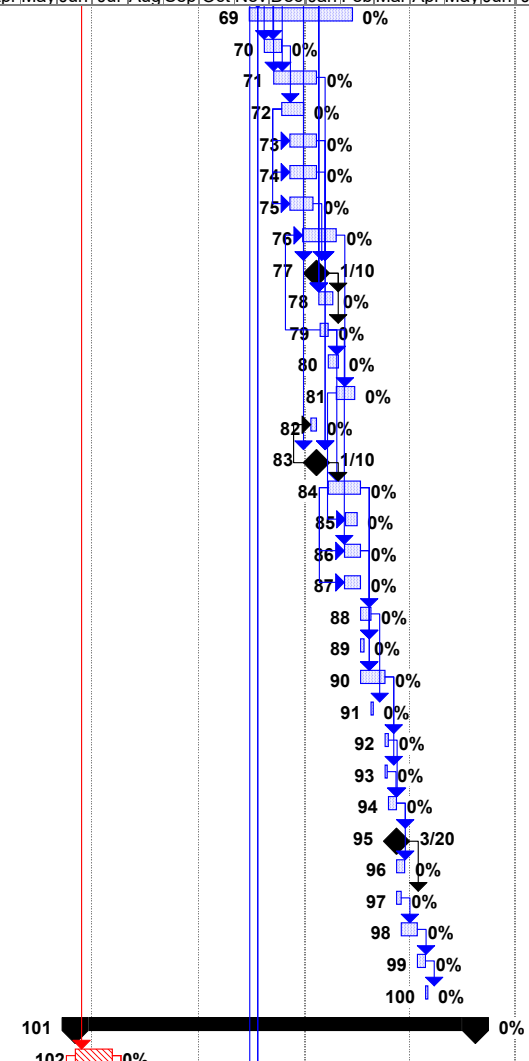

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25								
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25								
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25								
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24								
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24								
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24								
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24								
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24								
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24								
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24								
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24								
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24								
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24								
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24								
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24								
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24								
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24								
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24								
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24								
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24								
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24								
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25								
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25								
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25								
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24								
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25								
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25								
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25								
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25								
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25								

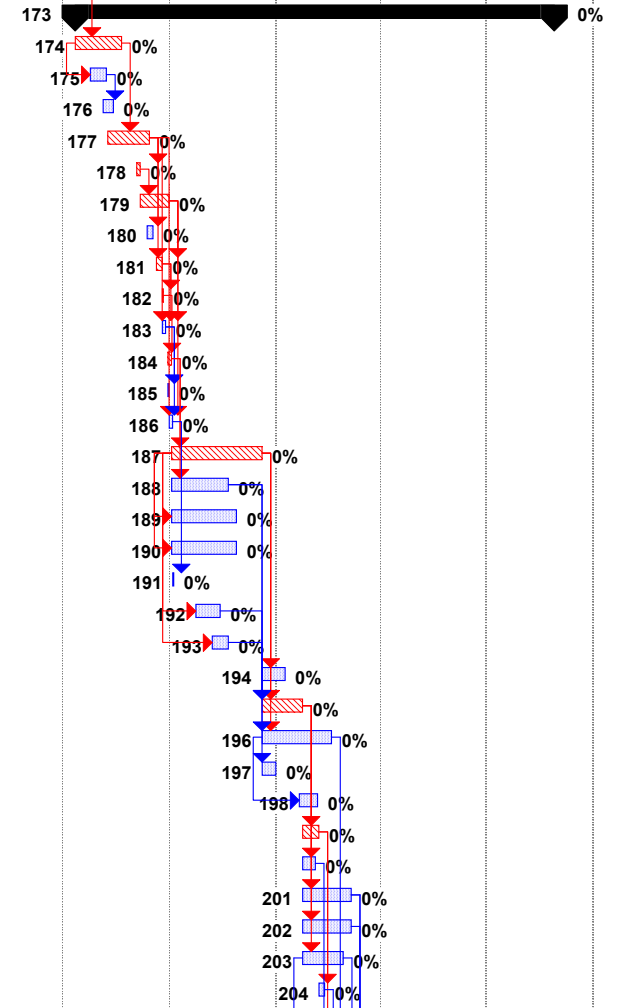

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM
Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf

Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

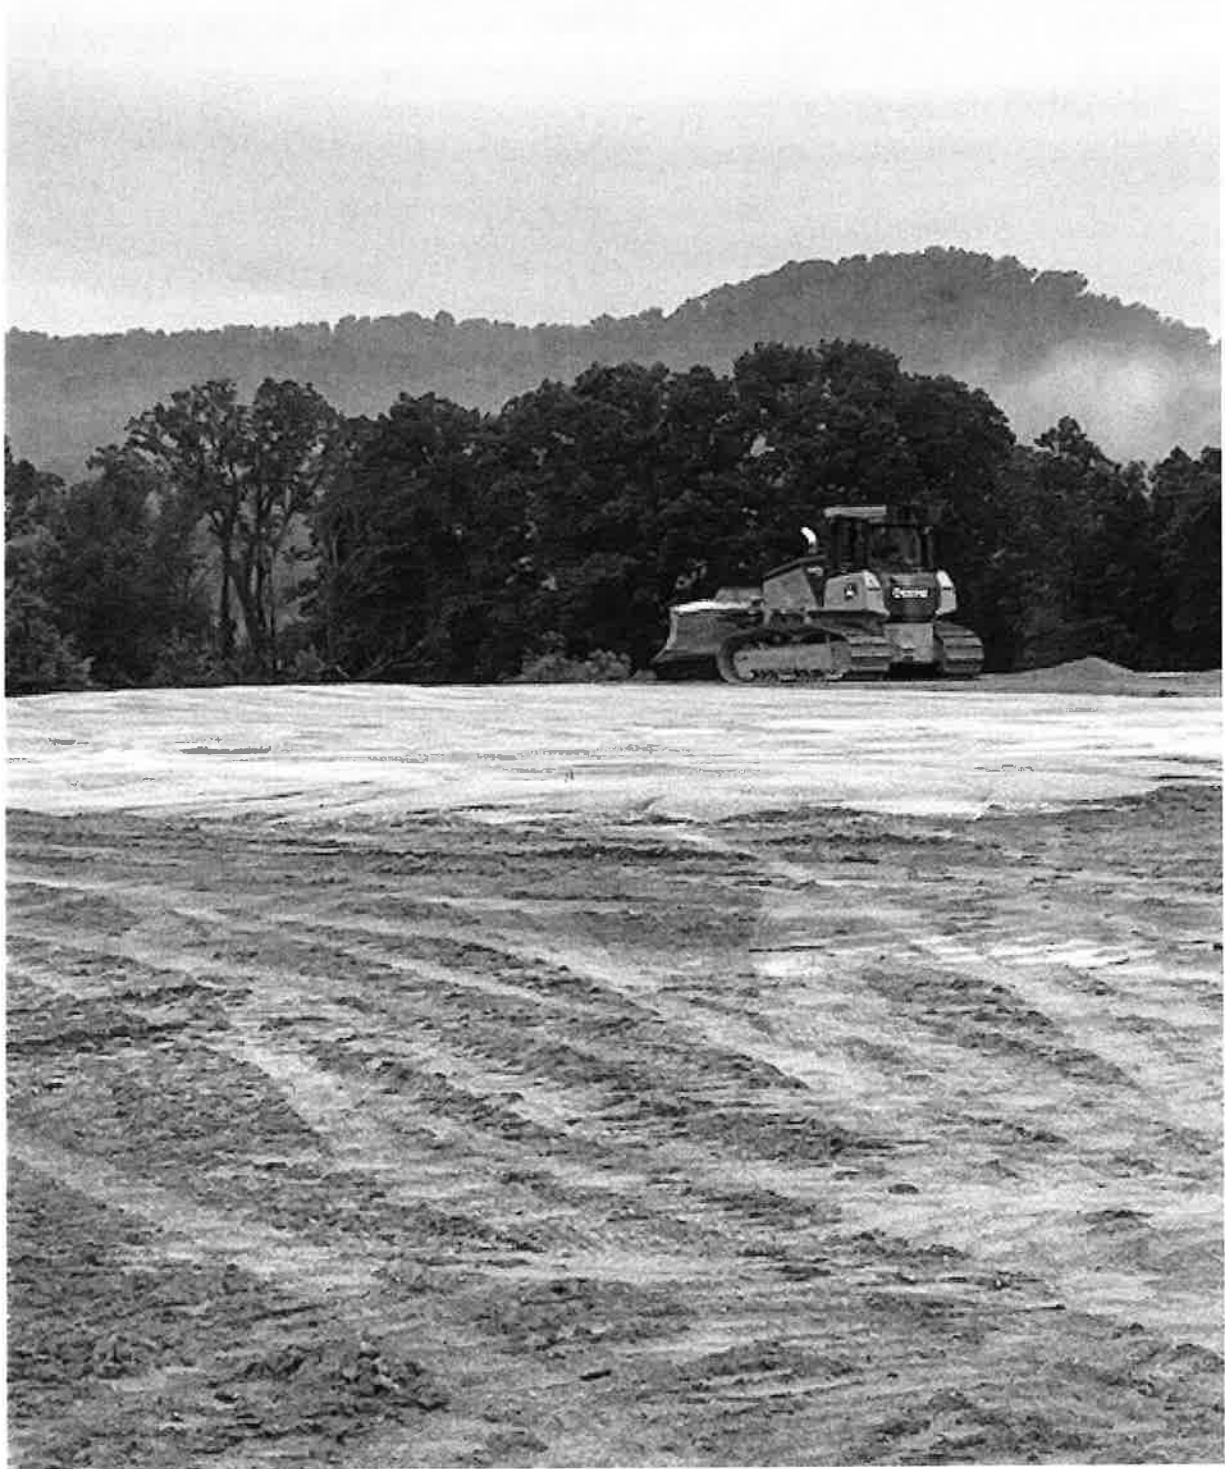



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

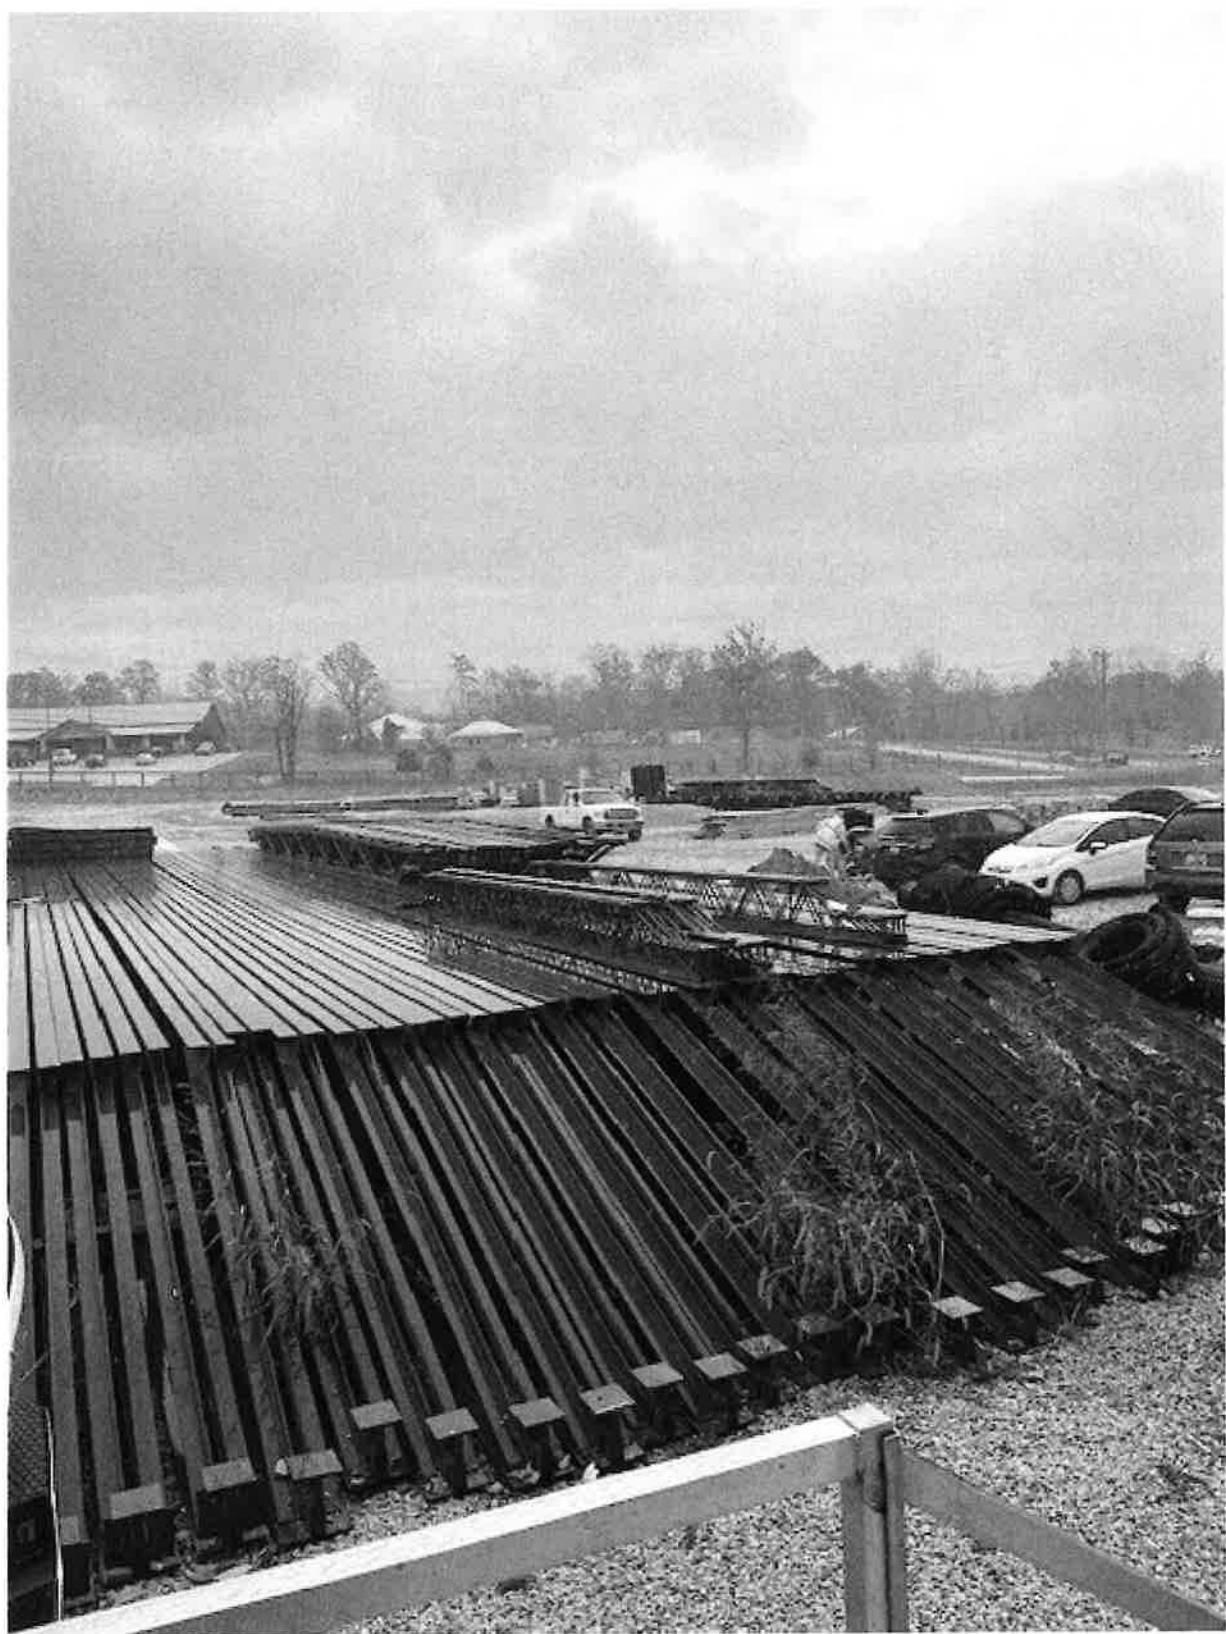



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

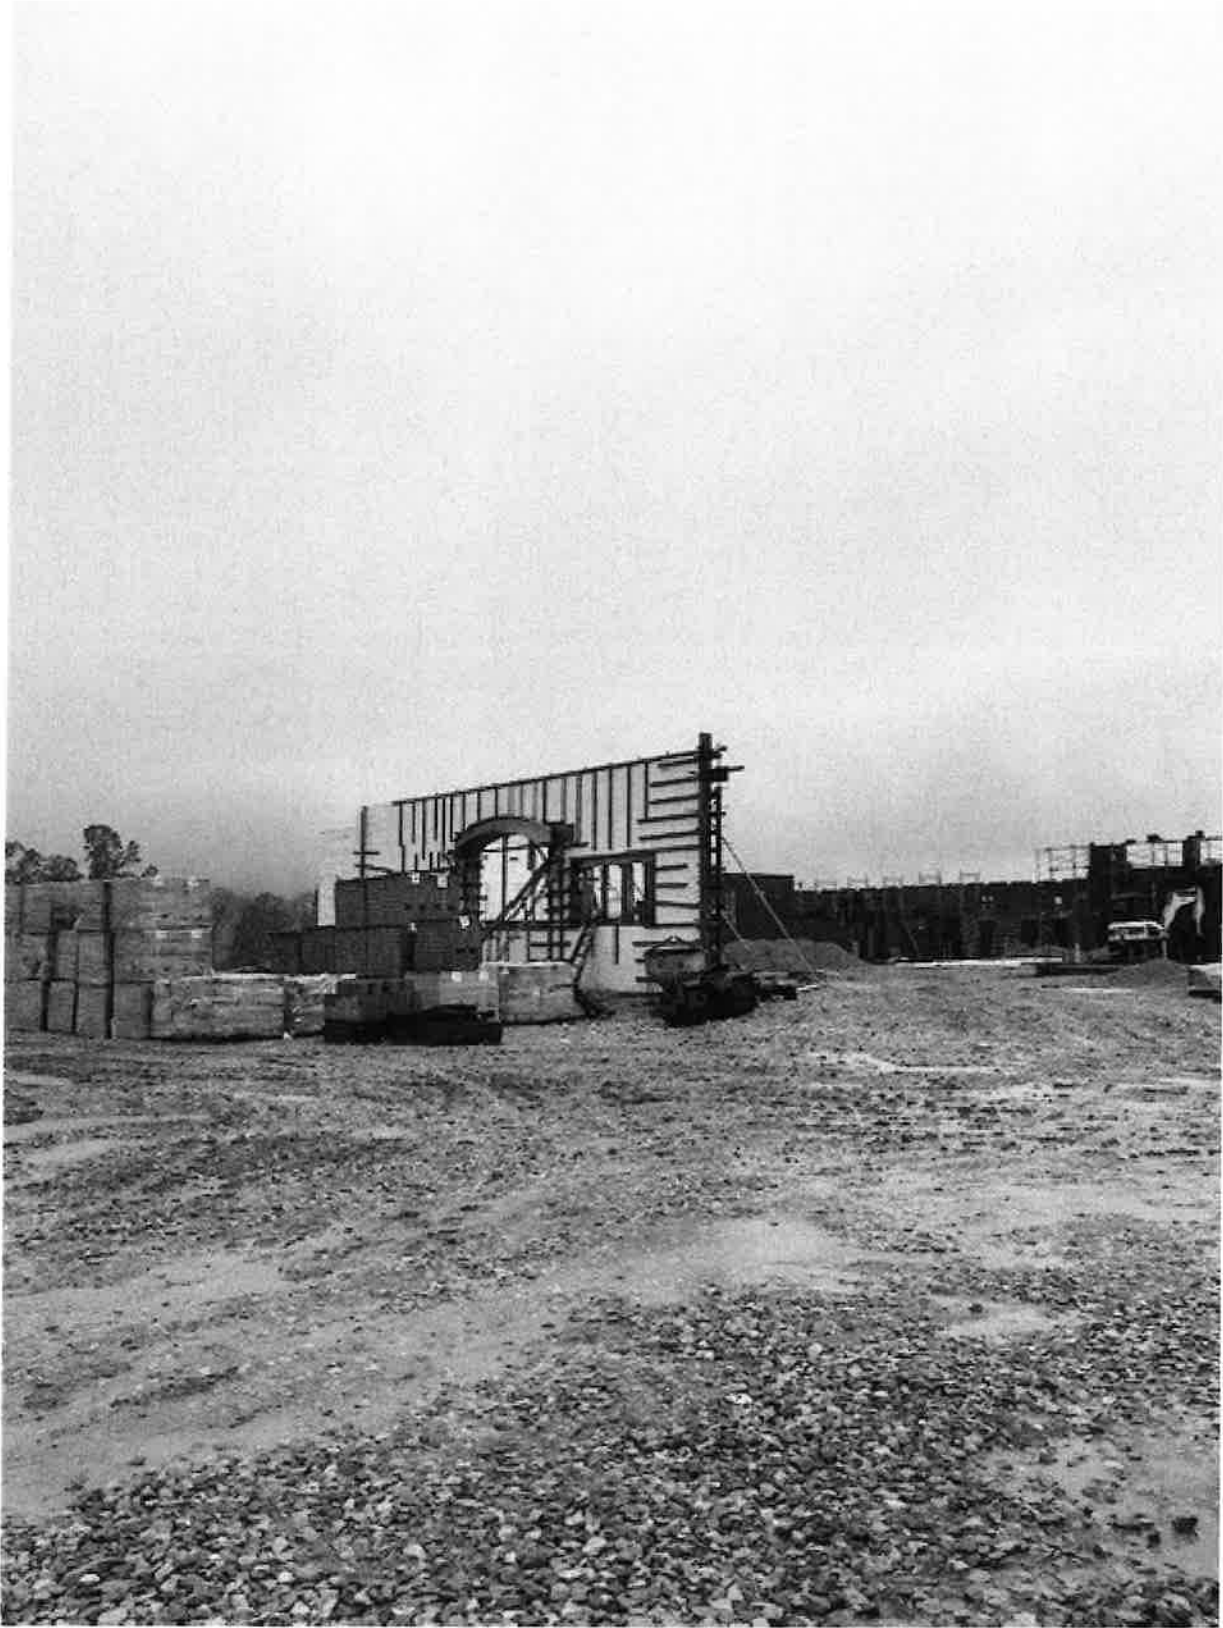



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00
hours

52° F
rain

1
notes

2
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM


File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM

File
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM

File
Daily Report 2024...
Michael Graf





Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

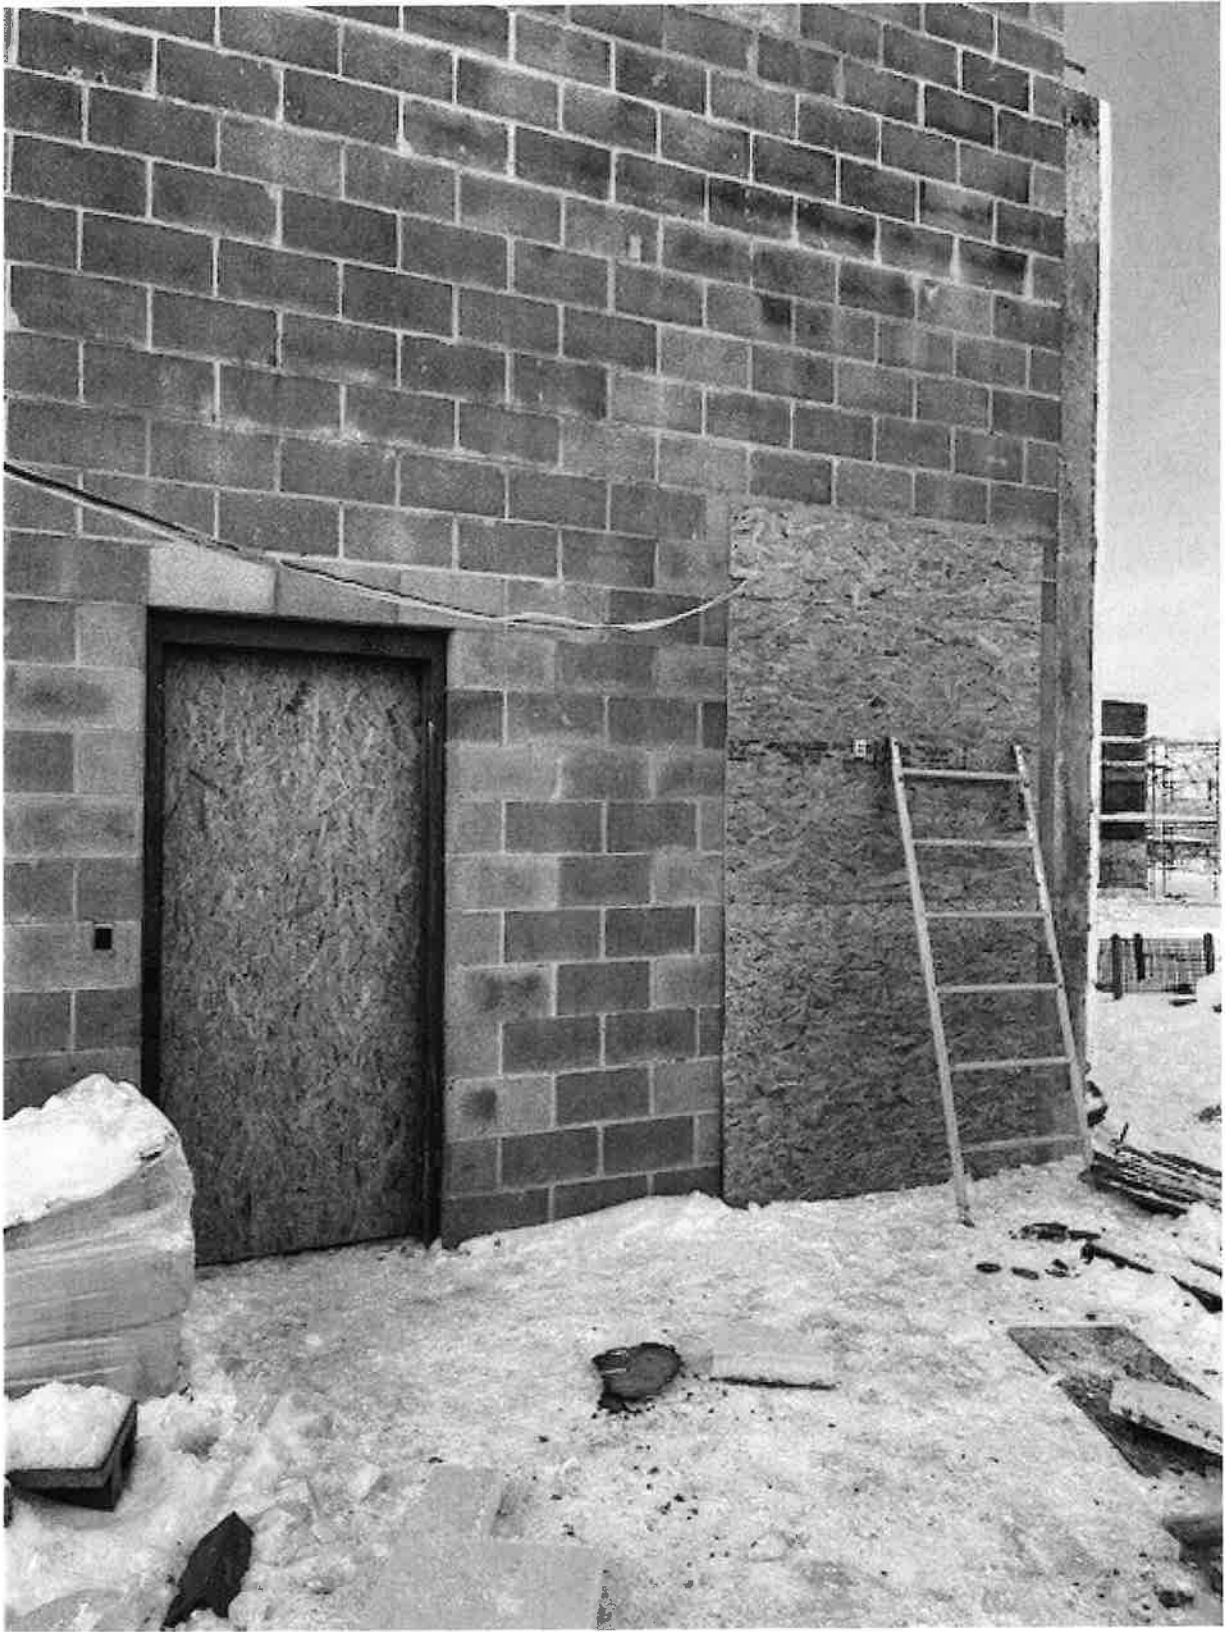



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00
hours

26° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM

File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

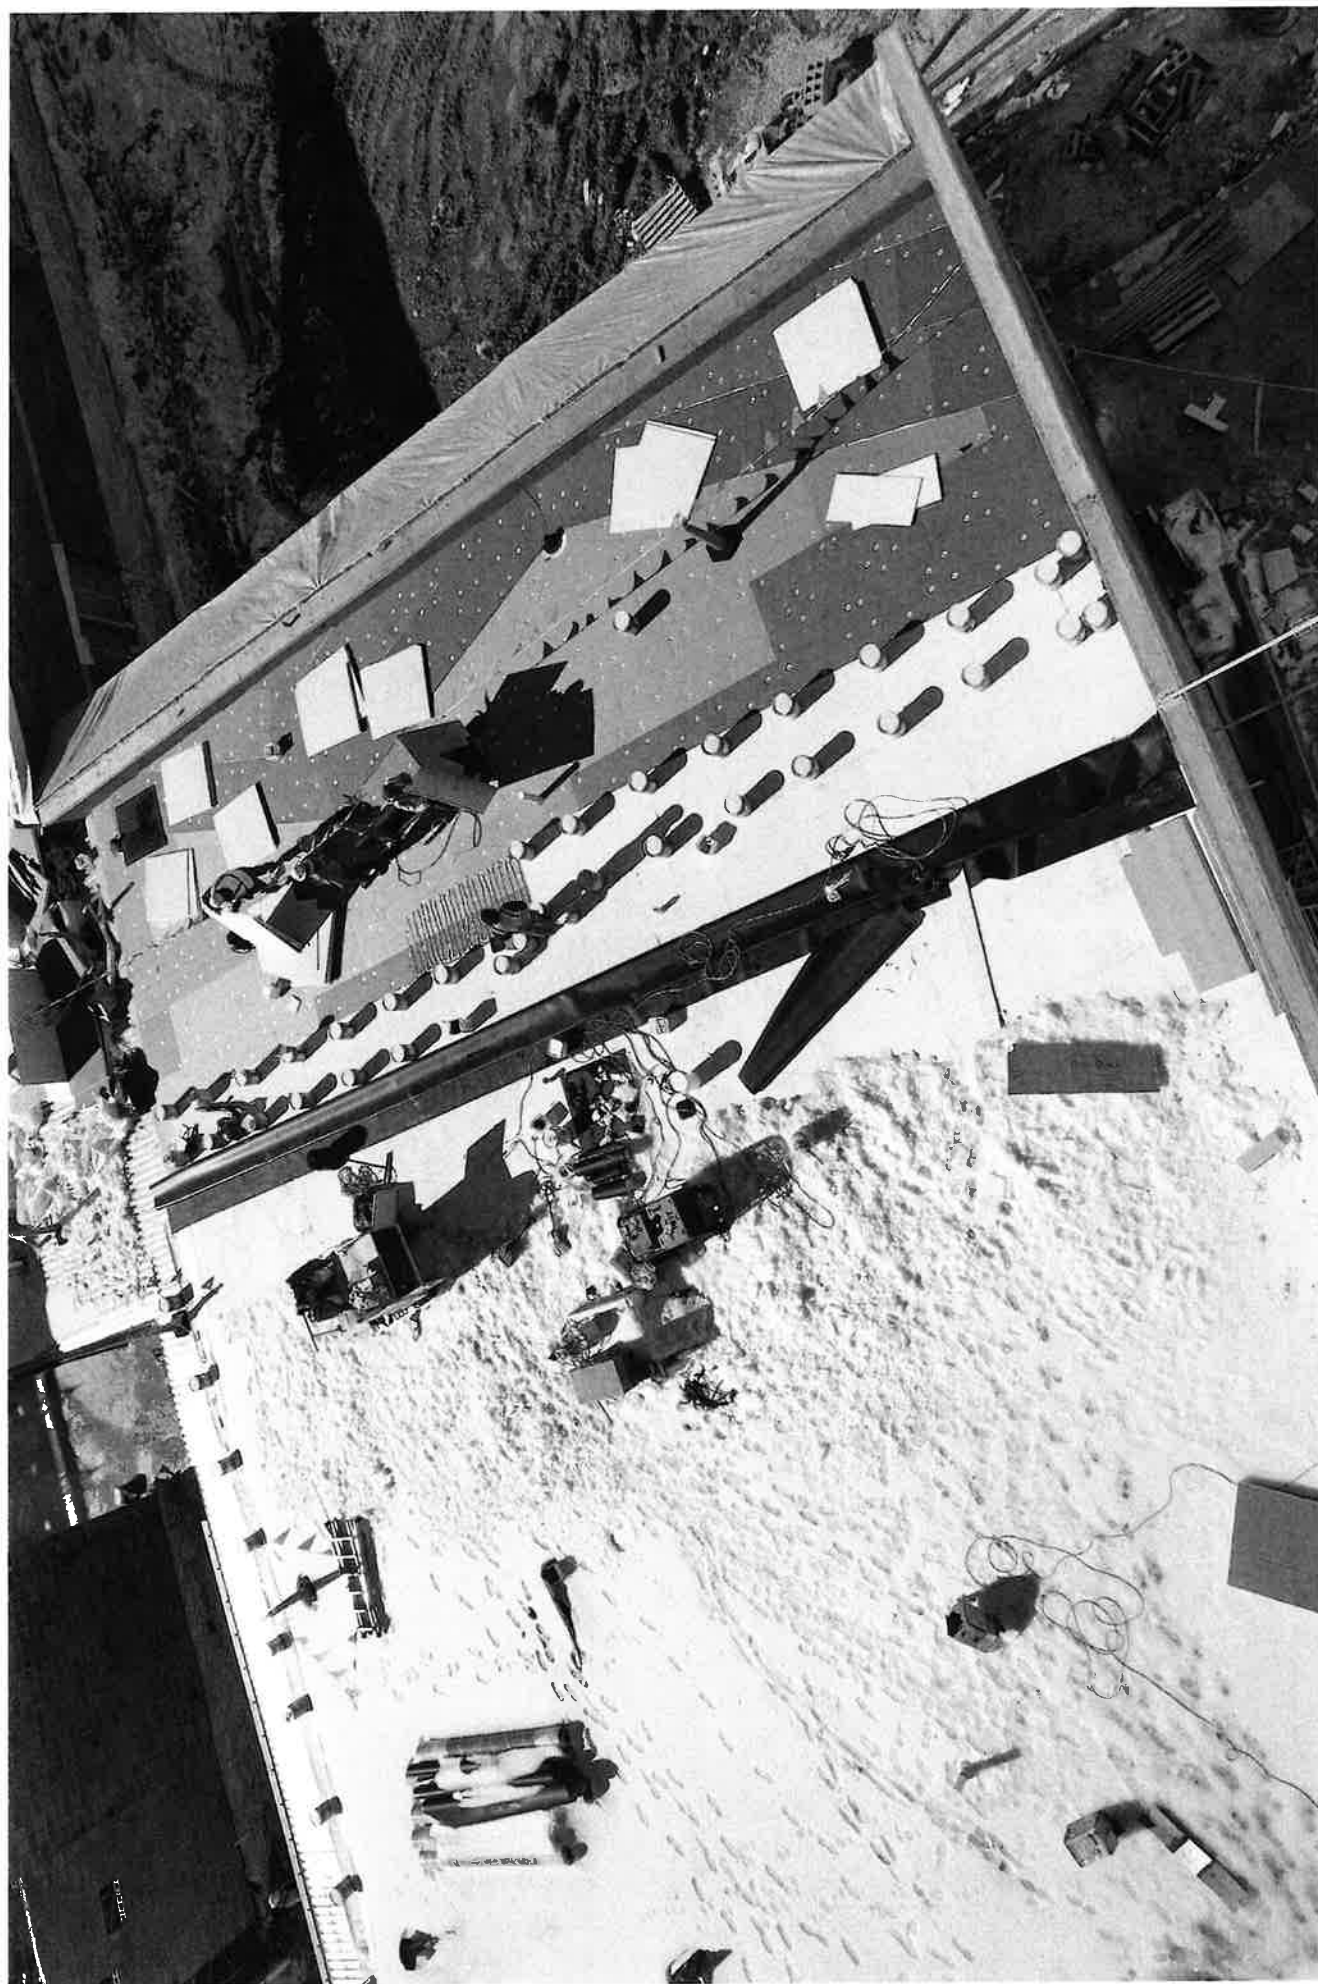



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
KENTUCKY SHEET	Installing floor drains in mezzanine				
METAL, INC (N/A)	(Area C)				
GRAYHAWK, LLC	Topping out masonry walls in (Area A)		4.00	32.00 Hours	Approved
(N/A)					
MASON	Laying up brick on north facade of (Area		8.00	64.00 Hours	Approved
STRUCTURE, INC.	B)				
(N/A)					
RIMAR ELECTRIC,	(4) Installing cable trays in (Area B)		9.00	72.00 Hours	Approved
LLC (N/A)	(5) Pulling wire in west wing of (Area B)				
RISING SUN	(2) Sealing exterior ICF wall bar joist		12.00	96.00 Hours	Approved
DEVELOPING	pockets.				
COMPANY (N/A)	(5) Prepping mezzanine HCP's for				
	topping coat.				
	(2) clean up.				
	(3) installing metal stud partition walls				
	wood blocking (Pre school)				
SPRAY FOAM	Applying initial finish coat in kitchen and		2.00	16.00 Hours	Approved
TECHNOLOGIES	cafeteria.				
OF KY (N/A)					

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00	63° F	2	6	● Approved
hours	thunderstorm	notes	equipment	status

Days Lost on Project: 65.00 Days Lost on this Month: 1.00

WEATHER Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✔ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✔ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✔ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✔ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✔ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✔ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✔ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✔ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✔ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✔ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✔ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✔ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✔ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✔ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✔ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✔ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✔ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✔ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✔ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✔ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✔ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✔ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✔ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✔ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✔ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD


Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1290110101010101

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62486)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Dixie Roofing, Inc., 0006, Roof

Type: CM Bid Package

Proposed

Change Order Number06-01

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency
Balance

Contract Change Requested By Construction Manager

Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62486)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 06-01
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 DIXIE ROOFING, INC.

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #06 ROOF

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	406,280.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	406,280.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	406,280.00

The Contract Time will be adjusted by 92 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

DIXIE ROOFING, INC.

CONTRACTOR (Firm Name)

ADDRESS

BY (Signature)

(Typed Name)

DATE:

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

BY (Signature)

(Typed Name)

DATE:

POWELL COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
 691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

BY (Signature)

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																				
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

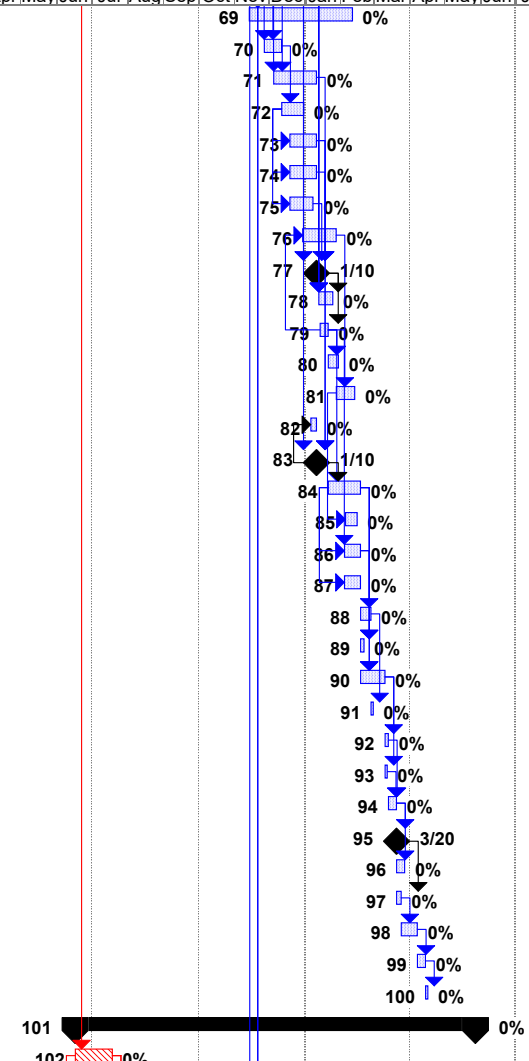

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25								
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25								
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25								
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24								
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24								
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24								
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24								
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24								
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24								
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24								
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24								
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24								
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24								
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24								
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24								
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24								
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24								
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24								
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24								
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24								
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24								
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25								
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25								
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25								
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24								
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25								
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25								
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25								
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25								
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25								

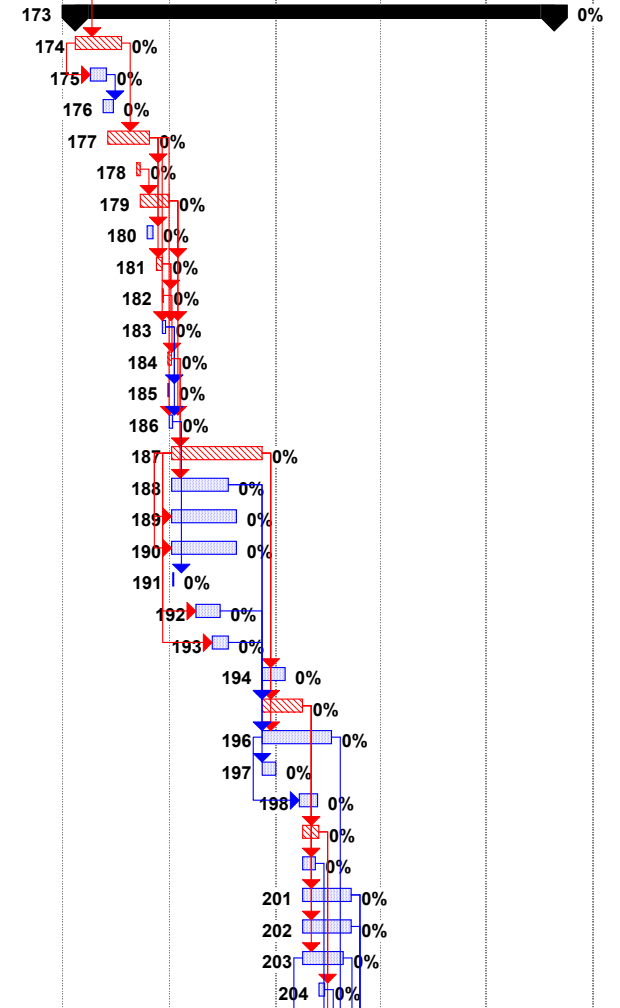

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																								
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																								
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																								
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																								
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																								
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																								
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																								
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																								
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																								
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																								
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																								
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																								
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																								
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																								
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																								
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																								
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																								
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																								
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																								
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																								
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																								
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																								
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																								
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																								
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																								
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																								
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																								
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																								
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																								
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																								
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																								
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

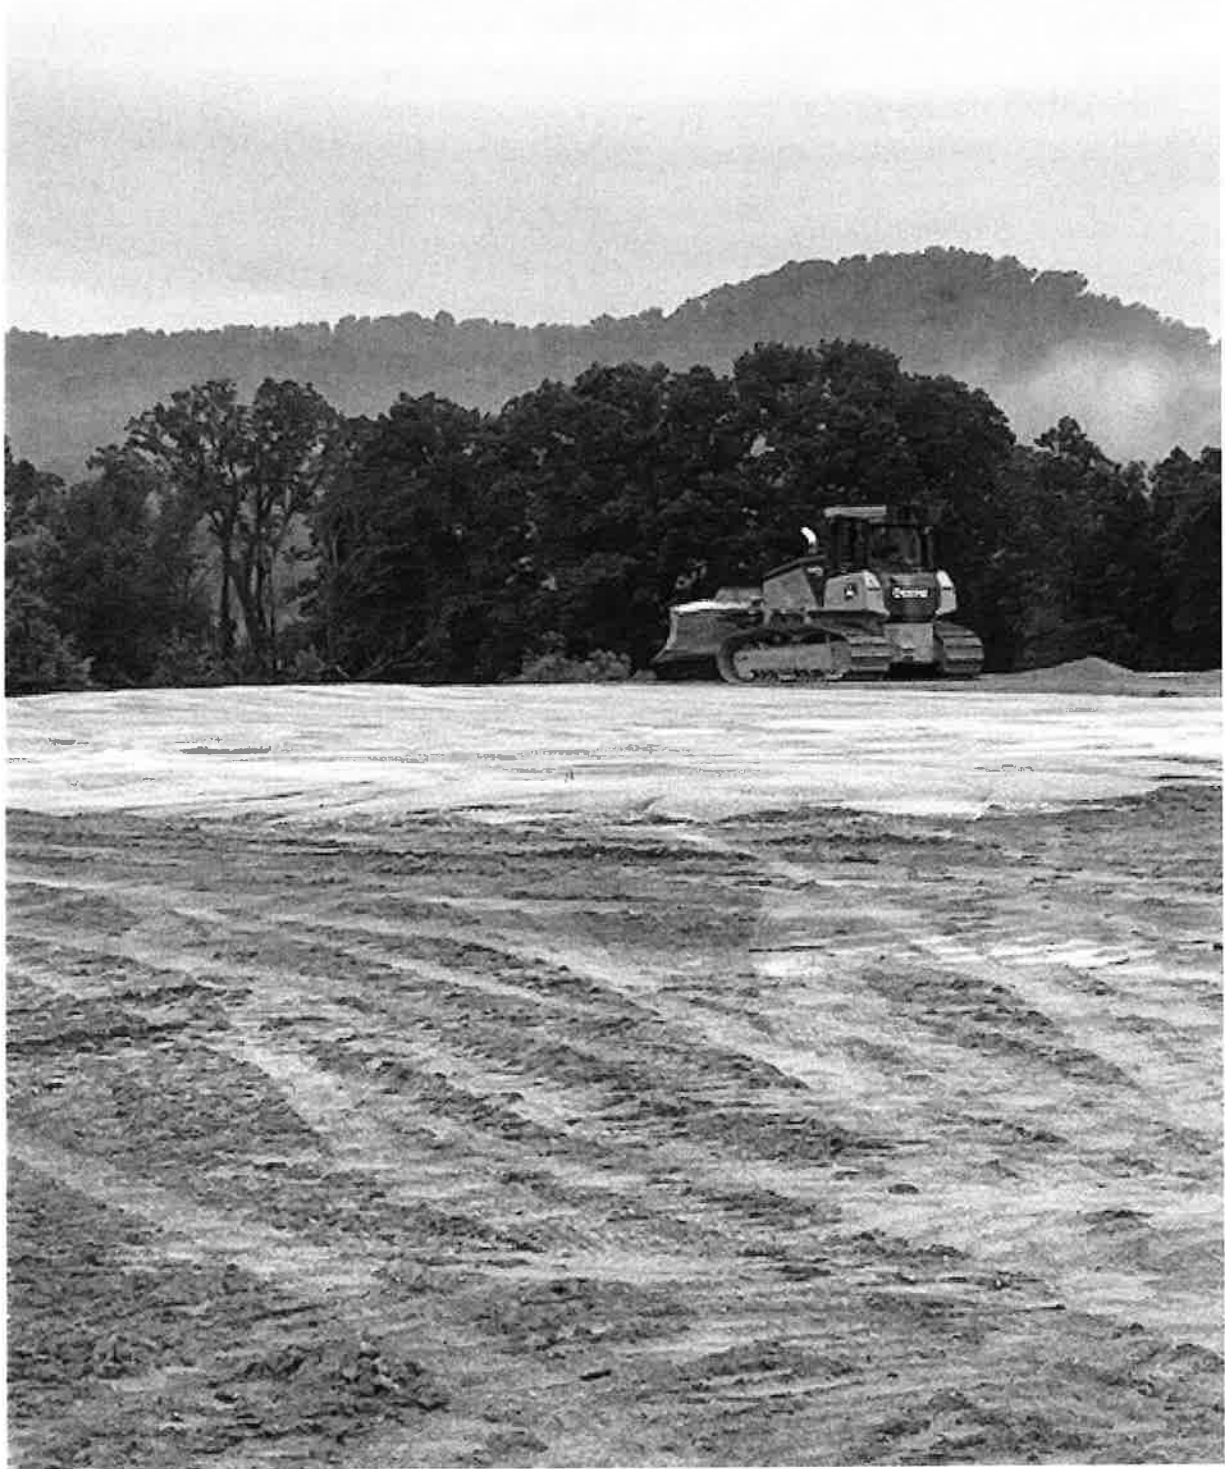



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf


Michael Graf on 9/24/2024 03:18 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

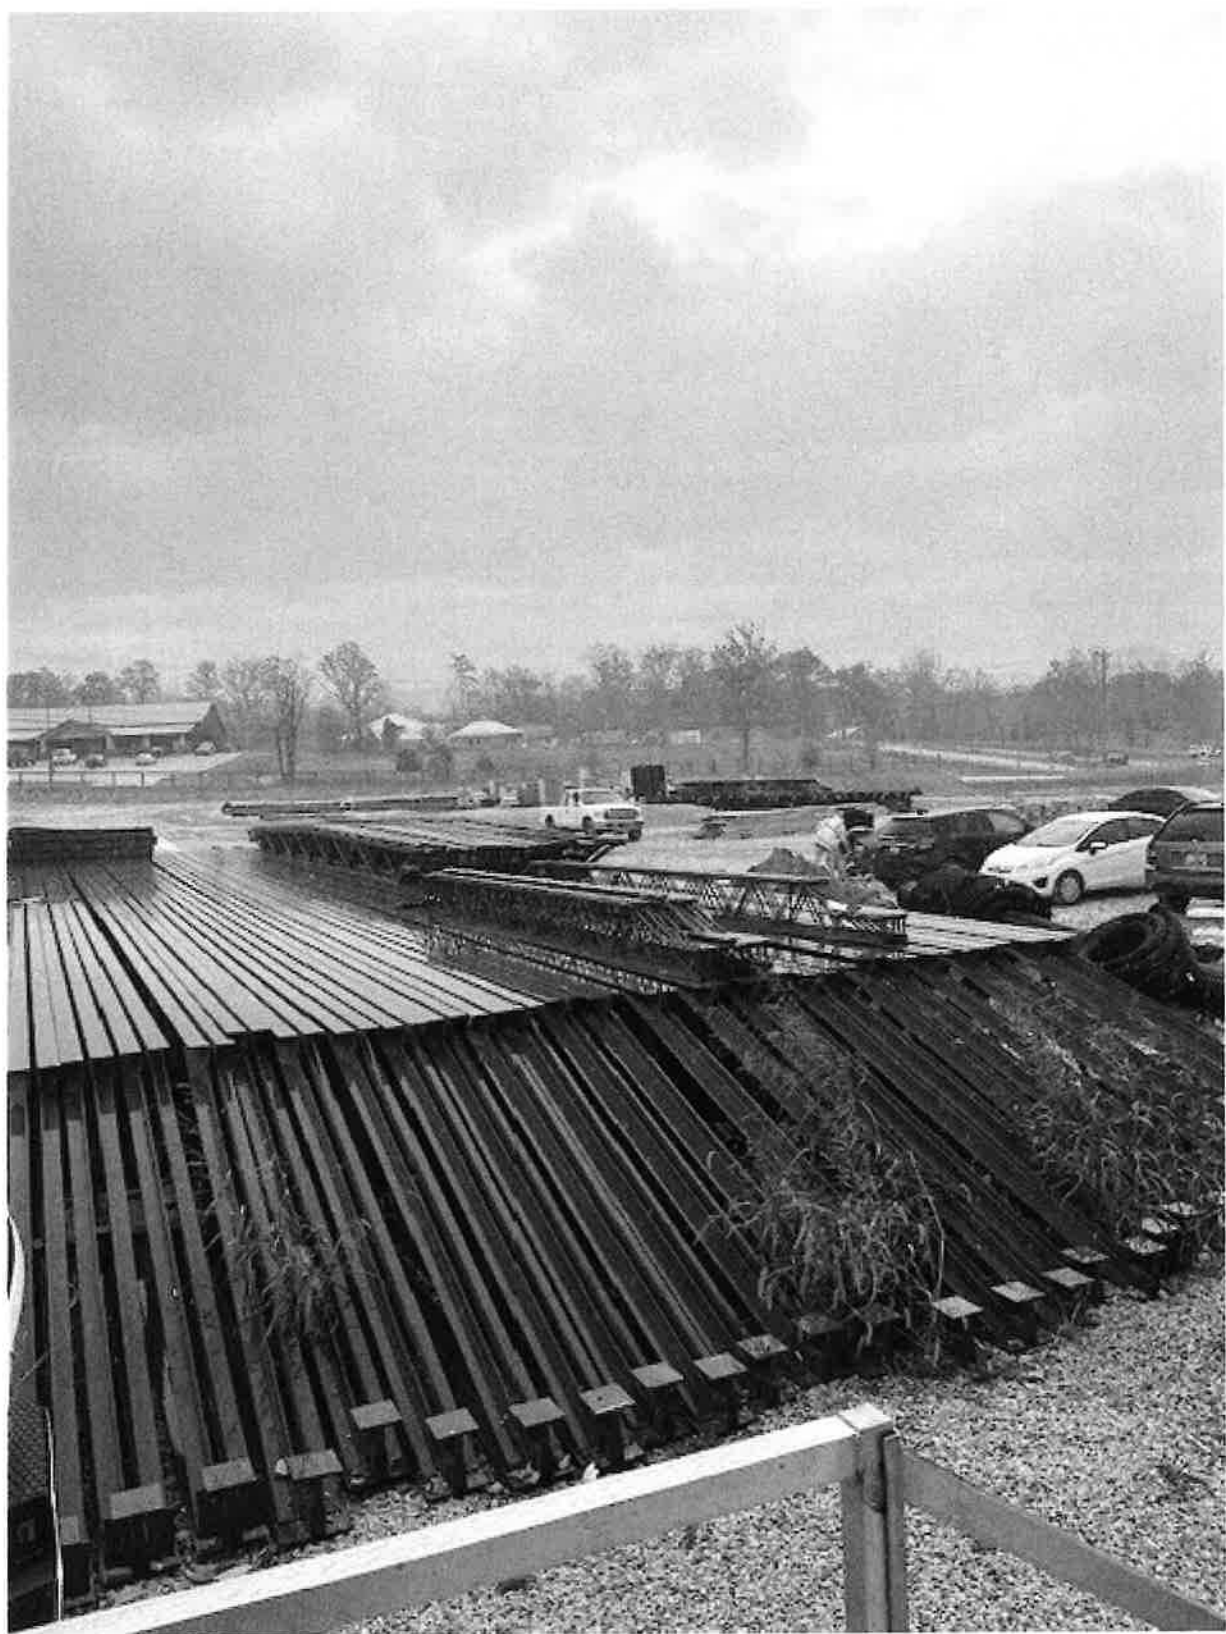



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

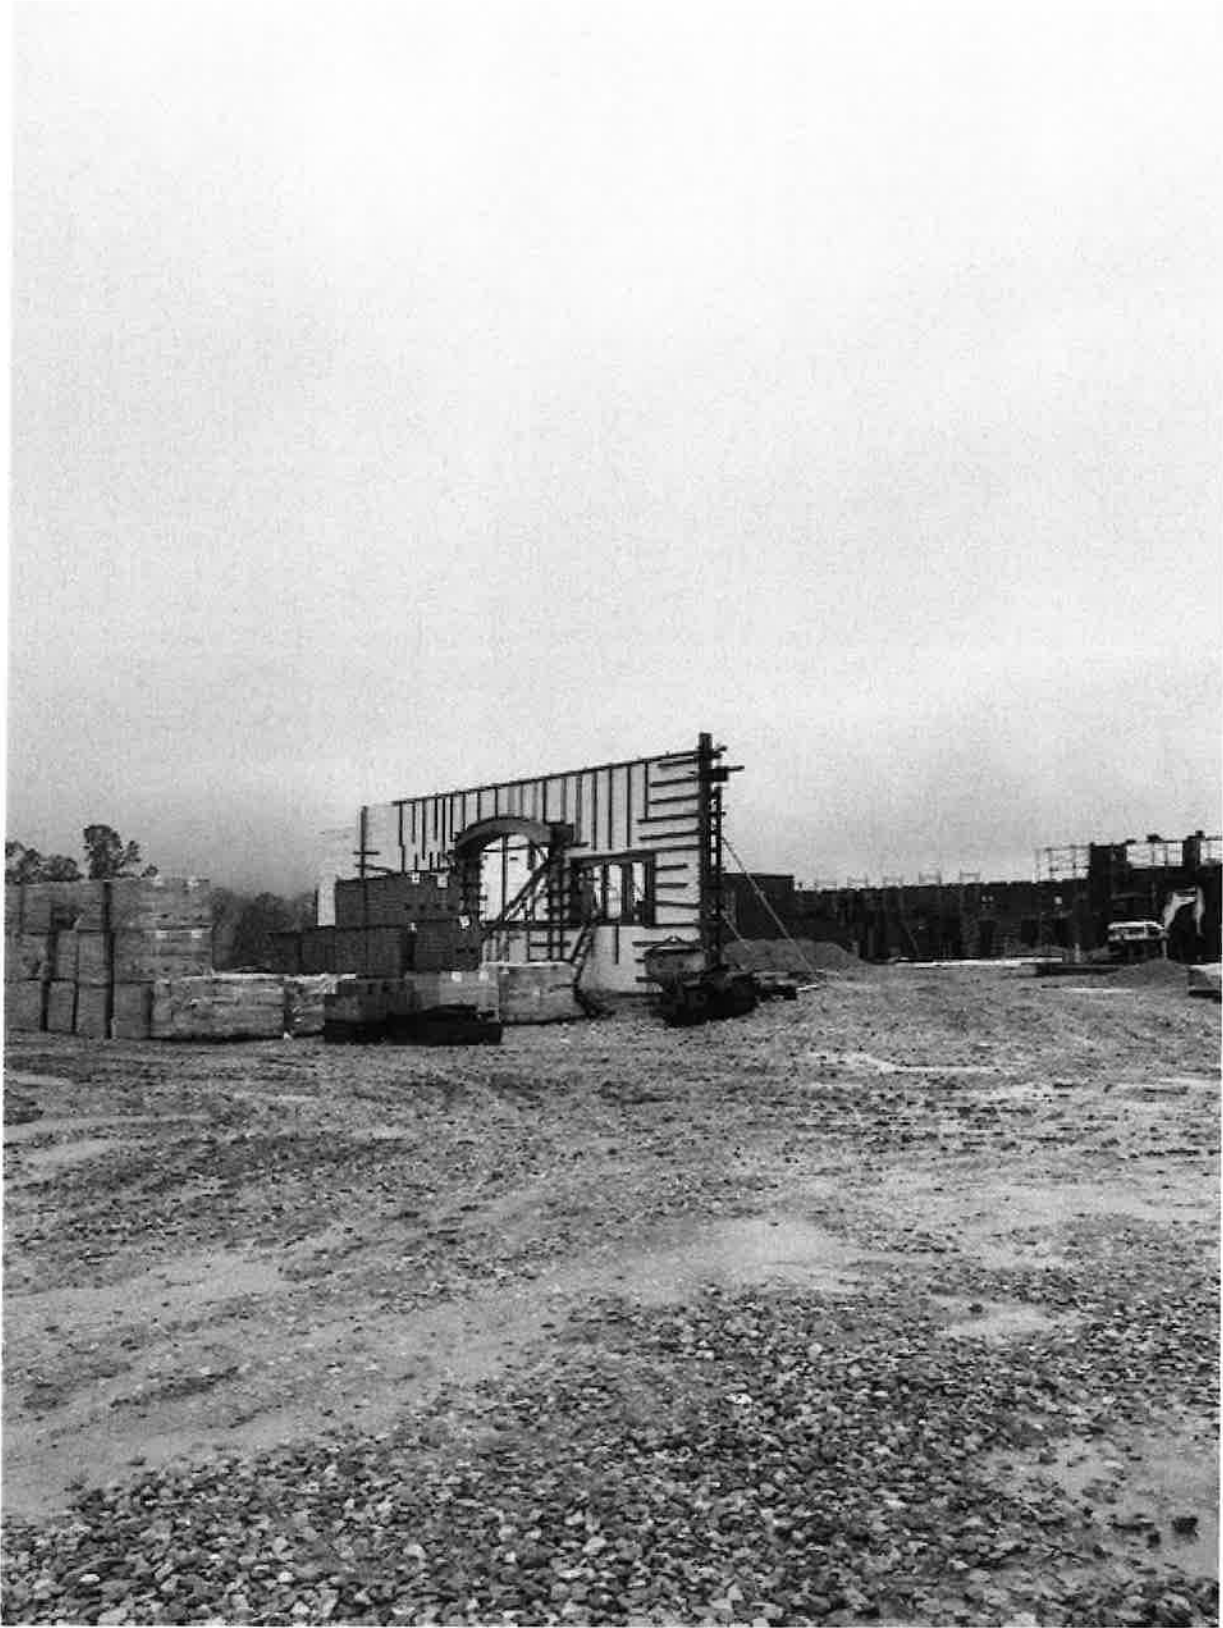



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**


Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM

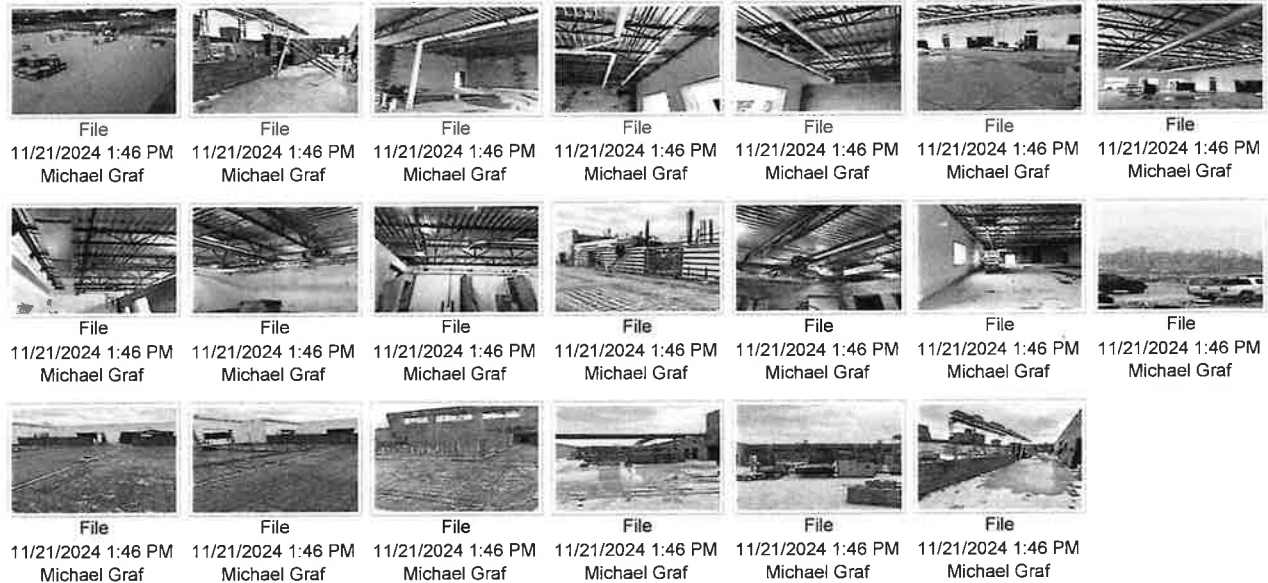

Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf




File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

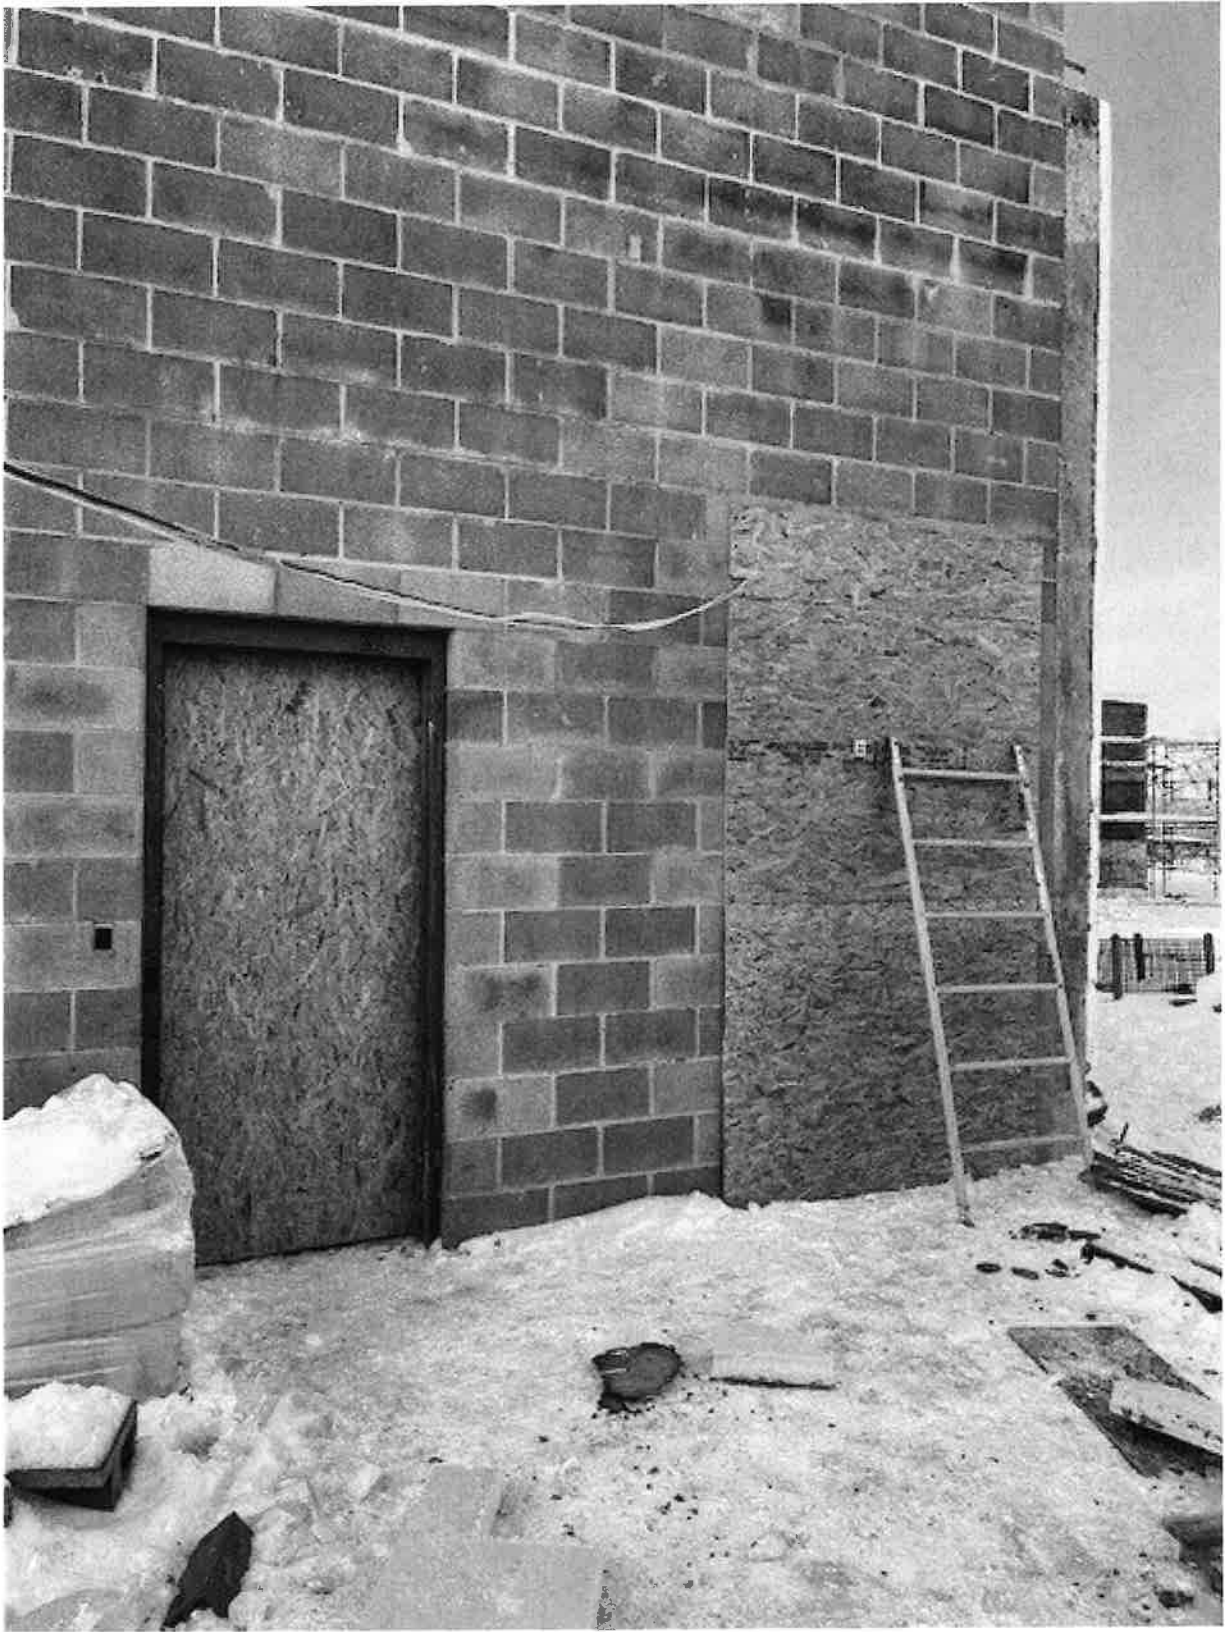



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
	Installing above ceiling hanger and ductwork in the North and West wings of (Area B).				
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area.		9.00	72.00 Hours	Approved
	(4) Hanging drywall the kitchen and cafeteria areas.				
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
	Grouting bearing walls. Approximately 7 cubic yards.				
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A)		9.00	72.00 Hours	Approved
	(2) Installing electrical rough-in's in metal stud partition walls in administration area.				
	(2) Pulling wire in the kitchen and cafeteria area				
	(2) Pulling wire and home runs in North wing of (Area B)				
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installed curb inlet 4D.				
	Inspecting steel decking in west wing of (Area B)		1.00	3.00 Hours	Approved
	Testing grout samples.				


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

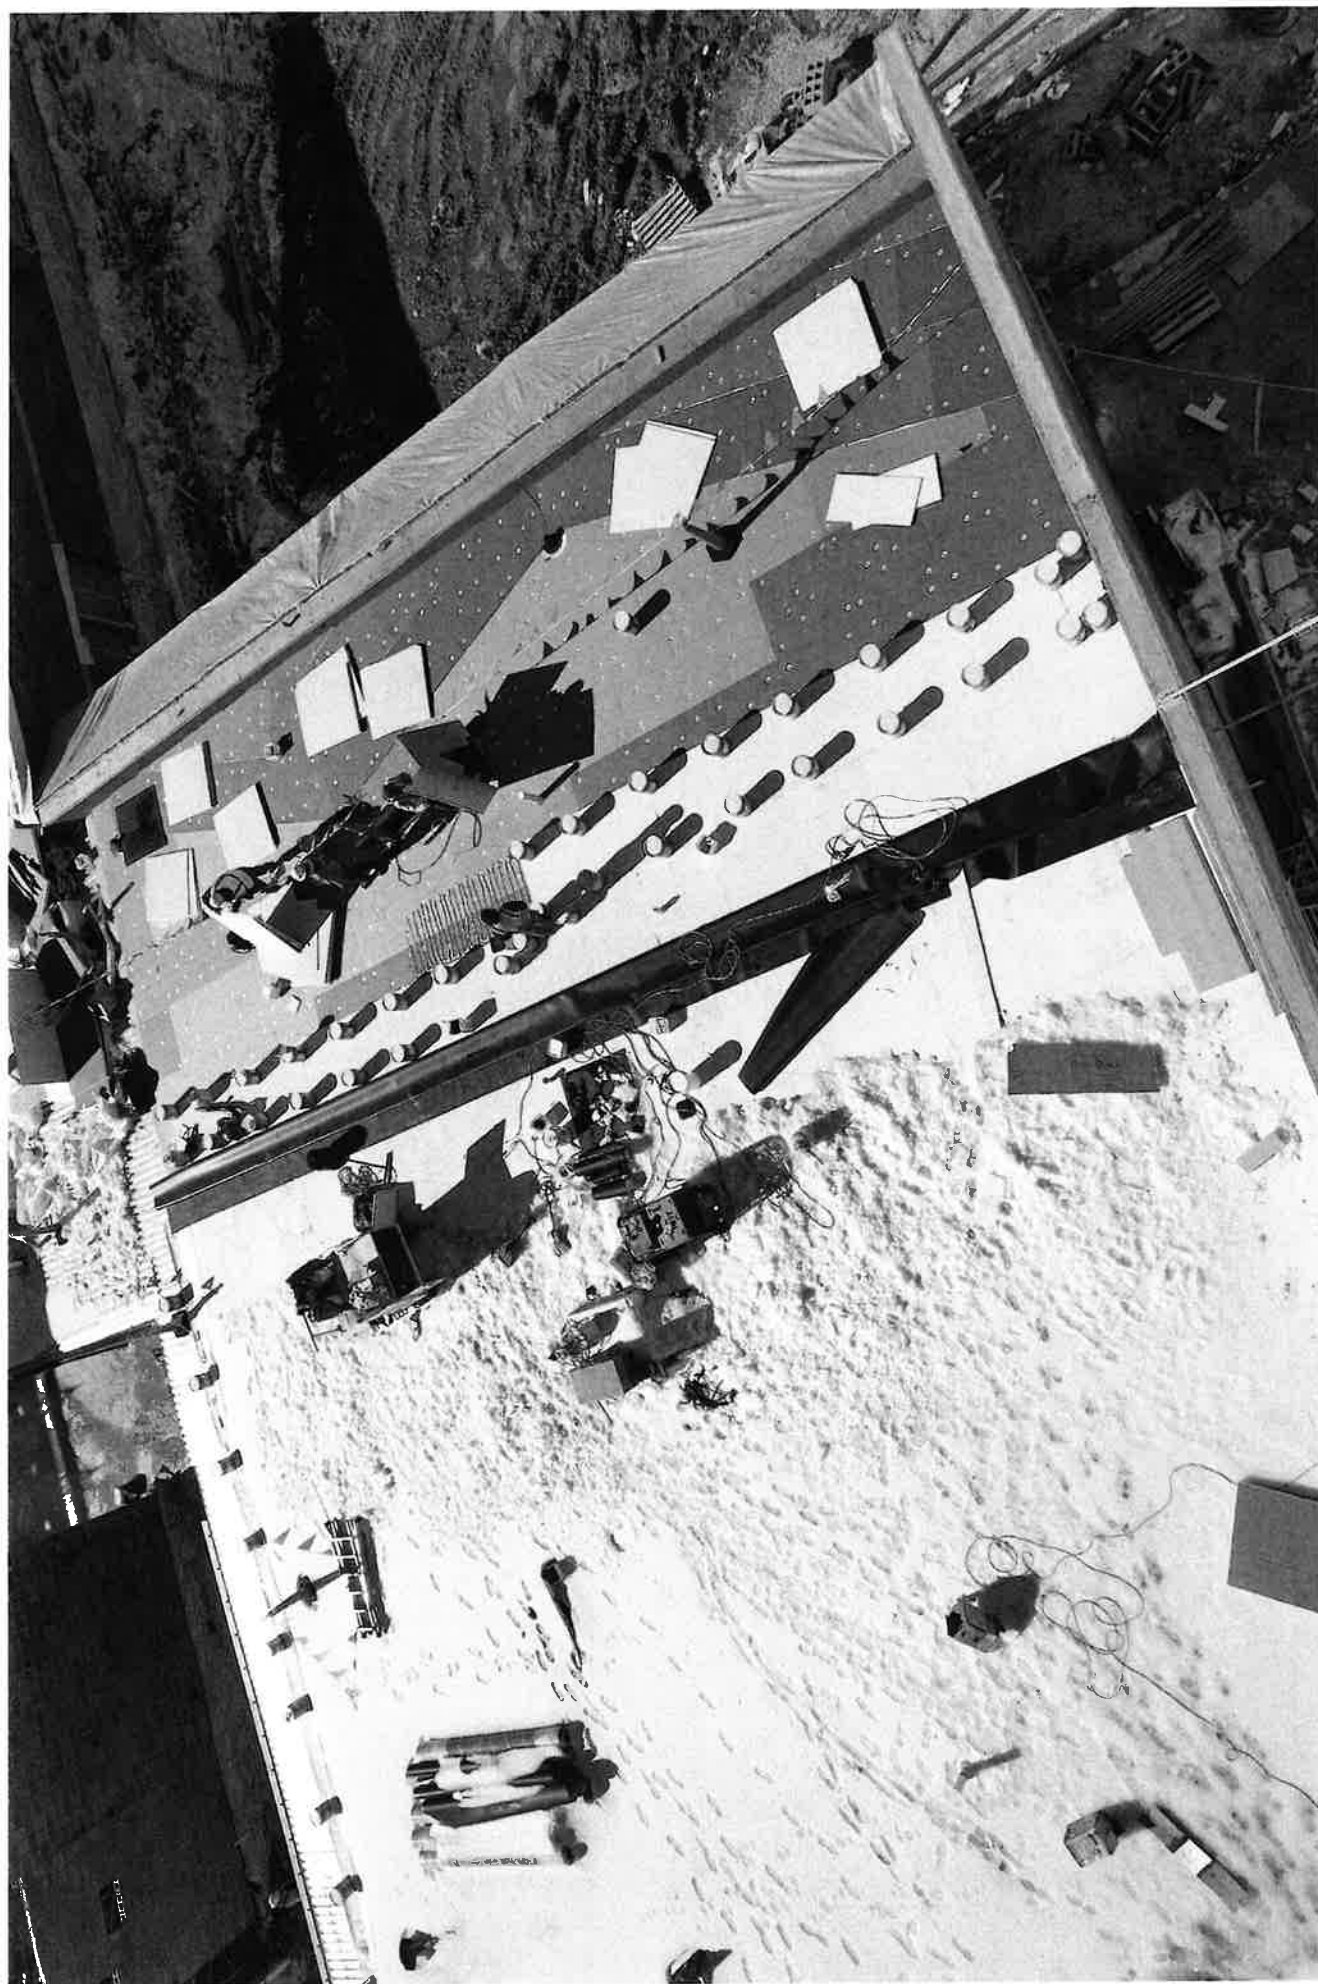



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00
hours

54° F
cloudy

2
notes

6
equipment

● Approved
status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM

File
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM


Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM

File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD


Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

1119990101010101

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62489)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School
BG Number: 21-072 District: Powell County (HB678) (495)
Status: Active Phase: Project Initiation (View Checklist)

Contract: Grayhawk LLC, 0007, Drywall
Type: CM Bid Package Proposed

Change Order Number 07-02
Time Extension Required Yes
If Yes Number Of Days 93
Date Of Change Order 6/9/2025
Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00
+/-
Change In A/E Fee This Change Order
+/-
Change In CM Fee This Change Order
+/-
Remaining Construction Contingency
Balance
Contract Change Requested By Construction Manager
Contract Change Reason Code Time Extension
Change Order Description And Justification
1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62489)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 07-02
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 GRAYHAWK, LLC

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #07 DRYWALL

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	502,000.00
Net change by previously authorized Change Orders	2,646.16
The Contract Sum prior to this Change Order was	504,646.16
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	504,646.16

The Contract Time will be adjusted by 93 days.

The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

GRAYHAWK, LLC

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24	13	14	15	16																
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

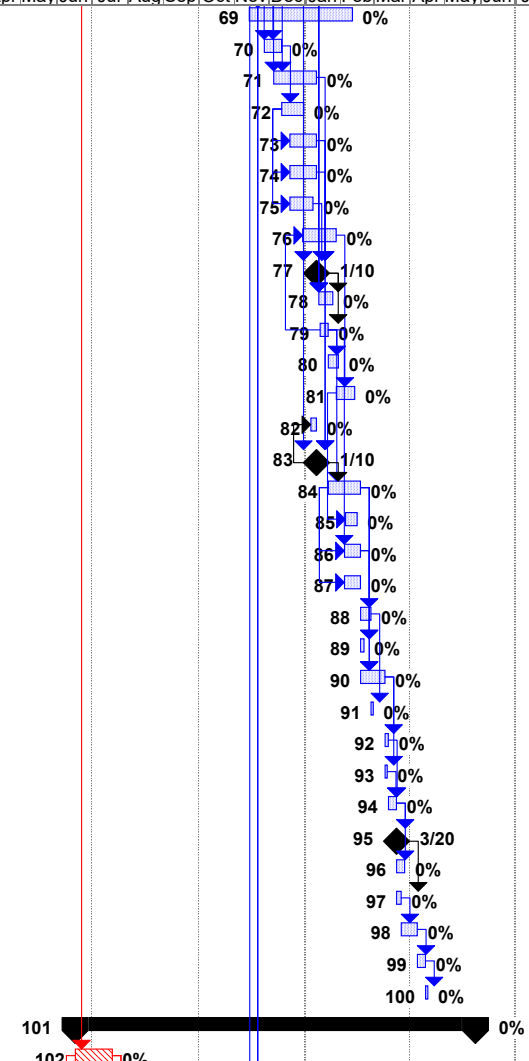

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

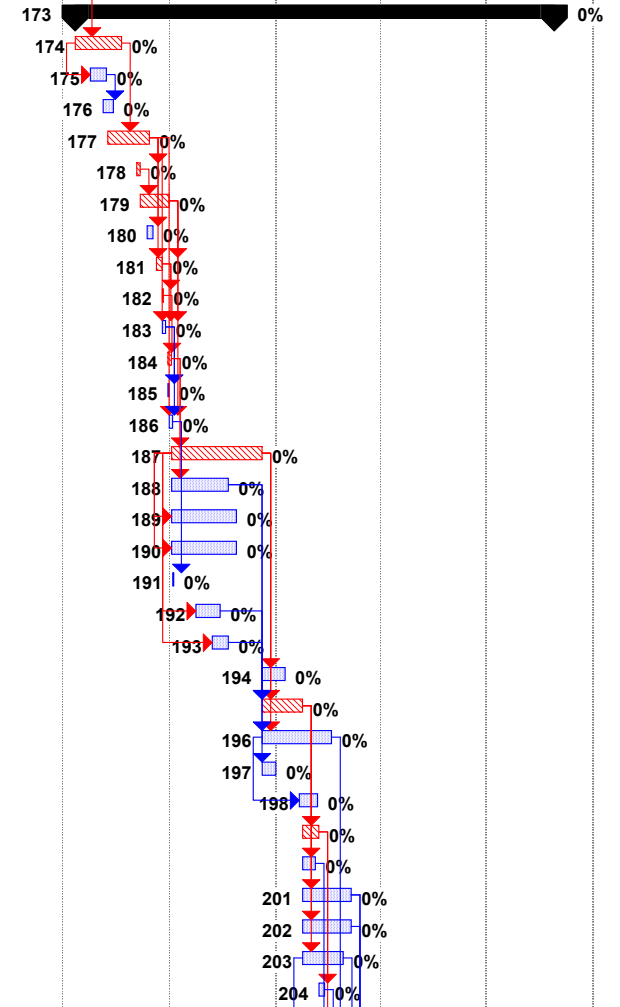

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																								
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																								
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																								
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																								
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																								
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																								
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																								
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																								
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																								
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																								
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																								
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																								
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																								
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																								
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																								
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																								
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																								
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																								
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																								
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																								
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																								
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																								
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																								
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																								
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																								
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																								
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																								
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																								
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																								
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																								
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																								
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf

Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

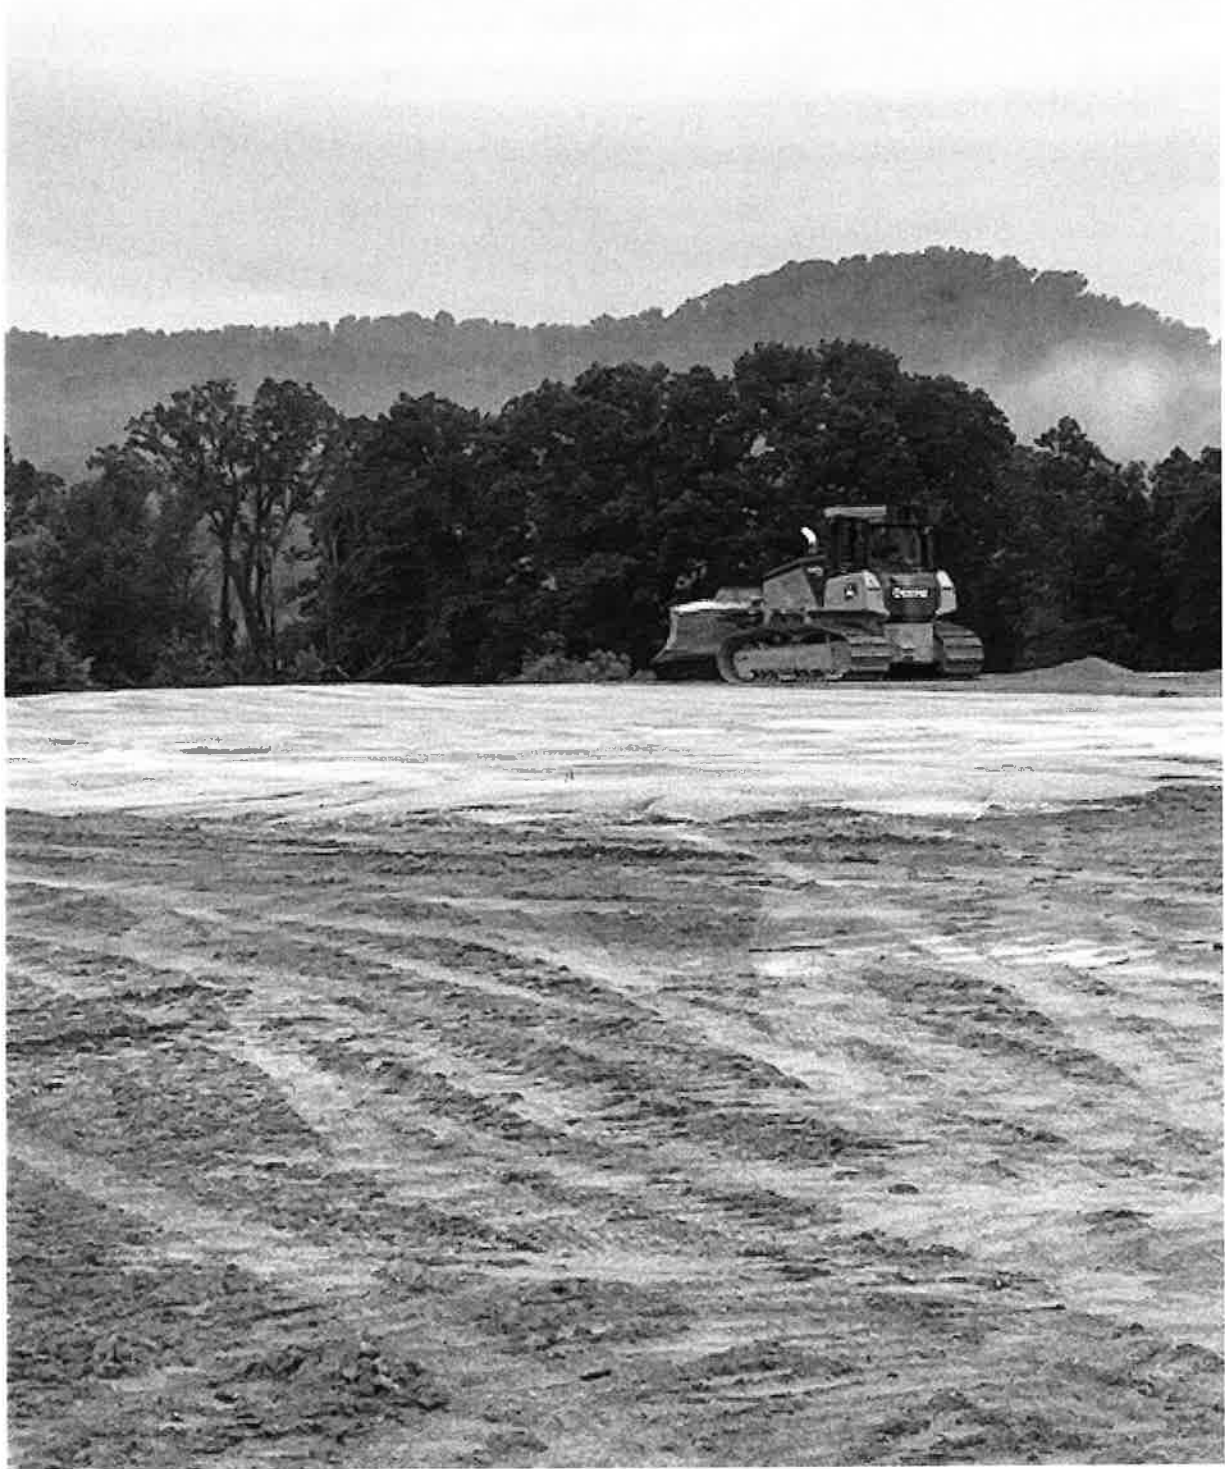



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024...,
Michael Graf

ASSIGNMENTS

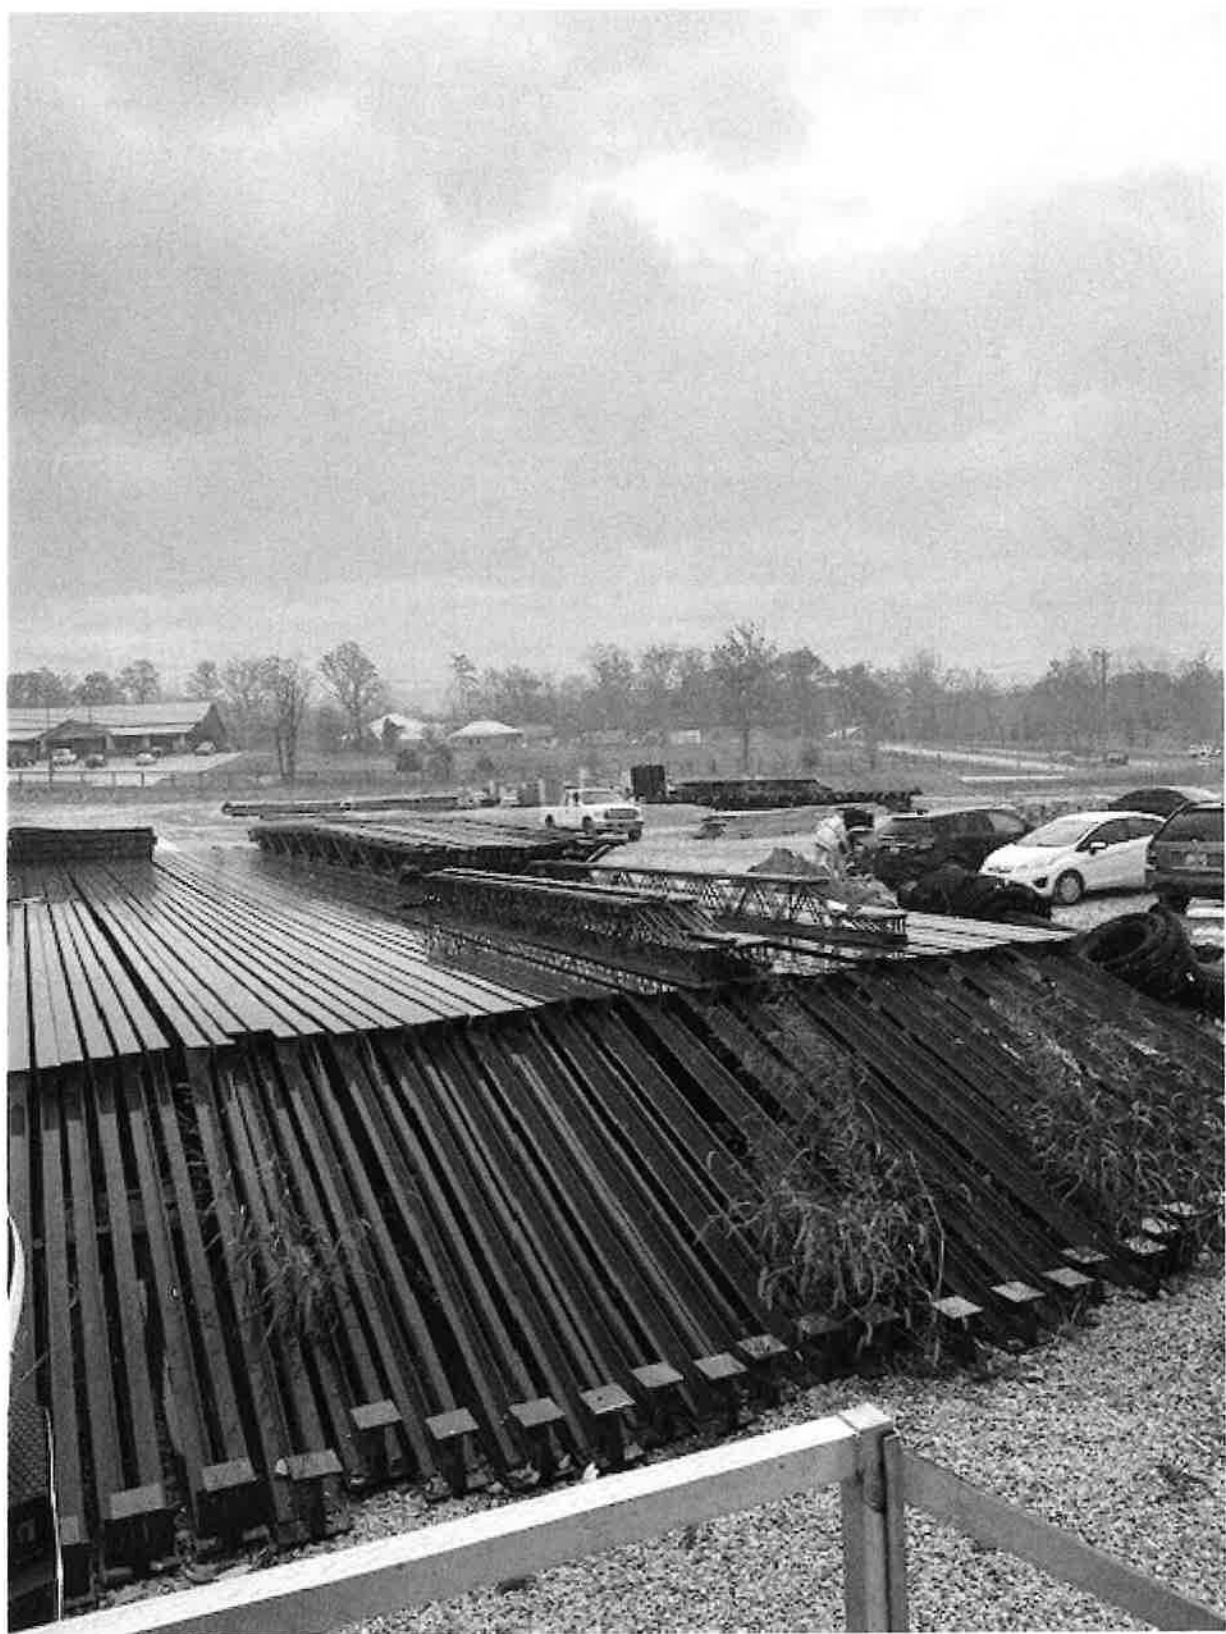



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

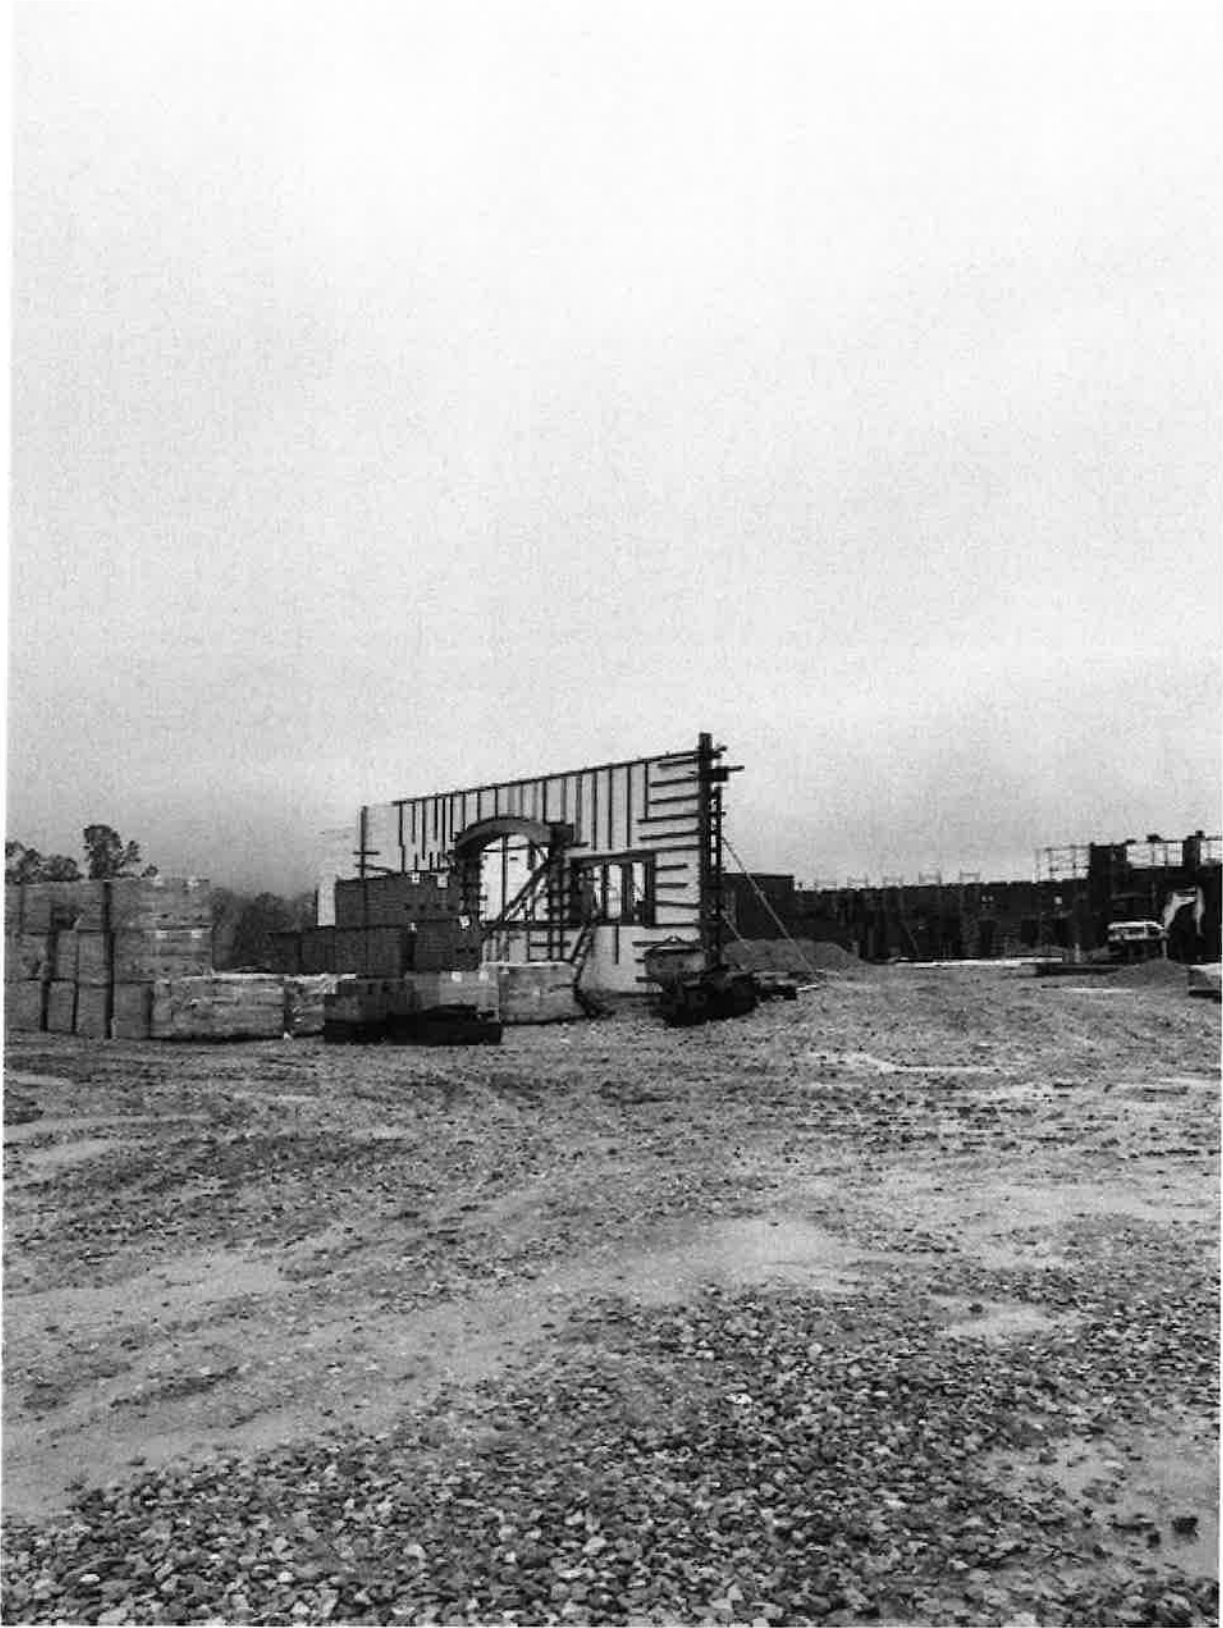



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM



File

Daily Report 2024...
Michael Graf





Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

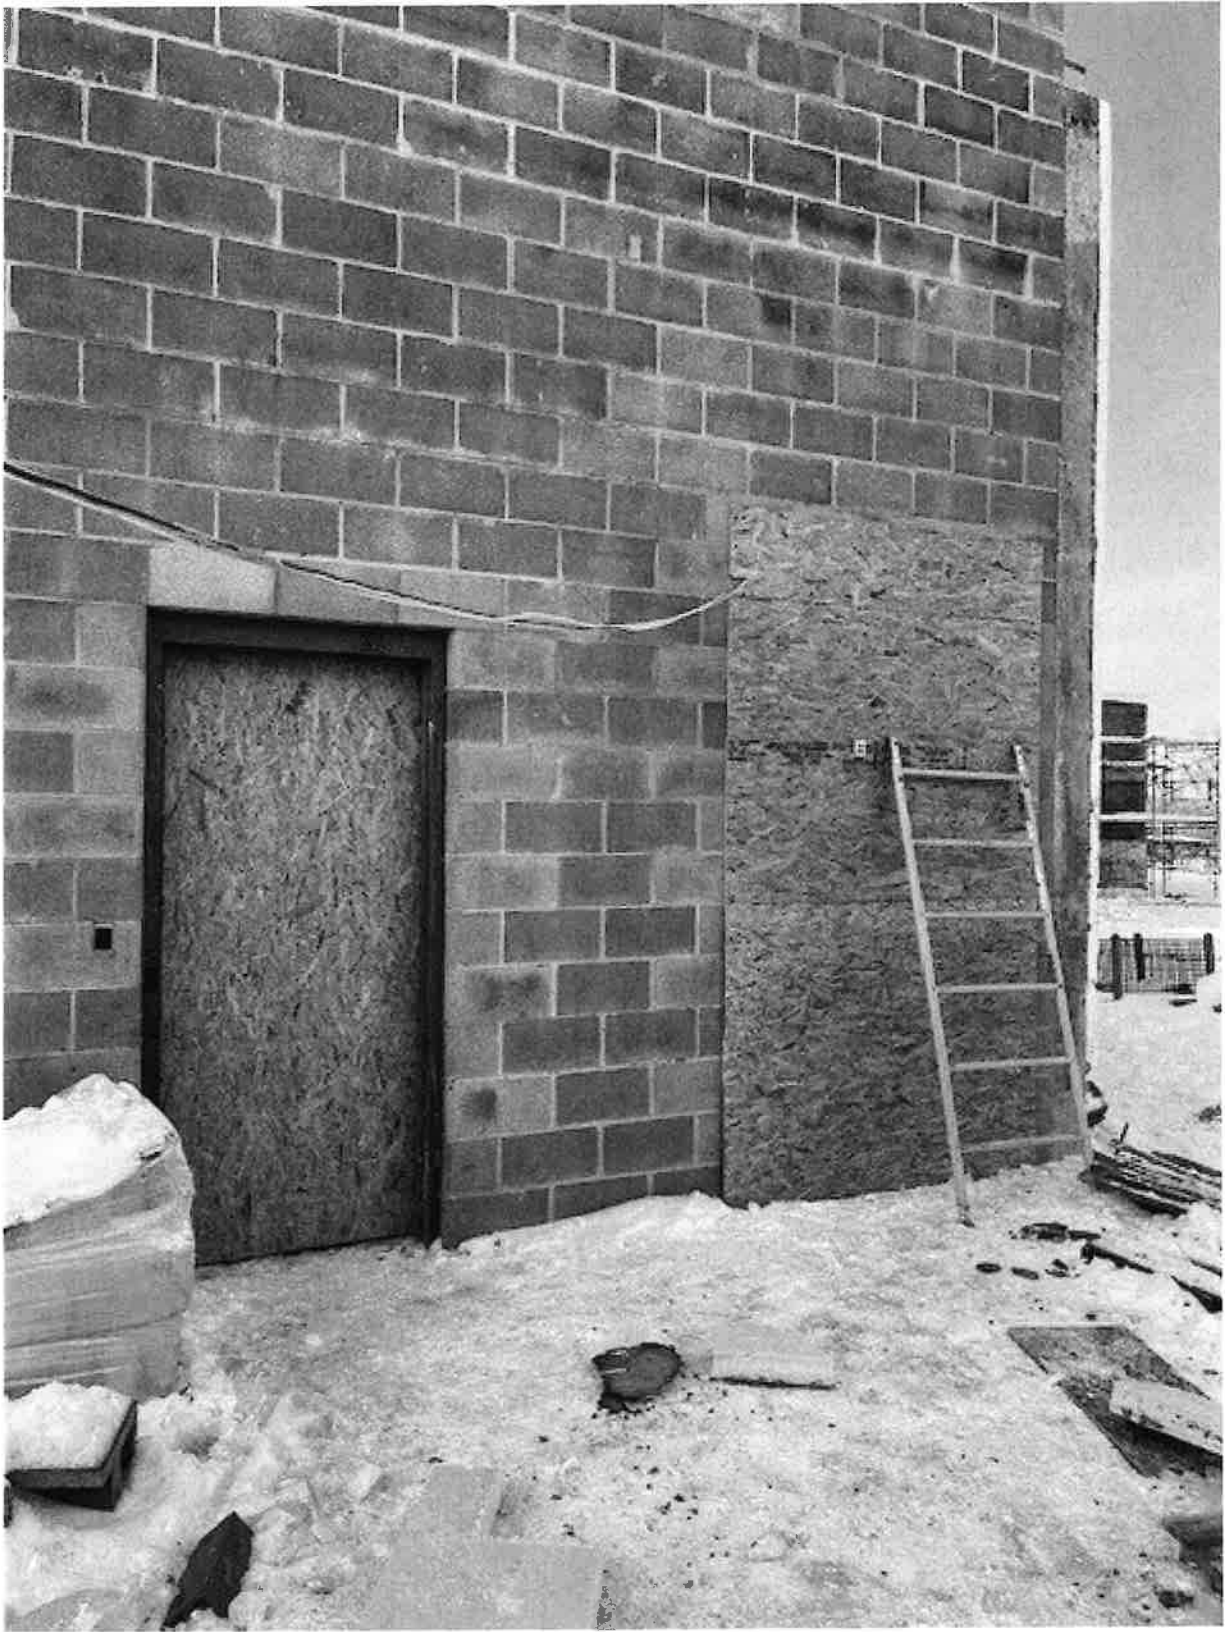



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

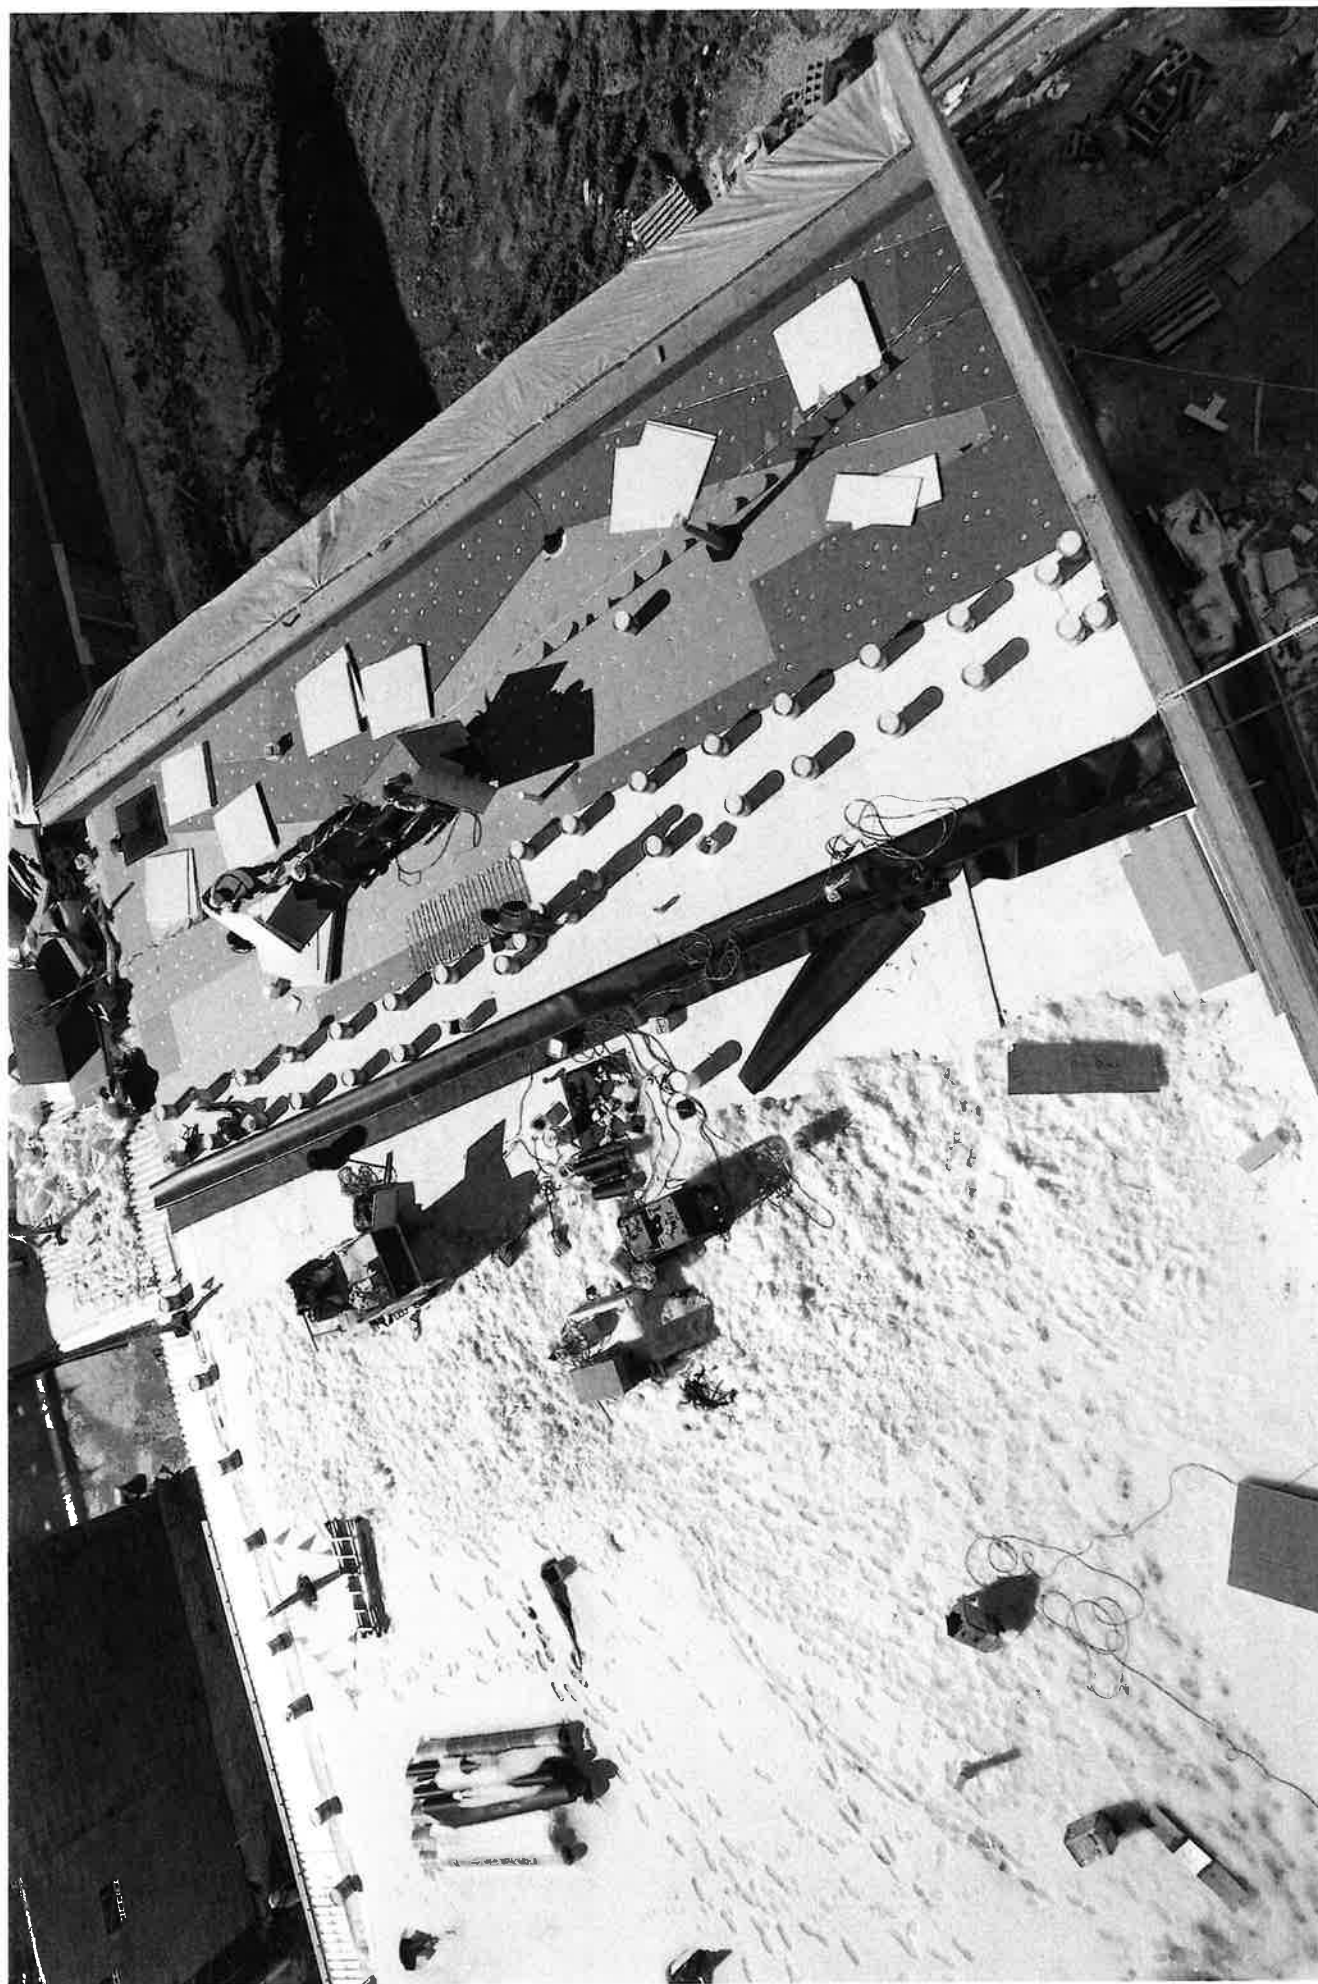



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RIISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM

File
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.


Michael Graf on 2/18/2025 03:33 PM



File

Daily Report 2025...

Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00
hours

18° F
cloudy

1
notes

3
equipment

● Pending
status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report
With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101101101101101

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Slanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

1111111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order

Supplemental Information Form (Ref#

62536)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Grayhawk LLC, 0007, Drywall

Type: CM Bid Package

Proposed

Change Order Number

07-03

Time Extension Required

No

Date Of Change Order

6/10/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$227,074.61
Remaining After Approved COs	\$1,008,546.50
Net All COs	\$232,501.01
Remaining After All COs	\$1,003,120.10

This Requested Change Order Amount \$1,350.00

+/-

Change In A/E Fee This Change Order \$72.90

+/-

Change In CM Fee This Change Order \$25.65

+/-

Remaining Construction Contingency

Balance

Contract Change Requested By Architect/Engineer

Contract Change Reason Code Improved Plans/Specs

Change Order Description And Justification

Pr #15 - Change to aCapella clouds in lieu of Serenda Clouds

Cost Benefit To Owner

Improved condition

Contract unit prices have been utilized No

to support the cost associated with this

change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$1,350.00	100.00%
Profit and Overhead		0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$1,350.00	
Cost for this Change Order supported by an alternate bid or competitive price quote		
Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62536)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 07-03
 INITIATION DATE: 6/10/2025

TO CONTRACTOR (Name and Address)
 GRAYHAWK, LLC

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #07 DRYWALL

THE CONTRACT IS CHANGED AS FOLLOWS: PR #15 - Change to aCapella clouds in lieu of Serenda Clouds

The original Contract Sum was	502,000.00
Net change by previously authorized Change Orders	2,646.16
The Contract Sum prior to this Change Order was	504,646.16
The Contract Sum will be Increased by this Change Order in the amount of	1,350.00
The new Contract Sum including this Change Order will be	505,996.16

The Contract Time will be adjusted by 0 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

GRAYHAWK, LLC

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)



Change Order Review Form

5 aCapella clouds in lieu of Serenada Cloud
aCapella clouds in lieu of Serenada Cloud

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

PR # 15 aCapella clouds in lieu of Serenada Cloud

Date: 6/2/2025

To: Sherman Carter Barnhart Architects, PLLC

From: Michael Graf

Attn:

CC: Kenny Davis

I have reviewed and approved the attachment pricing. Your approval and signature is required in order to process this change order. Please review the pricing and sign below it is acceptable.

PR # 15 aCapella clouds in lieu of Serenada Cloud

Description	BP	Amount
C&T DESIGN & EQUIPMENT CO.,	012	0.00
CENTRAL KENTUCKY SHEET METAL	018	0.00
DIXIE ROOFING, INC.	006	0.00
ELLIOTT CONTRACTING, INC.	008	0.00
FACILITY COMMISSIONING GROUP	020	0.00
GRAYHAWK, LLC	007	1,350.00
HINKLE CONTRACTING COMPANY LLC	002	0.00
IRWIN INSTALLATION SOURCE	013	0.00
MARTIN FLOORING COMPANY, INC.	014	0.00
MASON STRUCTURE, INC.	004	0.00
RIMAR ELECTRIC, LLC	019	0.00
RISING SUN DEVELOPING COMPANY	021	0.00
ROSA MOSAIC & TILE COMPANY	022	0.00
TWIN LAKES FIRE SERVICE, LLC	017	0.00

Summary

Total Days 0.00

Total

1,350.00

Sherman Carter Barnhart Architects, PLLC

06 JUN 25

Signature

DATE:

Codell Construction Company
Michael Graf
West College Avenue
Stanton, KY 40380
mgraf@codellconstruction.com



Request For Change

Wellington Elementary School - 4814

776 West College Ave
Stanton, KY 40380

RFC No. 3

Date: 03/20/2025
Sent By: ANDREW PARKER
aparker@grayhawk-ky.com

Responded By: 03/20/2025
Sent To: Kenny Davis
kdavis@codellconstruction.com

Change Reason: Change Request from Owner

Scope: Out Of Scope

Title: aCapella clouds in lieu of Serenade Cloud
Pinta 1 in Discovery HUB 115

Description: Adding aCapella Clouds in lieu of Serenade Cloud Pinta 1 in Discovery HUB 115. Excludes and custom colors. Includes all colors in previous submittal. No schedule impact if approved within 1 week.

Schedule Impact: 0 Days

Scope of Work

Item	Price Subtotal
Added aCapella Float Clouds (includes tax)	\$1,350.00
Price Subtotal:	\$1,350.00
Overhead:	
Total Price:	\$1,350.00

Review and Response

☐ Approved ☐ Rejected ☐ Request Formal Change Order ☐ Other

ANDREW PARKER

Grayhawk LLC

Kenny Davis

CODELL CONSTRUCTION COMPANY

Pricing is based upon conditions or documents provided by the date issued above and is valid for 15 days. Any changes to jobsite conditions, which may include but are not limited to weather, unforeseen conditions, progress of other trades, accelerated scheduling, and out-of-sequence work may result in additional costs. Unless stated otherwise the price above does not include overtime or costs for shift differential. Acceptance of this RFC by verbal direction, signed authorization, or issuance of a Change Order constitutes the acceptance of this document and all terms and conditions contained herein.

Lexington

2424 Merchant Street | Lexington, KY 40391 | P: 859-255-2784

Louisville

916 Lily Creek Drive | Suite 101 | Louisville, KY 40580 | P: 502-499-4044

No added labor.

[Andrew Parker](#)

Operations Manager

Grayhawk, LLC
2424 Merchant Street
Lexington, KY 40511

(251) 620-6227 Cell

[\(859\) 721-2447](#) Office

[\(859\) 259-0957](#) Fax

aparker@grayhawk-ky.com

Codell Construction Company
Michael Graf
West College Avenue
Stanton, KY 40380
mgraf@codellconstruction.com

FACPAC Contract Change Order Supplemental Information Form (Ref# 62487)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Elliott Contracting Inc, 0008, Aluminum Storefronts & Windows

Type: CM Bid Package

Proposed

Change Order Number08-01

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency
Balance

Contract Change Requested ByConstruction Manager

Contract Change Reason CodeTime Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner

No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62487)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
CONSTRUCTION MANAGER ☐
ARCHITECT ☐
CONTRACTOR ☐
FIELD ☐
OTHER ☐

PROJECT (Name and Address)
STANTON ELEMENTARY SCHOOL
WEST COLLEGE AVENUE
STANTON, KY 40380

CHANGE ORDER NUMBER: 08-01
INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
ELLIOTT CONTRACTING, INC.
PO BOX 3038
55 INDUSTRIAL BLVD (41501)

PROJECT NUMBERS: 000743
CONTRACT DATE: 3/4/2024
CONTRACT FOR: BID PACKAGE #8 ALUMINUM STOREFRONTS &
WINDOWS

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	310,750.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	310,750.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	310,750.00

The Contract Time will be adjusted by 93 days.
The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

ELLIOTT CONTRACTING, INC.

CONTRACTOR (Firm Name)
PO BOX 3038*55 INDUSTRIAL BLVD (41501)*PIKEVILLE,

ADDRESS

BY (Signature)

(Typed Name)

DATE:

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

ARCHITECT (Firm Name)
144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

BY (Signature)

(Typed Name)

DATE:

POWELL COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

BY (Signature)

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																				
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

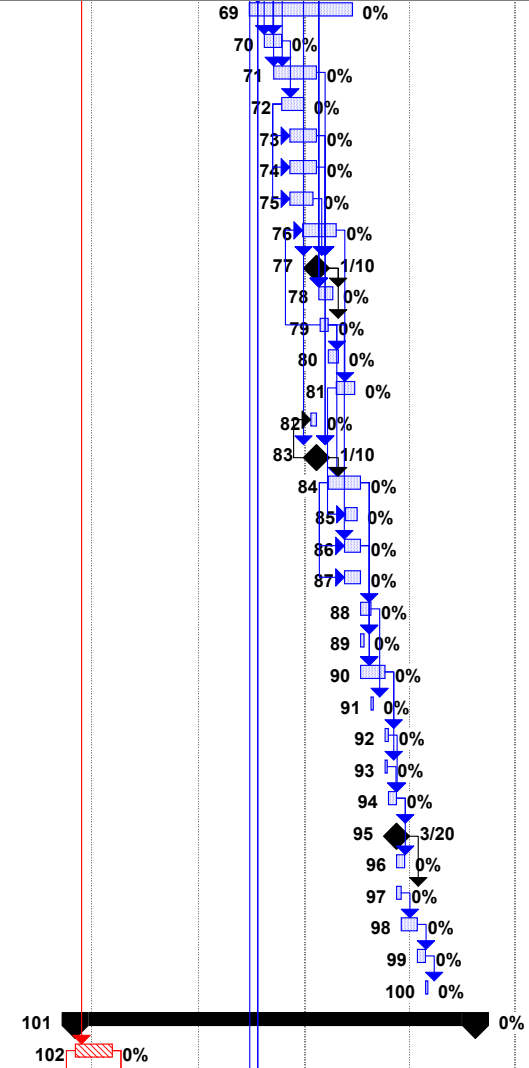

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

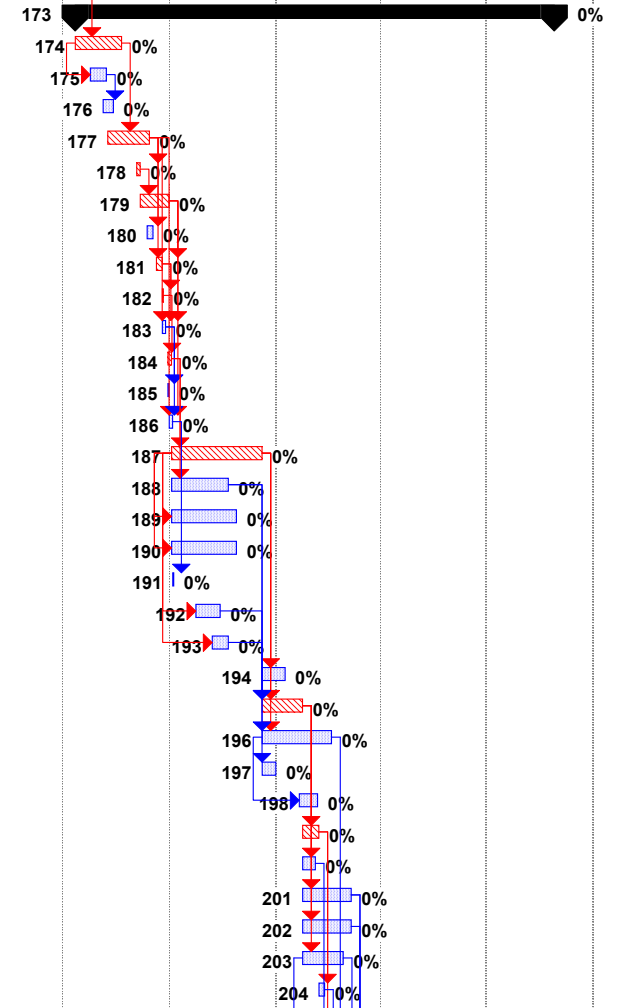

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf

Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

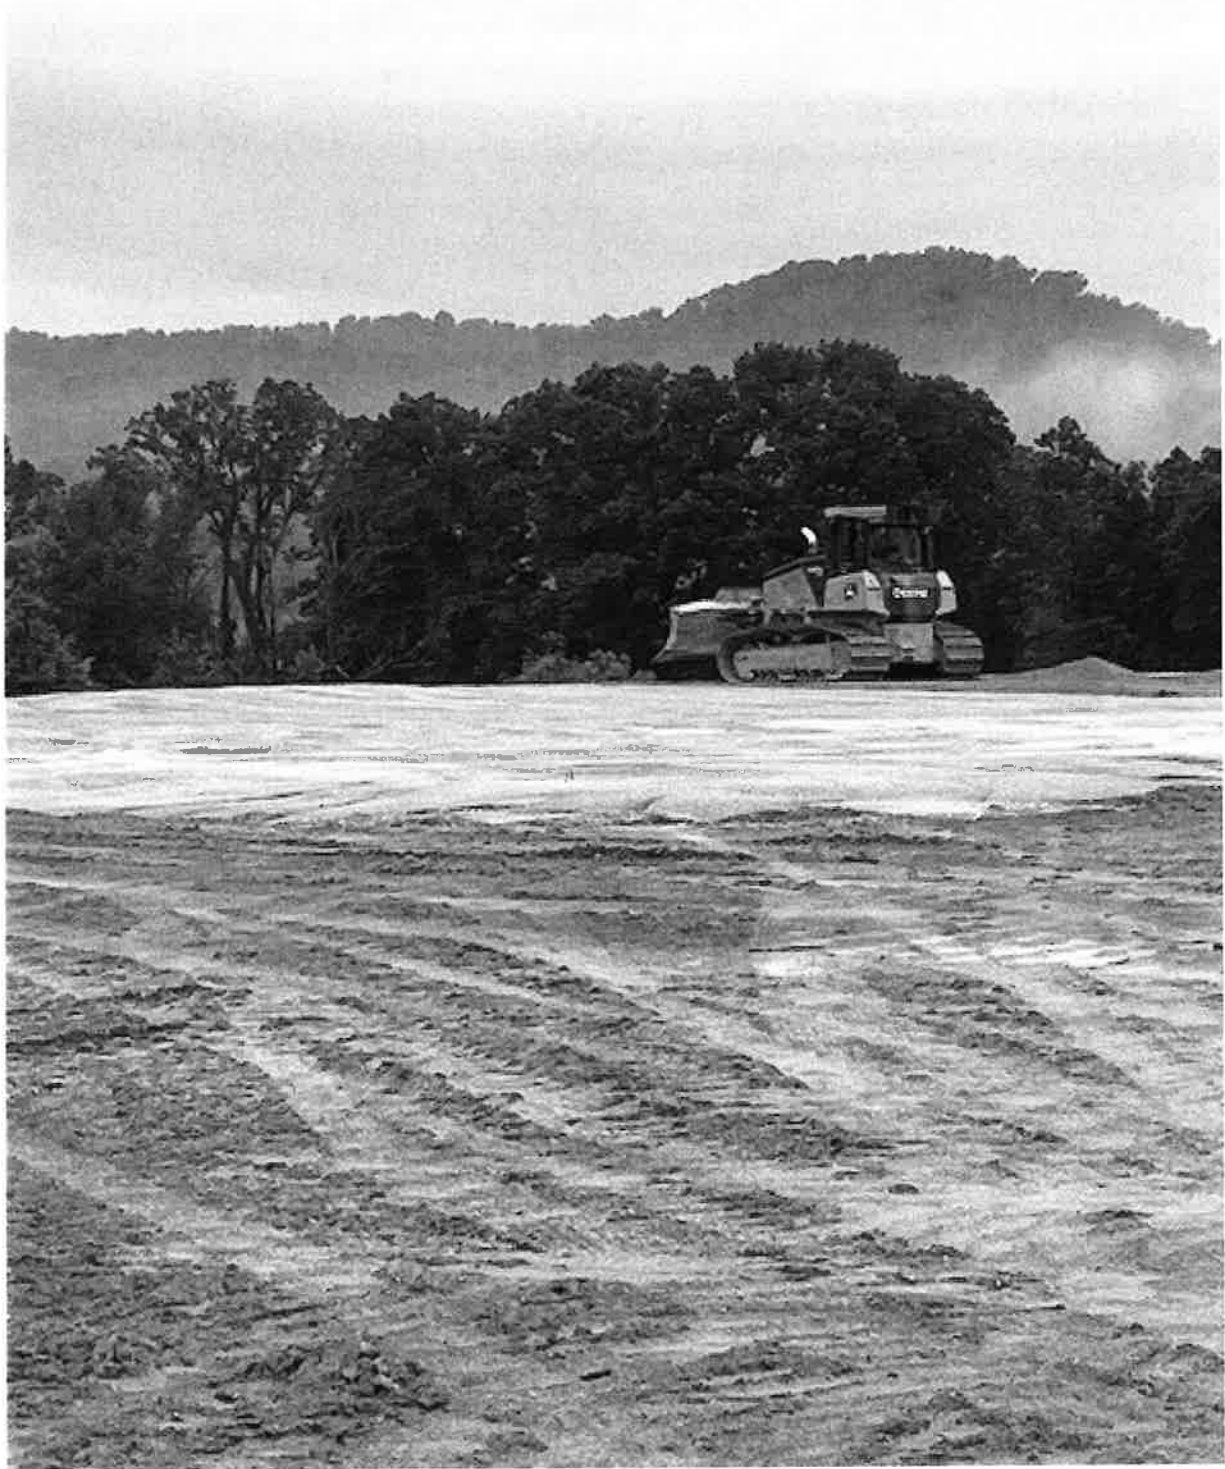



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File
5/23/2024 9:11 AM
Michael Graf



File
5/23/2024 9:11 AM
Michael Graf



File
5/23/2024 9:11 AM
Michael Graf



File
5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File
5/23/2024 12:24 PM
Michael Graf



File
5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File
5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024...,
Michael Graf

ASSIGNMENTS

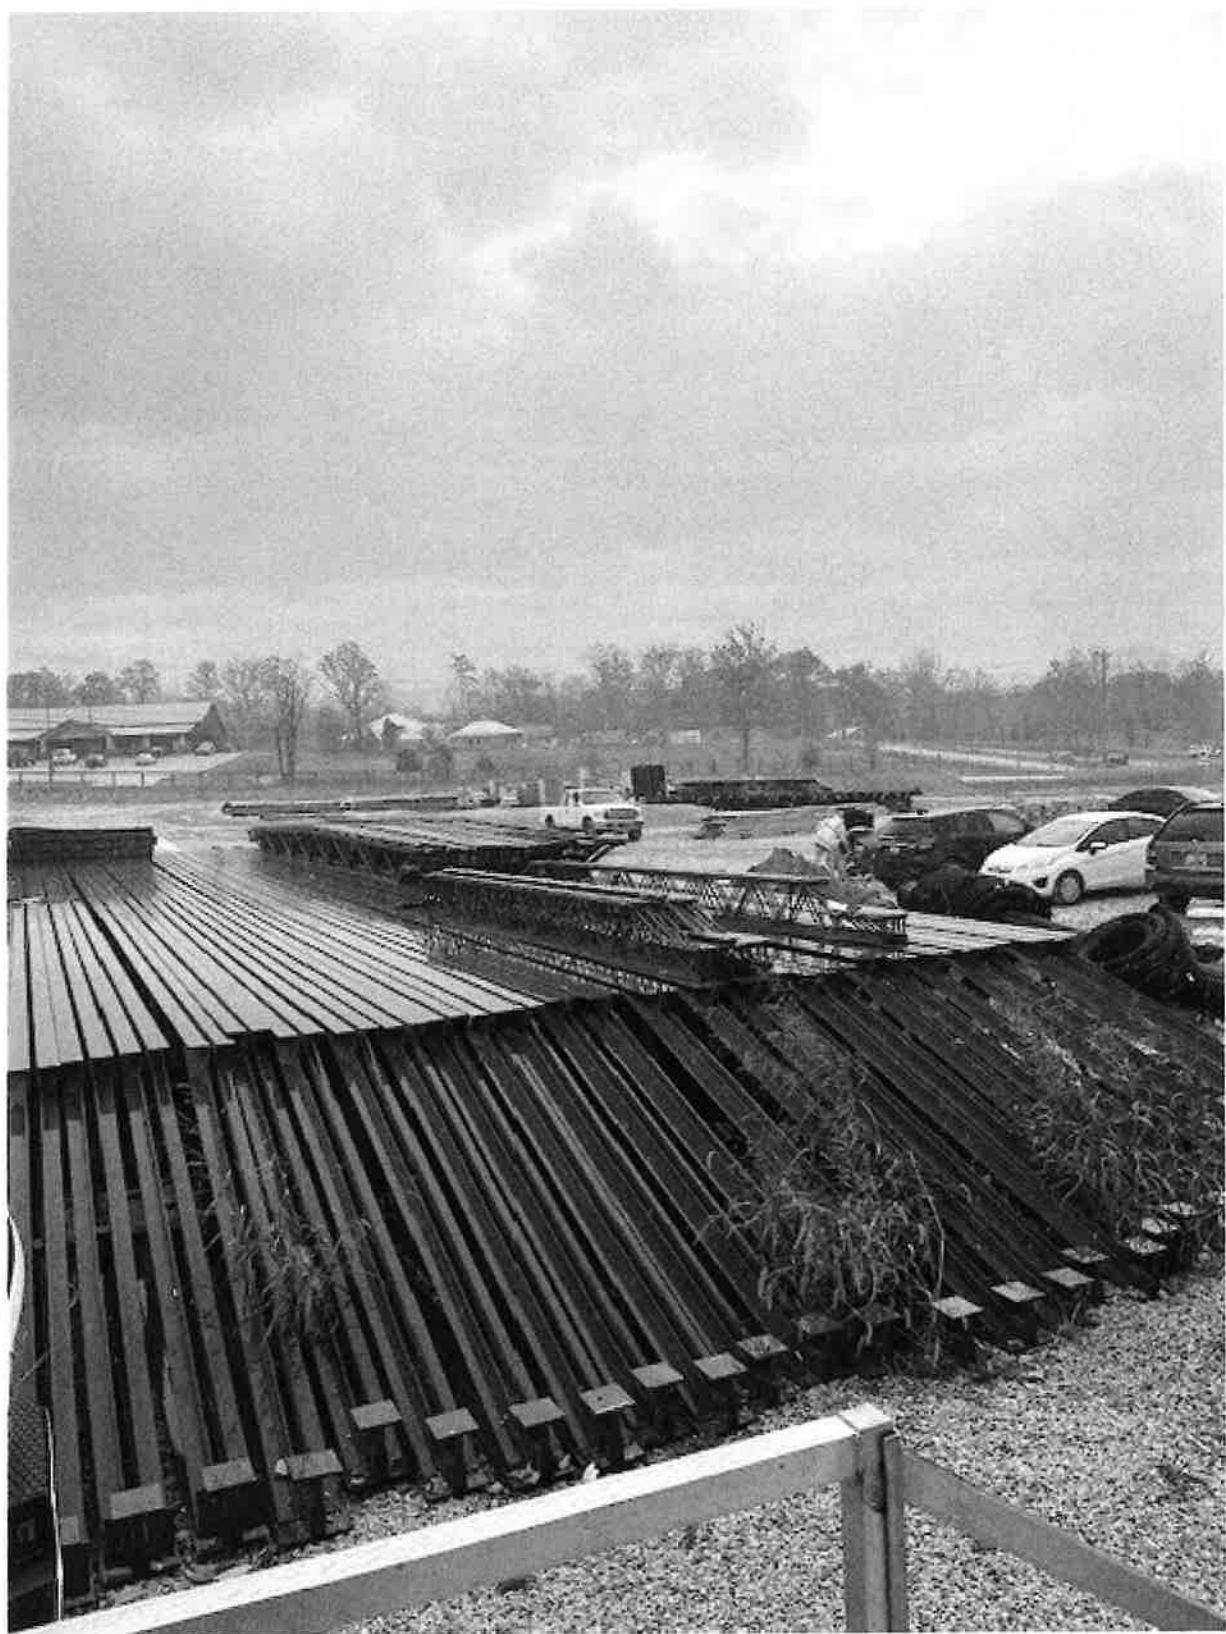



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

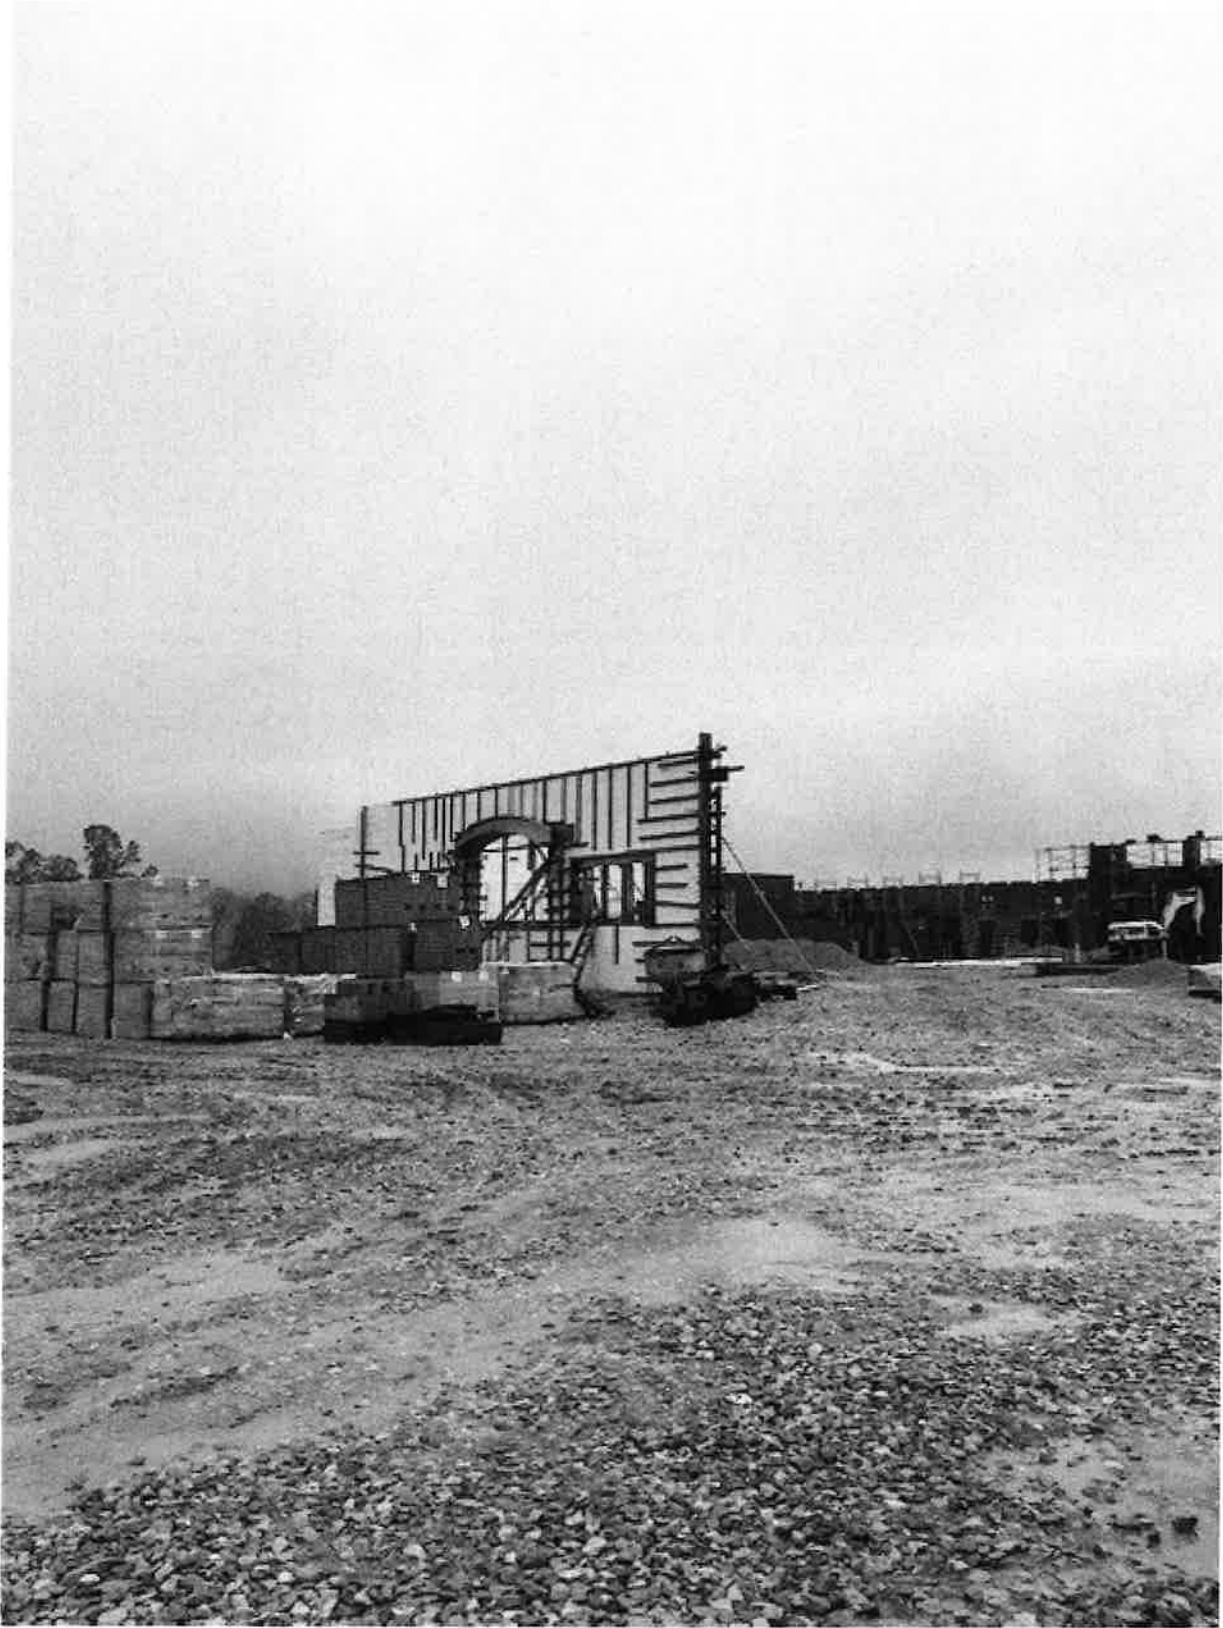



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00
hours

52° F
rain

1
notes

2
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM



File

Daily Report 2024...
Michael Graf





Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00
hours

60° F
cloudy

1
notes

6
equipment

● Approved
status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf




File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

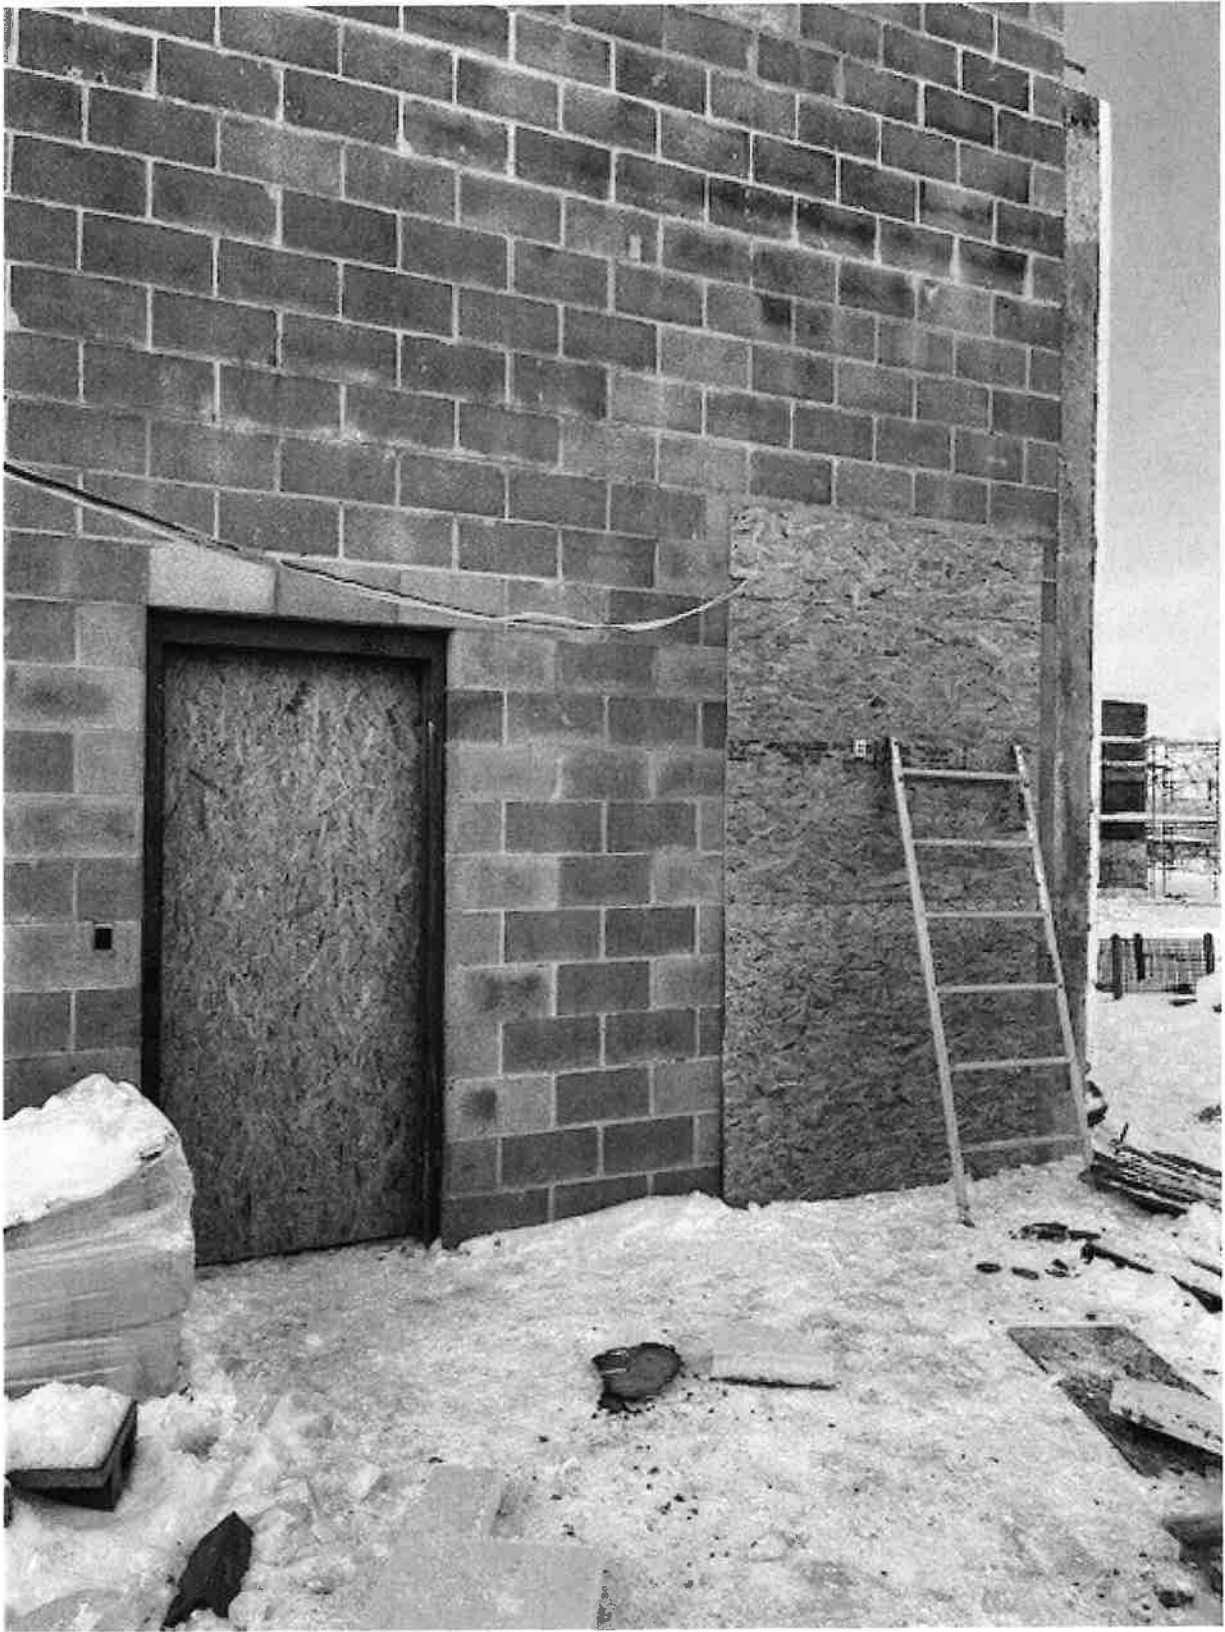



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

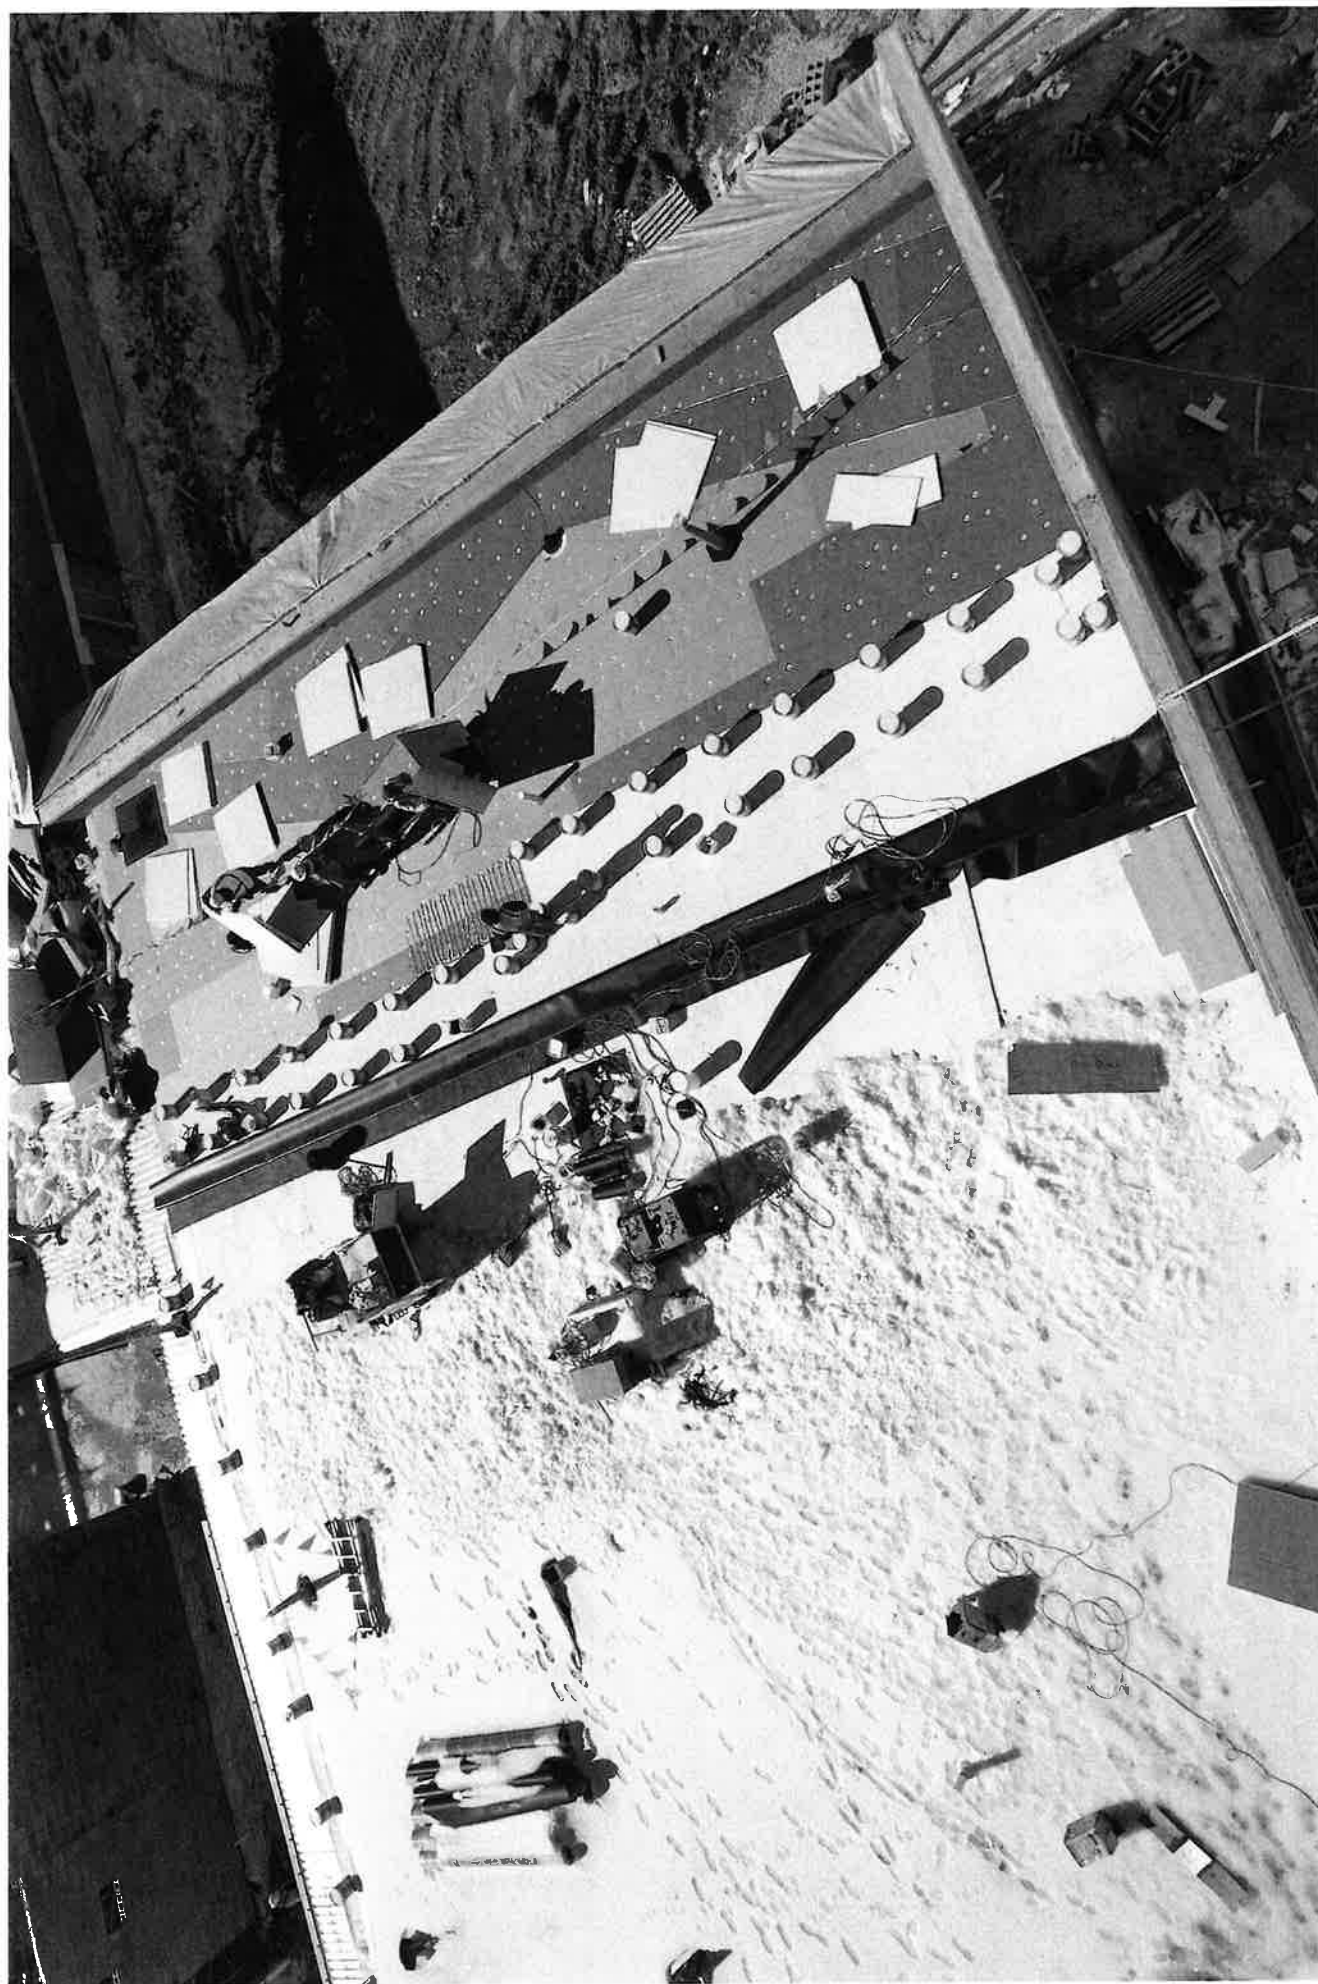



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM


Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM

File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00
hours

18° F
cloudy

1
notes

3
equipment

● Pending
status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontals/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62484)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School
BG Number: 21-072 District: Powell County (HB678) (495)
Status: Active Phase: Project Initiation (View Checklist)

Contract: C&T DESIGN AND EQUIPMENT COMPANY, INC., 0012, Kitchen Equipment
Type: CM Bid Package Proposed

Change Order Number 12-01
Time Extension Required Yes
If Yes Number Of Days 93
Date Of Change Order 6/8/2025
Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00
+/-

Change In A/E Fee This Change Order
+/-

Change In CM Fee This Change Order
+/-

Remaining Construction Contingency
Balance

Contract Change Requested By Construction Manager
Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No Costs from Contractors

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead		0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62484)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 12-01
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 C&T DESIGN & EQUIPMENT CO.,
 INC.
 6315 MIDLAND INDUSTRIAL DRIVE

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE # 12 KITCHEN EQUIPMENT

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	27,414.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	27,414.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	27,414.00

The Contract Time will be adjusted by 93 days.

The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

C&T DESIGN & EQUIPMENT CO.,

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)
 INC.*6315 MIDLAND INDUSTRIAL DRIVE*SHELBYVILLE, KY

OWNER (Firm Name)
 691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24	2	3	4																	
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24	3	4																		
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24	4																			
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24	5																			
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24	6																			
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24	7	8	9	10	11	12														
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24	8	9	10	11	12															
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24	9	10																		
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24	10	11																		
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24	11	12																		
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24	13	14																		
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24	14	15																		
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24	15	16																		
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24	16	17																		
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24	17	18																		
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24	18	19	20	21	22	23	24	25	26	27	28	29	30	31						
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24	19	20																		
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24	20	21	22	23	24	25	26	27	28	29	30	31								
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24	21	22																		
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24	22	23	24	25	26	27	28	29	30	31										
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24	23	24																		
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24	24	25	26	27	28	29	30	31												
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24	25	26	27	28	29	30	31													
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24	26	27	28	29	30	31														
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24	27	28	29	30	31															
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24	28	29	30	31																
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24	29	30	31																	
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24	30	31																		
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24	31	32																		
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25	32	33																		
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25	33																			
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

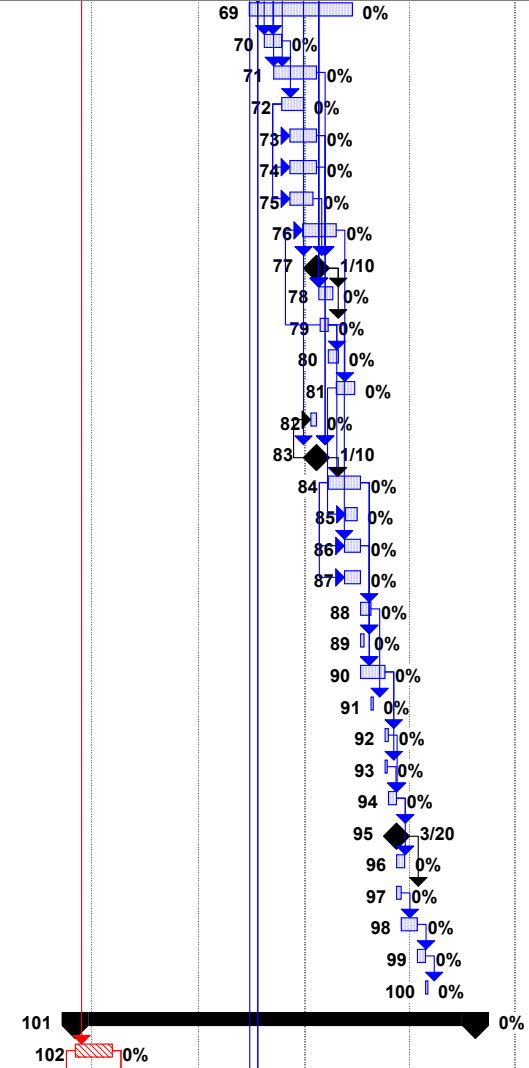

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25								
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25								
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25								
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24								
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24								
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24								
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24								
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24								
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24								
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24								
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24								
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24								
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24								
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24								
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24								
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24								
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24								
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24								
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24								
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24								
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24								
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25								
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25								
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25								
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24								
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25								
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25								
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25								
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25								
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25								

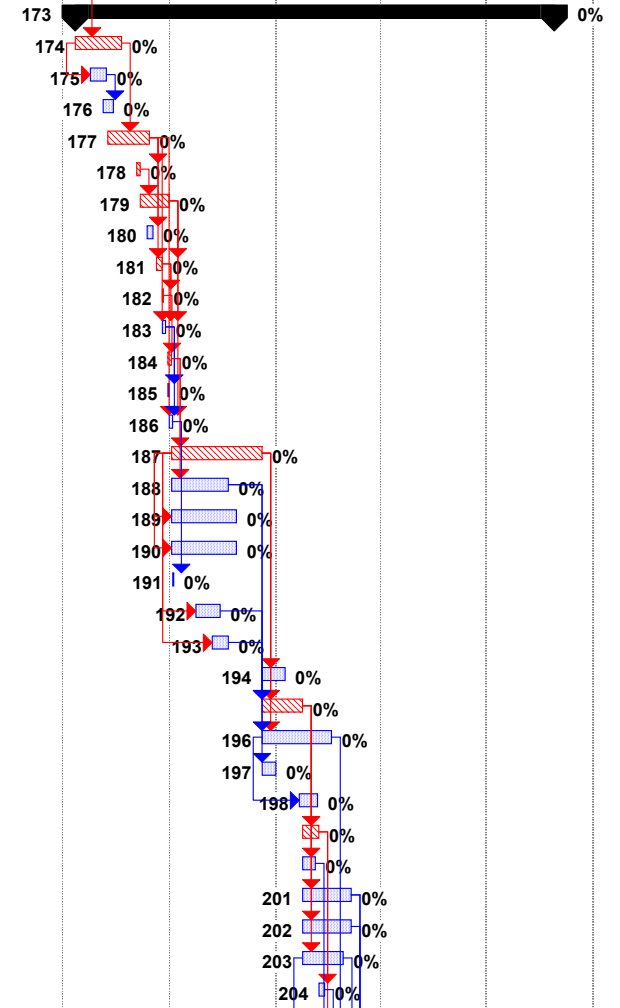

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																						
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																						
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																						
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																						
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																						
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																						
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																						
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																						
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																						
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																						
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																						
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																						
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																						
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																						
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																						
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																						
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																						
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																						
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																						
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																						
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																						
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																						
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																						
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																						
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																						
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																						
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																						
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																						
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																						
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																						
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																						
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																								
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																								
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																								
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																								
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																								
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																								
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																								
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																								
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																								
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																								
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																								
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																								
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																								
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																								
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																								
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																								
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																								
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																								
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																								
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																								
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																								
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																								
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																								
296	Architect Site Punch List Distrubuted - Site	0 days	Mon 8/11/25	Mon 8/11/25																								
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																								
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																								
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM
Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

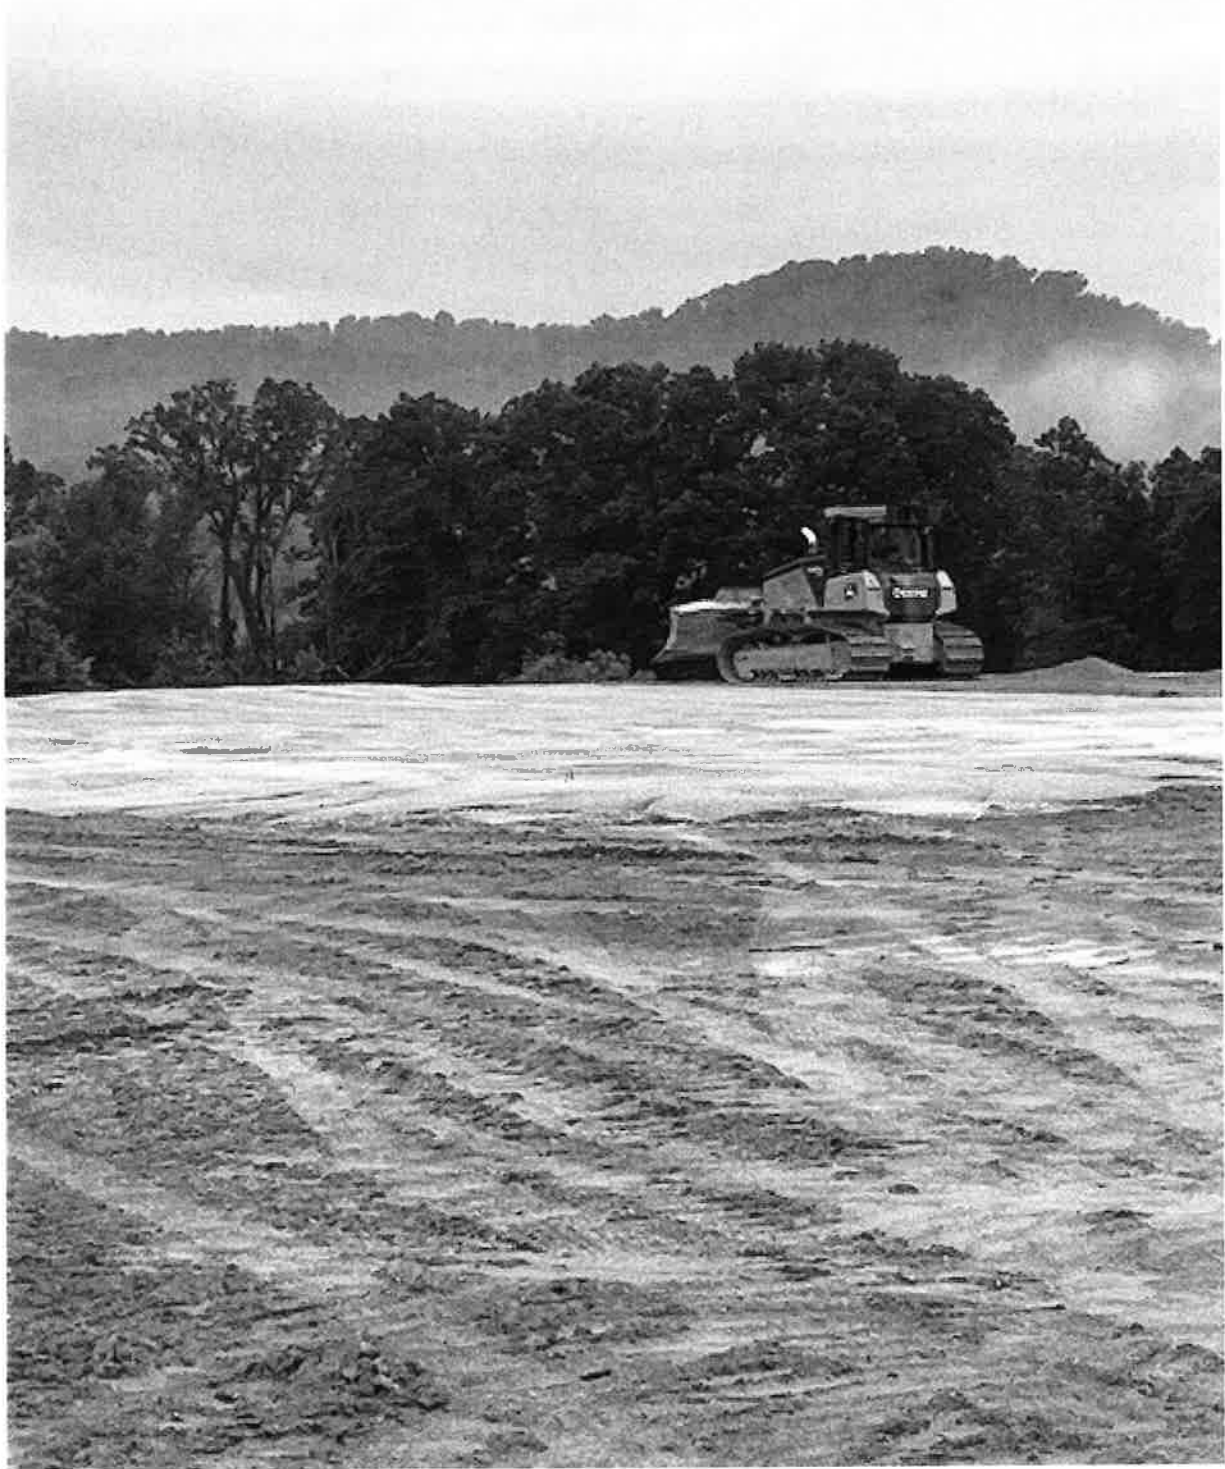



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM


File
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael GrafFile
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM

CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM

File
Daily Report 2024...,
Michael Graf**ASSIGNMENTS**

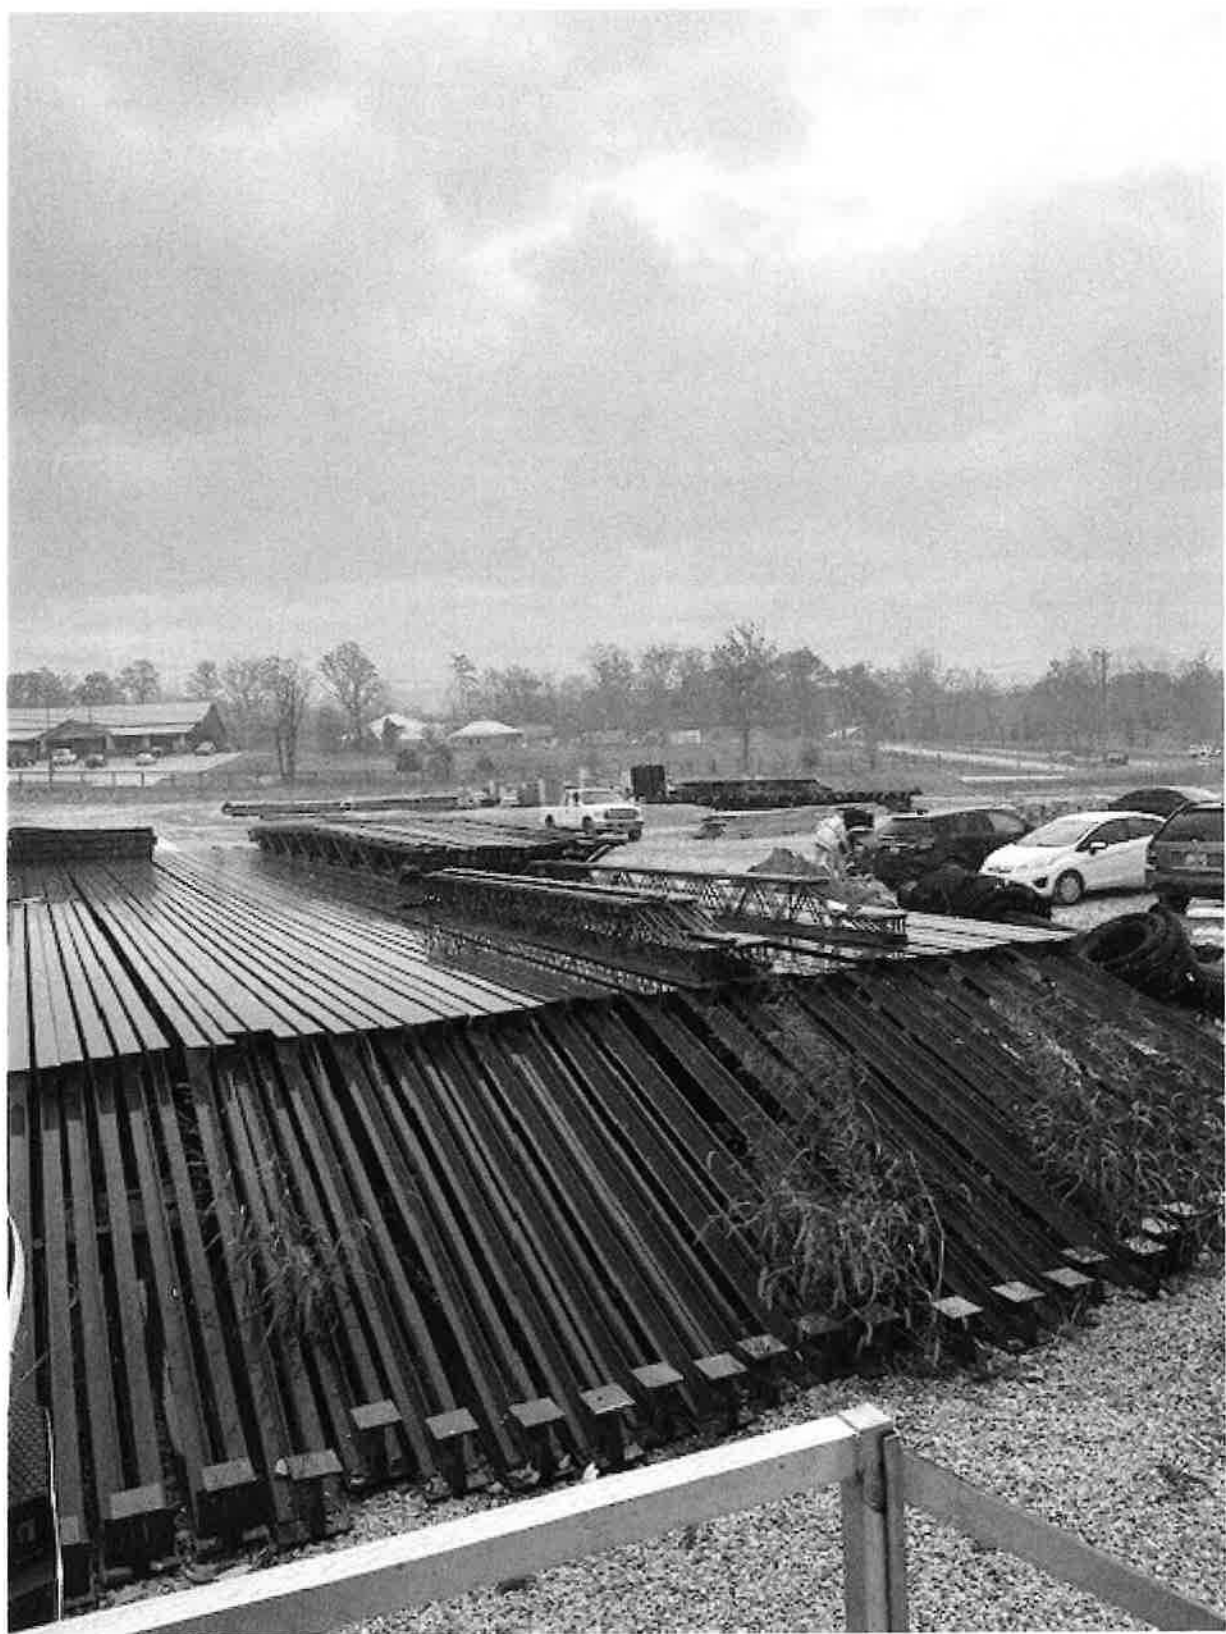



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

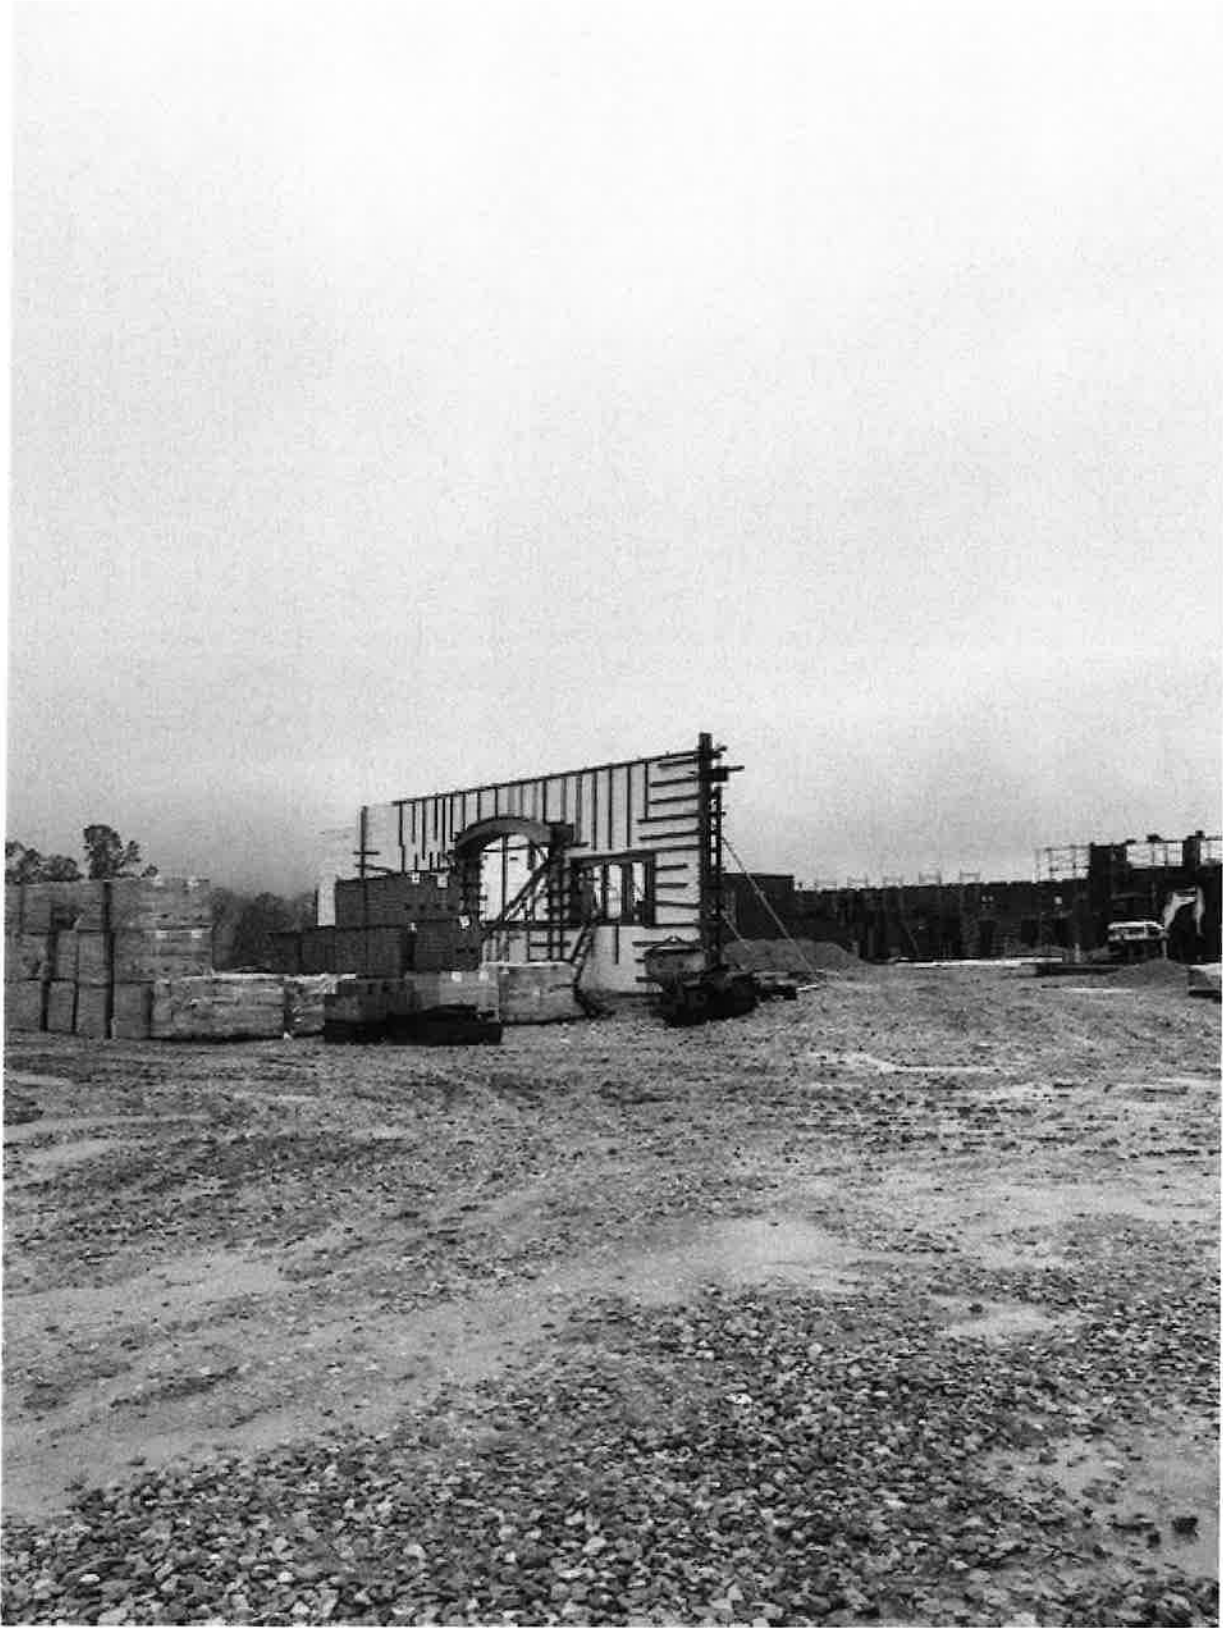



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report

With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00
hours

60° F
cloudy

1
notes

6
equipment

● Approved
status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00

hours

54° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

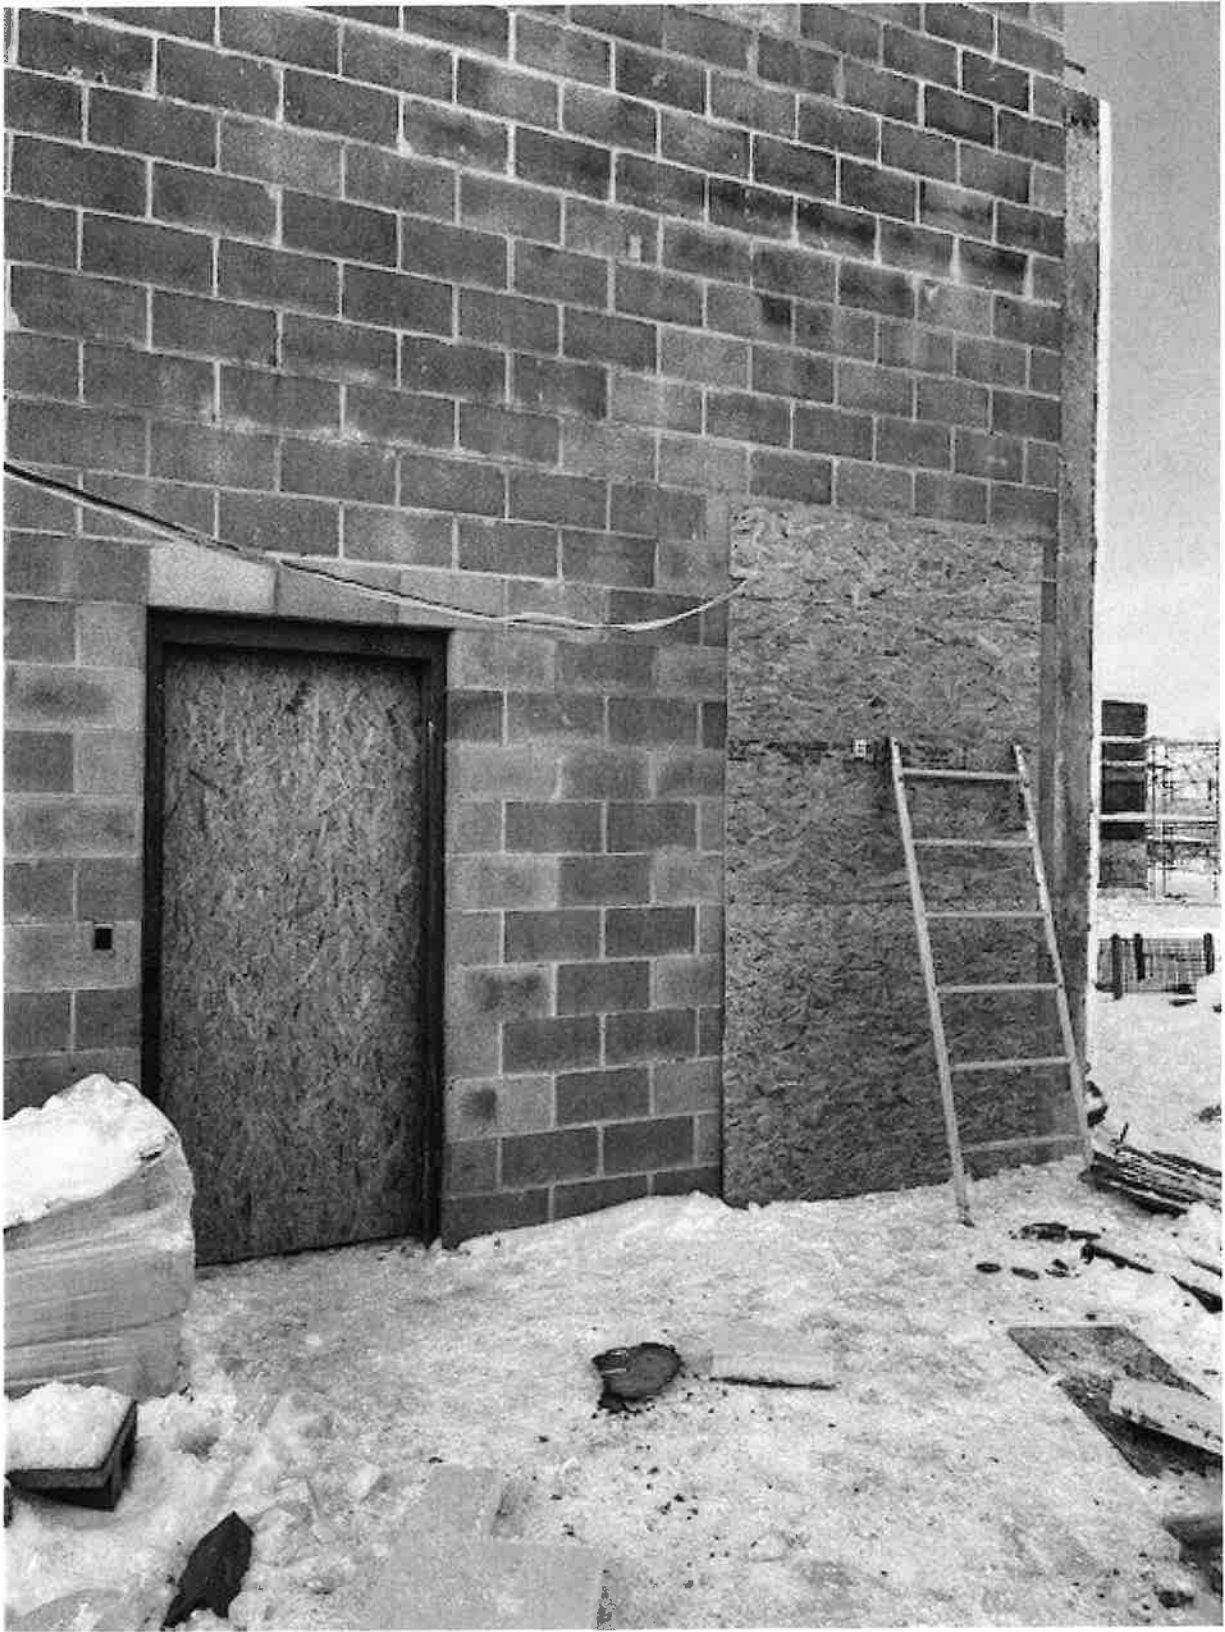



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM

File
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael GrafFile
1/14/2025 2:49 PM
Michael Graf


Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.

Michael Graf on 1/14/2025 03:13 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM

Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

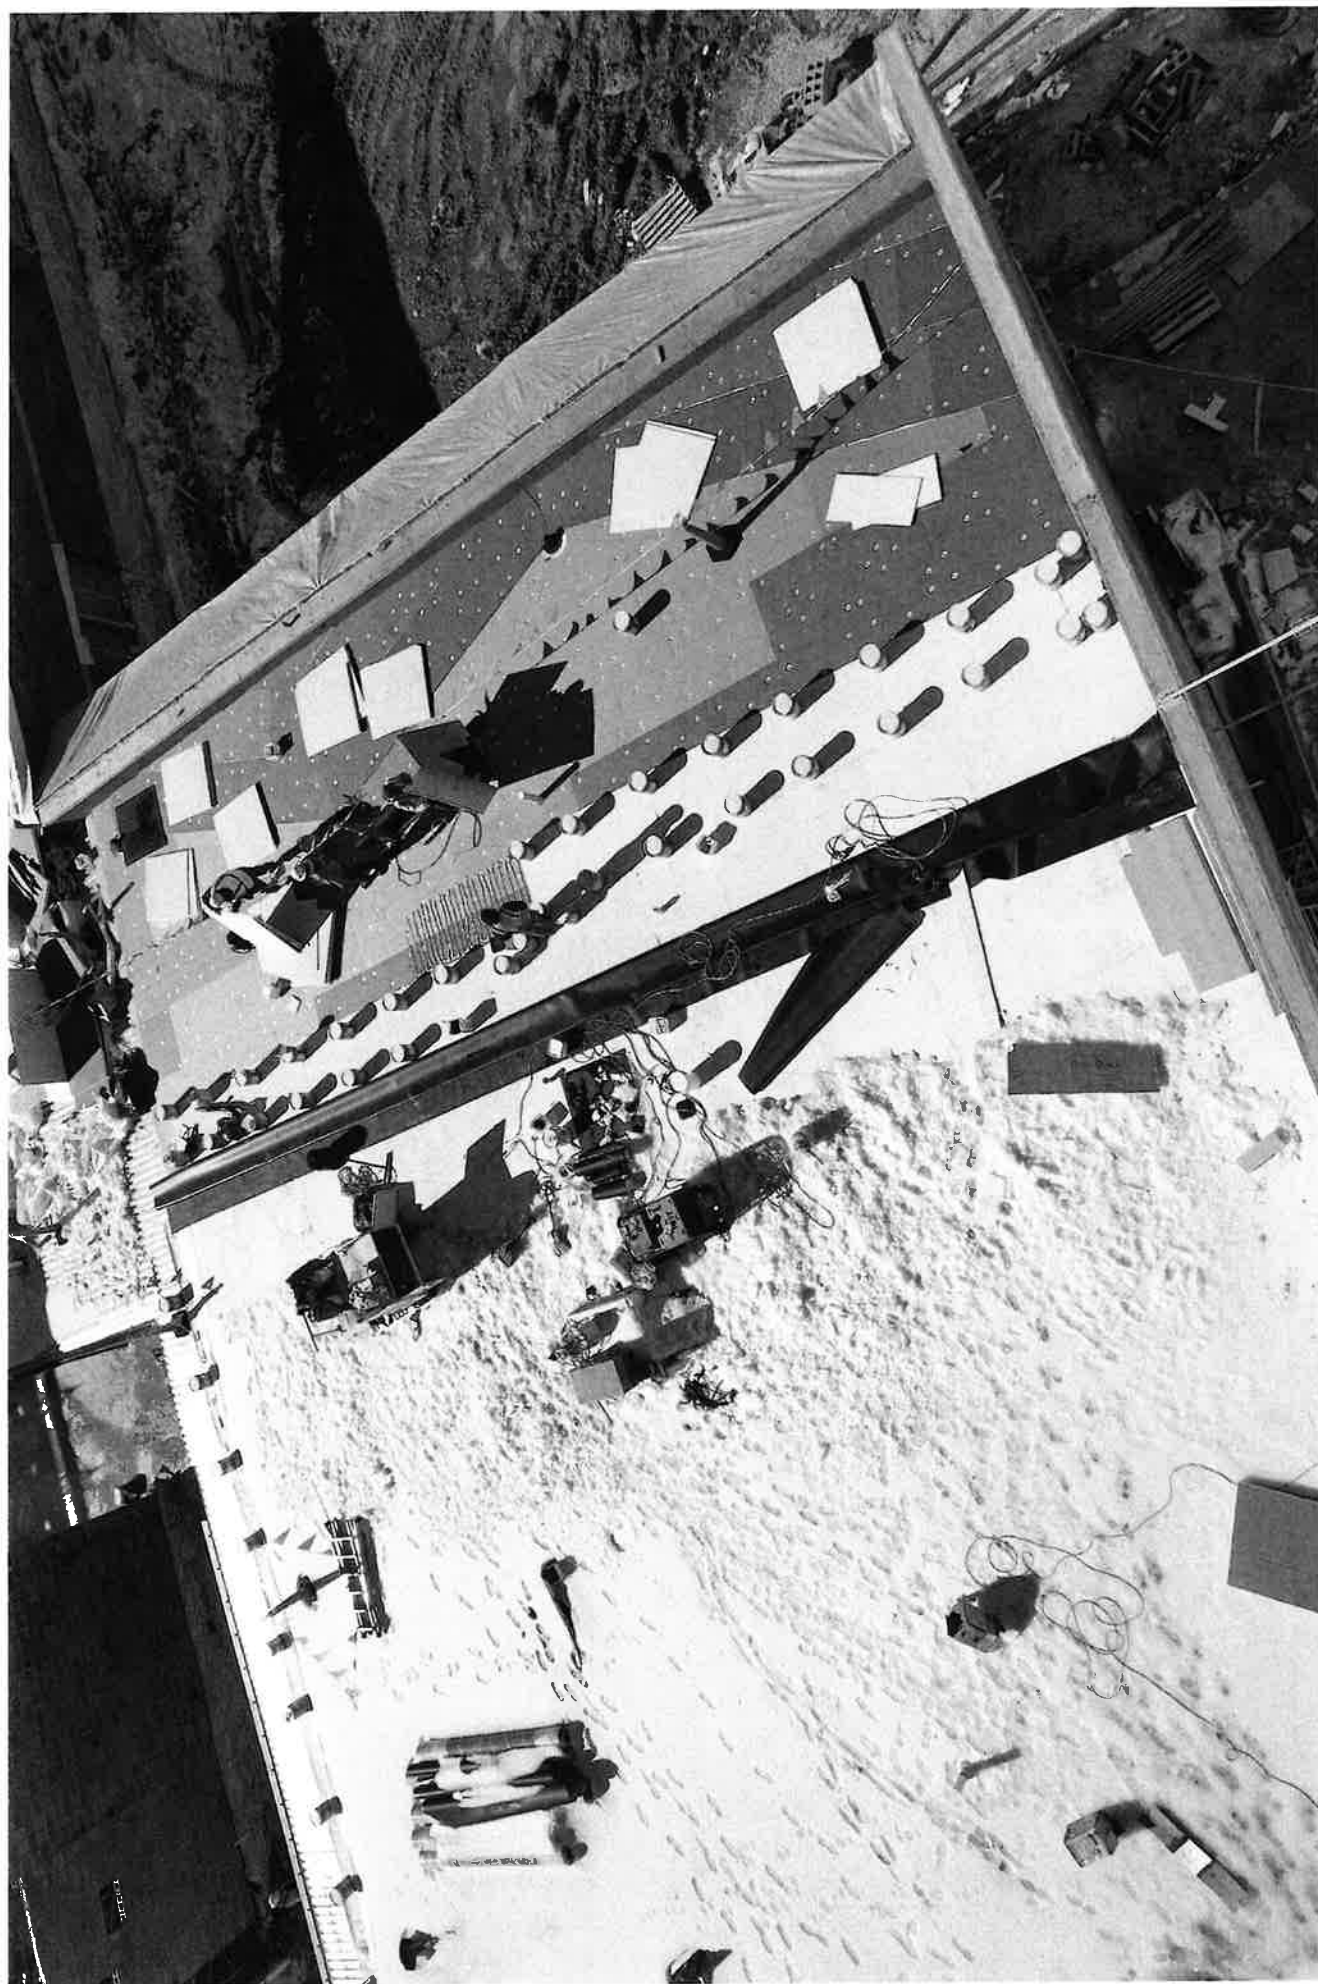



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf

Michael Graf on 1/23/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM

File
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM

File
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM


Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM

File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
KENTUCKY SHEET	Installing floor drains in mezzanine				
METAL, INC (N/A)	(Area C)				
GRAYHAWK, LLC	Topping out masonry walls in (Area A)		4.00	32.00 Hours	Approved
(N/A)					
MASON	Laying up brick on north facade of (Area		8.00	64.00 Hours	Approved
STRUCTURE, INC.	B)				
(N/A)					
RIMAR ELECTRIC,	(4) Installing cable trays in (Area B)		9.00	72.00 Hours	Approved
LLC (N/A)	(5) Pulling wire in west wing of (Area B)				
RISING SUN	(2) Sealing exterior ICF wall bar joist		12.00	96.00 Hours	Approved
DEVELOPING	pockets.				
COMPANY (N/A)	(5) Prepping mezzanine HCP's for				
	topping coat.				
	(2) clean up.				
	(3) installing metal stud partition walls				
	wood blocking (Pre school)				
SPRAY FOAM	Applying initial finish coat in kitchen and		2.00	16.00 Hours	Approved
TECHNOLOGIES	cafeteria.				
OF KY (N/A)					

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00

hours

63° F

thunderstorm

2

notes

6

equipment

● Approved

status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report
With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62491)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Irwin Installation Source Inc, 0013, Bleachers

Type: CM Bid Package

Proposed

Change Order Number13-01

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency Balance

Contract Change Requested By Construction Manager

Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62491)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
CONSTRUCTION MANAGER ☐
ARCHITECT ☐
CONTRACTOR ☐
FIELD ☐
OTHER ☐

PROJECT (Name and Address)
STANTON ELEMENTARY SCHOOL
WEST COLLEGE AVENUE
STANTON, KY 40380

CHANGE ORDER NUMBER: 13-01
INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
IRWIN INSTALLATION SOURCE

PROJECT NUMBERS: 000743
CONTRACT DATE: 3/4/2024
CONTRACT FOR: BID PACKAGE #13 BLEACHERS

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	14,350.95
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	14,350.95
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	14,350.95

The Contract Time will be adjusted by 93 days.
The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

IRWIN INSTALLATION SOURCE

CONTRACTOR (Firm Name)

ADDRESS

BY (Signature)

(Typed Name)

DATE:

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

ARCHITECT (Firm Name)
144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

BY (Signature)

(Typed Name)

DATE:

POWELL COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

BY (Signature)

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24																						
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																						
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																						
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																						
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																						
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																						
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																						
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																						
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																						
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																						
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																						
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																						
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																						
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																						
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																						
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																						
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																						
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																						
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																						
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																						
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																						
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																						
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																						
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																						
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																						
26	Install Fire Main, Vault and Hydrants	30 days	Wed 6/26/24	Wed 8/7/24																						
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																						
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																						
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																						
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																						
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																						
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																						
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																						
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

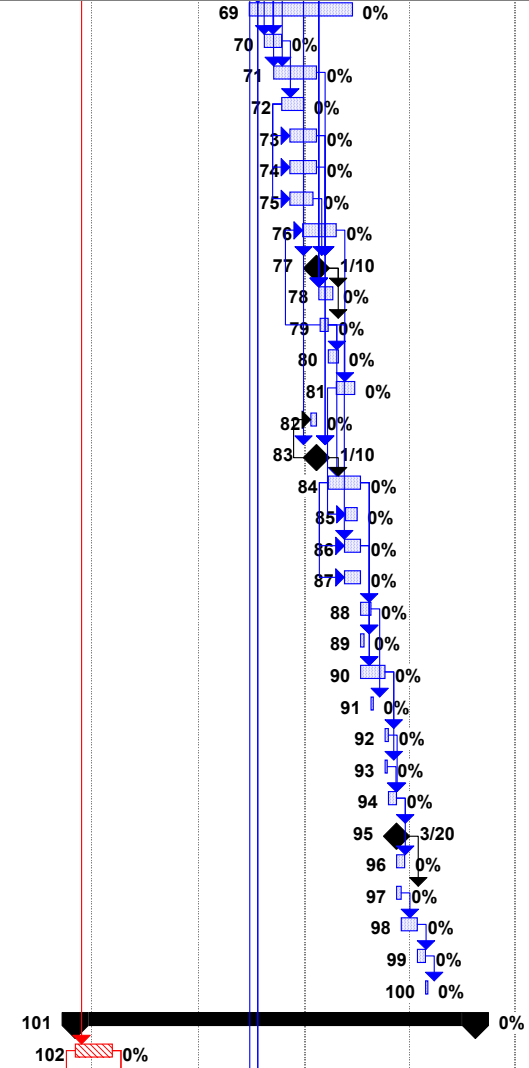

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

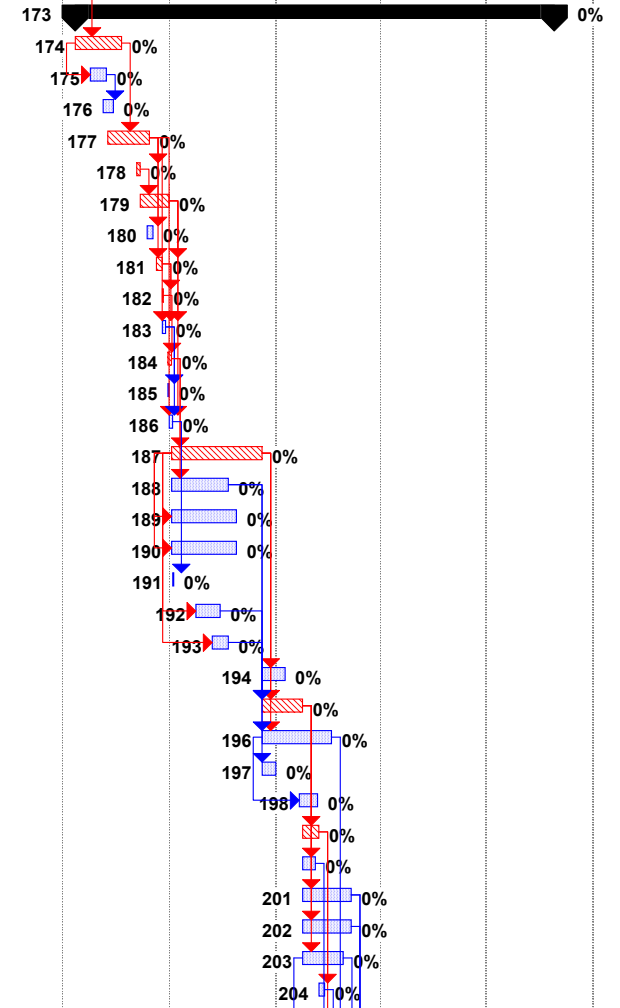

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																						
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																						
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																						
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																						
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																						
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																						
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																						
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																						
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																						
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																						
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																						
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																						
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																						
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																						
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																						
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																						
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																						
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																						
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																						
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																						
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																						
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																						
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																						
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																						
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																						
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																						
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																						
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																						
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																						
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																						
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																						
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

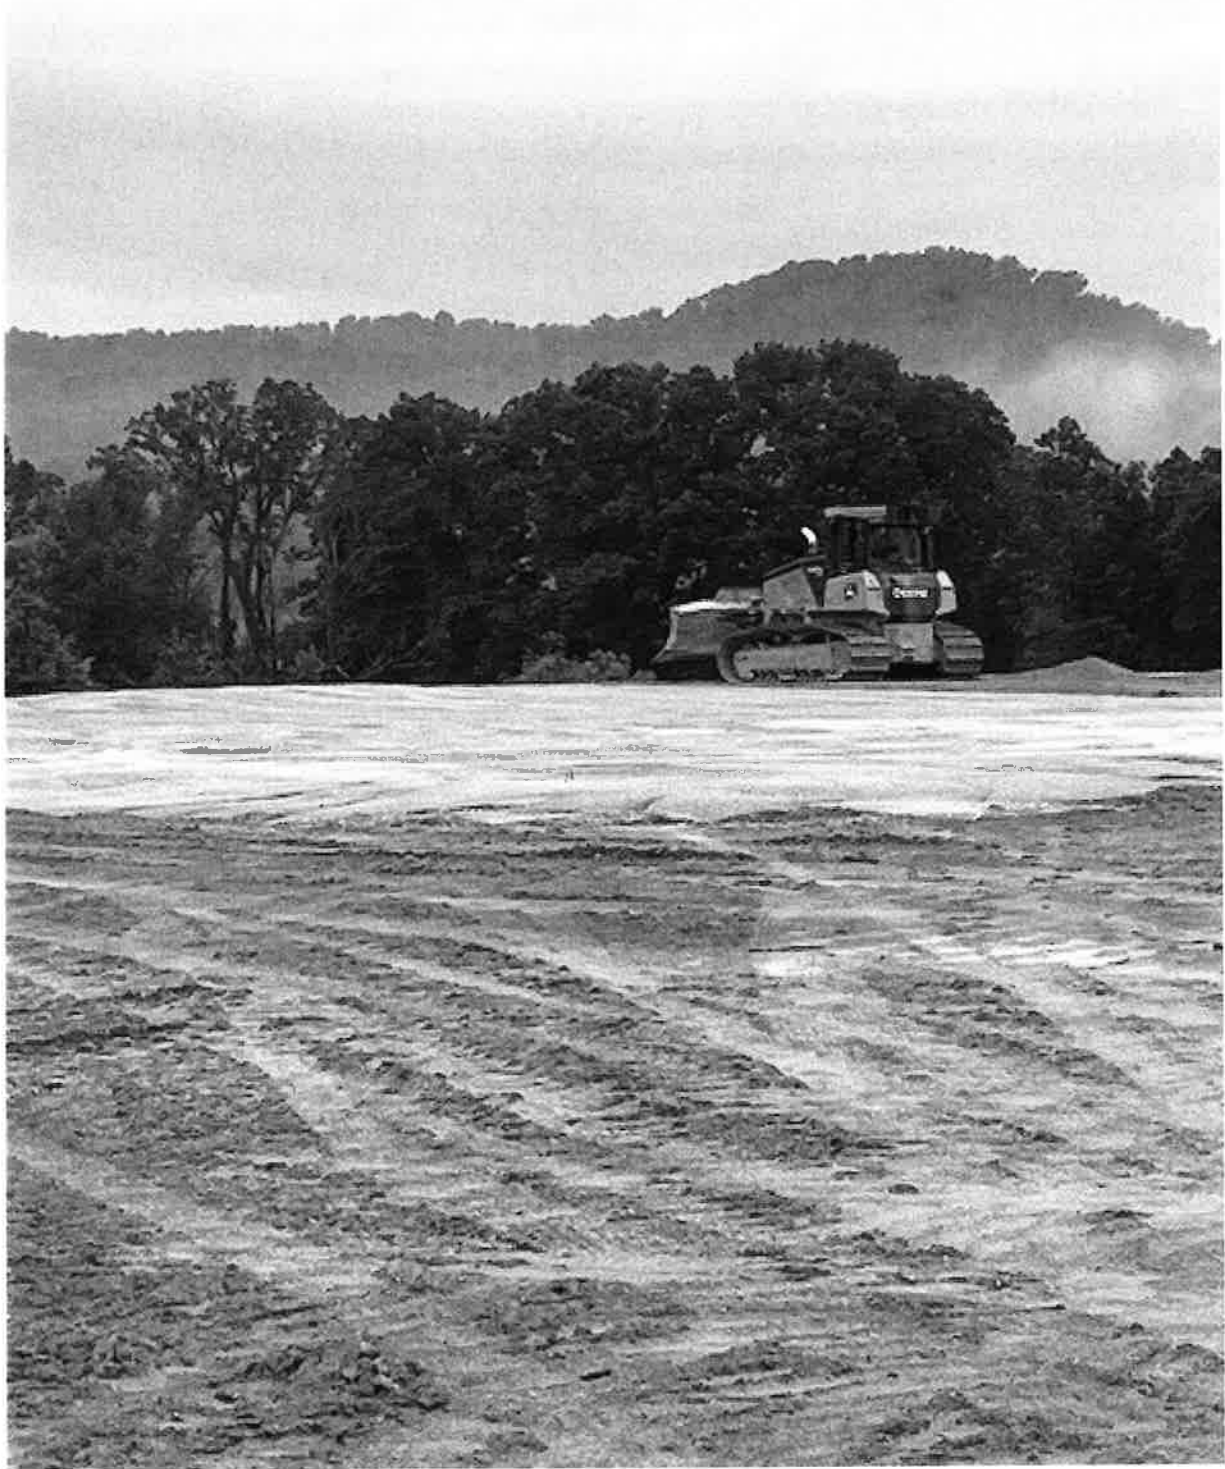



Daily Construction Report

With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf


Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material

Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM
Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM
CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024...,
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

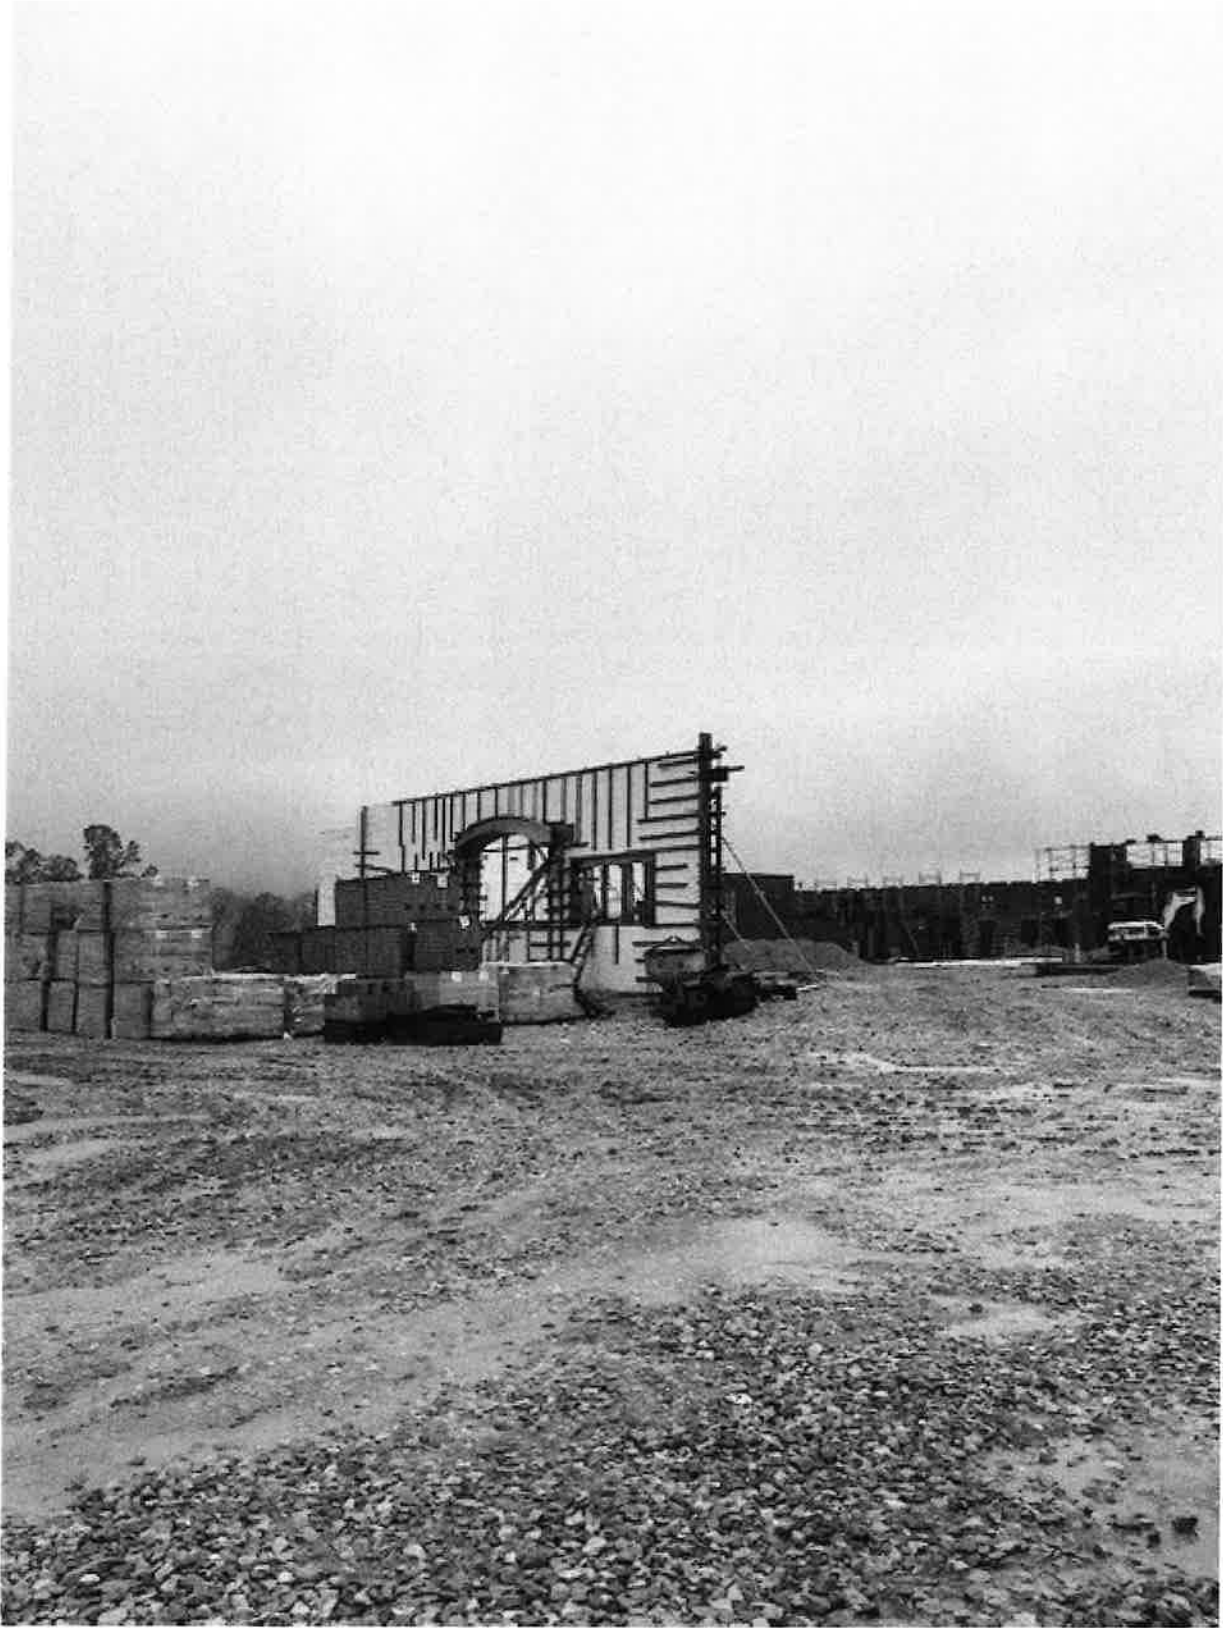



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00
hours

52° F
rain

1
notes

2
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00
hours

60° F
cloudy

1
notes

6
equipment

● Approved
status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf


File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

Page 2 of 2





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

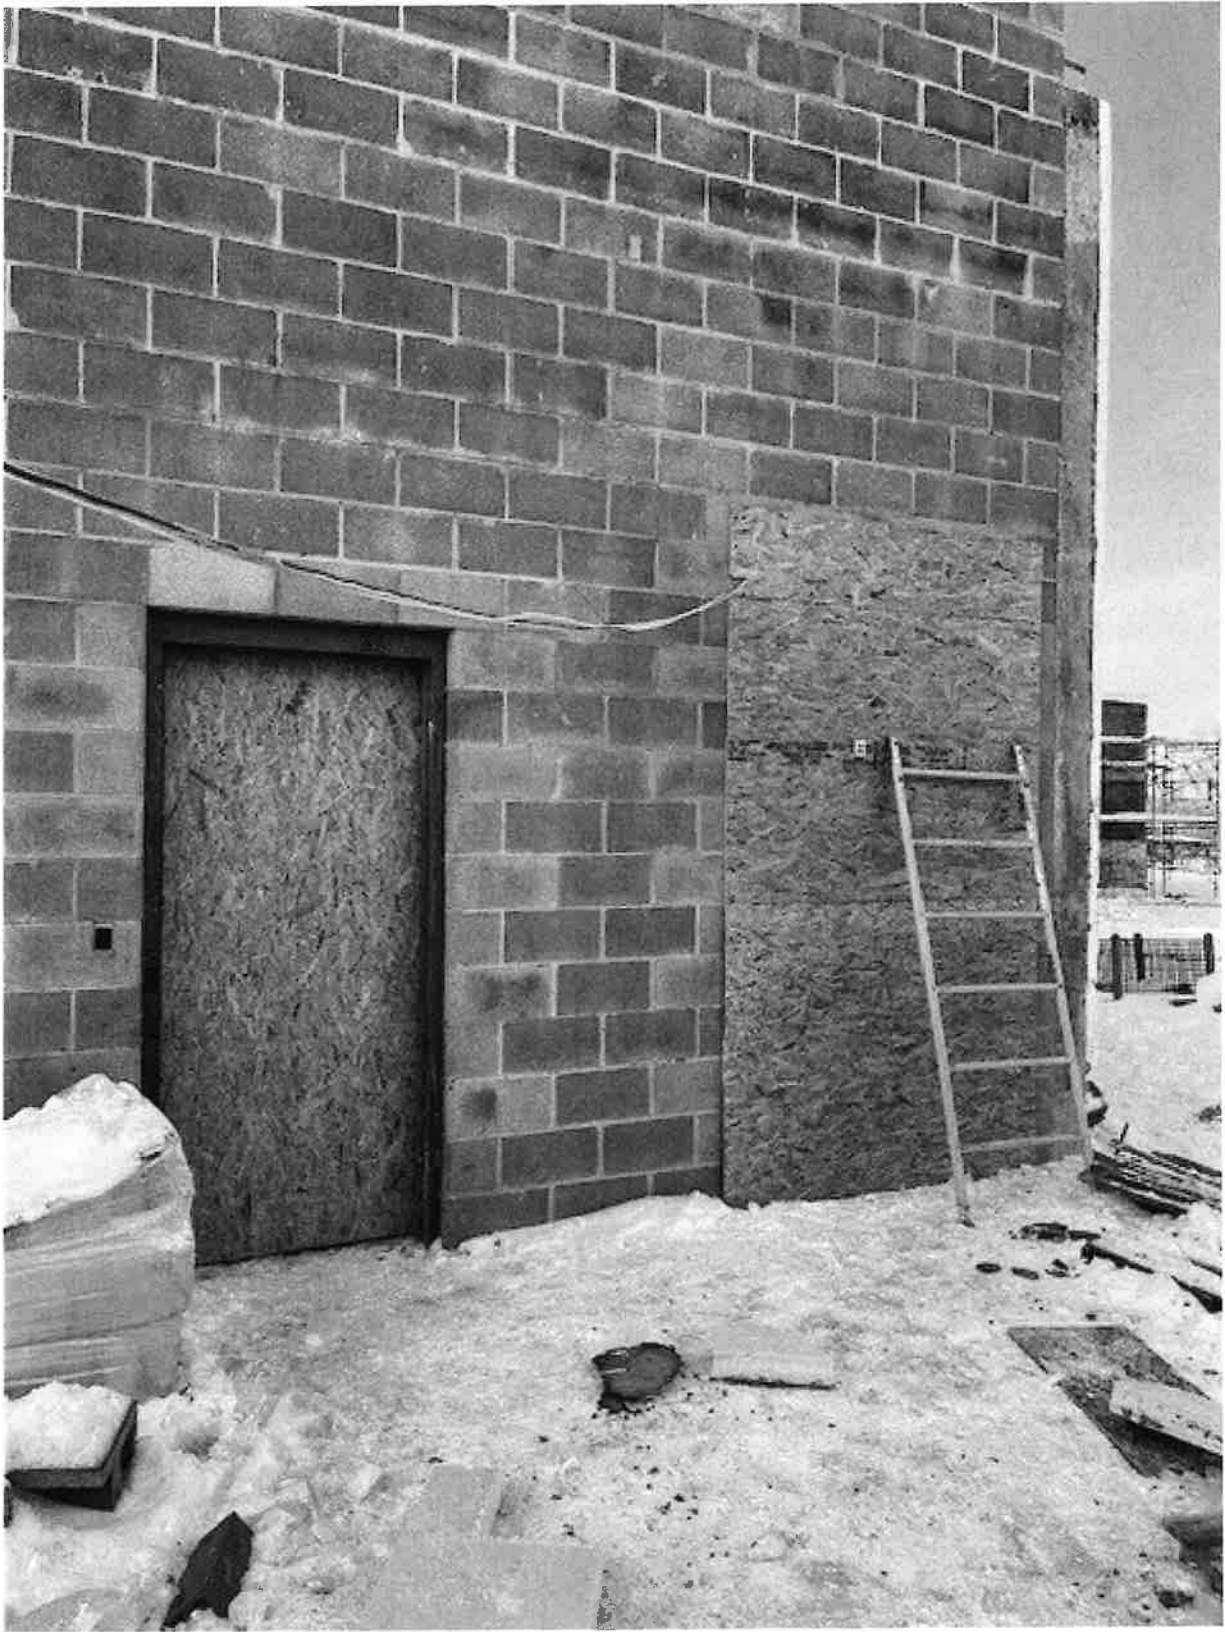



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM

Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
	Installing above ceiling hanger and ductwork in the North and West wings of (Area B).				
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area.		9.00	72.00 Hours	Approved
	(4) Hanging drywall the kitchen and cafeteria areas.				
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
	Grouting bearing walls. Approximately 7 cubic yards.				
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A)		9.00	72.00 Hours	Approved
	(2) Installing electrical rough-in's in metal stud partition walls in administration area.				
	(2) Pulling wire in the kitchen and cafeteria area				
	(2) Pulling wire and home runs in North wing of (Area B)				
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installed curb inlet 4D.				
	Inspecting steel decking in west wing of (Area B)		1.00	3.00 Hours	Approved
	Testing grout samples.				


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

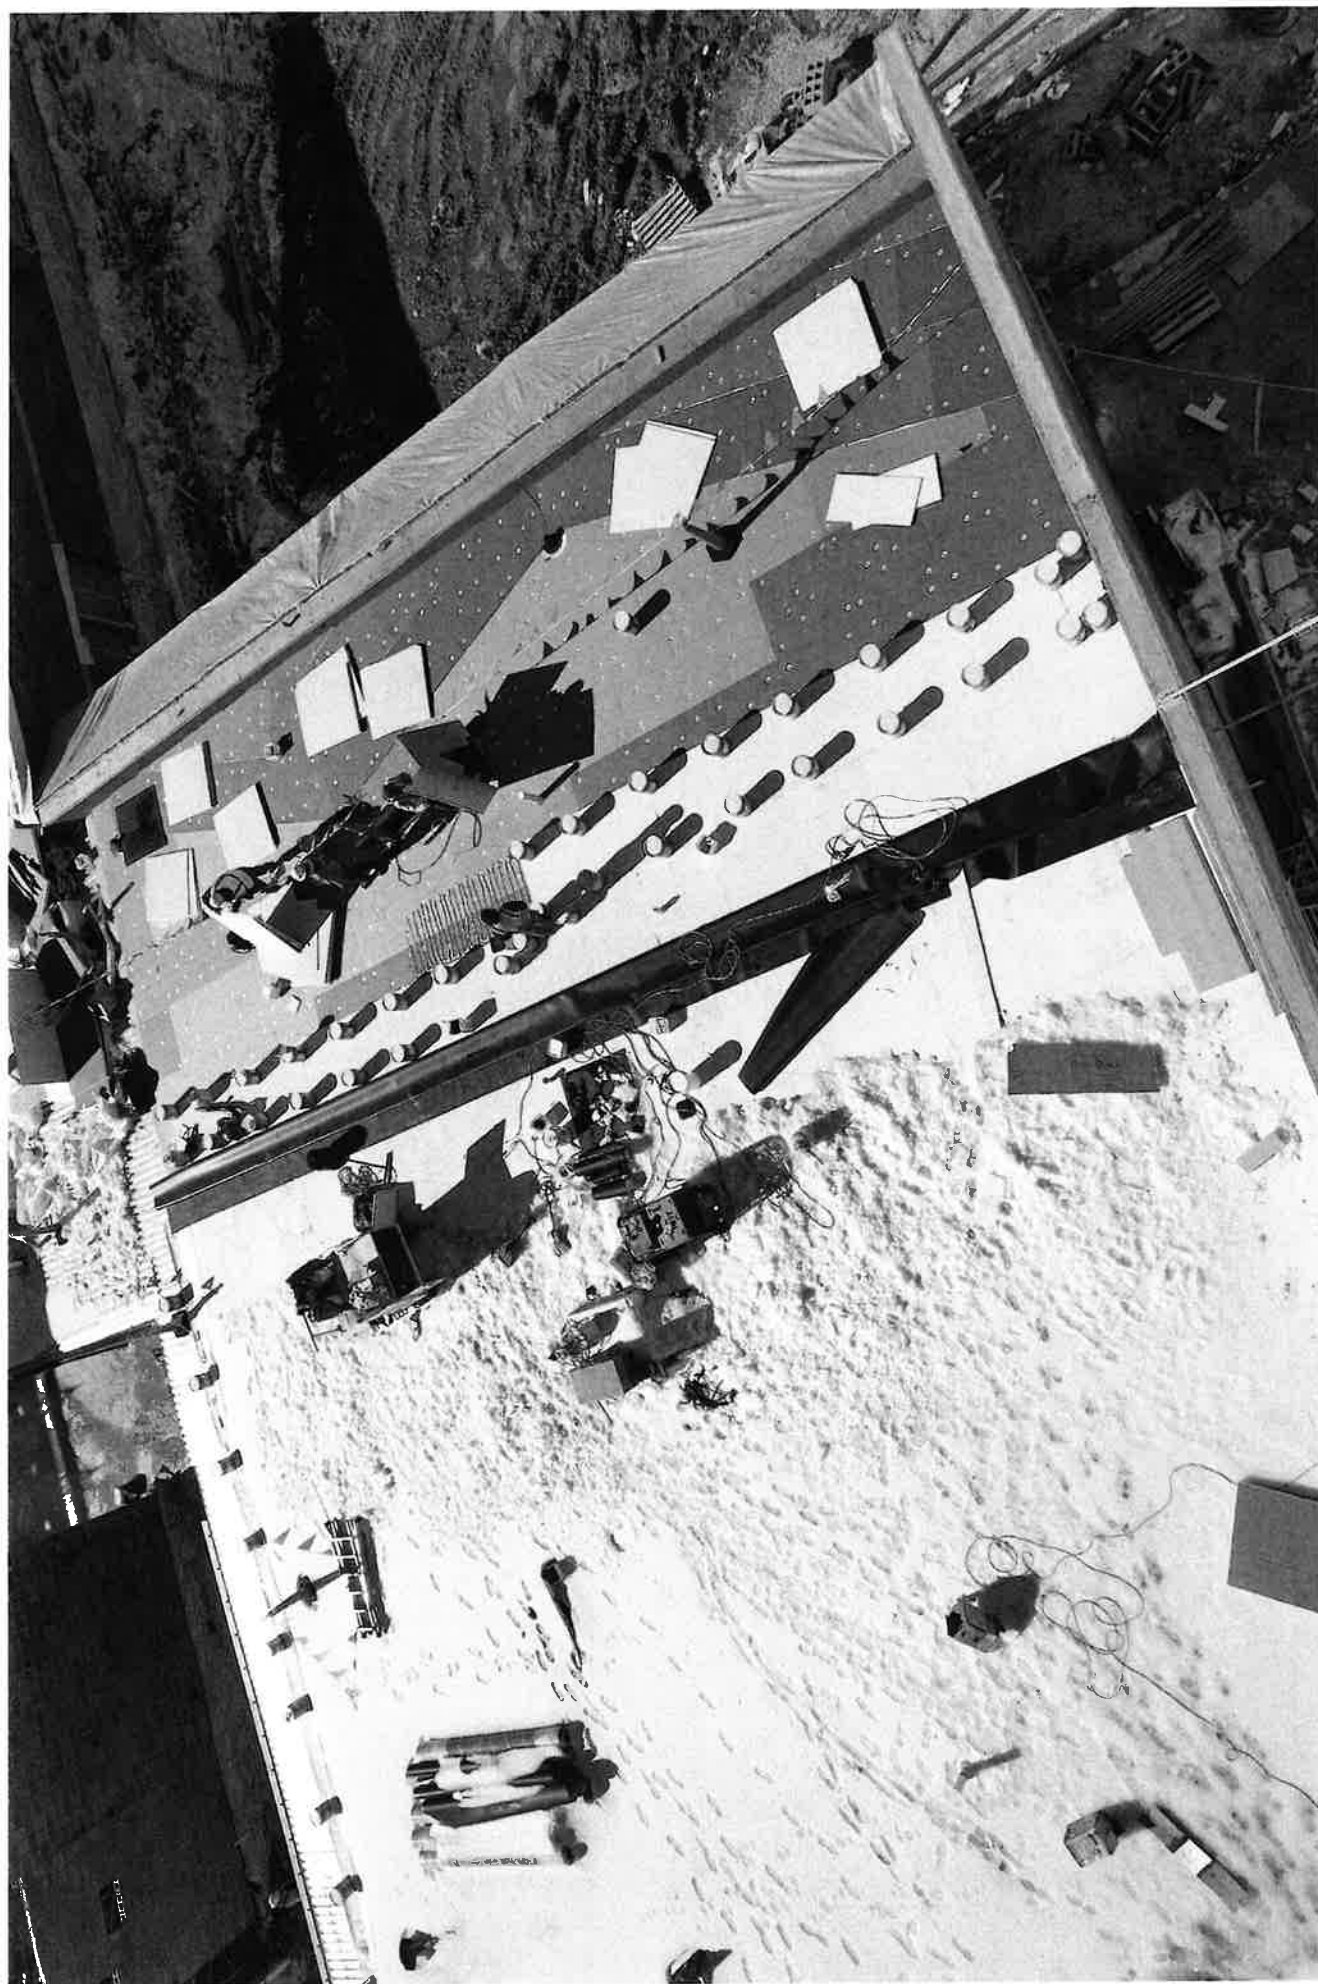



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM

 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf
 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf
 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	

Michael Graf on 1/23/2025 03:17 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM


File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM


Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM

File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES


Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
KENTUCKY SHEET	Installing floor drains in mezzanine				
METAL, INC (N/A)	(Area C)				
GRAYHAWK, LLC	Topping out masonry walls in (Area A)		4.00	32.00 Hours	Approved
(N/A)					
MASON	Laying up brick on north facade of (Area		8.00	64.00 Hours	Approved
STRUCTURE, INC.	B)				
(N/A)					
RIMAR ELECTRIC,	(4) Installing cable trays in (Area B)		9.00	72.00 Hours	Approved
LLC (N/A)	(5) Pulling wire in west wing of (Area B)				
RISING SUN	(2) Sealing exterior ICF wall bar joist		12.00	96.00 Hours	Approved
DEVELOPING	pockets.				
COMPANY (N/A)	(5) Prepping mezzanine HCP's for				
	topping coat.				
	(2) clean up.				
	(3) installing metal stud partition walls				
	wood blocking (Pre school)				
SPRAY FOAM	Applying initial finish coat in kitchen and		2.00	16.00 Hours	Approved
TECHNOLOGIES	cafeteria.				
OF KY (N/A)					

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101101101101101

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Slanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

11119930

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62492)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Martin Flooring Co Inc, 0014, Wood Flooring

Type: CM Bid Package

Proposed

Change Order Number14-01

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency Balance

Contract Change Requested By Construction Manager

Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62492)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
CONSTRUCTION MANAGER ☐
ARCHITECT ☐
CONTRACTOR ☐
FIELD ☐
OTHER ☐

PROJECT (Name and Address)
STANTON ELEMENTARY SCHOOL
WEST COLLEGE AVENUE
STANTON, KY 40380

CHANGE ORDER NUMBER: 14-01
INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
MARTIN FLOORING COMPANY, INC.

PROJECT NUMBERS: 000743
CONTRACT DATE: 3/4/2024
CONTRACT FOR: BID PACKAGE #14 WOOD FLOORING

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	68,418.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	68,418.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	68,418.00

The Contract Time will be adjusted by 93 days.
The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

MARTIN FLOORING COMPANY, INC.

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24																						
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																						
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																						
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																						
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																						
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																						
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																						
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																						
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																						
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																						
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																						
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																						
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																						
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																						
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																						
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																						
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																						
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																						
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																						
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																						
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																						
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																						
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																						
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																						
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																						
26	Install Fire Main, Vault and Hydrants	30 days	Wed 6/26/24	Wed 8/7/24																						
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																						
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																						
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																						
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																						
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																						
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																						
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																						
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

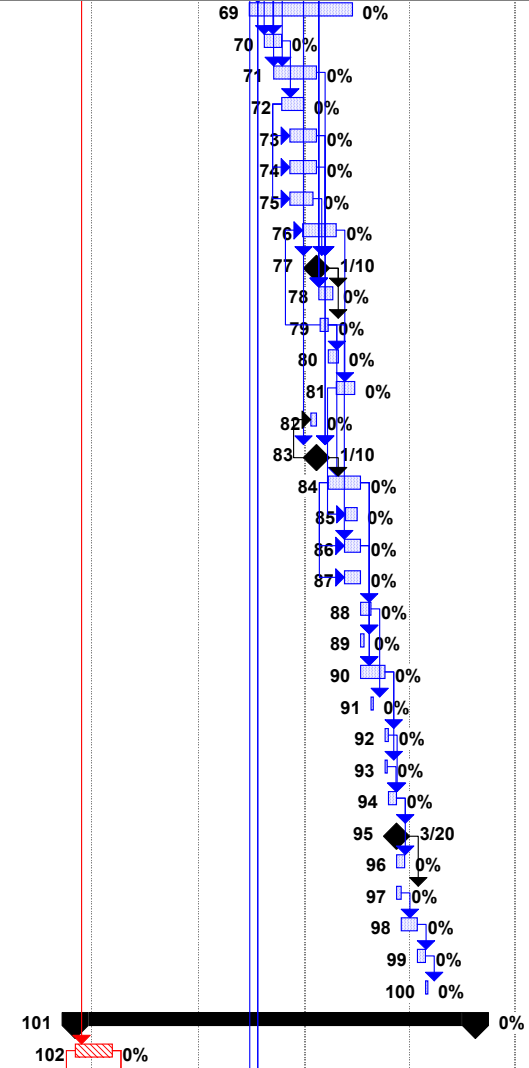

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																				
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																				
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																				
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																				
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																				
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																				
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																				
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																				
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																				
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																				
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																				
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																				
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																				
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																				
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																				
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																				
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																				
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																				
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																				
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																				
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																				
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																				
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																				
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																				
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																				
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																				
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																				
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																				
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																				
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																				
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																				
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																				
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																				
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25								
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25								
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25								
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24								
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24								
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24								
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24								
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24								
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24								
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24								
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24								
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24								
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24								
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24								
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24								
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24								
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24								
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24								
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24								
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24								
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24								
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25								
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25								
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25								
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24								
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25								
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25								
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25								
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25								
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25								

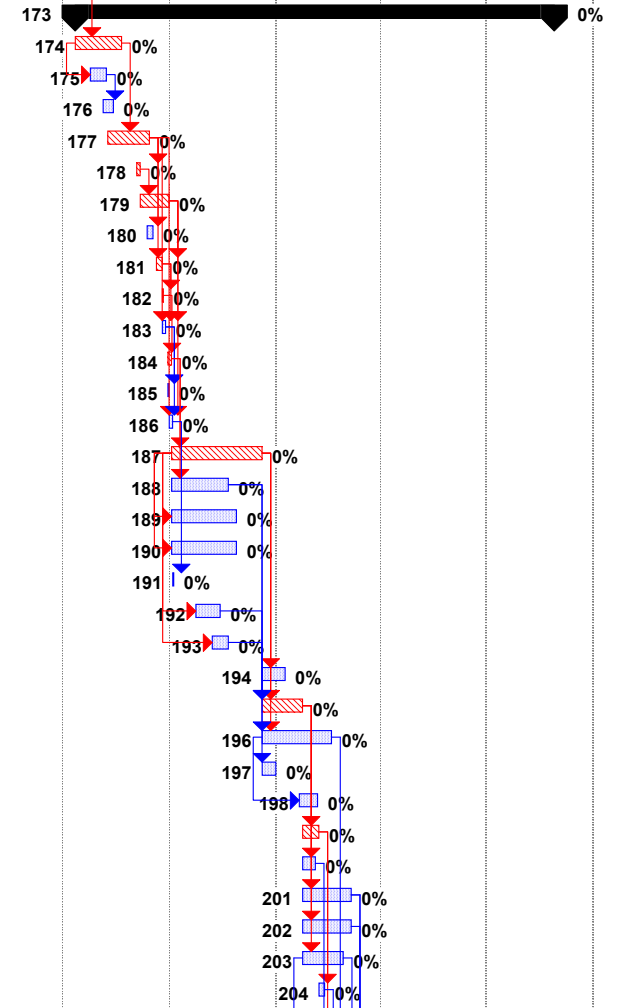

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																								
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																								
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																								
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																								
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																								
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																								
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																								
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																								
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																								
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																								
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																								
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																								
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																								
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																								
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																								
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																								
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																								
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																								
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																								
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																								
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																								
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																								
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																								
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																								
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																								
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																								
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																								
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																								
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																								
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																								
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																								
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																								
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																								
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																						
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																						
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																						
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																						
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																						
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																						
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																						
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																						
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																						
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																						
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																						
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																						
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																						
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																						
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																						
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																						
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																						
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																						
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																						
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																						
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																						
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																						
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																						
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																						
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																						
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																						
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																						
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																						
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																						
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																						
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																						
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25								
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25								
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25								
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25								
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25								
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25								
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25								
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25								
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25								
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25								
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25								
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25								
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25								
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25								
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25								
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25								
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25								
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25								
296	Architect Site Punch List Distrubuted - Site	0 days	Mon 8/11/25	Mon 8/11/25								
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25								
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25								
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

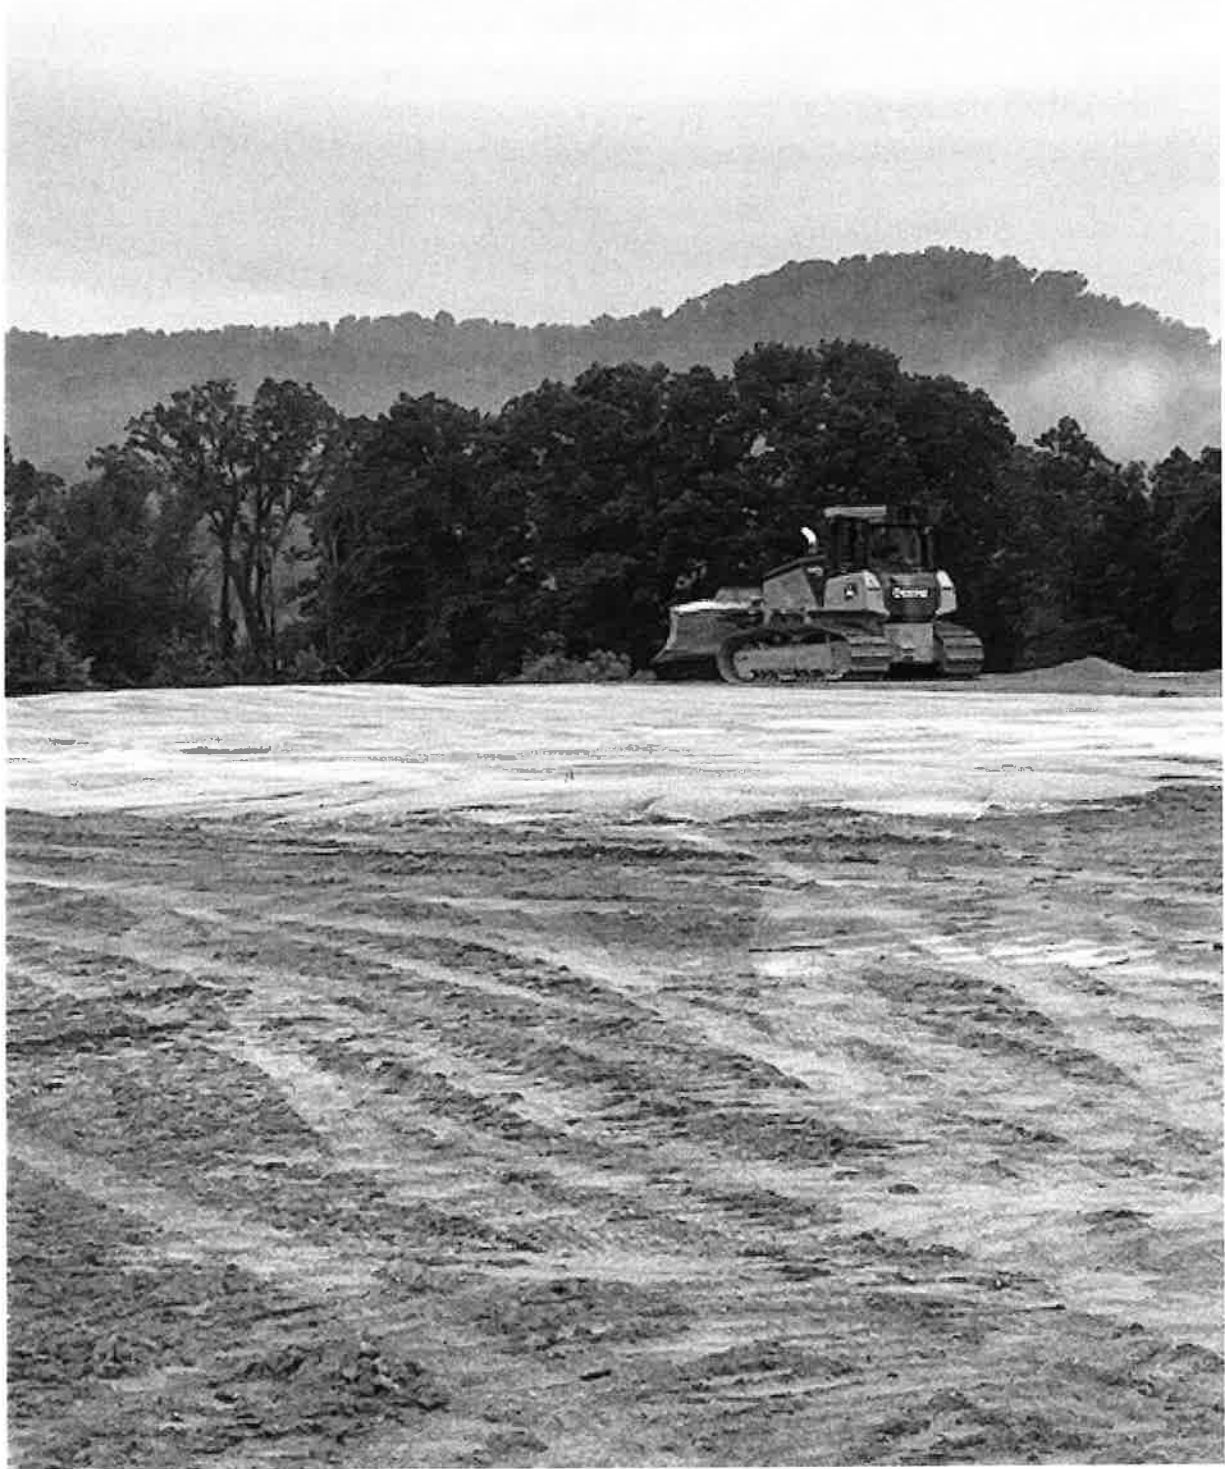



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM
Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM
CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024...,
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

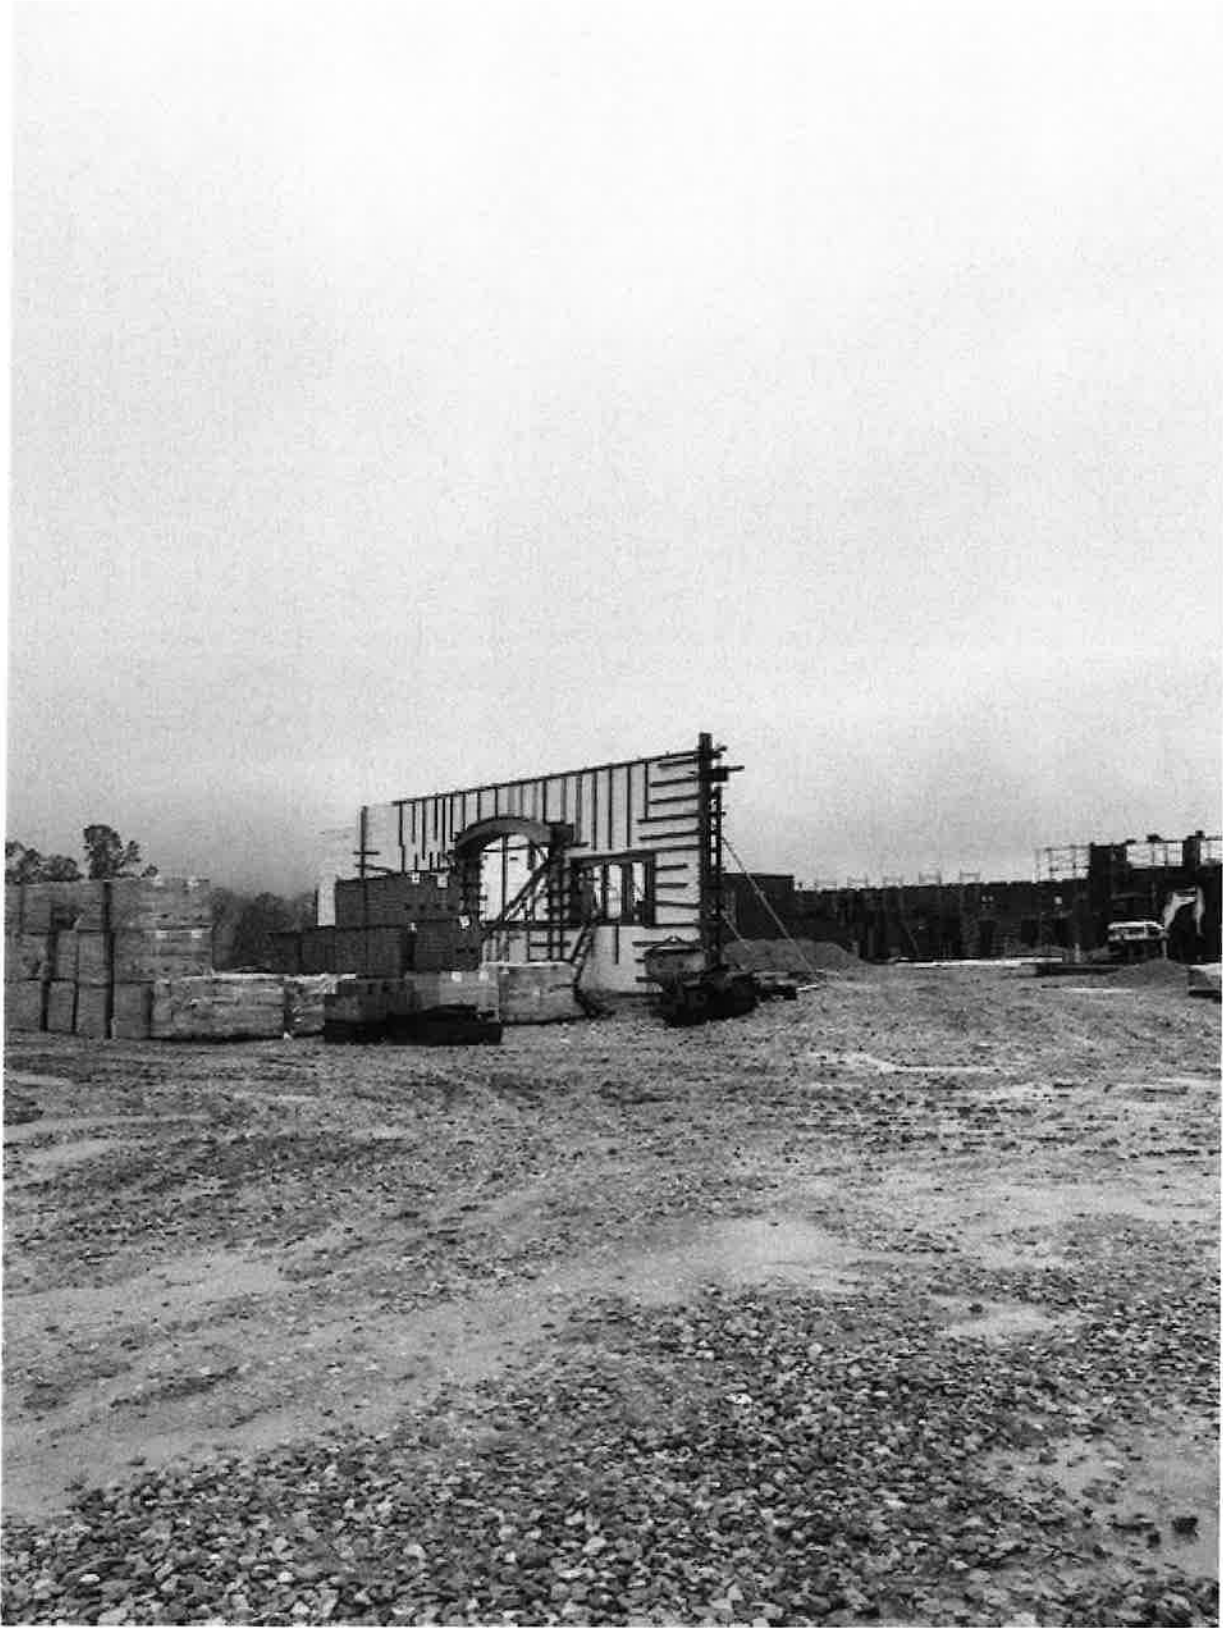



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

File

11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM



File

Daily Report 2024...
Michael Graf





Daily Construction Report

With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00
hours

21° F
cloudy

1
notes

2
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

Page 2 of 2





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

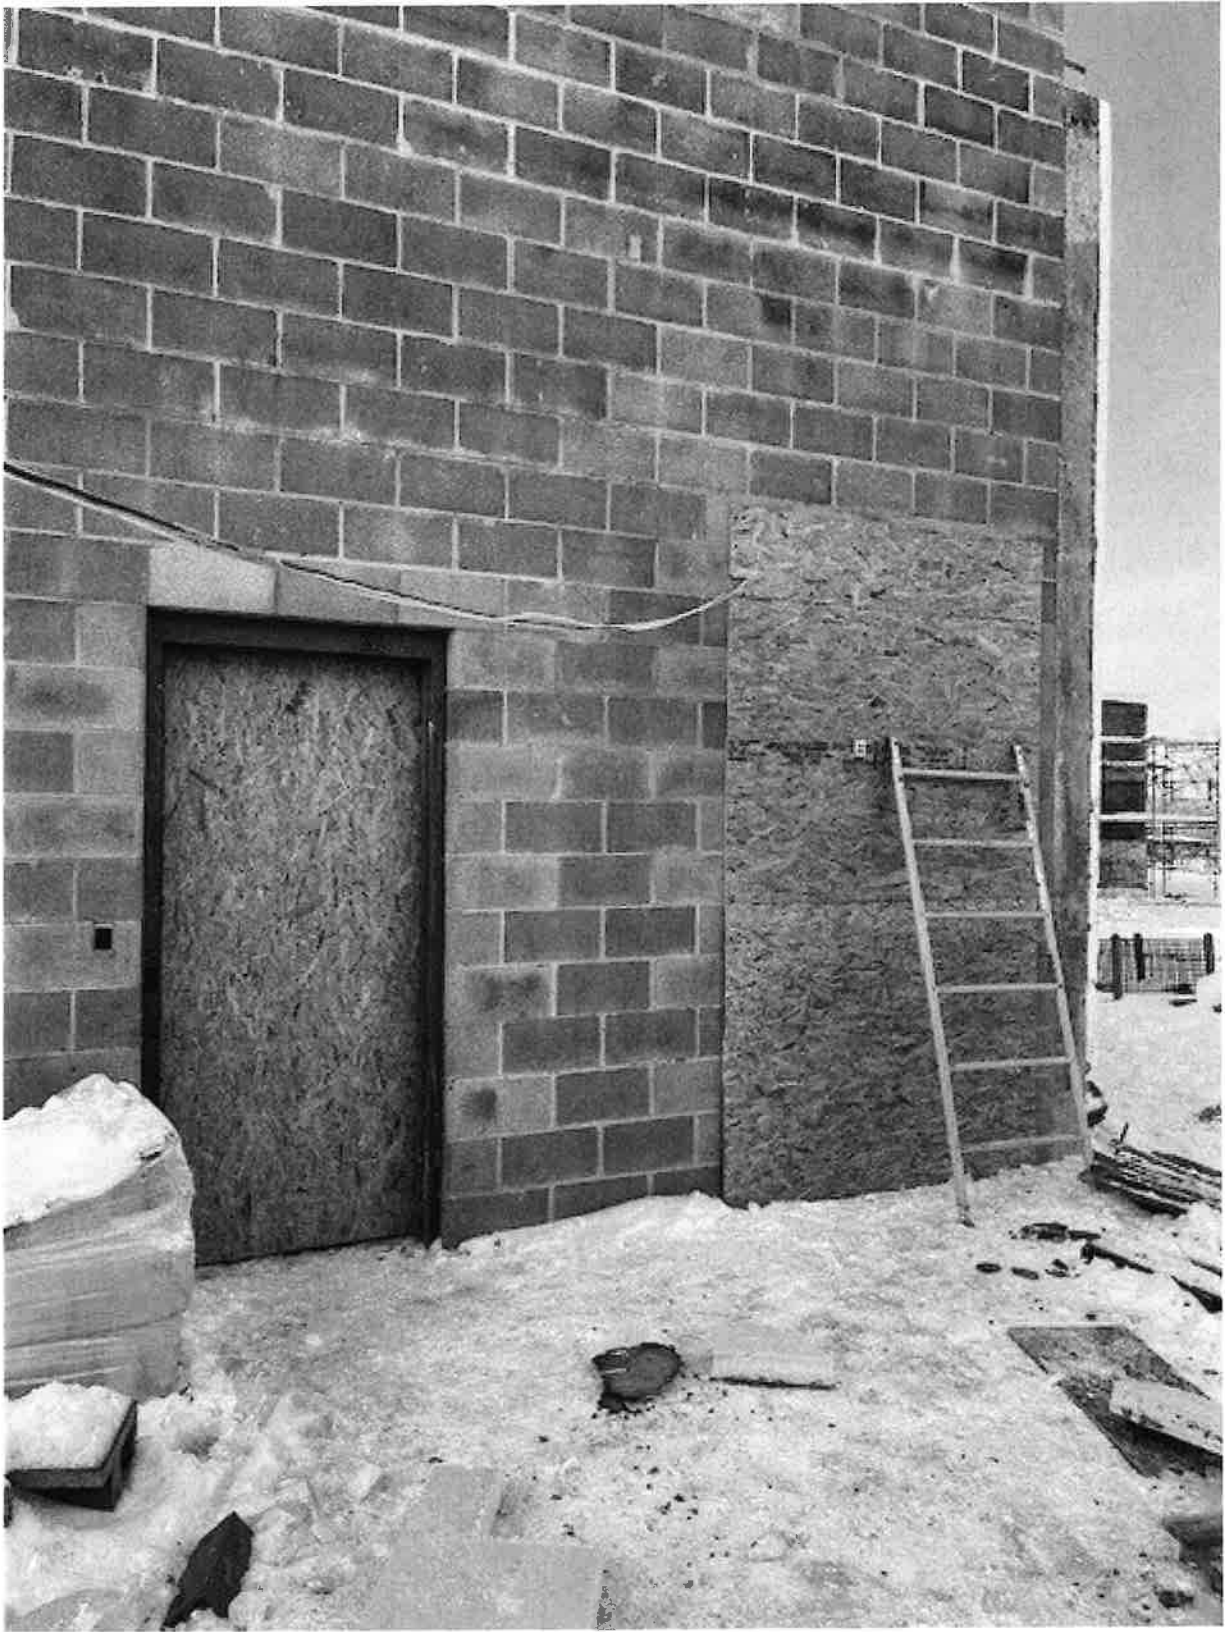



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

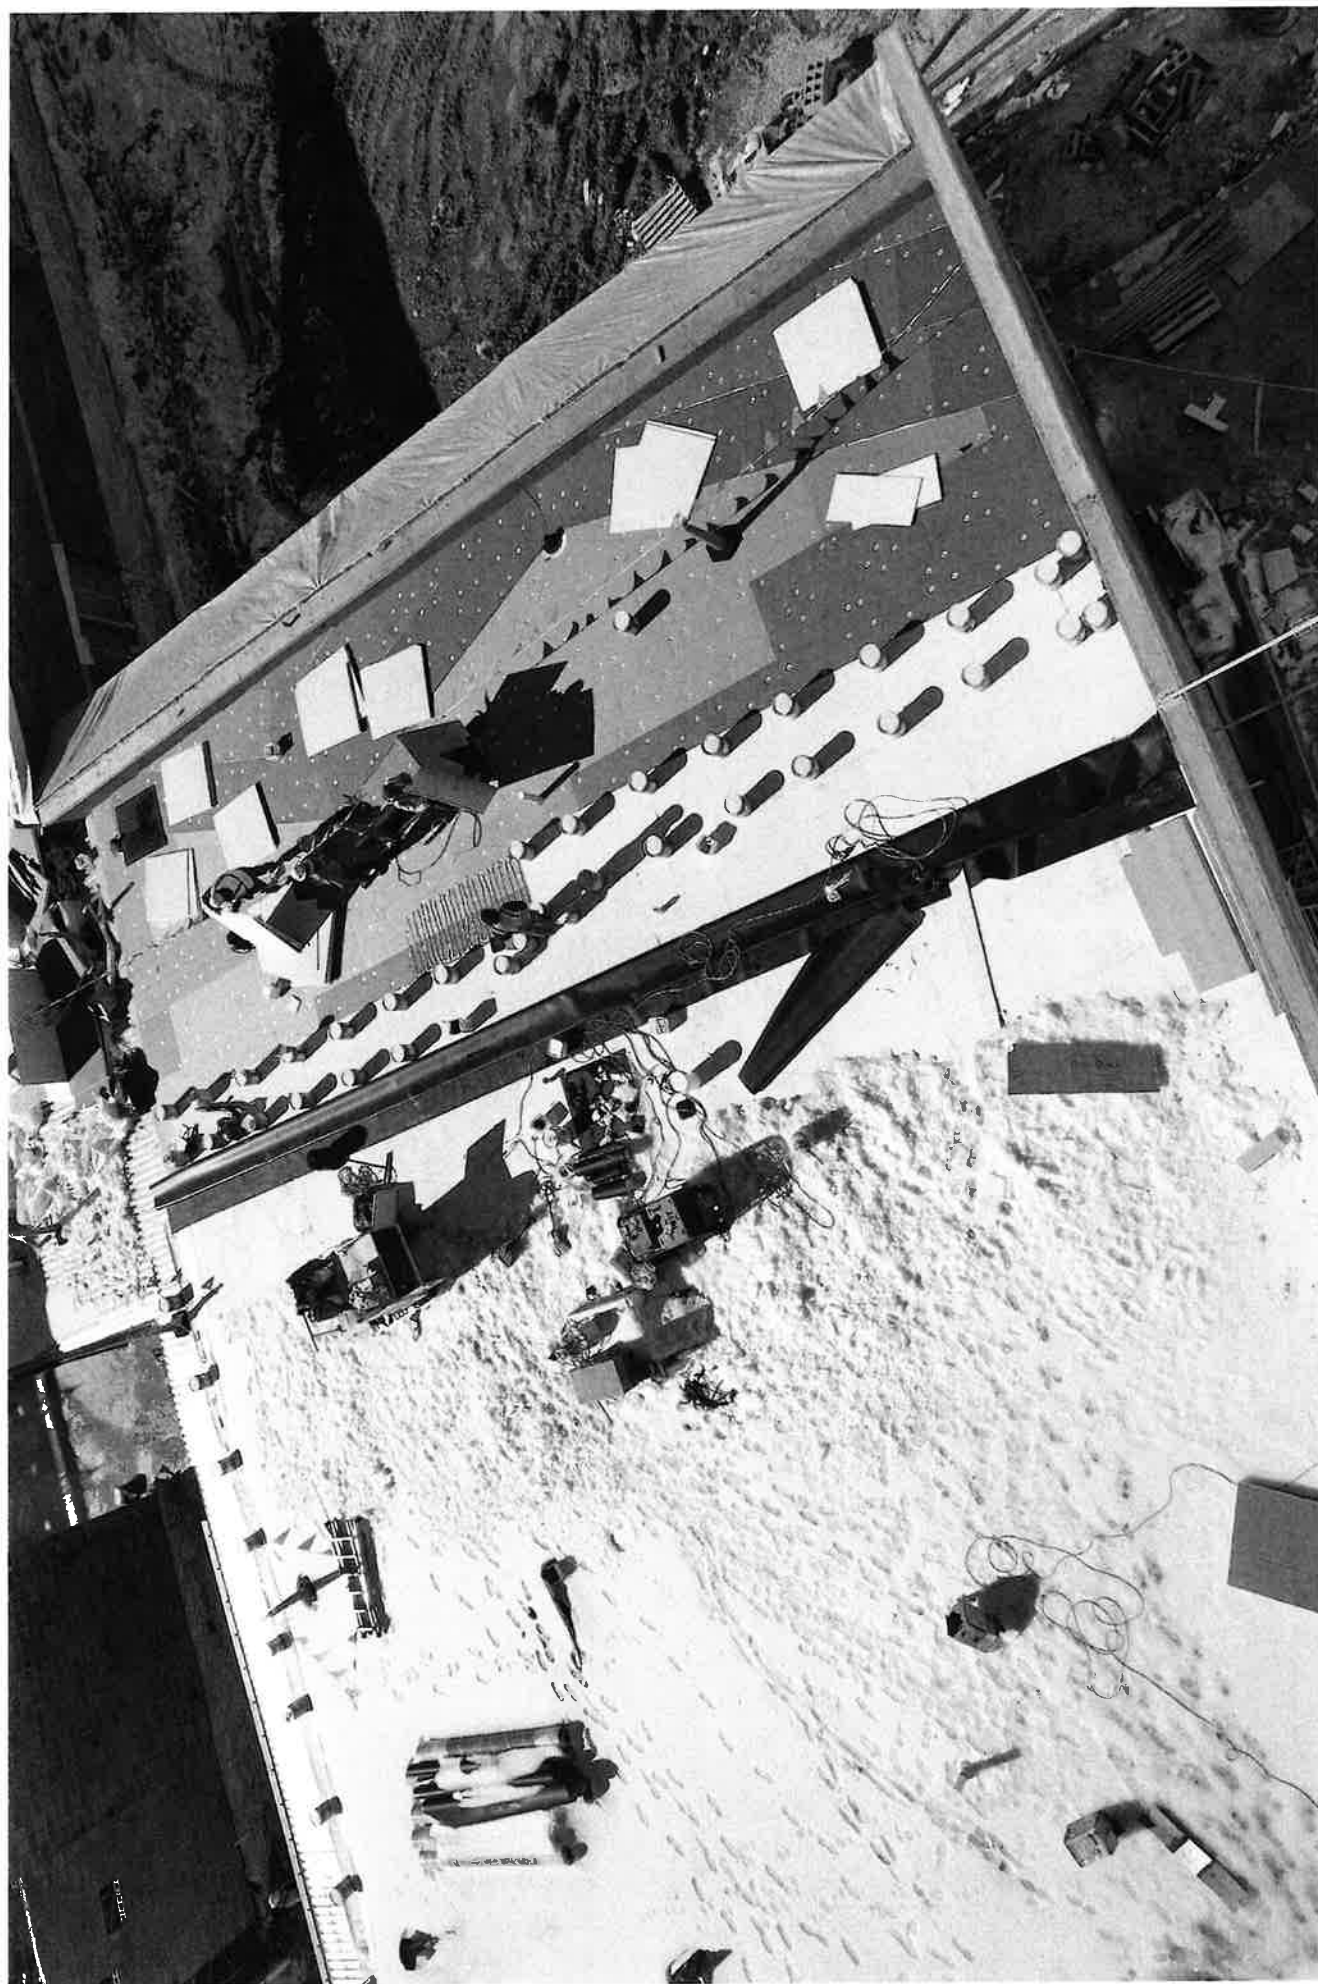



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf

Michael Graf on 1/23/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM

File
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM


Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM

File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00
hours

18° F
cloudy

1
notes

3
equipment

● Pending
status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62496)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School
BG Number: 21-072 District: Powell County (HB678) (495)
Status: Active Phase: Project Initiation (View Checklist)

Contract: Twin Lakes Fire Service, 0017, Fire Protection
Type: CM Bid Package Proposed

Change Order Number 17-01
Time Extension Required Yes
If Yes Number Of Days 93
Date Of Change Order 6/9/2025
Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-
Change In A/E Fee This Change Order
+/-
Change In CM Fee This Change Order
+/-
Remaining Construction Contingency
Balance
Contract Change Requested By Construction Manager
Contract Change Reason Code Time Extension
Change Order Description And Justification
1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner

No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62496)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
CONSTRUCTION MANAGER ☐
ARCHITECT ☐
CONTRACTOR ☐
FIELD ☐
OTHER ☐

PROJECT (Name and Address)
STANTON ELEMENTARY SCHOOL
WEST COLLEGE AVENUE
STANTON, KY 40380

CHANGE ORDER NUMBER: 17-01
INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
TWIN LAKES FIRE SERVICE, LLC
325 MIDLAND PLACE
LEXINGTON, KY 40505

PROJECT NUMBERS: 000743
CONTRACT DATE: 3/4/2024
CONTRACT FOR: BID PACKAGE #17 FIRE PROTECTION

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	503,280.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	503,280.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	503,280.00

The Contract Time will be adjusted by 93 days.
The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

TWIN LAKES FIRE SERVICE, LLC

CONTRACTOR (Firm Name)
325 MIDLAND PLACELEXINGTON, KY 40505

ADDRESS

BY (Signature)

(Typed Name)

DATE:

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

ARCHITECT (Firm Name)
144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

BY (Signature)

(Typed Name)

DATE:

POWELL COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

BY (Signature)

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																				
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

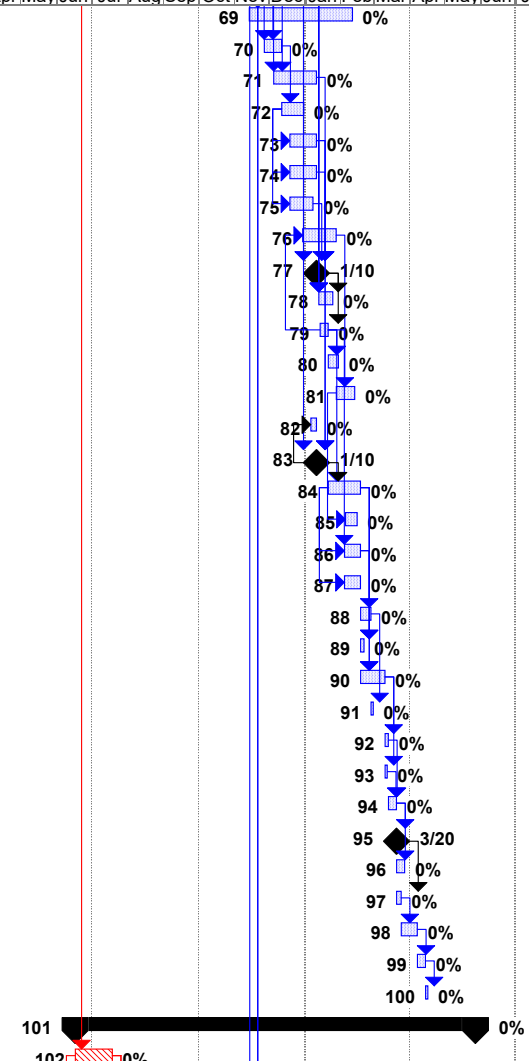

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																171	0%					
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																172	0%					
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						0%
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

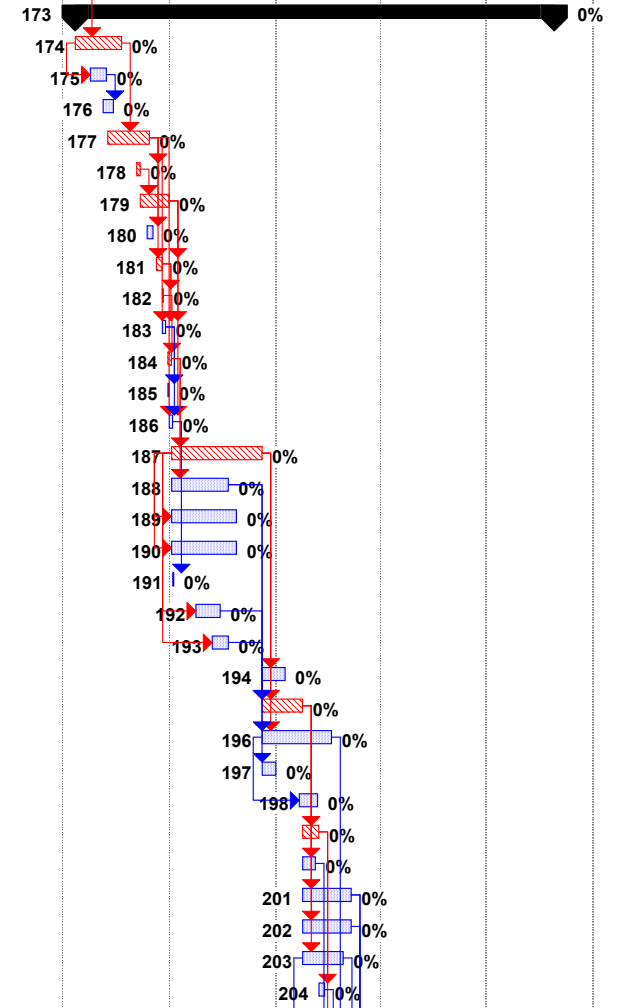

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												</

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical  Task  Milestone 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

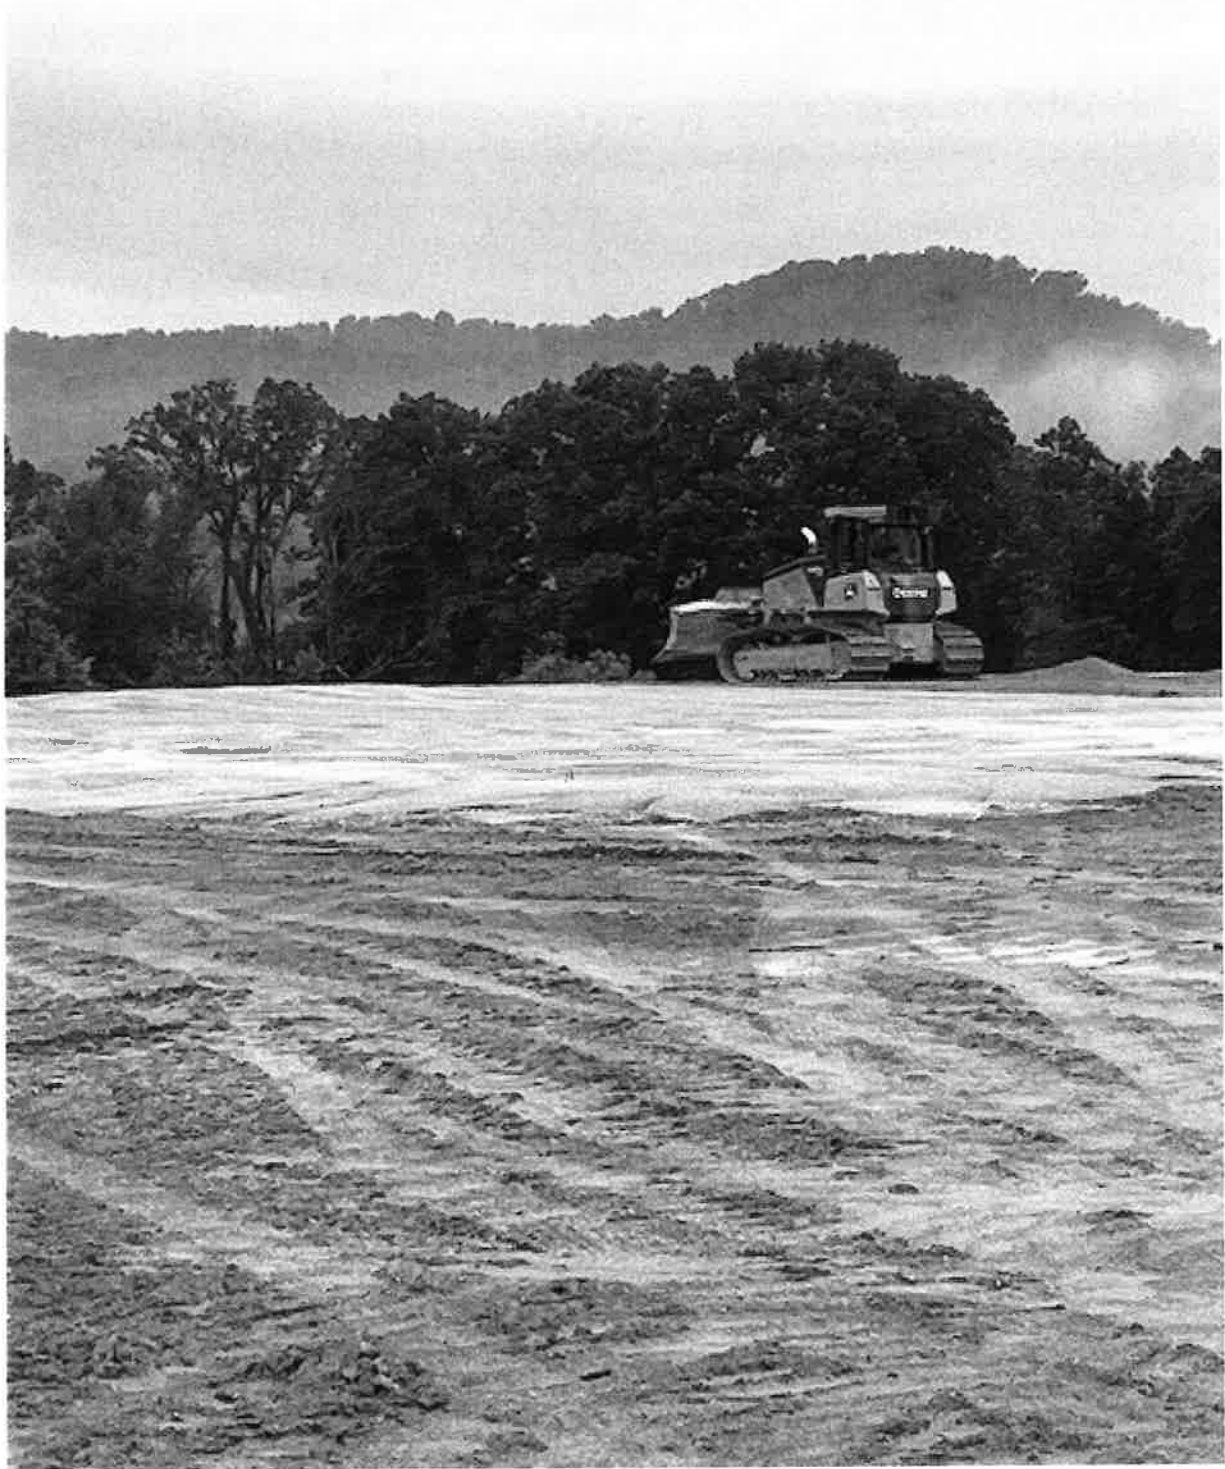



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00

hours

72° F

clear

1

notes

1

equipment

● Approved

status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf



File
9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

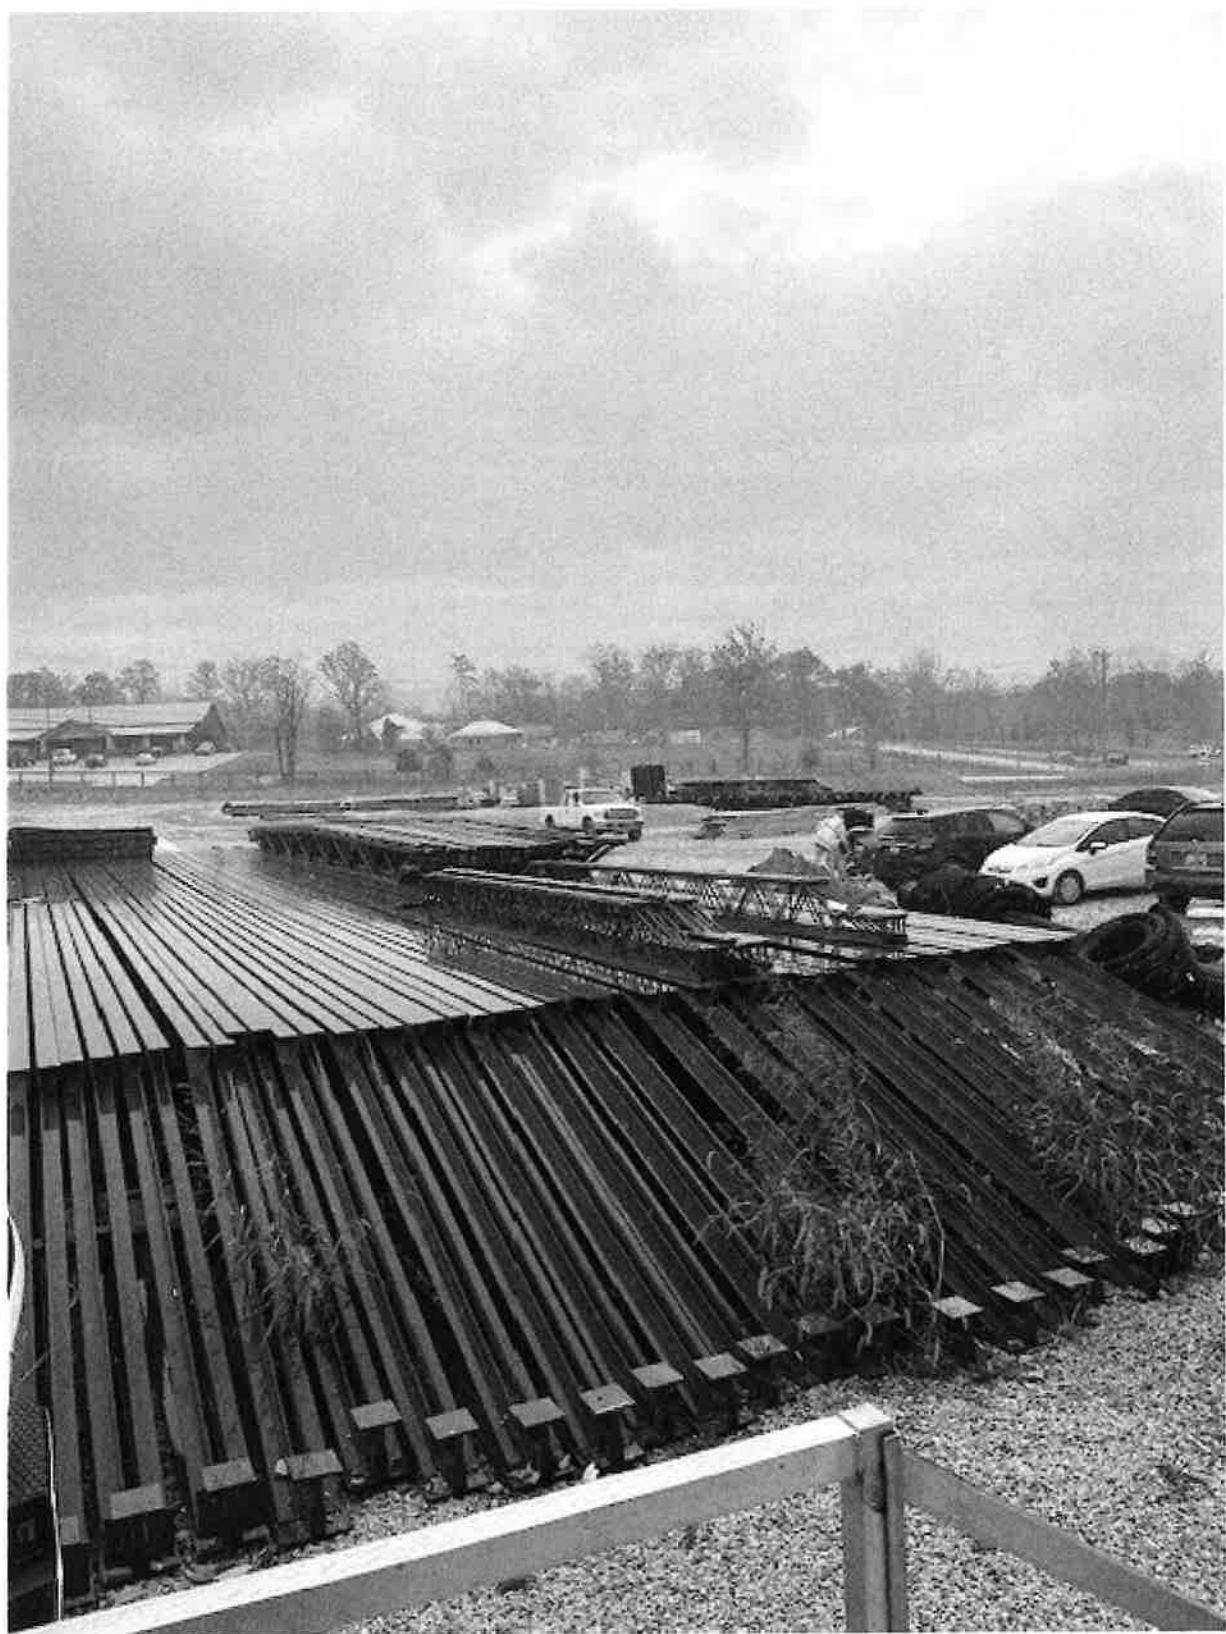



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

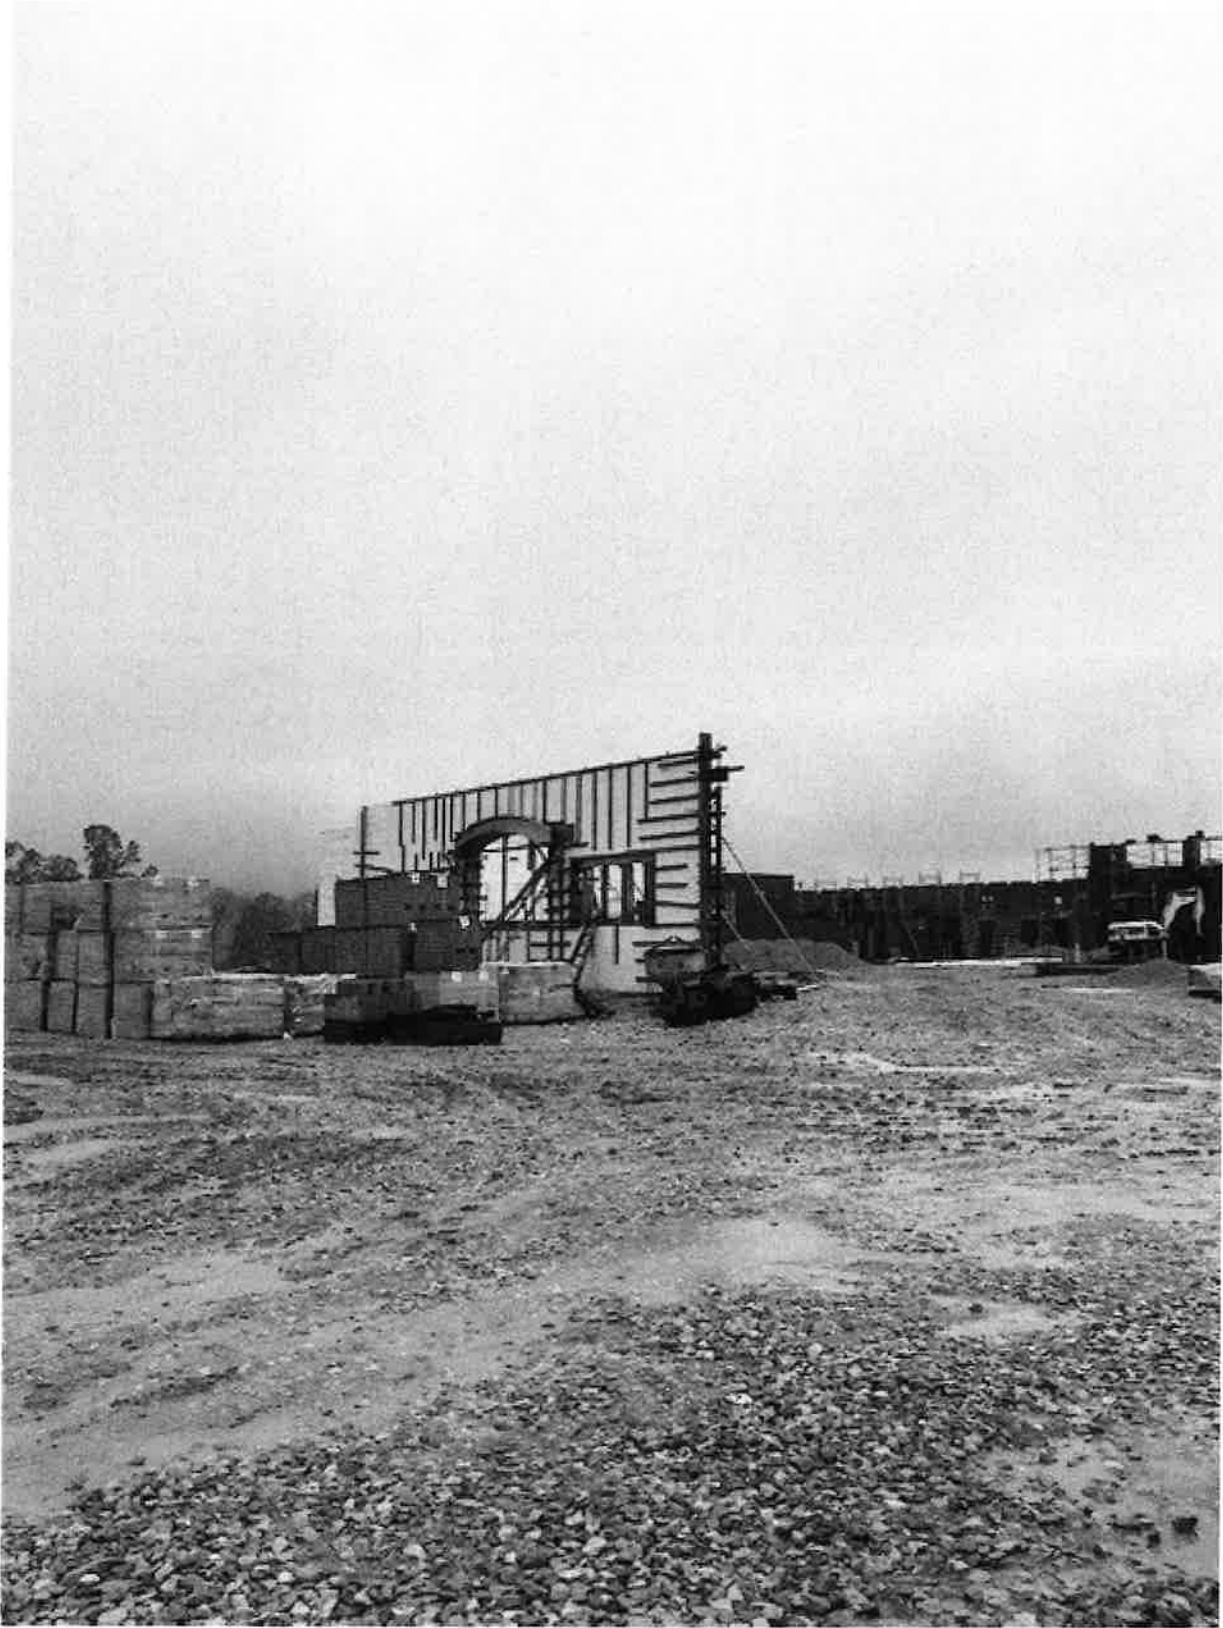



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00
hours

52° F
rain

1
notes

2
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM


File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00
hours

60° F
cloudy

1
notes

6
equipment

● Approved
status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM

File
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM

File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM

File
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

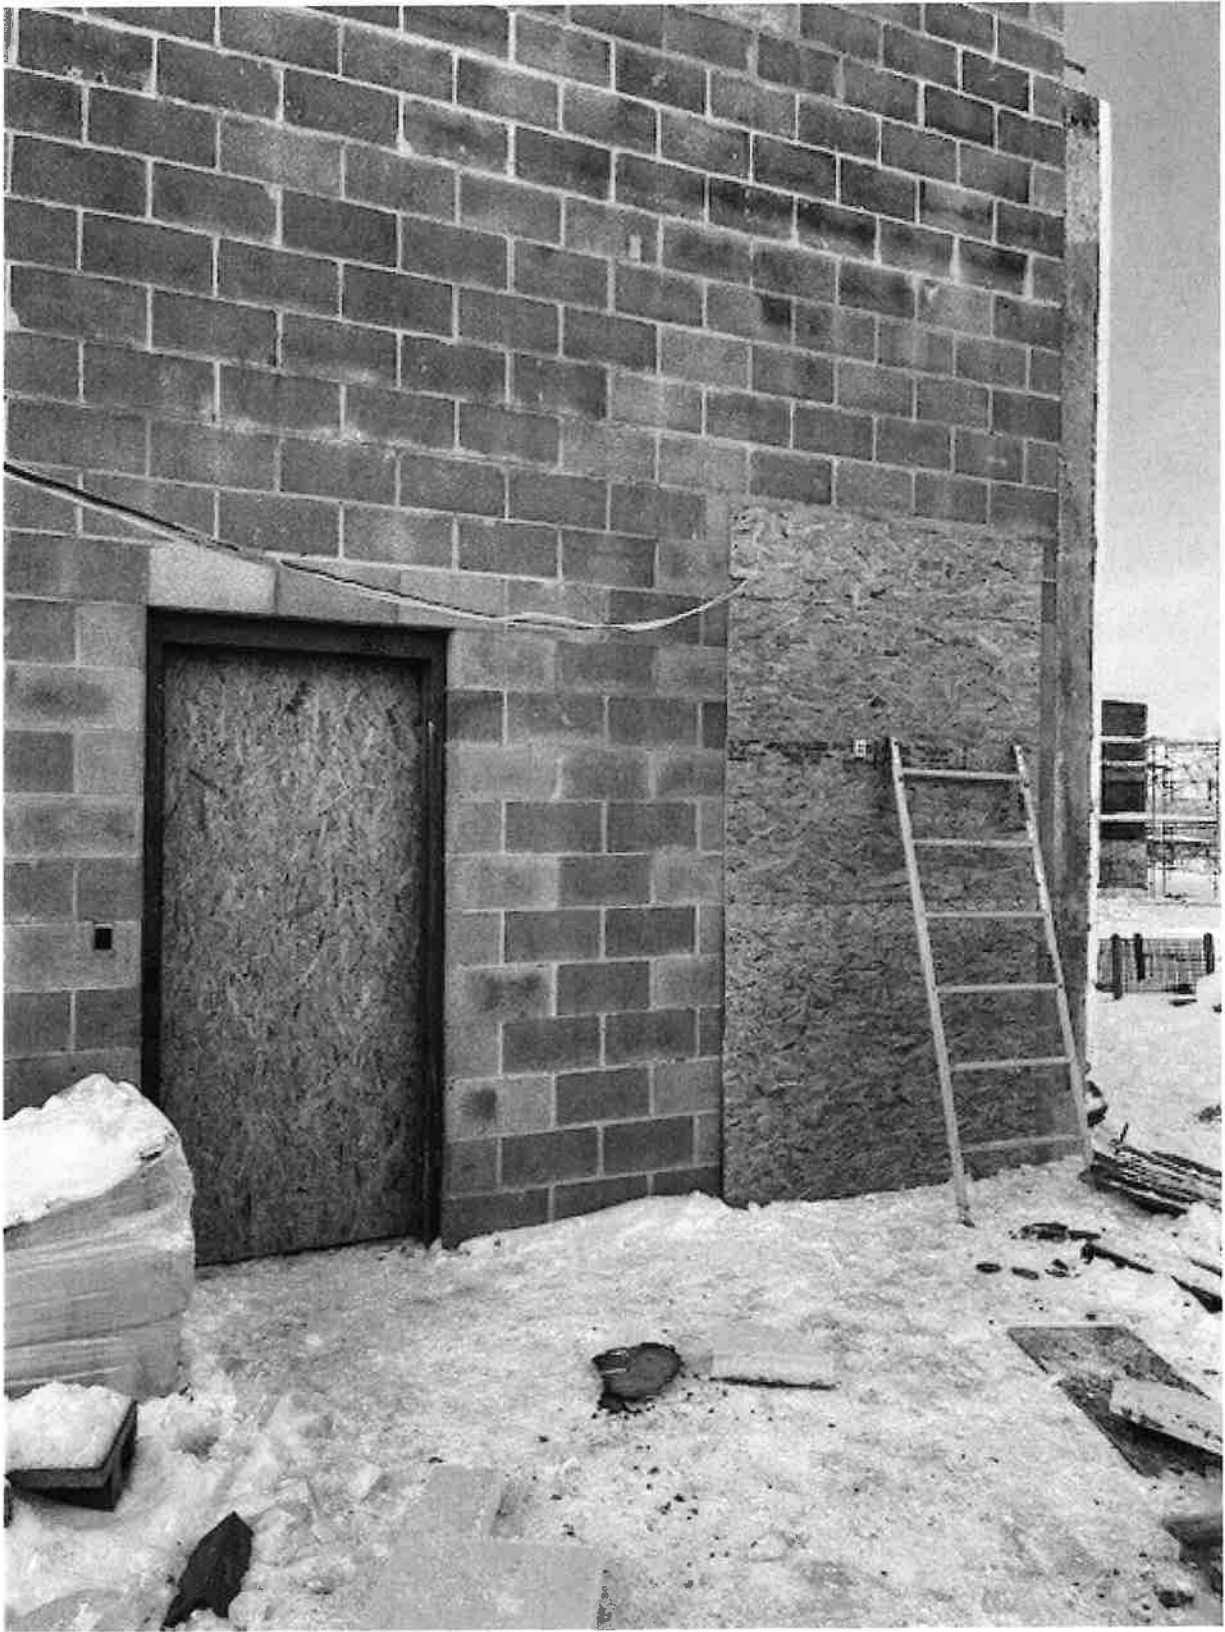



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
	Installing above ceiling hanger and ductwork in the North and West wings of (Area B).				
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area.		9.00	72.00 Hours	Approved
	(4) Hanging drywall the kitchen and cafeteria areas.				
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
	Grouting bearing walls. Approximately 7 cubic yards.				
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A)		9.00	72.00 Hours	Approved
	(2) Installing electrical rough-in's in metal stud partition walls in administration area.				
	(2) Pulling wire in the kitchen and cafeteria area				
	(2) Pulling wire and home runs in North wing of (Area B)				
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installed curb inlet 4D.				
	Inspecting steel decking in west wing of (Area B)		1.00	3.00 Hours	Approved
	Testing grout samples.				


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

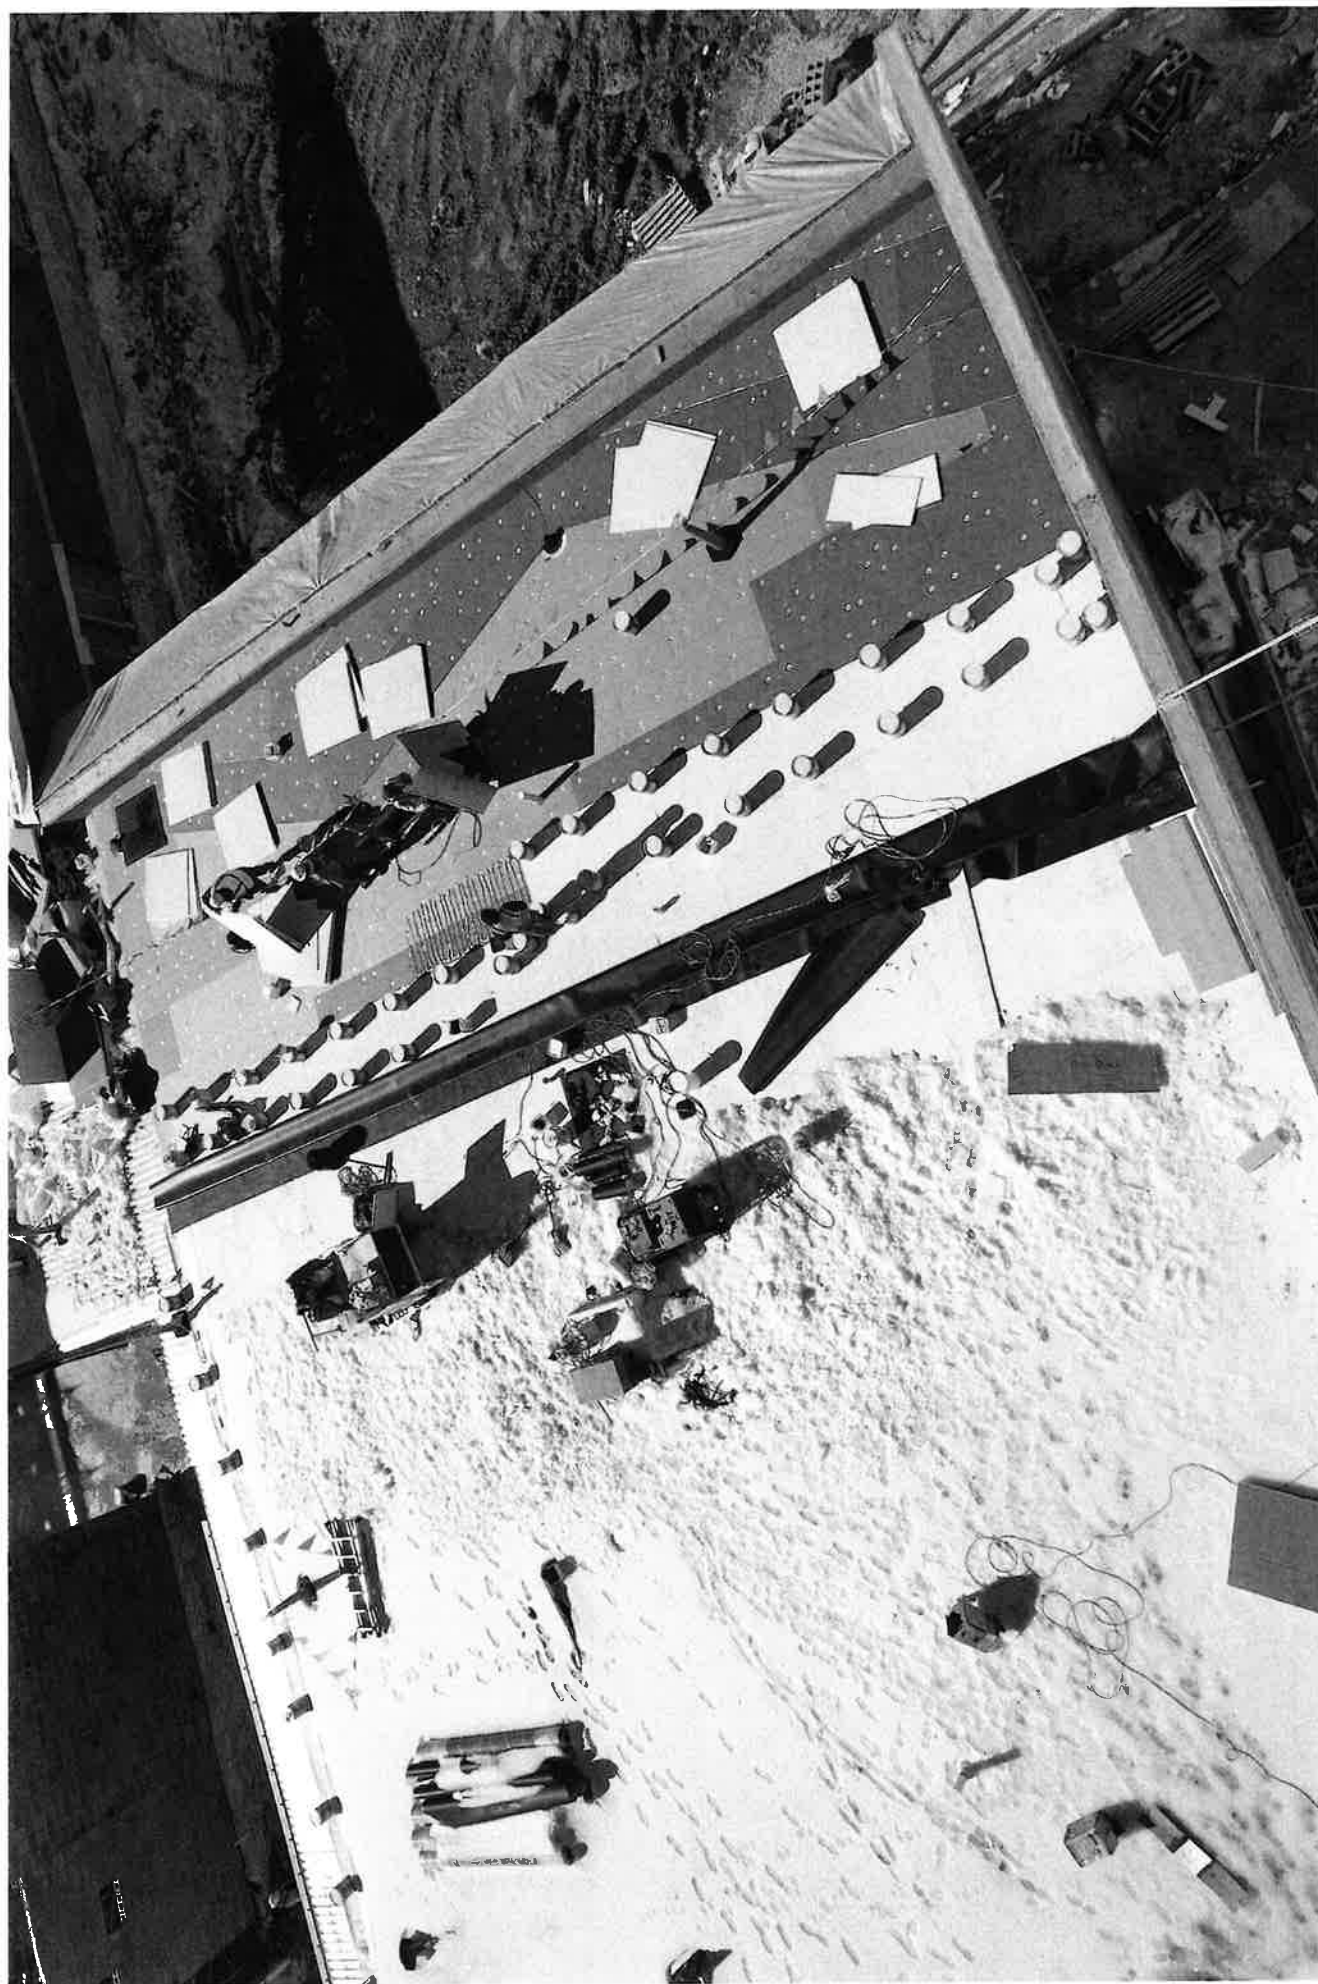



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM

File
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.


Michael Graf on 2/18/2025 03:33 PM



File

Daily Report 2025...

Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES


Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report
With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62485)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Central Kentucky Sheet Metal, Inc., 0018, Plumbing & Mechanical

Type: CM Bid Package

Proposed

Change Order Number18-03

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency Balance

Contract Change Requested By Construction Manager

Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead		0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62485)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 18-03
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 CENTRAL KENTUCKY SHEET METAL

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #18 PLUMBING & MECHANICAL

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	3,263,567.00
Net change by previously authorized Change Orders	-4,683.00
The Contract Sum prior to this Change Order was	3,258,884.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	3,258,884.00

The Contract Time will be adjusted by 32 days.

The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

CENTRAL KENTUCKY SHEET METAL

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																				
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

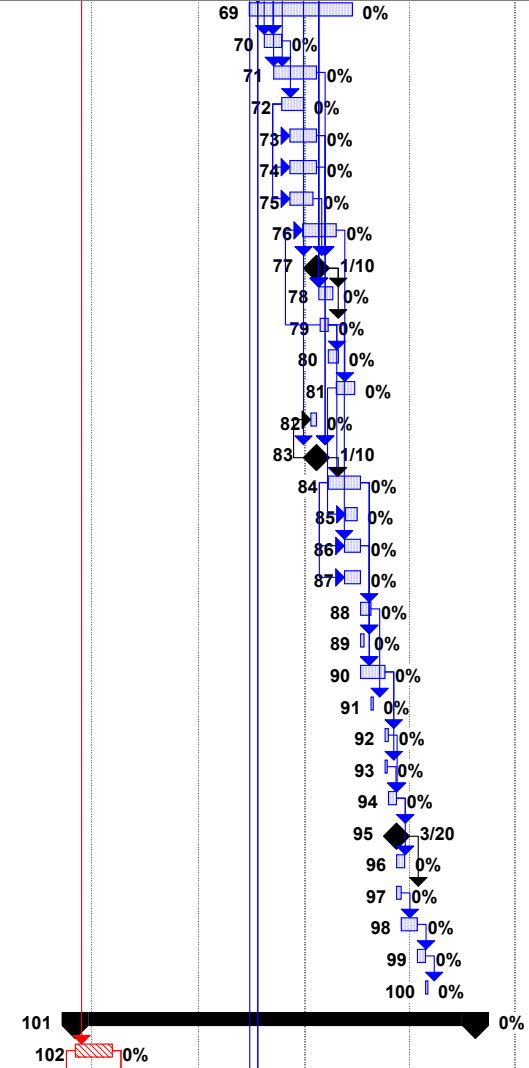

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

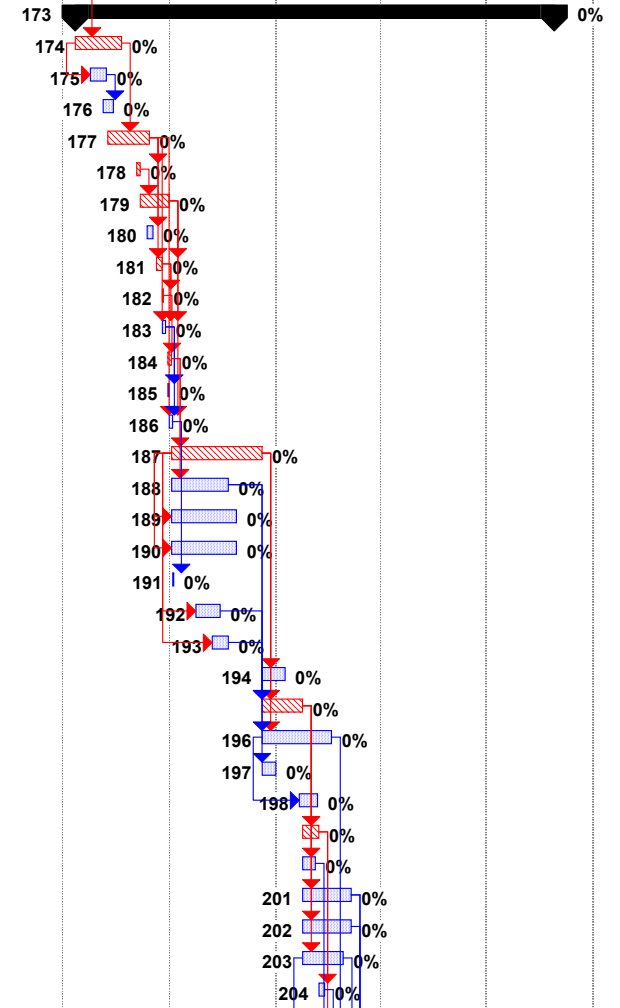

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																								
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																								
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																								
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																								
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																								
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																								
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																								
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																								
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																								
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																								
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																								
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																								
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																								
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																								
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																								
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																								
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																								
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																								
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																								
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																								
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																								
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																								
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																								
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																								
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																								
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																								
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																								
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																								
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																								
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																								
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																								
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																								
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																								
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

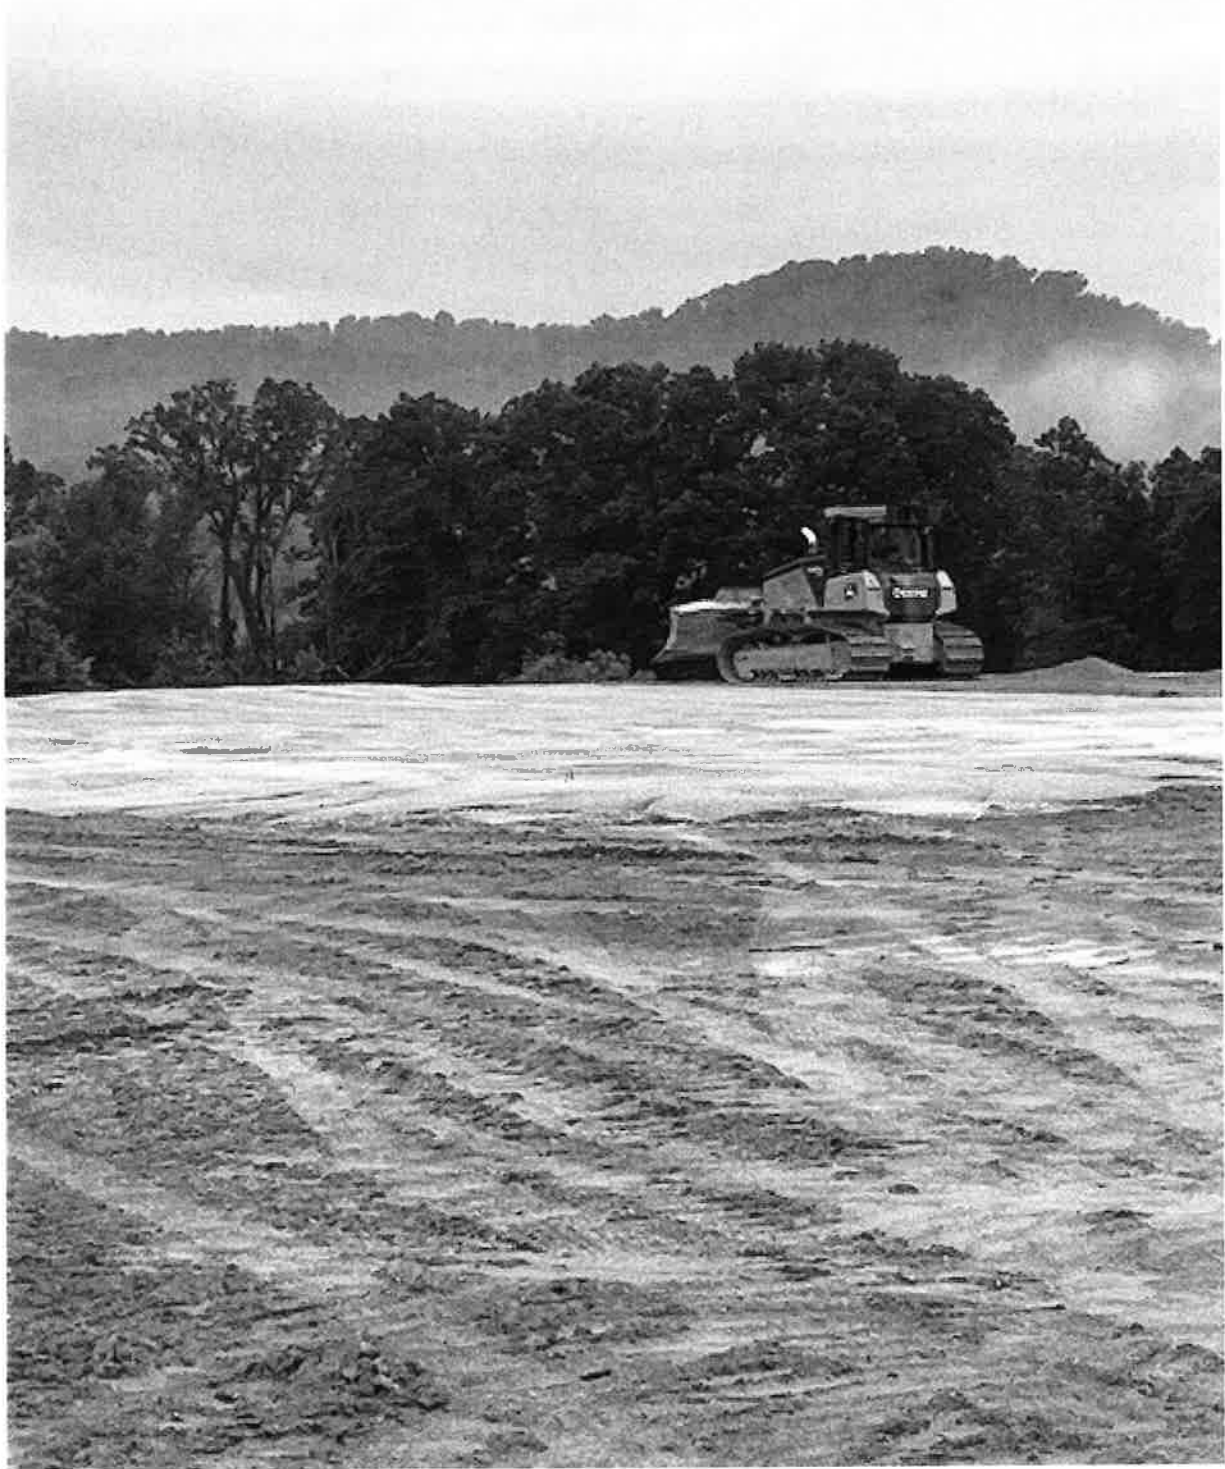



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

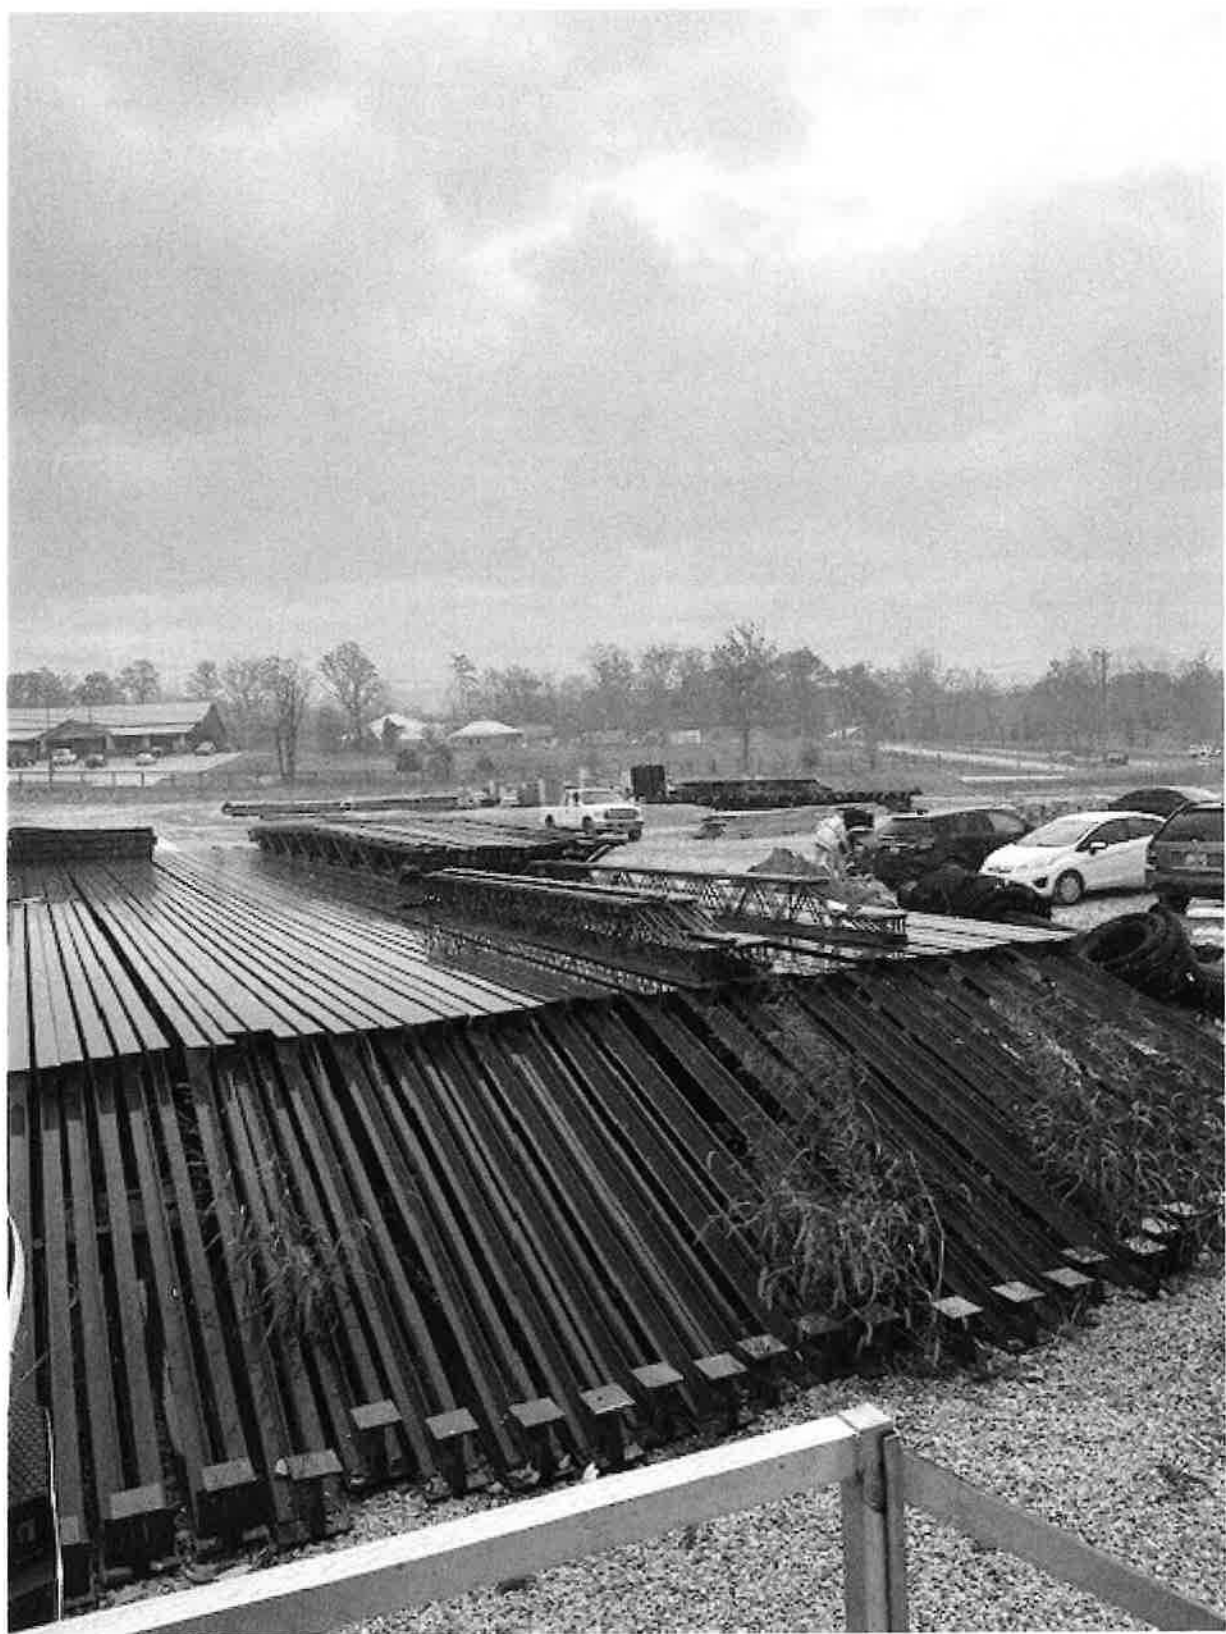



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

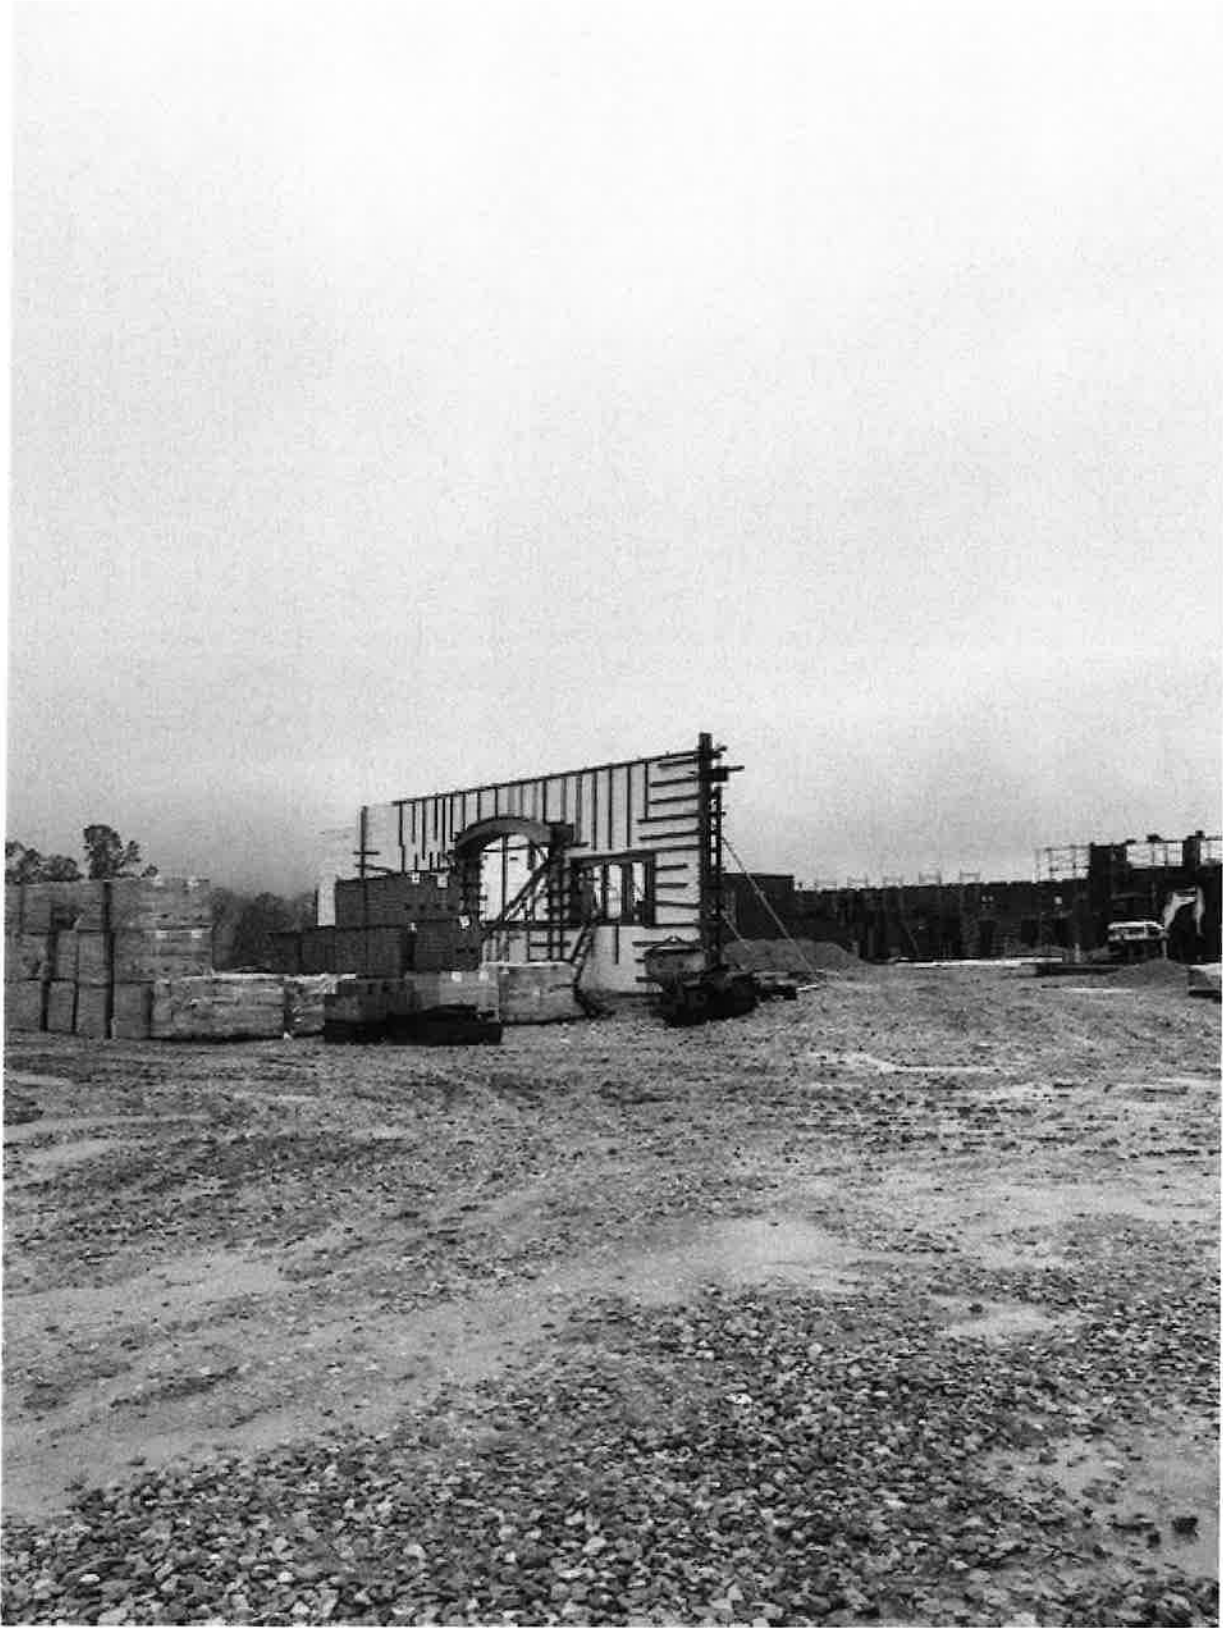



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00
hours

52° F
rain

1
notes

2
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM


File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM

File
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM

File
Daily Report 2024...
Michael Graf





Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00

hours

54° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

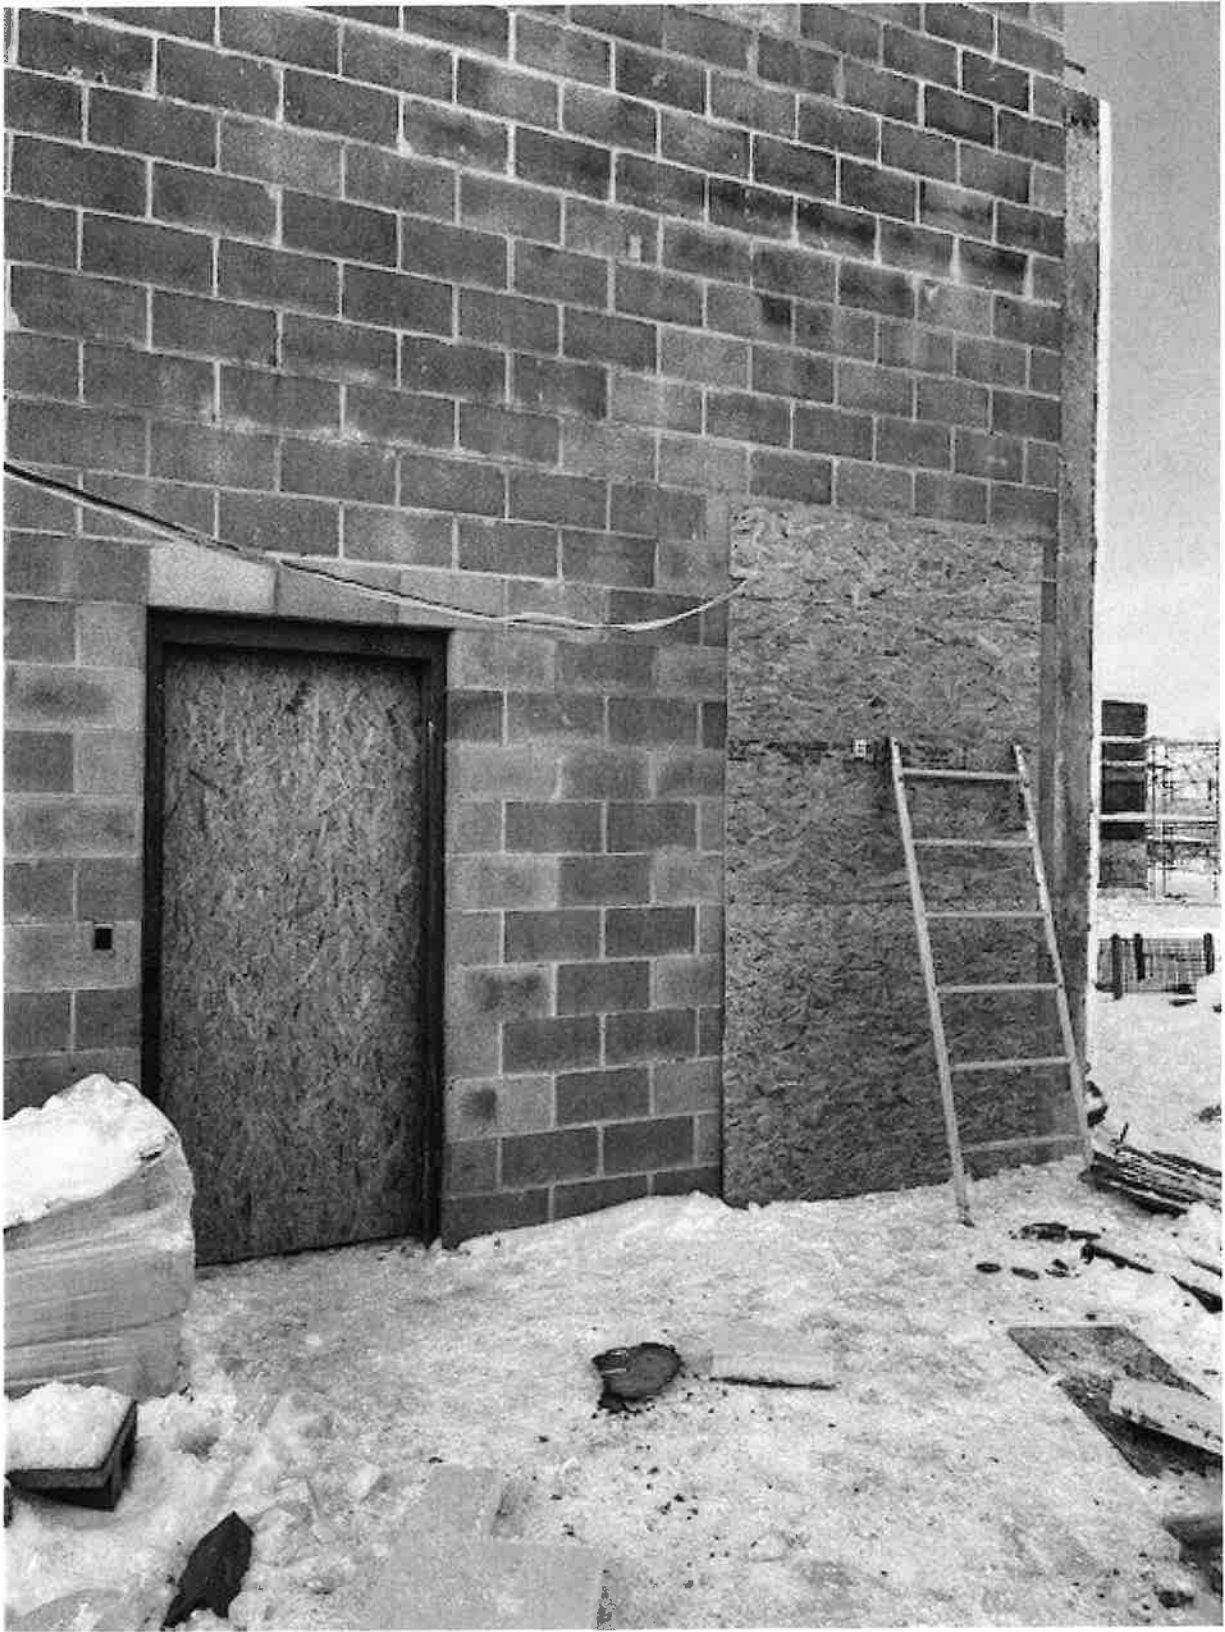



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
	Installing above ceiling hanger and ductwork in the North and West wings of (Area B).				
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area.		9.00	72.00 Hours	Approved
	(4) Hanging drywall the kitchen and cafeteria areas.				
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
	Grouting bearing walls. Approximately 7 cubic yards.				
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A)		9.00	72.00 Hours	Approved
	(2) Installing electrical rough-in's in metal stud partition walls in administration area.				
	(2) Pulling wire in the kitchen and cafeteria area				
	(2) Pulling wire and home runs in North wing of (Area B)				
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installed curb inlet 4D.				
	Inspecting steel decking in west wing of (Area B)		1.00	3.00 Hours	Approved
	Testing grout samples.				


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

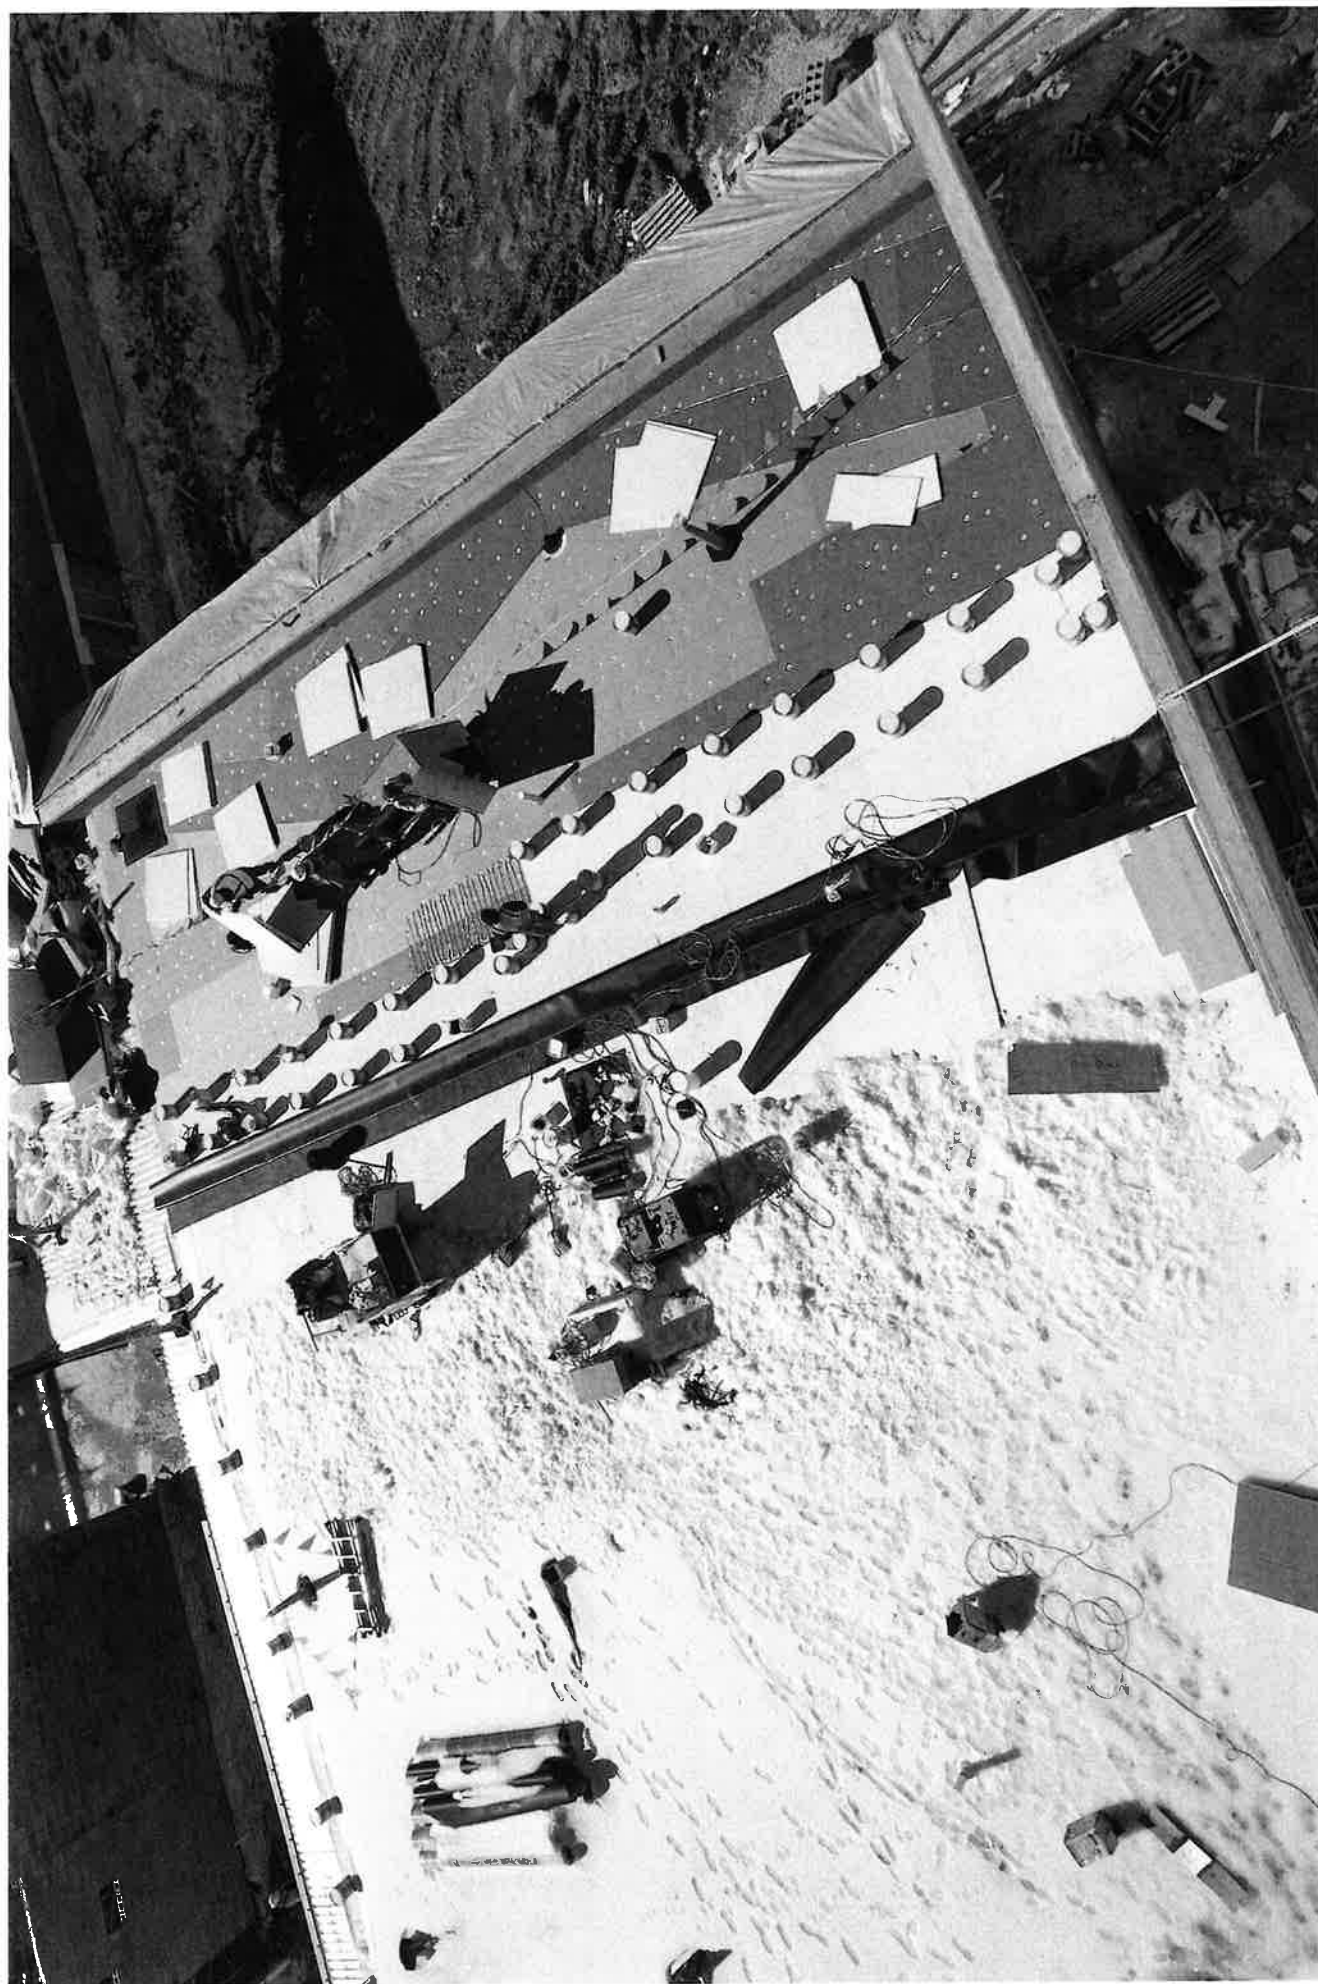



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM

 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf
 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf
 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	 File 1/23/2025 2:44 PM Michael Graf	

Michael Graf on 1/23/2025 03:17 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM


File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM


Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM

File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES


Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00

hours

63° F

thunderstorm

2

notes

6

equipment

● Approved

status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report
With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✔ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✔ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✔ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✔ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✔ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✔ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✔ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✔ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✔ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✔ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✔ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✔ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✔ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✔ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✔ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✔ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✔ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✔ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✔ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✔ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✔ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✔ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✔ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✔ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✔ Install Geothermal Well Field (verticals/horizontal/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placément 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62494)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School
BG Number: 21-072 District: Powell County (HB678) (495)
Status: Active Phase: Project Initiation (View Checklist)

Contract: Rimar Electric LLC, 0019, Electric
Type: CM Bid Package Proposed

Change Order Number 19-05
Time Extension Required Yes
If Yes Number Of Days 93
Date Of Change Order 6/9/2025
Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-
Change In A/E Fee This Change Order
+/-
Change In CM Fee This Change Order
+/-
Remaining Construction Contingency
Balance
Contract Change Requested By Construction Manager
Contract Change Reason Code Time Extension
Change Order Description And Justification
1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No Cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62494)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 19-05
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 RIMAR ELECTRIC, LLC

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE # 19 ELECTRIC

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	1,688,259.62
Net change by previously authorized Change Orders	-10,217.00
The Contract Sum prior to this Change Order was	1,678,042.62
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	1,678,042.62

The Contract Time will be adjusted by 93 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

RIMAR ELECTRIC, LLC

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)

OWNER (Firm Name)

691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24		2	3	4																
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24		3	4	5																
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24		4	5	6																
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24		5	6	7																
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24		6	7	8																
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24		7	8	9	10															
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24		8	9	10	11															
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24		9	10	11	12															
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24		10	11	12	13															
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24		11	12	13	14															
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24		12	13	14	15	16														
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24		13	14	15	16	17														
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24		14	15	16	17	18														
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24		15	16	17	18	19														
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24		16	17	18	19	20														
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24		17	18	19	20	21														
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24		18	19	20	21	22														
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24		19	20	21	22	23														
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24		20	21	22	23	24	25	26	27	28	29	30								
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24		21	22	23	24	25														
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24		22	23	24	25	26														
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24		23	24	25	26	27														
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24		24	25	26	27	28														
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24		25	26	27	28	29	30													
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24		26	27	28	29	30														
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24		27	28	29	30	31														
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24		28	29	30	31	32														
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24		29	30	31	32	33														
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24		30	31	32	33	34														
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24		31	32	33	34	35														
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25		32	33	34	35	36														
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25		33	34	35	36	37														
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25		34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

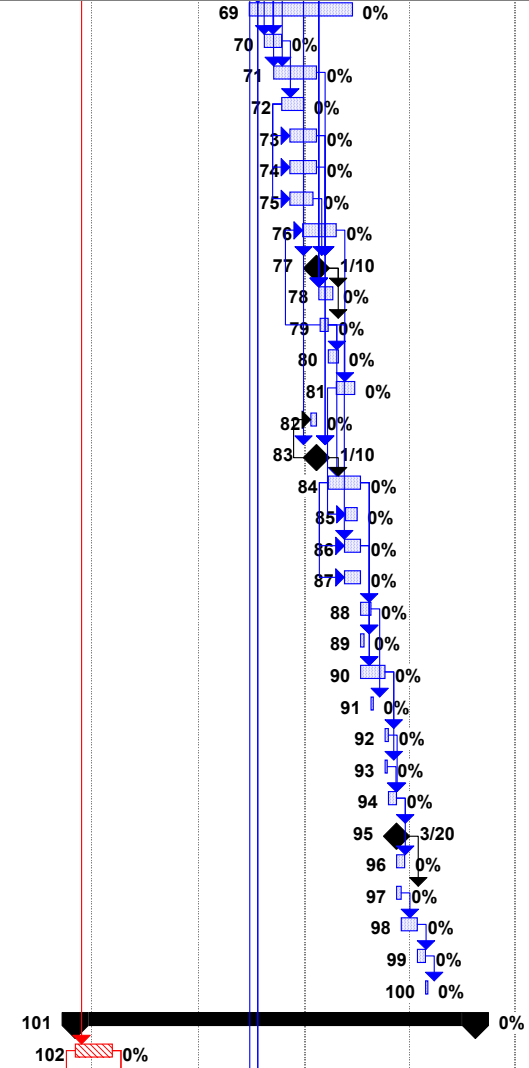

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																						
104	Underslab Plumbing Rough in - Area B	20 days	Tue 7/9/24	Mon 8/5/24																						
105	Underslab CMU - Area B	5 days	Fri 7/5/24	Thu 7/11/24																						
106	Stone Backfill non plumbing areas - Area B	2 days	Wed 7/24/24	Thu 7/25/24																						
107	Underslab Electrical Rough in - Area B	12 days	Fri 7/26/24	Mon 8/12/24																						
108	Stone Backfill at pumbing areas - Area B	2 days	Fri 8/2/24	Mon 8/5/24																						
109	Slab Prep 1st Floor - Area B	3 days	Tue 8/13/24	Thu 8/15/24																						
110	Slab Placement 1st Floor - Area B	1 day	Fri 8/16/24	Fri 8/16/24																						
111	Hollow Metal Doorframes installation 1st Floor - Area B	3 days	Wed 8/21/24	Fri 8/23/24																						
112	CMU Bearing Walls - Area B	30 days	Mon 8/26/24	Mon 10/7/24																						
113	ICF Walls - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
114	Plumbing Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
115	Electrical Wall Rough in - Area B	20 days	Mon 8/26/24	Mon 9/23/24																						
116	Steel Columns/Beams/Bent Plate - Area B	12 days	Tue 9/10/24	Wed 9/25/24																						
117	CMU Non Bearing Walls/Rub all walls - Area B	10 days	Tue 10/8/24	Mon 10/21/24																						
118	Set Steel Joists - Area B	15 days	Tue 10/8/24	Mon 10/28/24																						
119	Exterior Brick/Stone - Area B	25 days	Thu 10/17/24	Wed 11/20/24																						
120	Roof Deck installation/inspection - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
121	ICF Parapet Walls - Area B	7 days	Tue 10/29/24	Wed 11/6/24																						
122	Roof Wood Blocking - Area B	7 days	Thu 11/7/24	Fri 11/15/24																						
123	Windows/Glazing/Caulking - Area B	12 days	Thu 11/14/24	Mon 12/2/24																						
124	Duct installation - Above Ceiling - Area B	35 days	Thu 11/7/24	Fri 12/27/24																						
125	TPO Roof - Area B	15 days	Mon 11/18/24	Mon 12/9/24																						
126	Clean Brick - Area B	5 days	Thu 11/21/24	Wed 11/27/24																						
127	Brick Caulking - Area B	3 days	Thu 11/21/24	Mon 11/25/24																						
128	Electrical Rough-In - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
129	Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	Thu 11/14/24	Mon 1/13/25																						
130	Block Filler - Area B	10 days	Mon 11/25/24	Mon 12/9/24																						
131	Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	Tue 12/3/24	Wed 1/8/25																						
132	Install Clearstory Windows - Area B	5 days	Tue 12/3/24	Mon 12/9/24																						
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	Fri 11/29/24	Fri 12/27/24																						
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	Tue 12/10/24	Wed 1/8/25																						
135	Set Mechanical Equipment/Tie In - Area B	25 days	Tue 12/10/24	Wed 1/15/25																						
136	Metal Coping, Trim etc... - Area B	15 days	Tue 12/10/24	Tue 12/31/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							</

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

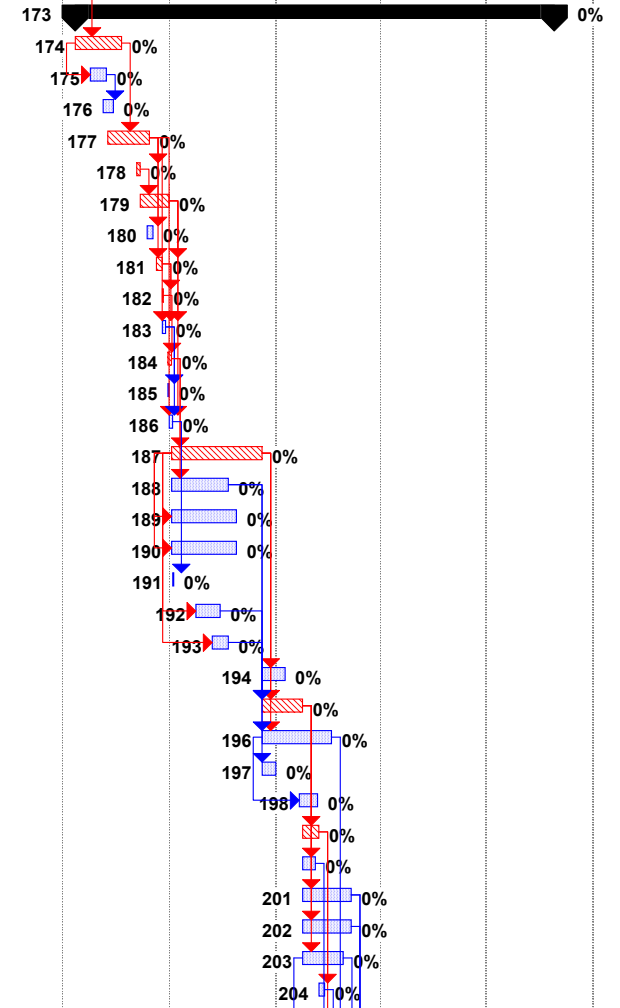

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																						
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																						
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																						
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																						
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																						
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																						
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																						
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																						
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																						
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																						
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																						
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																						
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																						
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																						
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																						
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																						
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																						
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																						
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																						
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																						
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																						
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																						
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																						
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																						
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																						
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																						
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																						
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																						
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																						
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																						
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																						
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																						
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf

Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

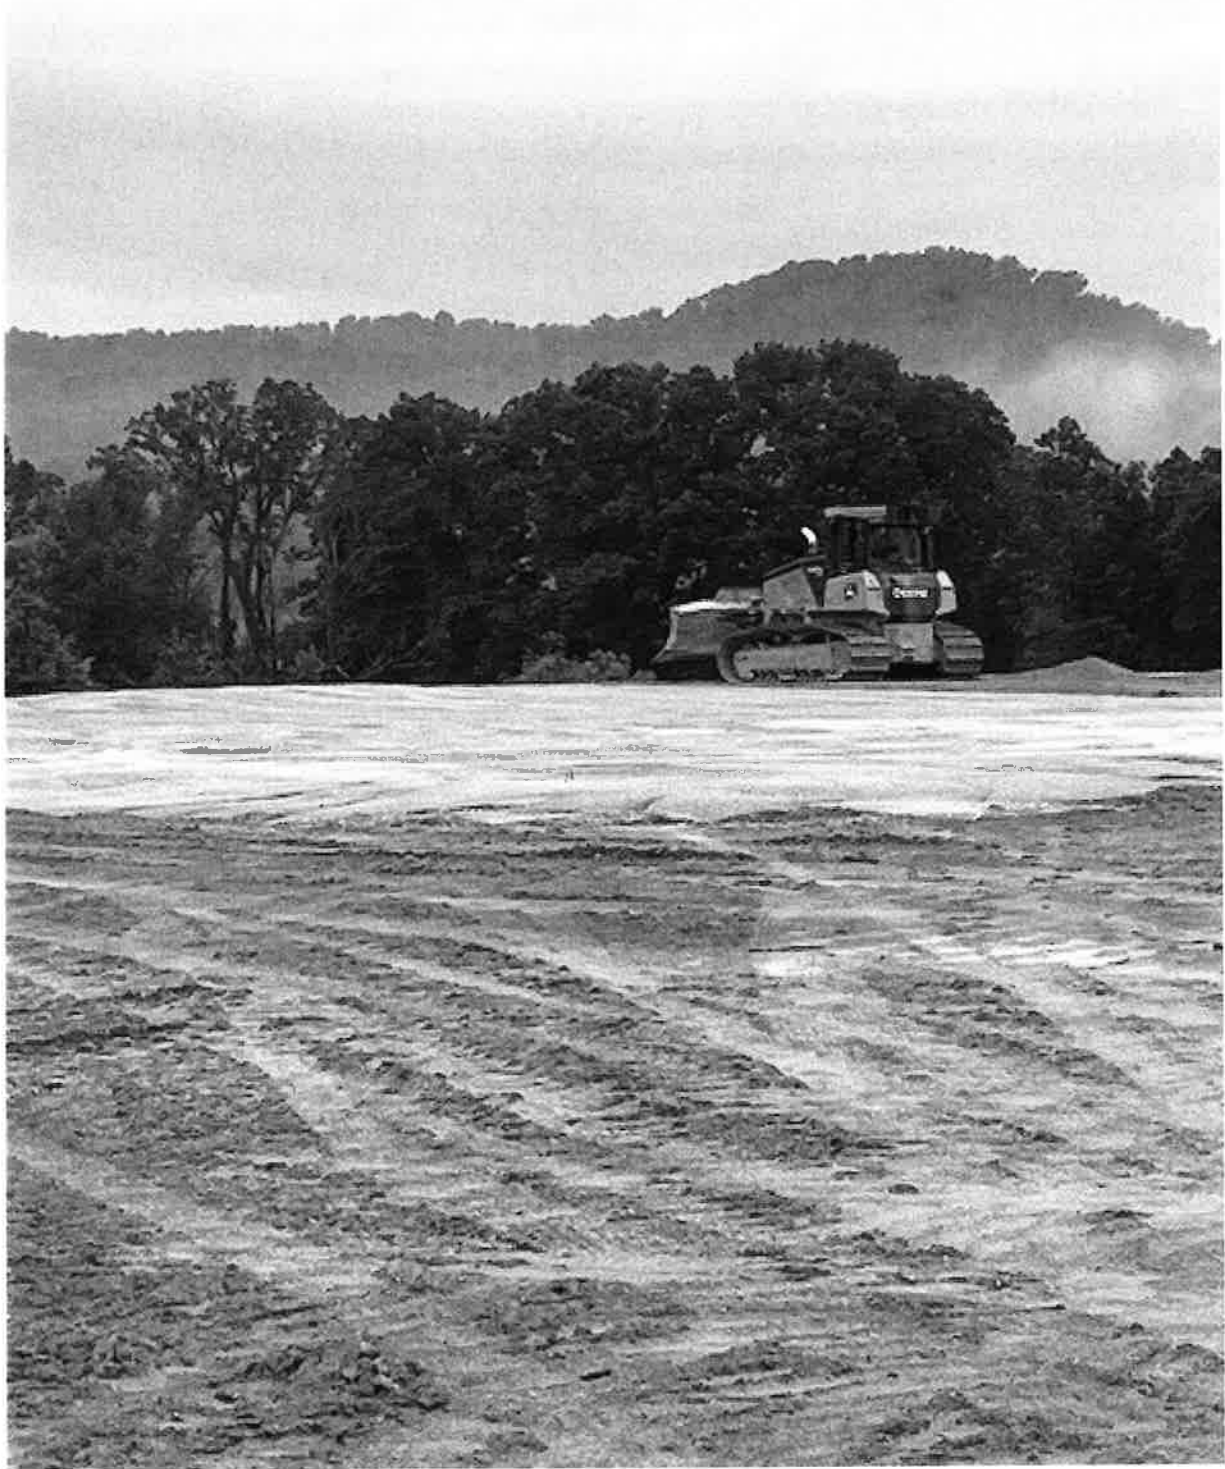



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

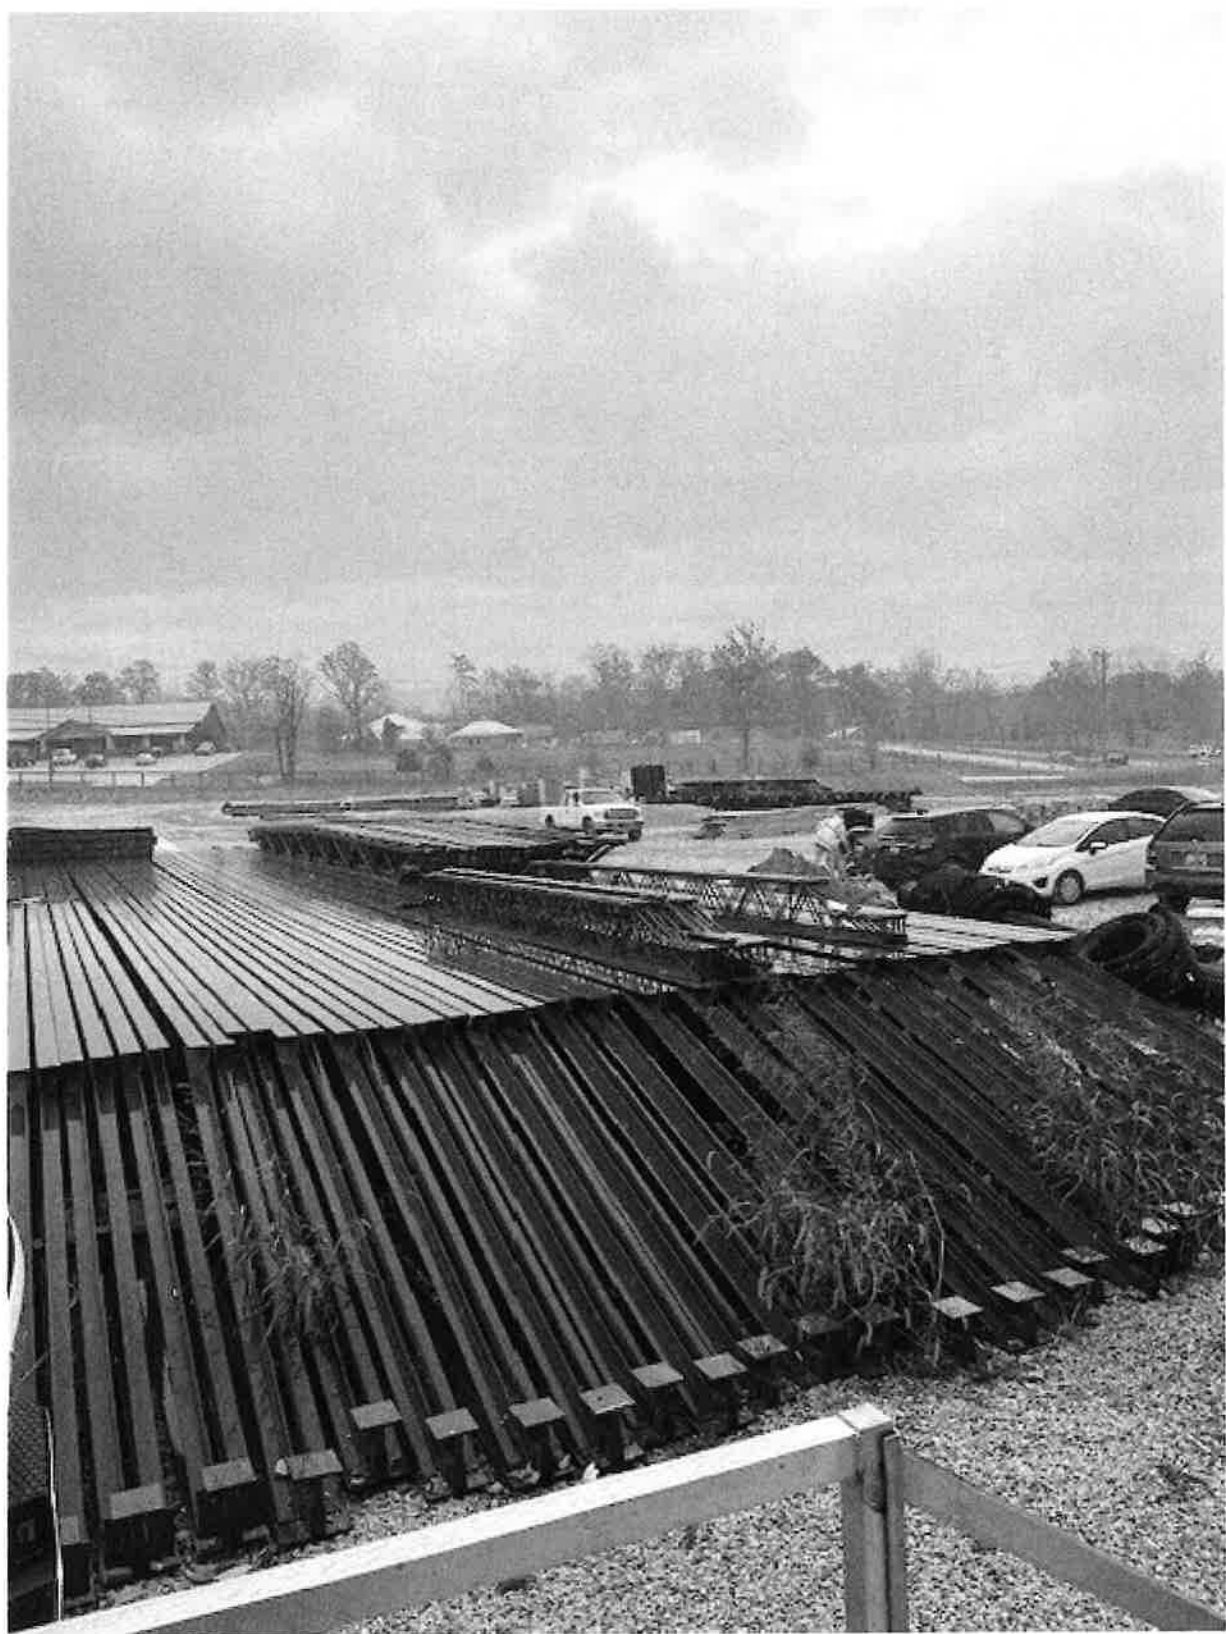



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

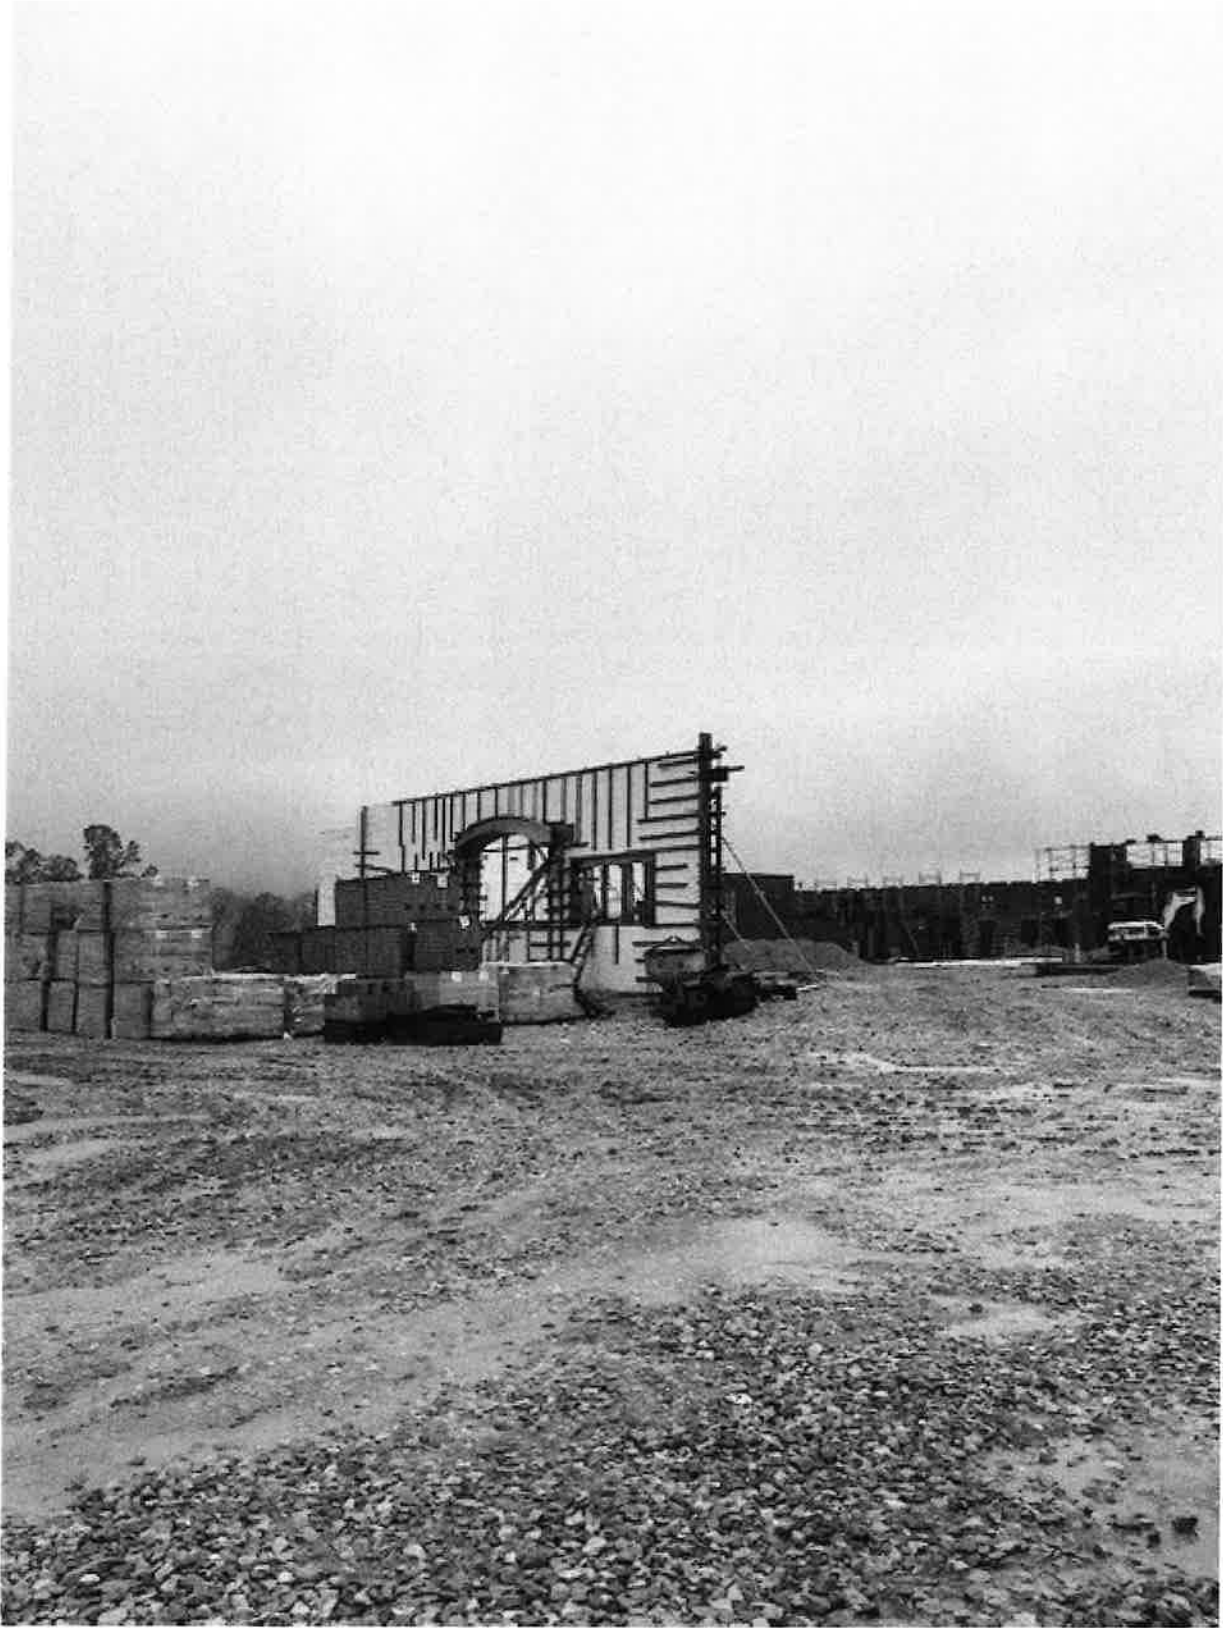



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf



File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf



File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM

File
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael GrafFile
11/21/2024 1:46 PM
Michael Graf

Michael Graf on 11/21/2024 03:16 PM

File
Daily Report 2024...
Michael Graf





Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM

File
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael GrafFile
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM

File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM

File
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael GrafFile
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM

File
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael GrafFile
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM


Lost Production Day due to weather.


Michael Graf on 1/9/2025 03:25 PM

Hardy Gas delivered 800 gallons of propane.

Michael Graf on 1/9/2025 03:25 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**

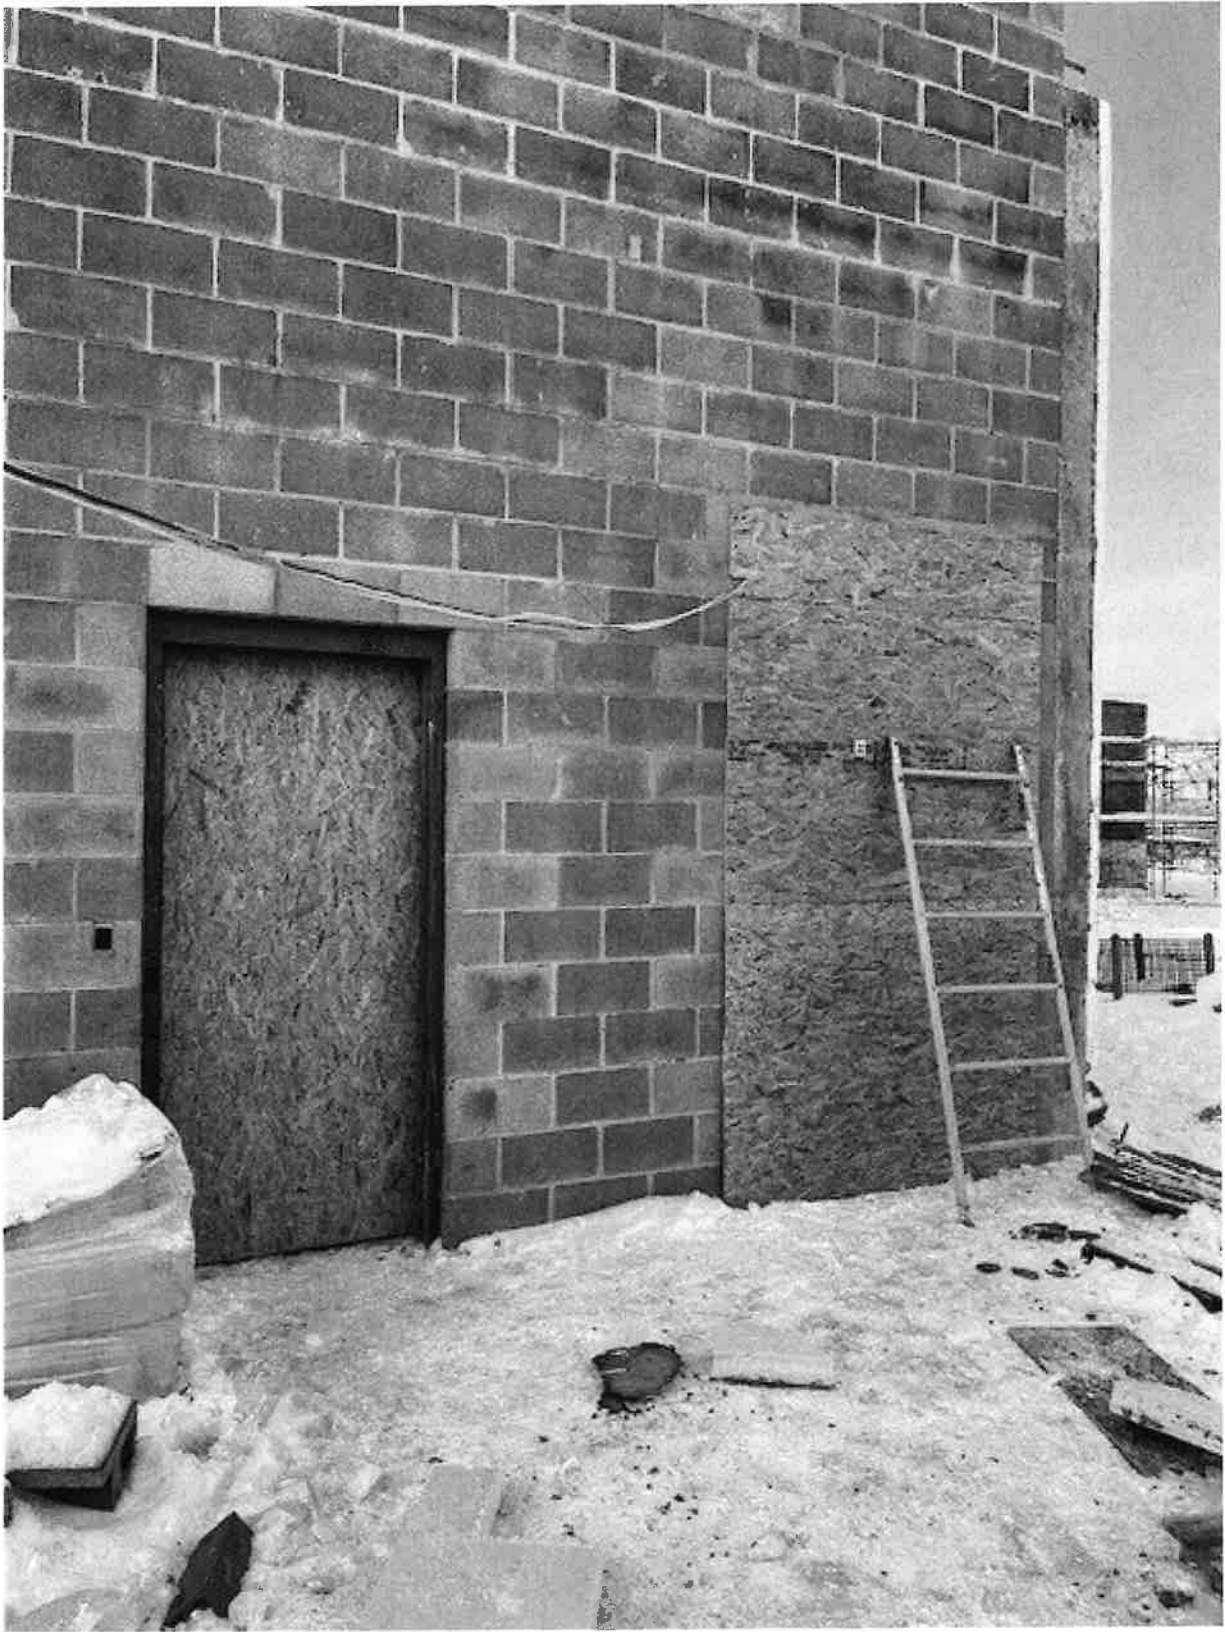



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf



File
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED

NOTES

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf



File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

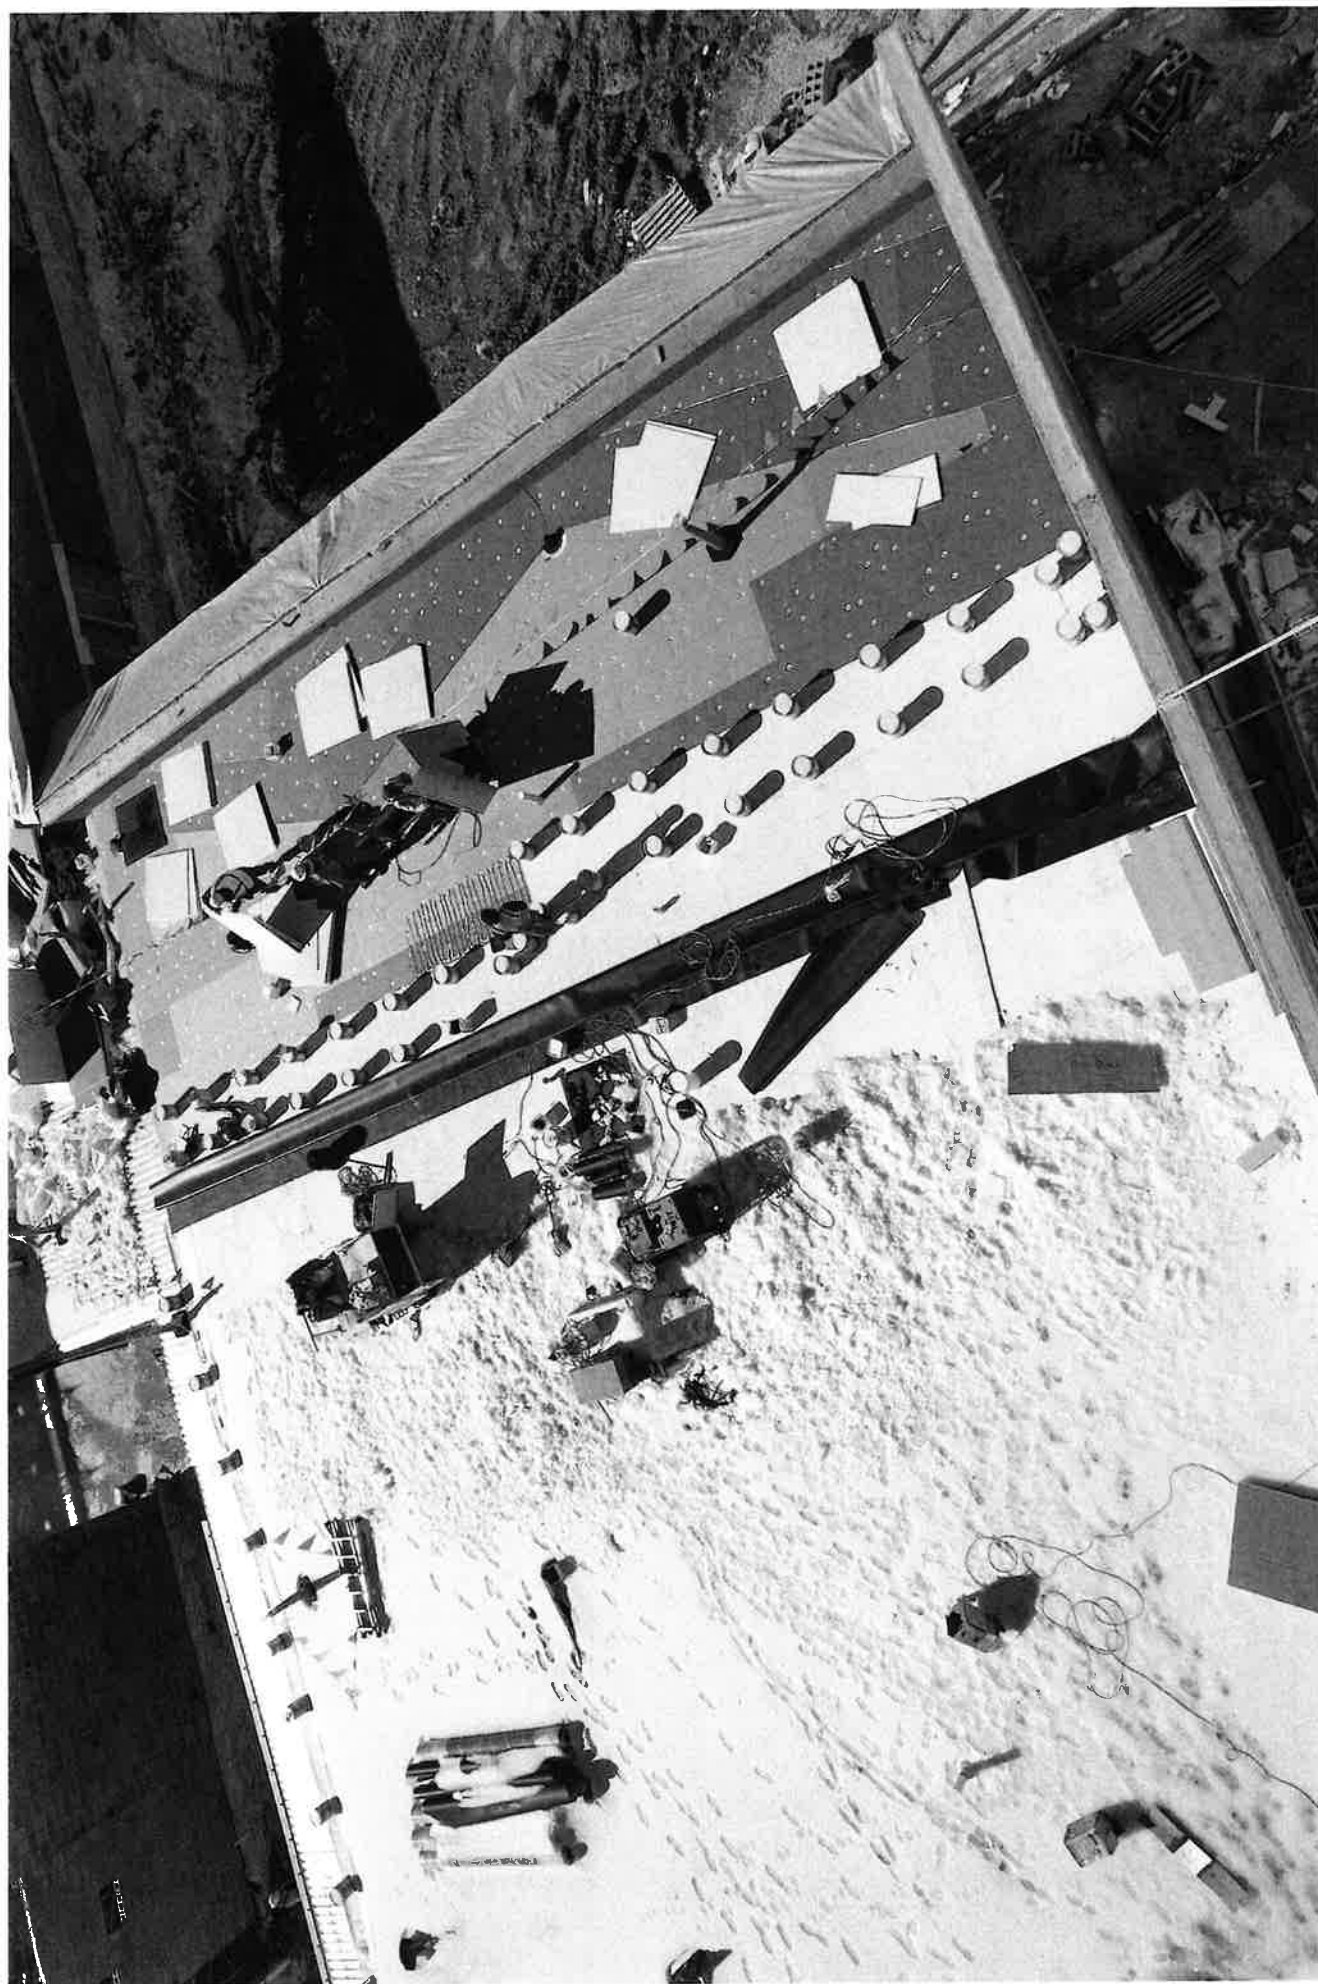



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RIISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM



File


Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.


Michael Graf on 2/18/2025 03:33 PM



File

Daily Report 2025...

Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES


Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00
hours

18° F
cloudy

1
notes

3
equipment

● Pending
status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontals/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order

Supplemental Information Form (Ref#

62488)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

Status: Active

District: Powell County (HB678) (495)

Phase: Project Initiation (View Checklist)

Contract: Facility Commissioning Group, Inc., 0020, Commissioning

Type: CM Bid Package

Proposed

Change Order Number

20-01

Time Extension Required

Yes

If Yes Number Of Days

93

Date Of Change Order

6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency Balance

Contract Change Requested By Construction Manager

Contract Change Reason Code Time Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. FInal Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported No by an alternate bid or competitive price quote Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62488)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
CONSTRUCTION MANAGER ☐
ARCHITECT ☐
CONTRACTOR ☐
FIELD ☐
OTHER ☐

PROJECT (Name and Address)
STANTON ELEMENTARY SCHOOL
WEST COLLEGE AVENUE
STANTON, KY 40380

CHANGE ORDER NUMBER: 20-01
INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
FACILITY COMMISSIONING GROUP

PROJECT NUMBERS: 000743
CONTRACT DATE: 3/4/2024
CONTRACT FOR: BID PACKAGE #20 COMMISSIONING

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
 2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
- Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	53,350.00
Net change by previously authorized Change Orders	0.00
The Contract Sum prior to this Change Order was	53,350.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	53,350.00

The Contract Time will be adjusted by 93 days.
The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

FACILITY COMMISSIONING GROUP

CONTRACTOR (Firm Name)

ADDRESS

BY (Signature)

(Typed Name)

DATE:

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

ARCHITECT (Firm Name)
144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

BY (Signature)

(Typed Name)

DATE:

POWELL COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

BY (Signature)

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24	2	3	4																	
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24	3	4																		
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24	4																			
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24	5																			
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24	6																			
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24	7	8	9	10	11	12														
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24	8	9	10	11	12															
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24	9	10																		
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24	10	11																		
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24	11	12																		
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24	13	14																		
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24	14	15																		
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24	15	16																		
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24	16	17																		
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24	17	18																		
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24	18	19	20	21	22	23	24	25	26	27	28	29	30	31						
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24	19	20																		
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24	20	21	22	23	24	25	26	27	28	29	30	31								
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24	21	22																		
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24	22	23	24	25	26	27	28	29	30	31										
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24	23	24																		
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24	24	25	26	27	28	29	30	31												
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24	25	26	27	28	29	30	31													
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24	26	27	28	29	30	31														
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24	27	28	29	30	31															
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24	28	29	30	31																
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24	29	30	31																	
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24	30	31																		
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24	31	32																		
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25	32	33																		
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25	33																			
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

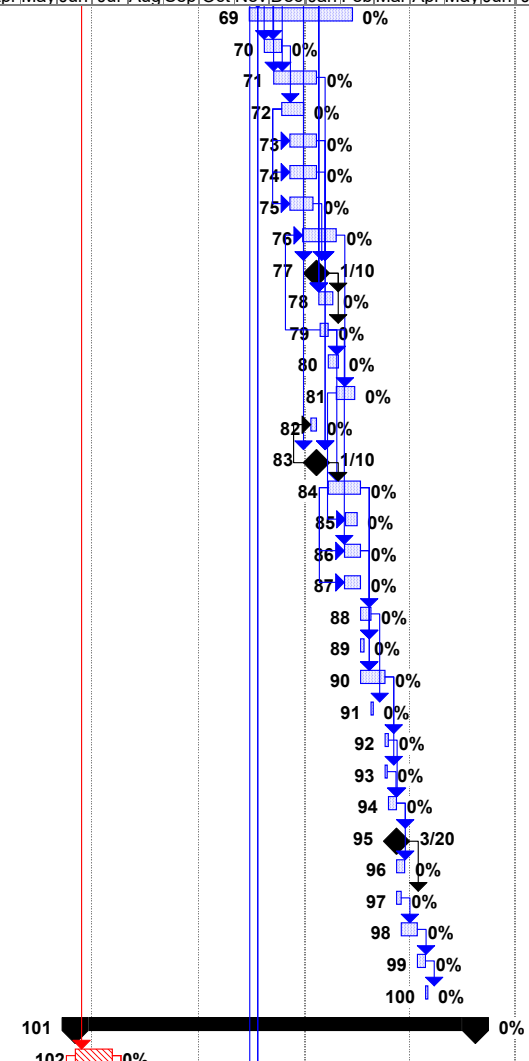

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	</

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																						
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																						
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

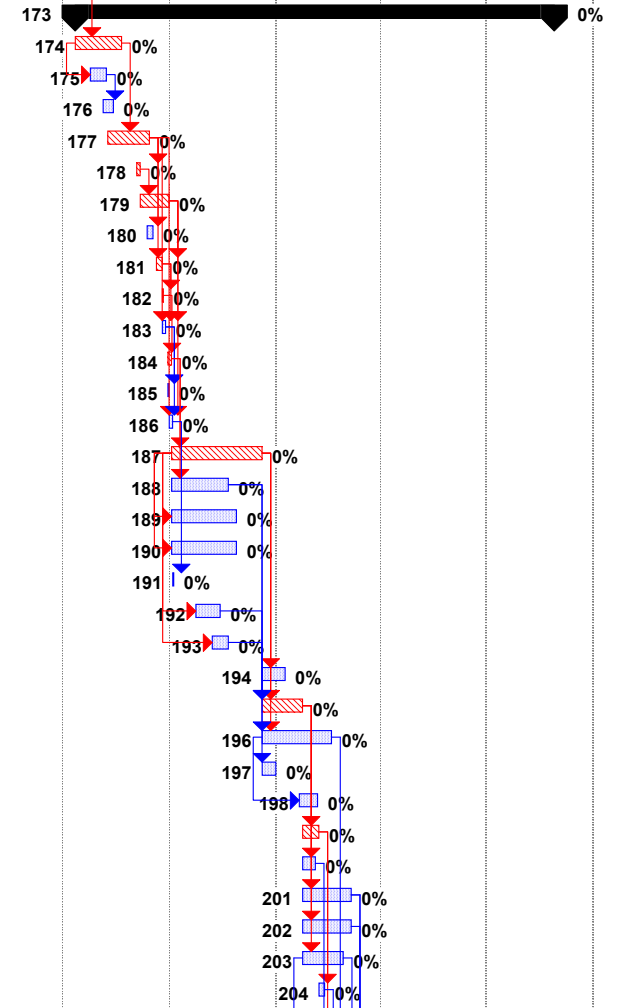

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct		
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																								
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																								
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																								
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																								
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																								
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																								
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																								
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																								
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																								
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																								
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																								
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																								
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																								
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																								
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																								
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																								
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																								
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																								
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																								
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																								
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																								
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																								
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																								
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																								
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																								
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																								
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																								
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																								
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																								
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																								
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																								
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																								
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf

Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/15/2024

20.00
hours

67° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

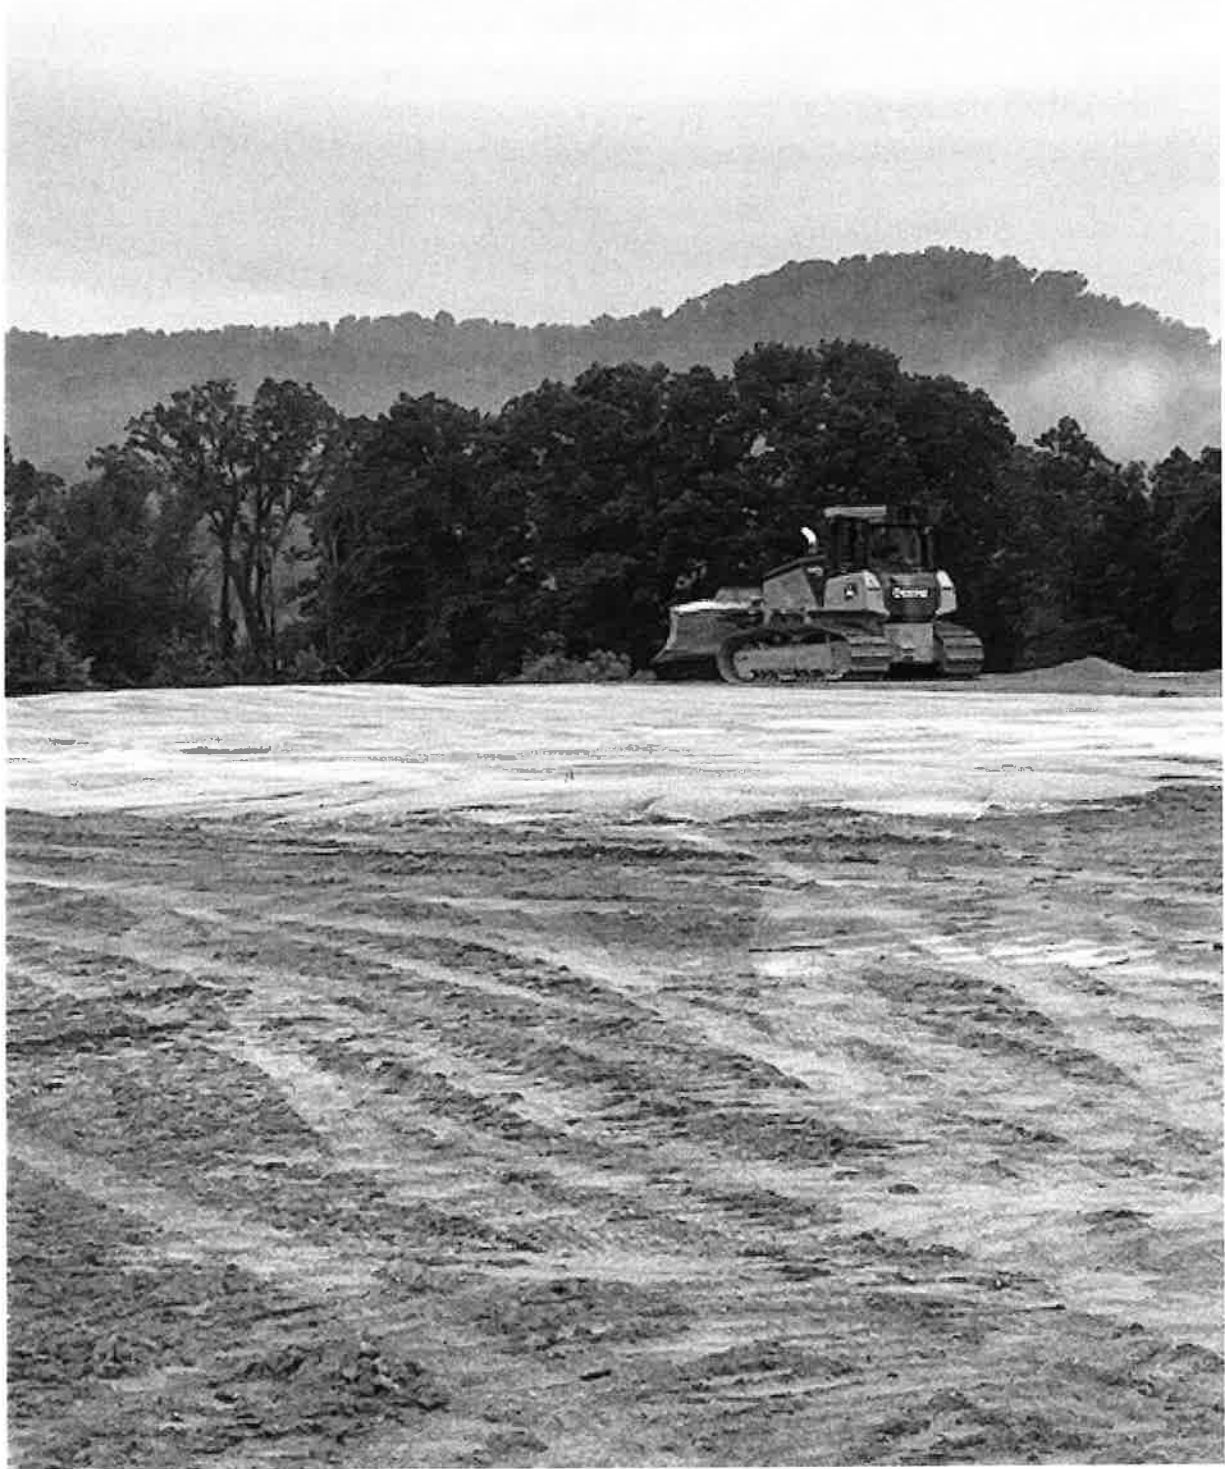



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material

Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

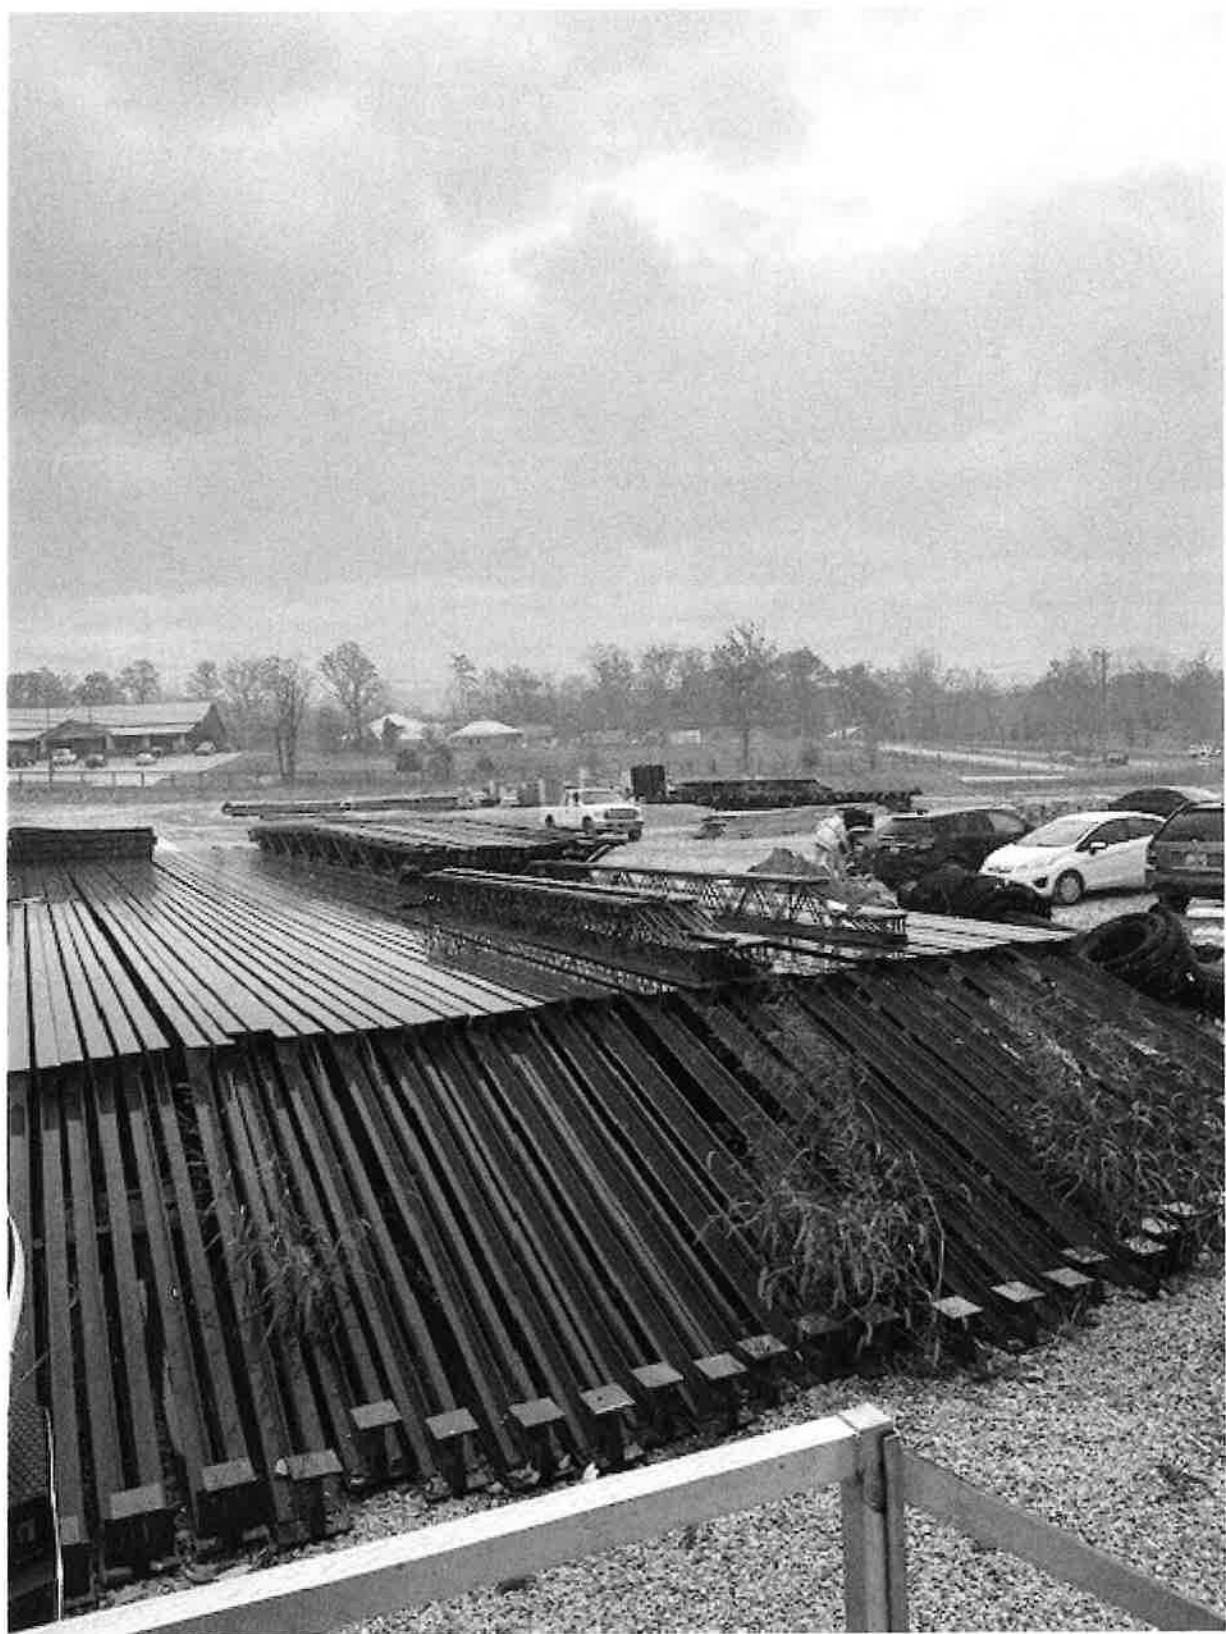



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

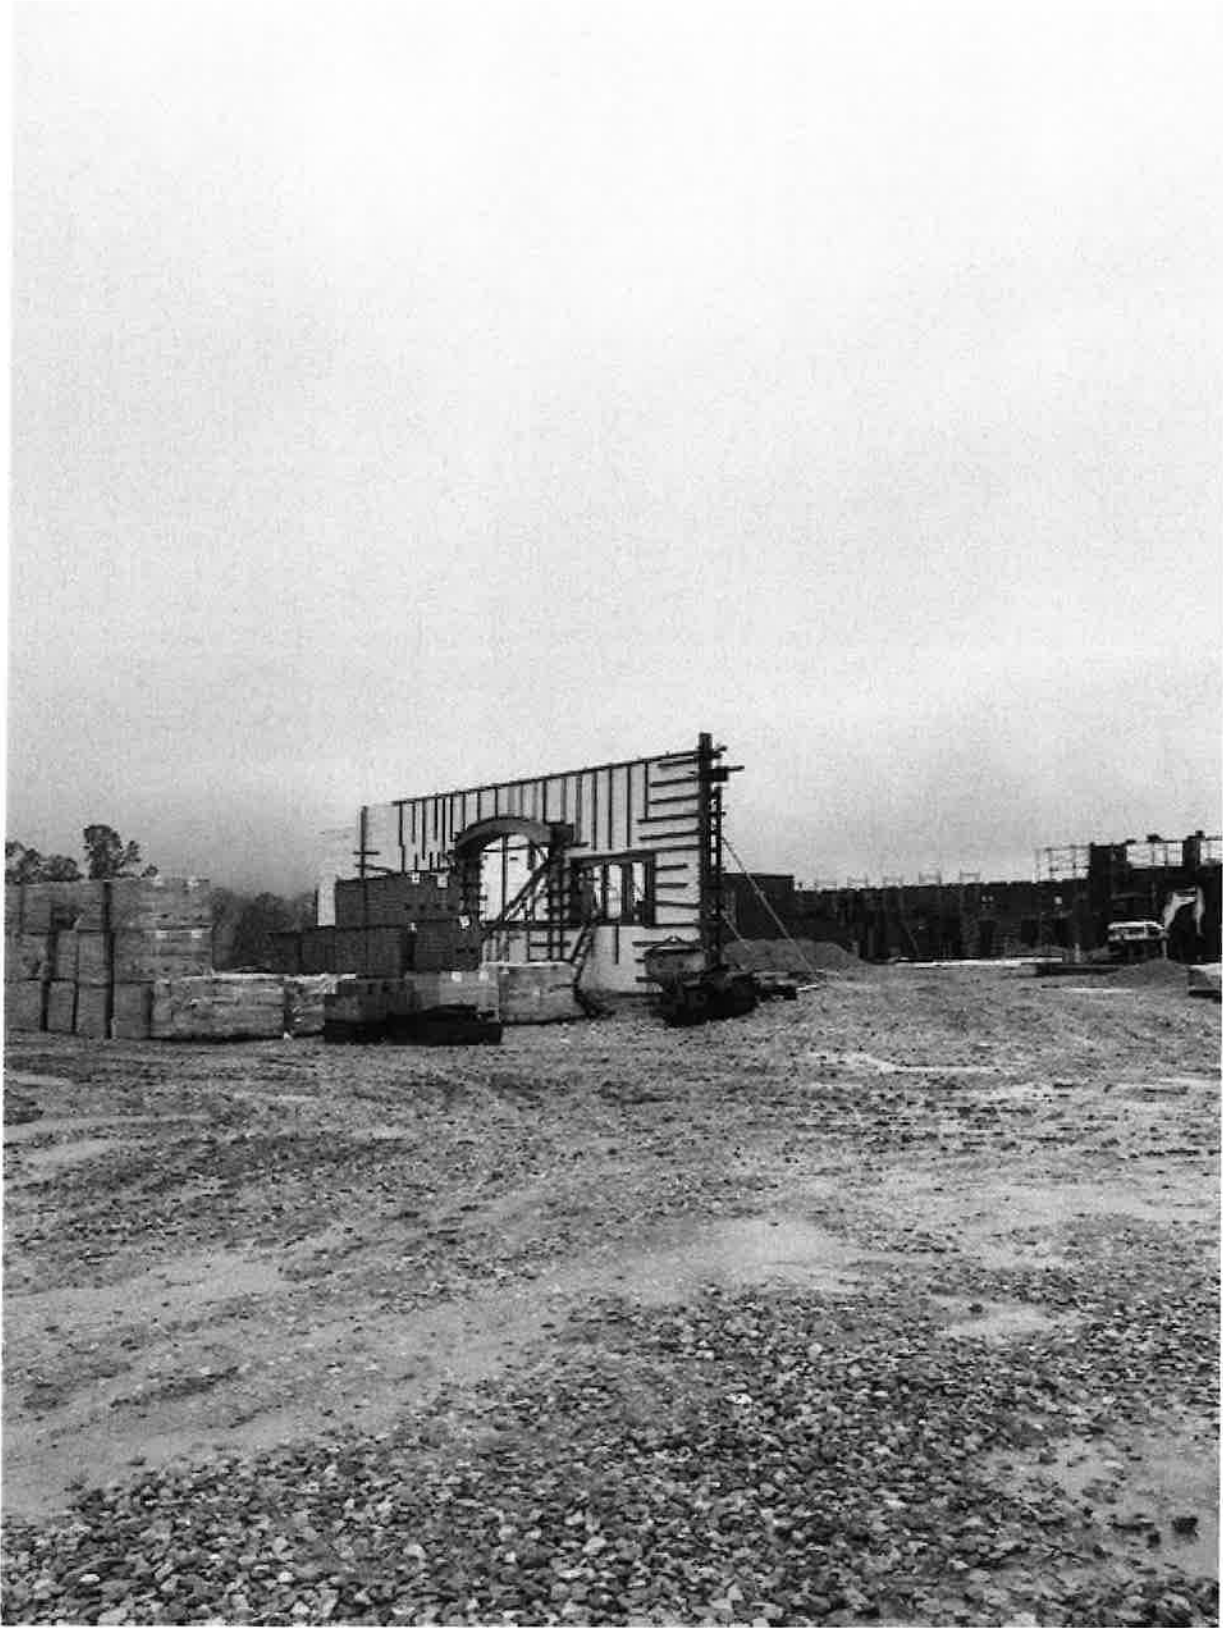



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM


File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report

With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00

hours

26° F

clear

1

notes

0

equipment

● Approved

status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00
hours

60° F
cloudy

1
notes

6
equipment

● Approved
status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days














Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00






MATERIAL DELIVERED

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 11:00 AM
Michael Graf

File
1/8/2025 1:48 PM
Michael Graf



File
Daily Report 2025
Michael Graf

Page 2 of 2





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

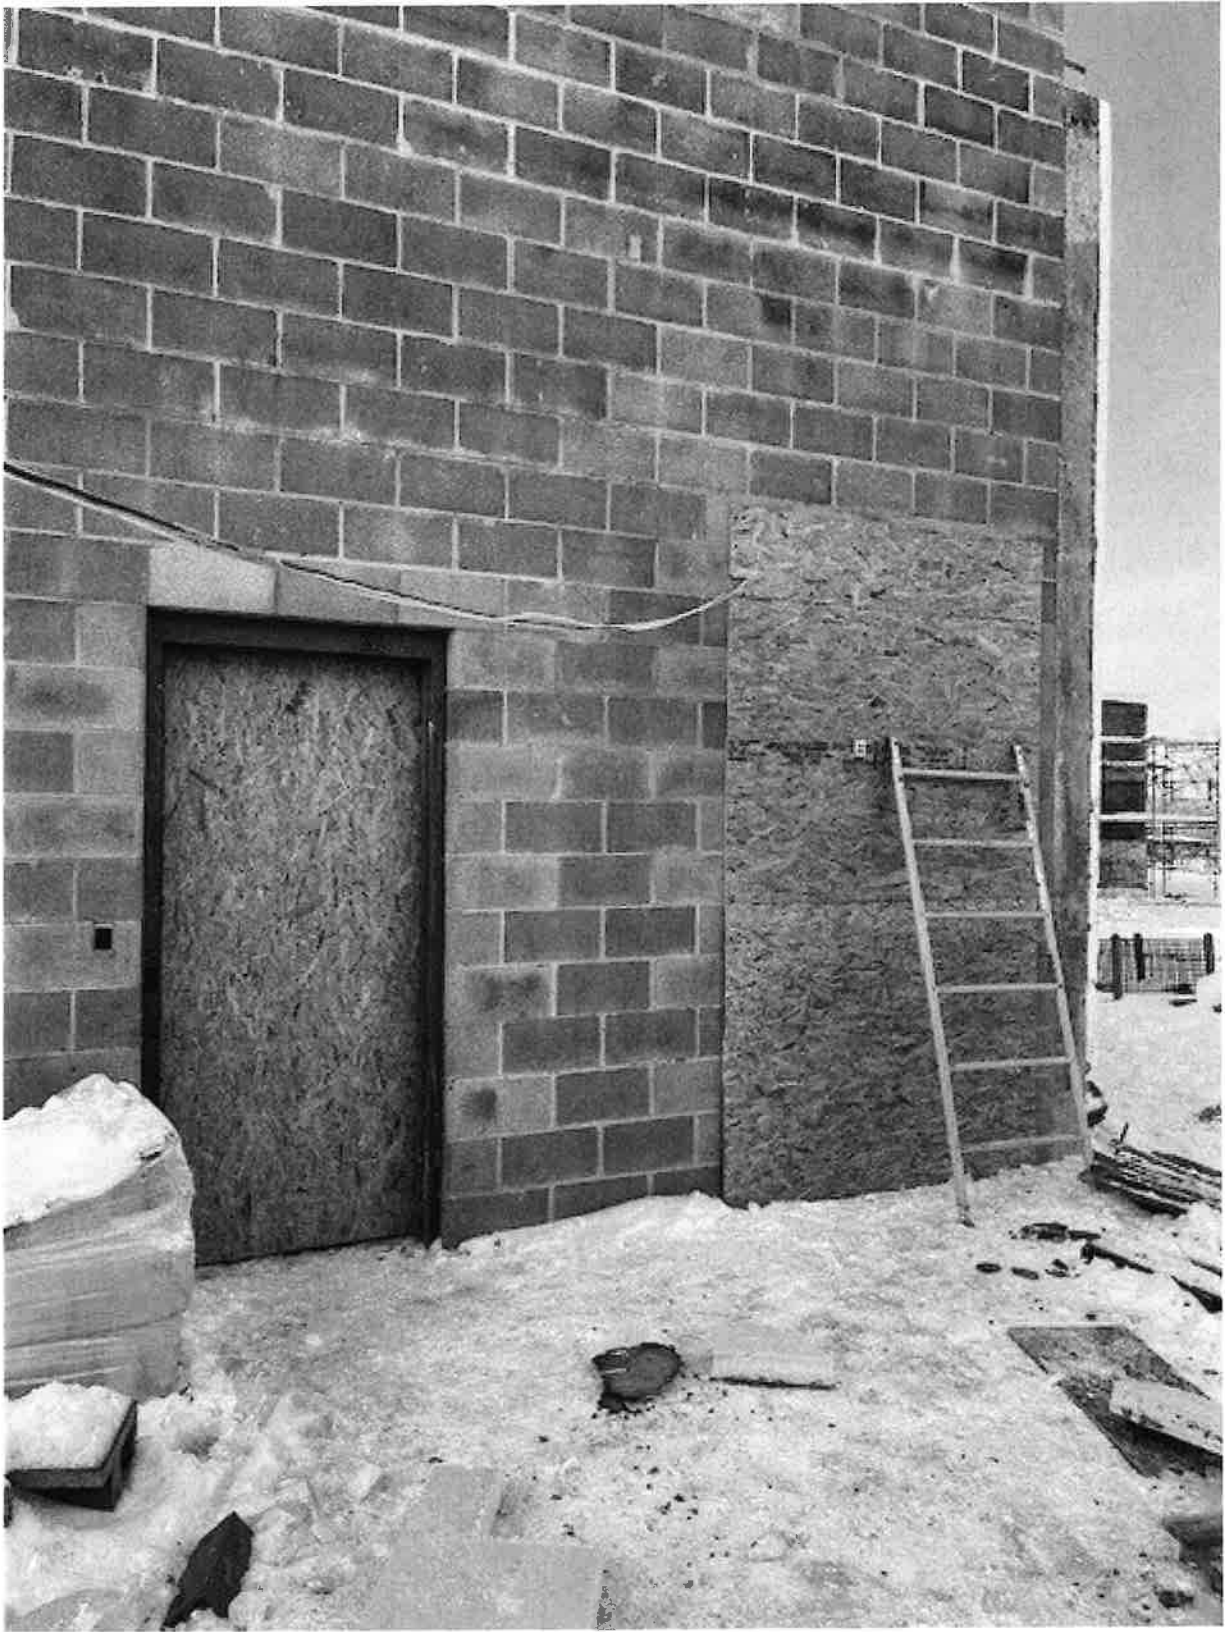



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

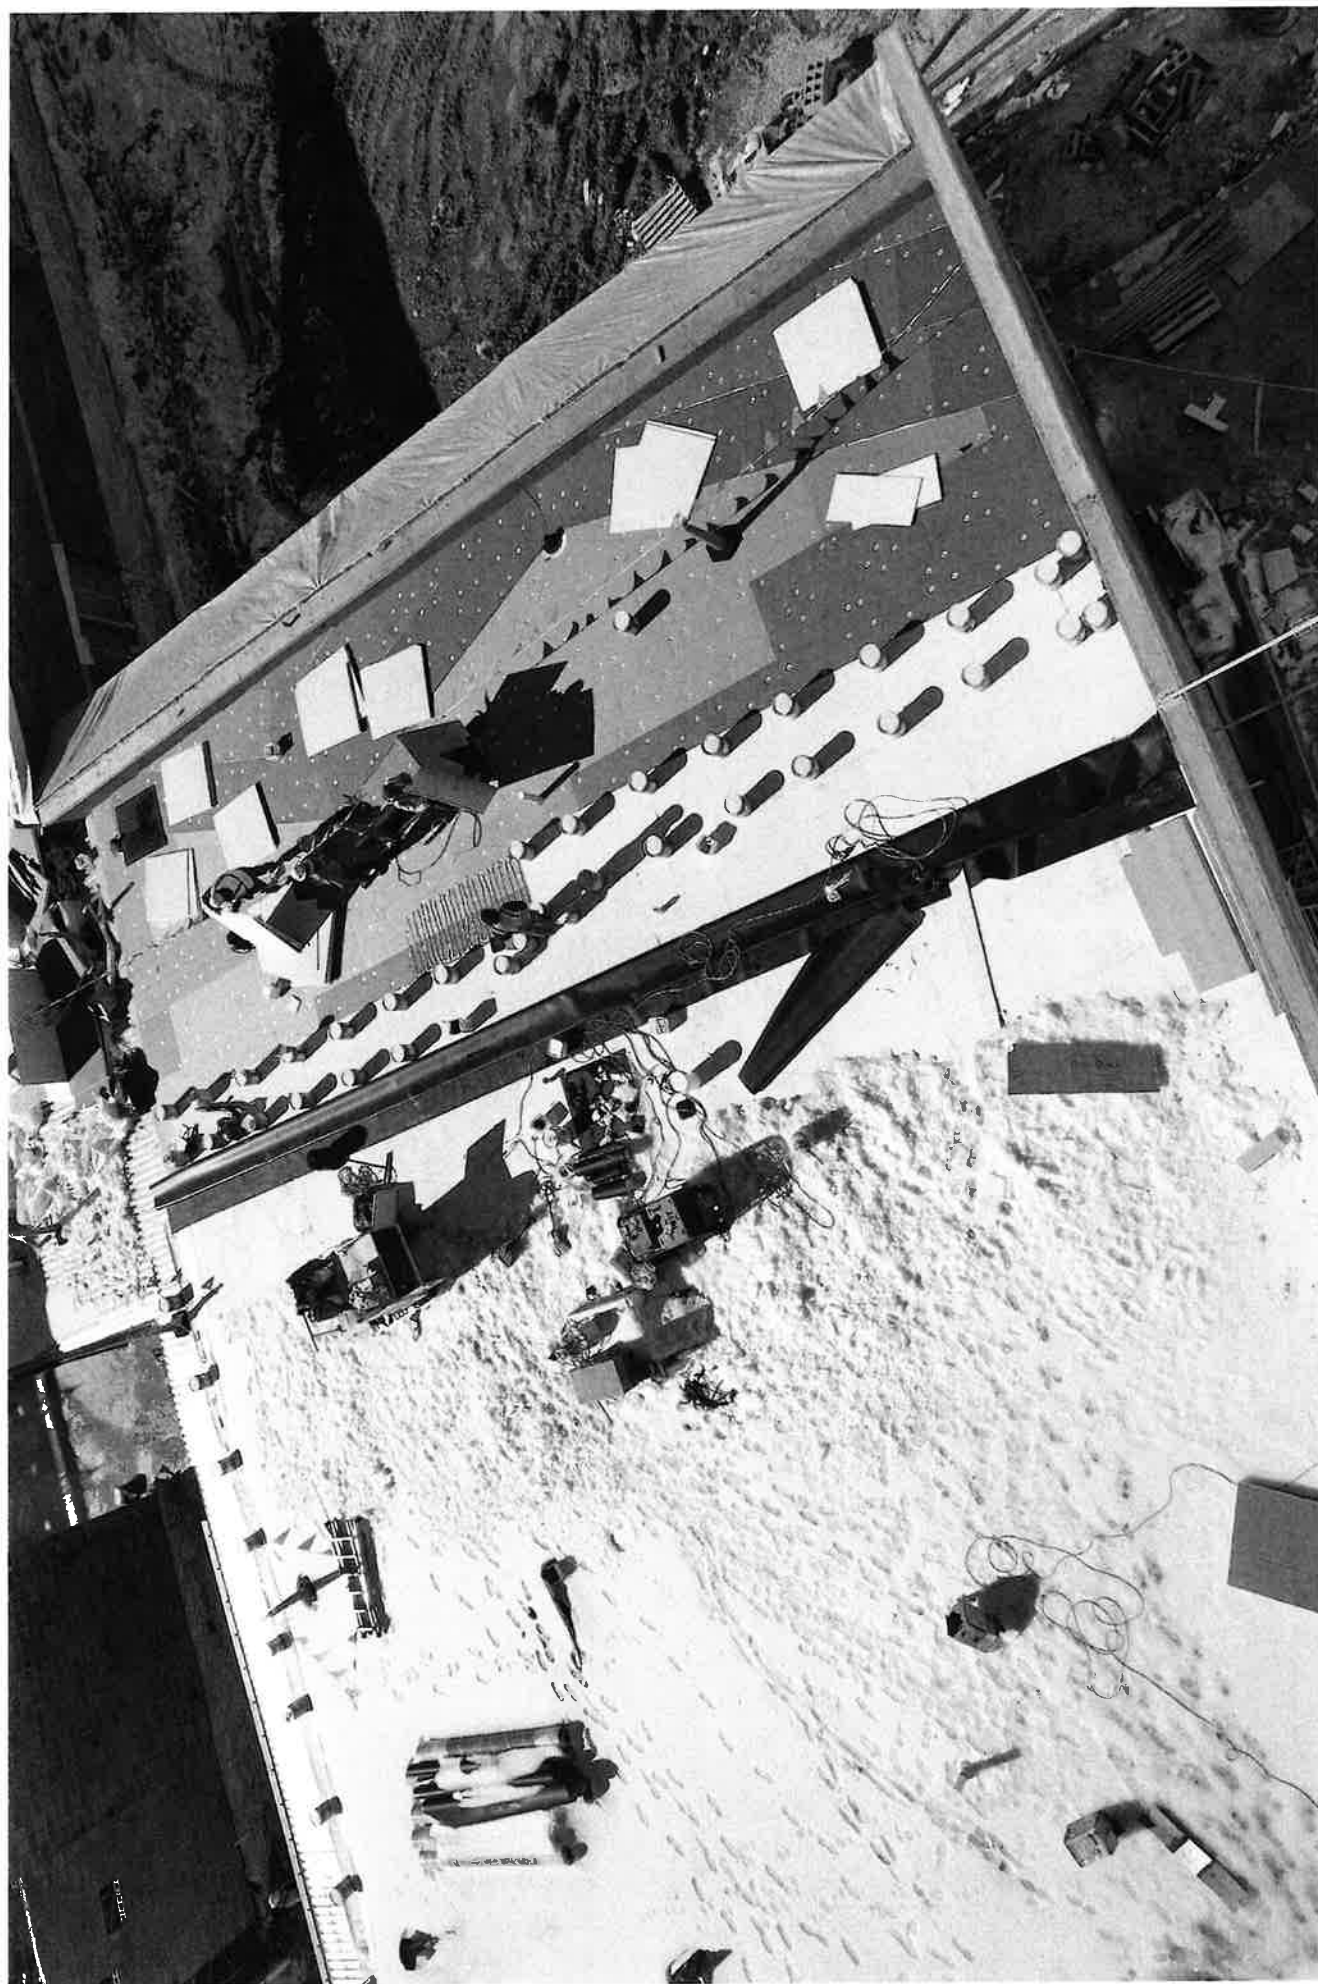



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf



File
1/23/2025 2:44 PM
Michael Graf

Michael Graf on 1/23/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM

File
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael GrafFile
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM


File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.


Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00
hours

18° F
cloudy

1
notes

3
equipment

● Pending
status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf



File
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM


Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✔ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✔ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✔ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✔ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✔ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✔ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✔ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✔ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✔ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✔ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✔ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✔ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✔ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✔ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✔ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✔ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✔ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✔ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✔ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✔ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✔ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✔ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✔ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✔ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✔ Install Geothermal Well Field (verticals/horizontals/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Slanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

11119930

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62483)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School
BG Number: 21-072 District: Powell County (HB678) (495)
Status: Active Phase: Project Initiation (View Checklist)

Contract: Rising Sun Developing Company, 0021, Combination Bid (BP#1 Site Work, BP#3
General Trades, BP#5 Steel, BP#9 Paint)
Type: CM Bid Package Proposed

Change Order Number 21-06
Time Extension Required No
Date Of Change Order 6/8/2025
Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may
require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount (\$2,850.00)
+/-
Change In A/E Fee This Change Order \$0.00
+/-
Change In CM Fee This Change Order \$0.00
+/-
Remaining Construction Contingency
Balance
Contract Change Requested By Local Board of Education
Contract Change Reason Code Reduction of Scope
Change Order Description And Justification
pr #12 - Delete paint on ceilings in IDF and Mechanical Rooms

Cost Benefit To Owner
Reduction in Scope

Contract unit prices have been utilized No
to support the cost associated with this

change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	(\$2,300.00)	80.70%
Materials	(\$550.00)	19.30%
Profit and Overhead		0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$-2,850.00	
Cost for this Change Order supported by an alternate bid or competitive price quote		
Explain Why		

Change Order Supplemental Information Form Signature Page (Online Form Ref# 62483)

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 21-06
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 RISING SUN DEVELOPING COMPANY
 2555 PALUMBO DRIVE
 SUITE 110

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #21 (BP#1 SITE WORK, 3
 GENERAL TRADES, 5 STEEL, 9 PAINT)

THE CONTRACT IS CHANGED AS FOLLOWS: PR #12 - Delete paint on ceilings in IDF & Mechanical Rooms

The original Contract Sum was	6,892,783.85
Net change by previously authorized Change Orders	34,727.81
The Contract Sum prior to this Change Order was	6,927,511.66
The Contract Sum will be Decreased by this Change Order in the amount of	-2,850.00
The new Contract Sum including this Change Order will be	6,924,661.66

The Contract Time will be adjusted by 0 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 9/5/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

RISING SUN DEVELOPING COMPANY

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)
 2555 PALUMBO DRIVE*SUITE 110*LEXINGTON, KY 40509

OWNER (Firm Name)
 691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)



Change Order Review Form

Delete Dryfall in IDF and Mechanical Rooms
delete Dryfall in IDF and Mech rooms.

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

PR # 12 Delete Dryfall in IDF and Mechanical Rooms

Date: 4/11/2025

To: Sherman Carter Barnhart Architects, PLLC

From: Michael Graf

Attn:

CC: Kenny Davis

I have reviewed and approved the attachment pricing. Your approval and signature is required in order to process this change order. Please review the pricing and sign below it is acceptable.

PR # 12 Delete Dryfall in IDF and Mechanical Rooms

Description	BP	Amount
C&T DESIGN & EQUIPMENT CO.,	012	0.00
CENTRAL KENTUCKY SHEET METAL	018	0.00
DIXIE ROOFING, INC.	006	0.00
ELLIOTT CONTRACTING, INC.	008	0.00
FACILITY COMMISSIONING GROUP	020	0.00
GRAYHAWK, LLC	007	0.00
HINKLE CONTRACTING COMPANY LLC	002	0.00
IRWIN INSTALLATION SOURCE	013	0.00
MARTIN FLOORING COMPANY, INC.	014	0.00
MASON STRUCTURE, INC.	004	0.00
RIMAR ELECTRIC, LLC	019	0.00
RISING SUN DEVELOPING COMPANY	021	-2,850.00
ROSA MOSAIC & TILE COMPANY	022	0.00
TWIN LAKES FIRE SERVICE, LLC	017	0.00

Summary

Total

Total Days 0.00

-2,850.00

Sherman Carter Barnhart Architects, PLLC

16MAY25

Signature

DATE:

Codell Construction Company
Michael Graf
West College Avenue
Stanton, KY 40380
mgraf@codellconstruction.com



AIA[®] Document G709[™] – 2018

Proposal Request

PROJECT: *(name and address)*

Stanton Elementary School

870 W. College Avenue
Stanton, KY 40380

OWNER: *(name and address)*

Powell County Schools

691 Breckinridge Street
Stanton, KY 40380

CONTRACT INFORMATION:

Contract For:

General Construction

Date:

09-20-2023

Architect's Project Number: 2060

Proposal Request Number: 12

Proposal Request Date:

ARCHITECT: *(name and address)*

Sherman Carter Barnhart Architects PLLC

144 Turner Commons Way Suite 110
Lexington, KY 40508

CONTRACTOR: *(name and address)*

Codell Construction Co. (CM) -
Winchester

4475 Rockwell Road
Winchester, KY 40392

The Owner requests an itemized proposal for changes to the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. The Contractor shall submit this proposal within (0) days or notify the Architect in writing of the anticipated date of submission.

(Insert a detailed description of the proposed modifications to the Contract Documents and, if applicable, attach or reference specific exhibits.)

Provide itemized credit pricing for labor and materials to omit painting the exposed structure in the following rooms (reflected ceiling plans keynote 9):

Mech 107B
Mech 121
IDF 130
Mech 133A
Mech 136
Mech 150A
IDF 147
Mech 153
Elec. Rm. 154
Mech. 156A
Mech 167
IDF 170
Mech 173
Mech 176
Mezz Stor 195
Cust. Rec. 196
Mech 197

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE, OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

REQUESTED BY THE ARCHITECT

Allison Commings

ARCHITECT (Signature)

BY: Allison Commings, AIA, Associate Principal

(Printed name, title, and license number if required)



PR 12

4/15/2025

Project: Stanton Elementary
Attn- Kenny Davis

Description: Pricing Per Direction In PR# 12

Item	QTY	Unit	Unit \$	Cost
Material				
Dryfall	1	lot	-\$550.00	(\$550)
Labor				
Install	1	lot	-\$2,300.00	(\$2,300)
				\$ -
Summary				
				\$ -
Material	1	ea	-\$550.00	\$ (550.00)
Labor	1	ea	-\$2,300.00	\$ (2,300.00)
Tx On Material	0.06	\$		
OHP @ 15%	0.15	\$	\$ (2,850.00)	
Credit				-\$2,850.00

Donnie Napier
Project Manager
Rising Sun Developing, Inc.
2555 Palumbo Drive, Ste 110
Lexington, KY 40509
Phone: 859-543-0205 / Fax: 859-543-0230



FACPAC Contract Change Order

Supplemental Information Form (Ref#

62497)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072District: Powell County (HB678) (495)

Status: ActivePhase: Project Initiation (View Checklist)

Contract: Rising Sun Developing Company, 0021, Combination Bid (BP#1 Site Work, BP#3

General Trades, BP#5 Steel, BP#9 Paint)

Type: CM Bid PackageProposed

Change Order Number21-07

Time Extension RequiredYes

If Yes Number Of Days65

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency

Balance

Contract Change Requested ByConstruction Manager

Contract Change Reason CodeTime Extension

Change Order Description And Justification

1. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported by an alternate bid or competitive price quote		
Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62497)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 21-07
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 RISING SUN DEVELOPING COMPANY
 2555 PALUMBO DRIVE
 SUITE 110

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #21 (BP#1 SITE WORK, 3
 GENERAL TRADES, 5 STEEL, 9 PAINT)

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.
 Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	6,892,783.85
Net change by previously authorized Change Orders	31,877.81
The Contract Sum prior to this Change Order was	6,924,661.66
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	6,924,661.66

The Contract Time will be adjusted by 63 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

RISING SUN DEVELOPING COMPANY

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)
 2555 PALUMBO DRIVE*SUITE 110*LEXINGTON, KY 40509

OWNER (Firm Name)
 691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025												
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	2	3	4																
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24																				
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24																				
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24																				
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24																				
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24																				
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24																				
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24																				
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24																				
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24																				
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24																				
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24																				
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24																				
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24																				
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24																				
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24																				
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24																				
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24																				
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24																				
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24																				
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24																				
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24																				
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24																				
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24																				
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24																				
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24																				
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24																				
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24																				
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24																				
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24																				
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24																				
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25																				
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25																				
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25																				

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

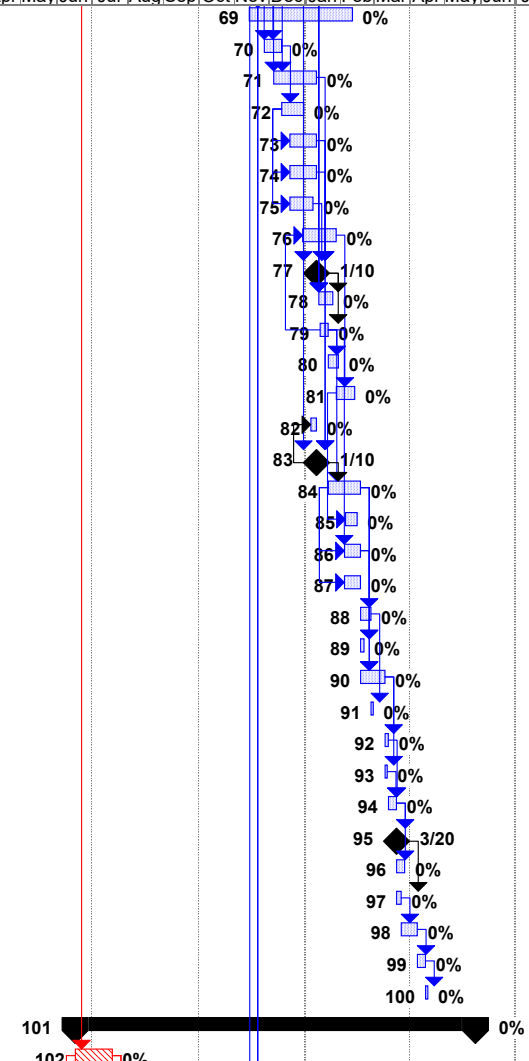

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25																171	0%					
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25																172	0%					
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25																						0%
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24																						
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24																						
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24																						
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24																						
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24																						
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24																						
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24																						
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24																						
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24																						
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24																						
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24																						
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24																						
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24																						
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24																						
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24																						
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24																						
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24																						
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24																						
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24																						
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25																						
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25																						
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25																						
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24																						
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25																						
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25																						
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25																						
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25																						
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25																						
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25																						

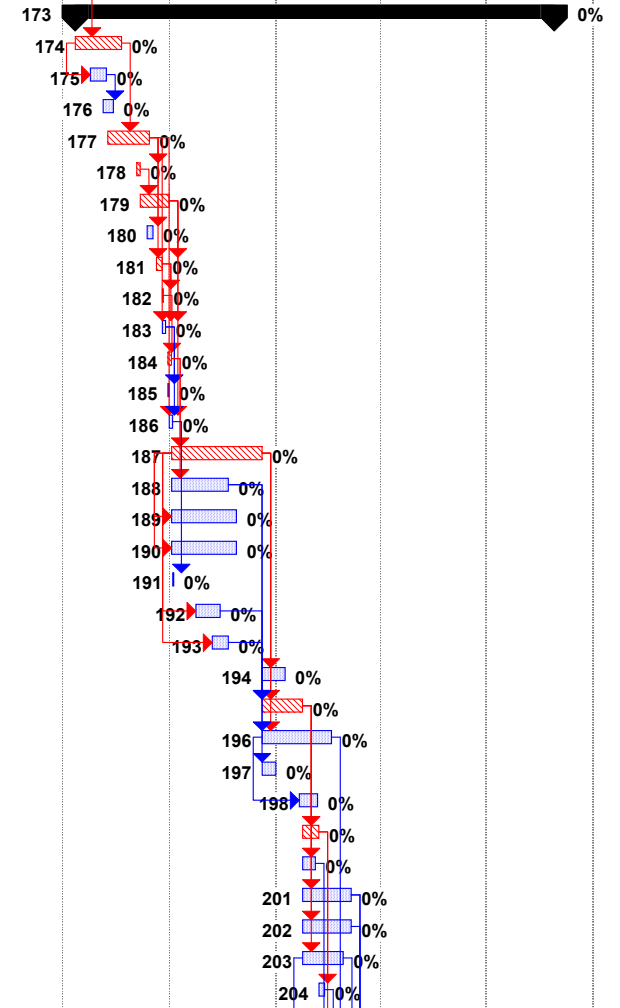

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25																						
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25																						
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25																						
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25																						
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25																						
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25																						
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25																						
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25																						
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25																						
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25																						
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25																						
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25																						
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25																						
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25																						
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25																						
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25																						
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25																						
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25																						
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25																						
296	Architect Site Punch List Distributed - Site	0 days	Mon 8/11/25	Mon 8/11/25																						
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25																						
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25																						
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

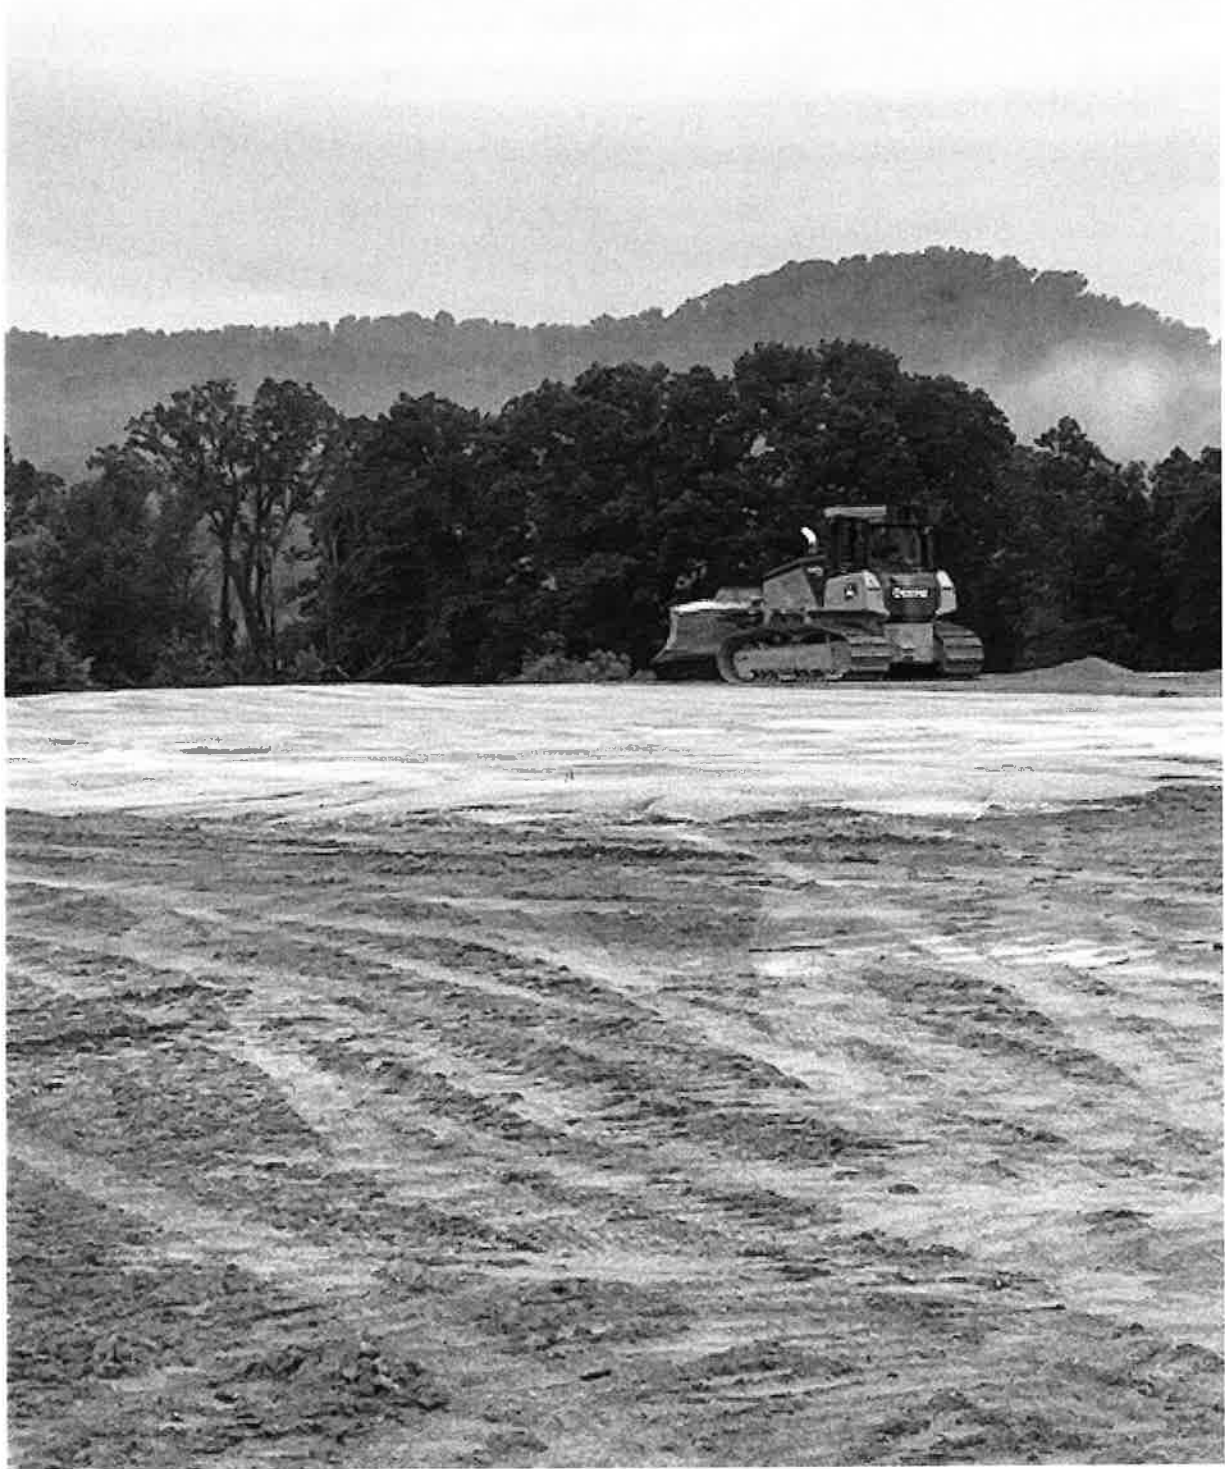



Daily Construction Report
With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A).				
	Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

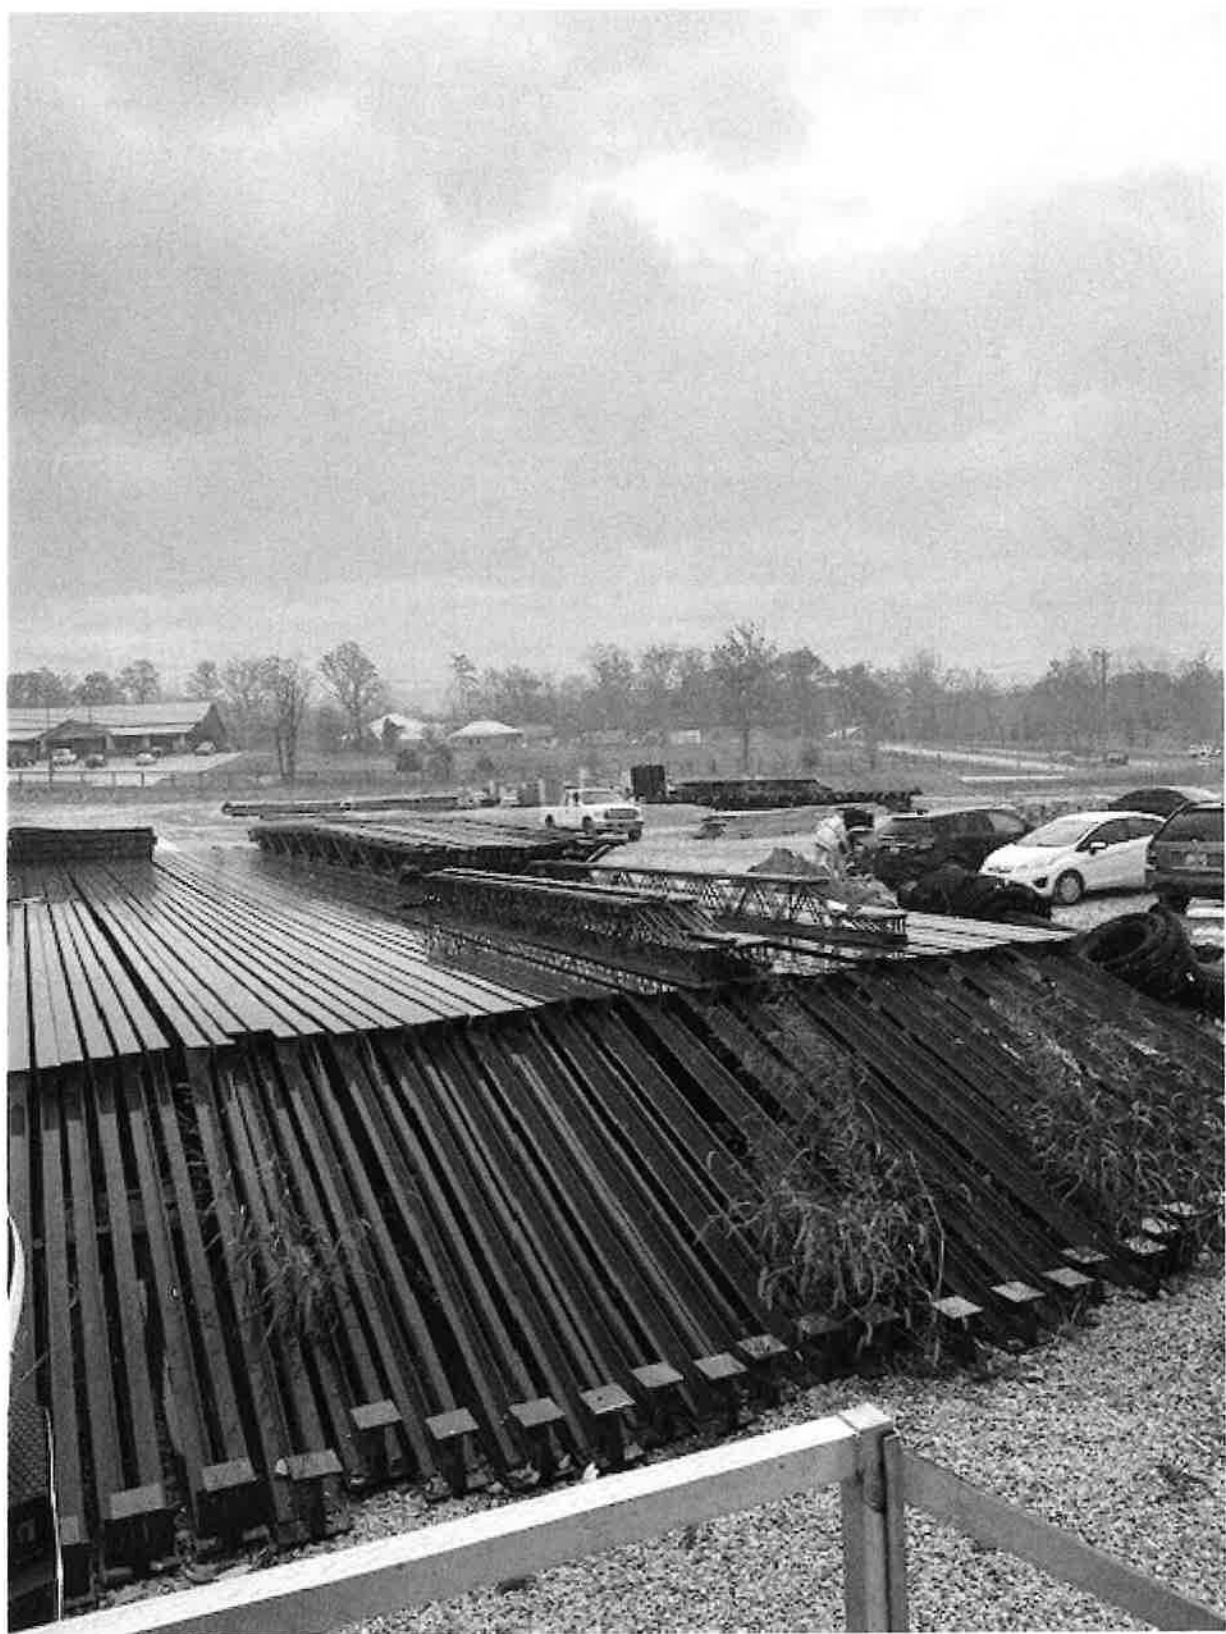



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

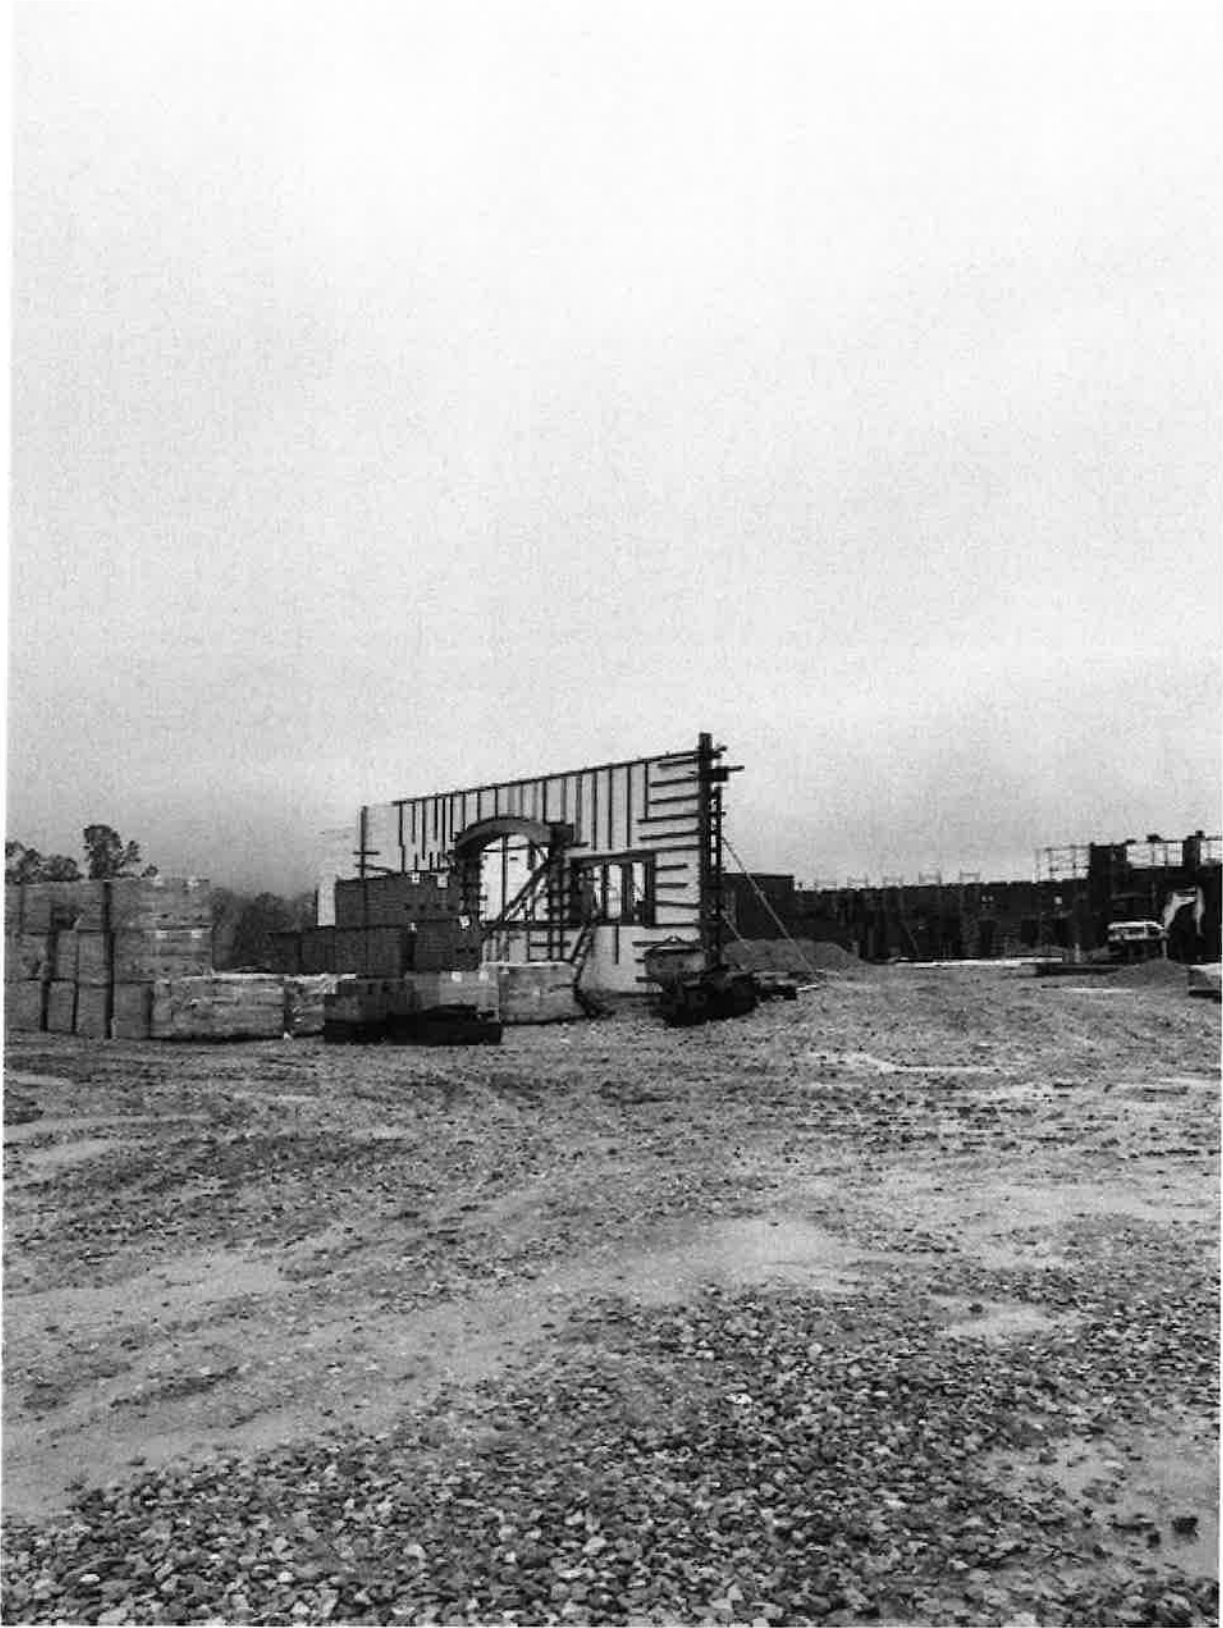



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00

hours

52° F

rain

1

notes

2

equipment

● Approved

status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM


File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM



Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00

hours

31° F

clear

1

notes

0

equipment

● Approved

status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00
hours

60° F
cloudy

1
notes

6
equipment

● Approved
status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days














Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00






MATERIAL DELIVERED

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 11:00 AM
Michael Graf

File
1/8/2025 1:48 PM
Michael Graf



File
Daily Report 2025
Michael Graf

Page 2 of 2





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

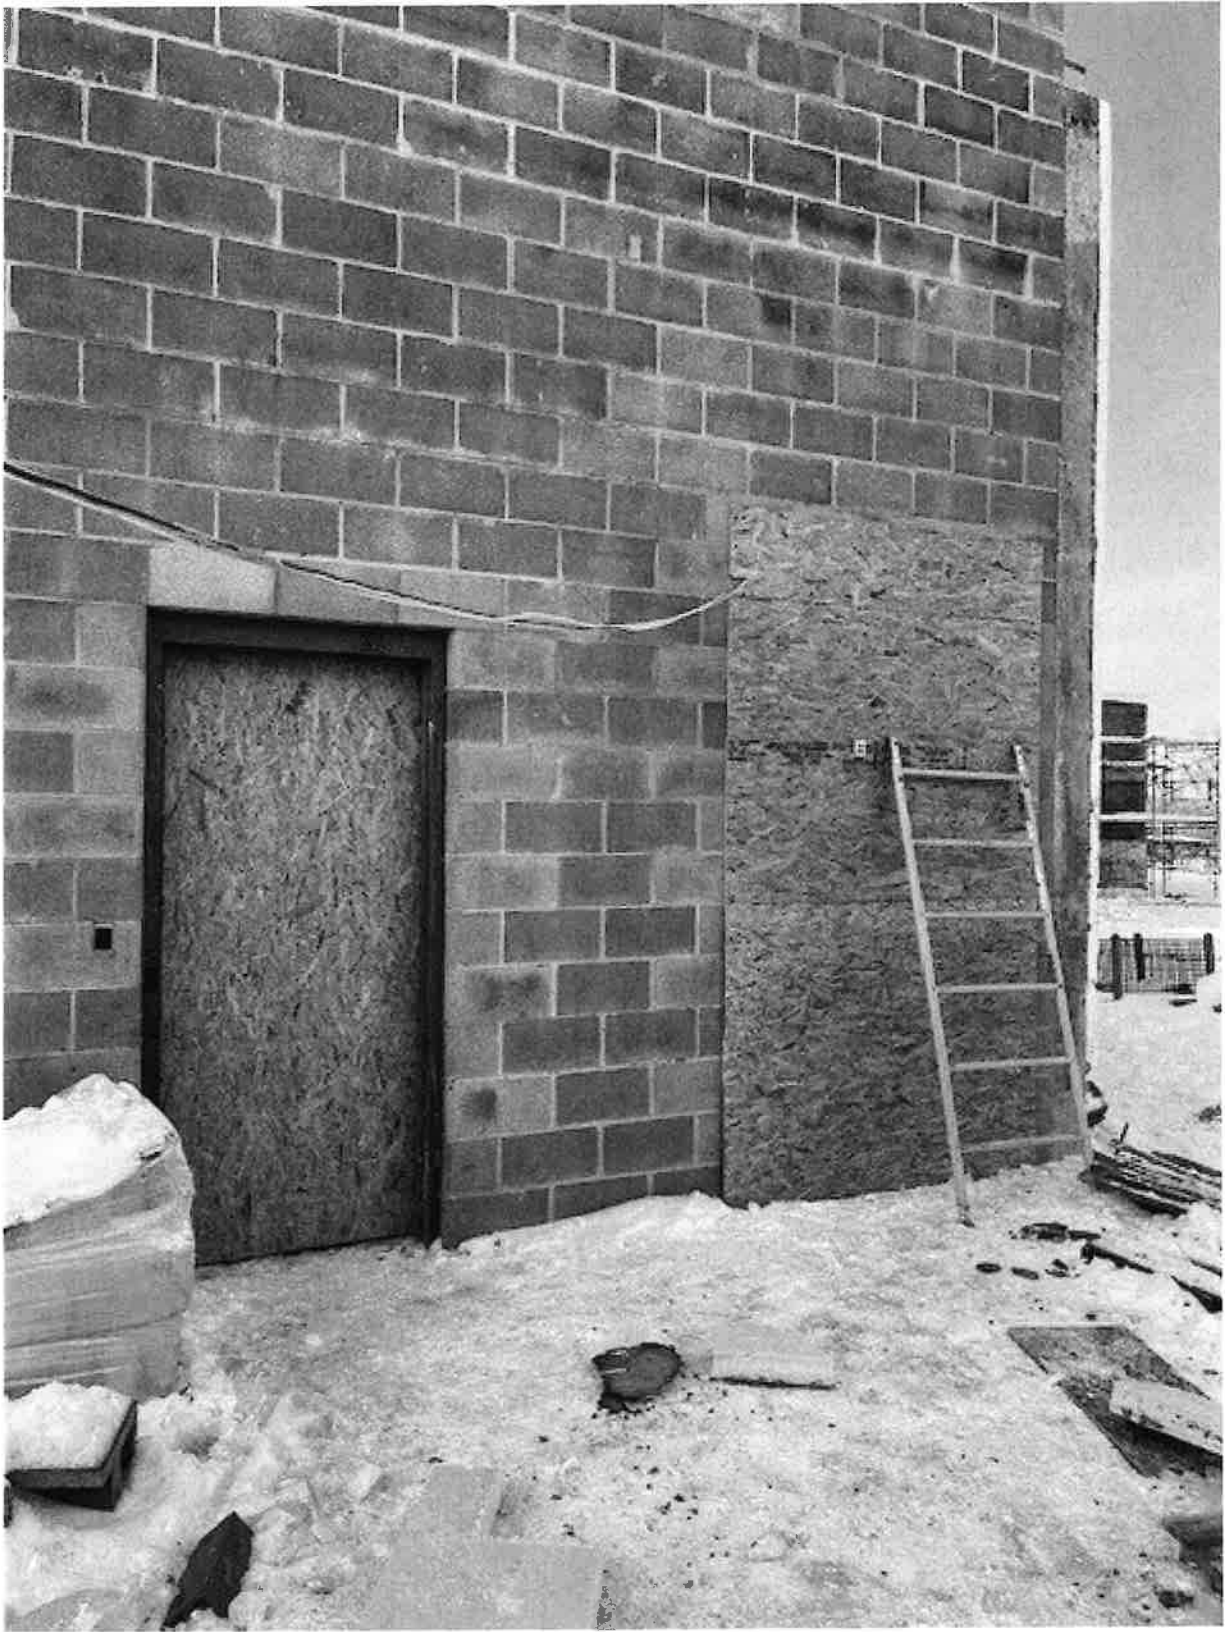



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM

Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

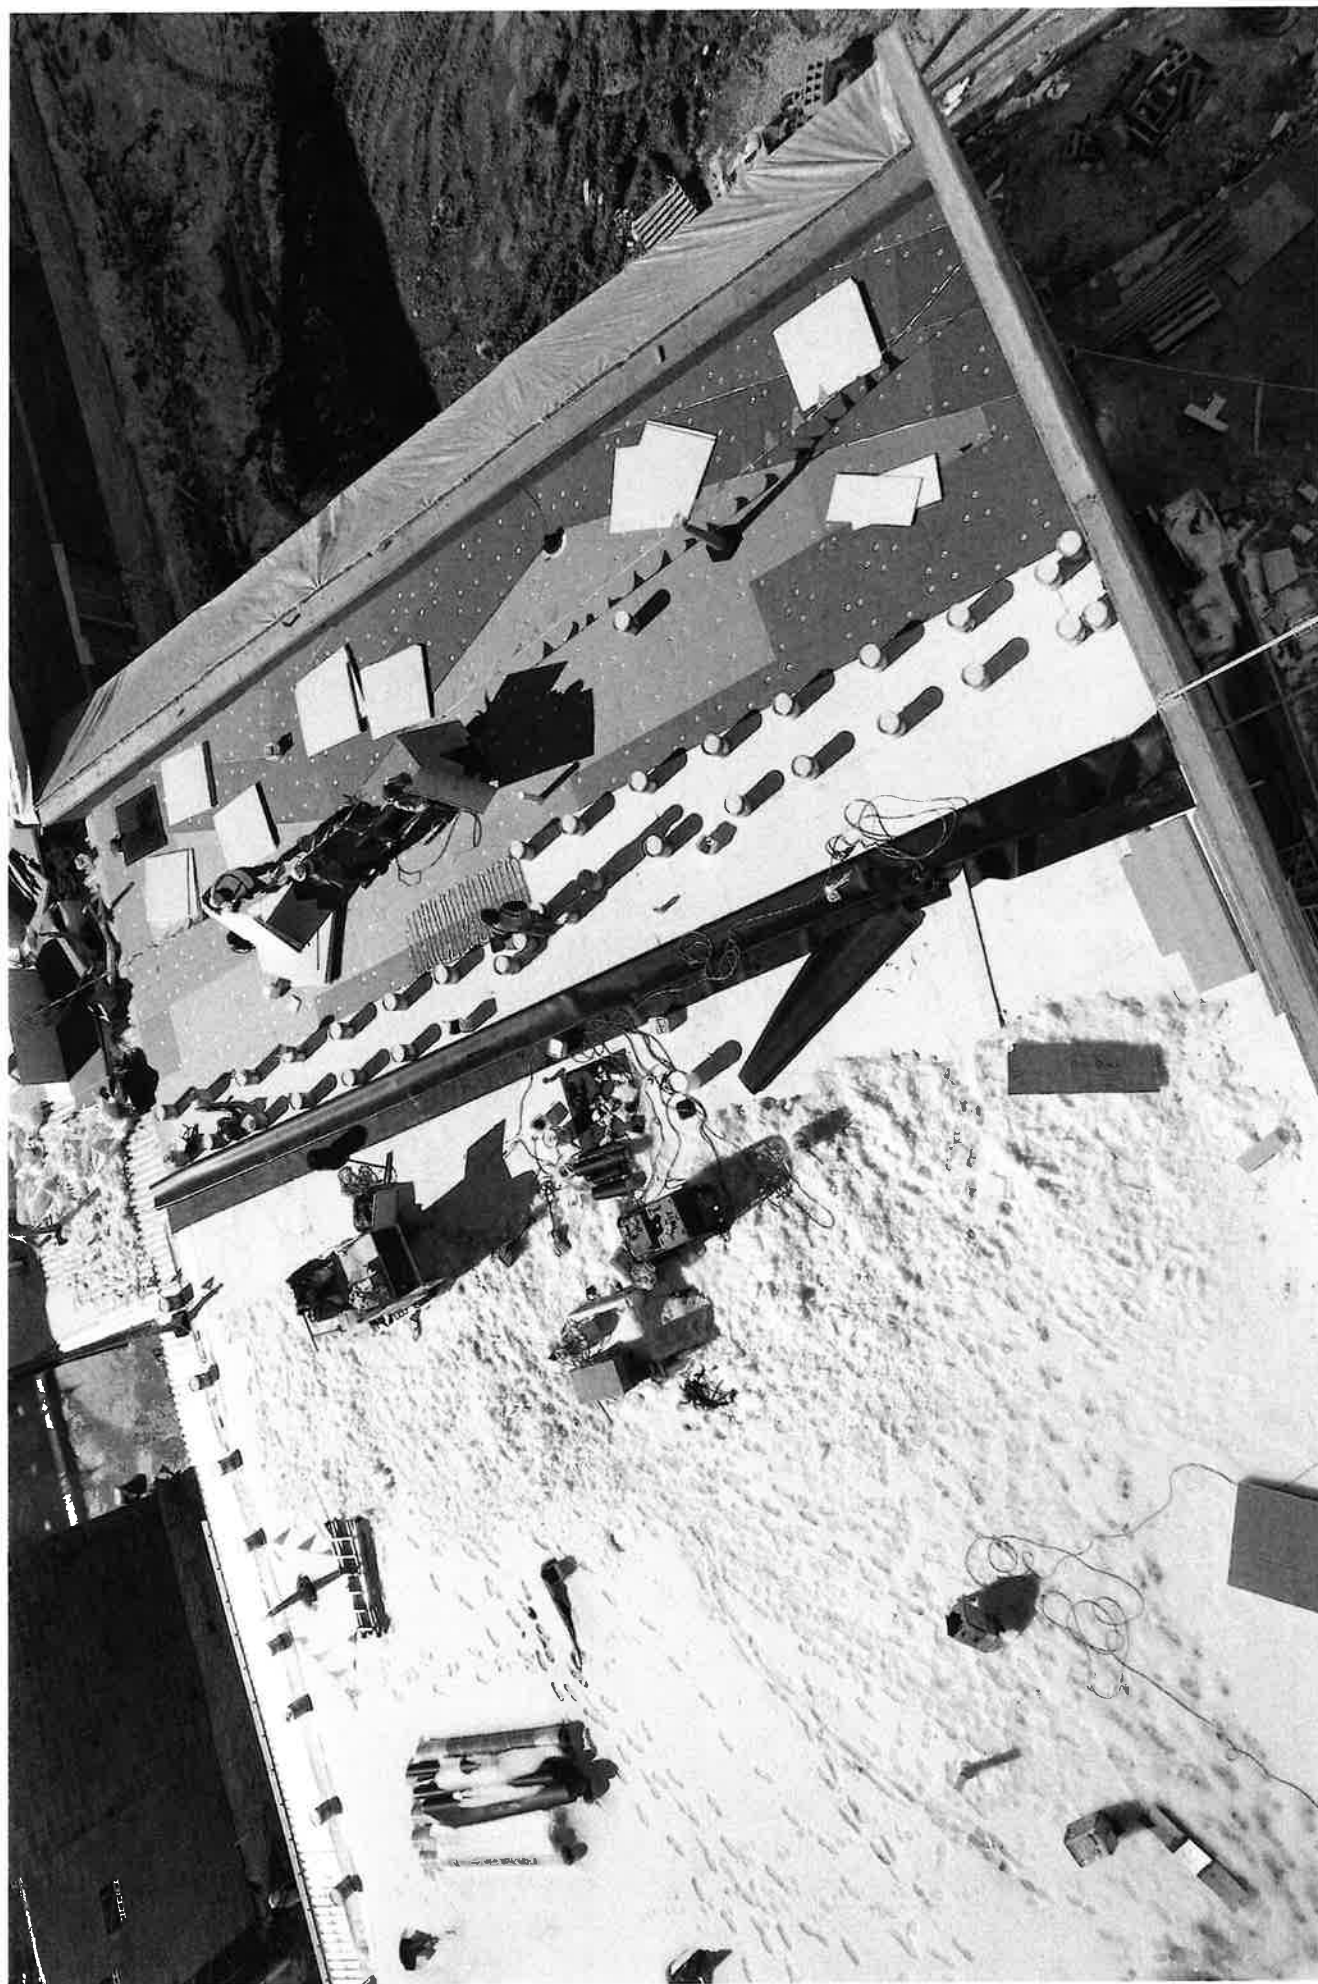



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM



Michael Graf on 1/23/2025 03:17 PM



Michael Graf on 1/23/2025 03:37 PM



ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

File

2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM



File


Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf



File
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

● Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.

Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.


Michael Graf on 2/18/2025 03:33 PM



File

Daily Report 2025...

Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A).		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(1) Sealing duct penetrations. (3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf



File
4/4/2025 1:13 PM
Michael Graf


Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM



File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontals/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD


Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1101111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	

FACPAC Contract Change Order Supplemental Information Form (Ref# 62535)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072

District: Powell County (HB678) (495)

Status: Active

Phase: Project Initiation (View Checklist)

Contract: Rising Sun Developing Company, 0021, Combination Bid (BP#1 Site Work, BP#3 General Trades, BP#5 Steel, BP#9 Paint)

Type: CM Bid Package

Proposed

Change Order Number 21-08
Time Extension Required No
Date Of Change Order 6/10/2025
Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$227,074.61
Remaining After Approved COs	\$1,008,546.50
Net All COs	\$231,151.01
Remaining After All COs	\$1,004,470.10

This Requested Change Order Amount \$7,033.40

+/-

Change In A/E Fee This Change Order \$379.80

+/-

Change In CM Fee This Change Order \$133.63

+/-

Remaining Construction Contingency

Balance

Contract Change Requested By Local Board of Education

Contract Change Reason Code Improved Plans/Specs

Change Order Description And Justification

PR #14 - Change the locking functionsto Bwst 45H7T14HVIB for the fpllowing doors:

135,155, 191, 116A, 120A, 175A, 177A.

Cost Benefit To Owner

Improved conditons

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$600.00	8.53%
Materials	\$5,516.00	78.43%
Profit and Overhead	\$917.40	13.04%
Bond Insurance		0.00%
Cost Breakdown Total:	\$7,033.40	
Cost for this Change Order supported by an alternate bid or competitive price quote		
Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62535)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 21-08
 INITIATION DATE: 6/10/2025

TO CONTRACTOR (Name and Address)
 RISING SUN DEVELOPING COMPANY
 2555 PALUMBO DRIVE
 SUITE 110

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #21 (BP#1 SITE WORK, 3
 GENERAL TRADES, 5 STEEL, 9 PAINT)

THE CONTRACT IS CHANGED AS FOLLOWS: PR #14 - Change the locking functions to BEST 45H7T14HVIB for the following doors 135, 155, 191, 116A, 120A, 175A, 177A

The original Contract Sum was	6,892,783.85
Net change by previously authorized Change Orders	31,877.81
The Contract Sum prior to this Change Order was	6,924,661.66
The Contract Sum will be Increased by this Change Order in the amount of	7,033.40
The new Contract Sum including this Change Order will be	6,931,695.06

The Contract Time will be adjusted by 0 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

RISING SUN DEVELOPING COMPANY

POWELL COUNTY BOARD OF EDUCATION

CONTRACTOR (Firm Name)
 2555 PALUMBO DRIVE*SUITE 110*LEXINGTON, KY 40509

OWNER (Firm Name)
 691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

ADDRESS

BY (Signature)

BY (Signature)

(Typed Name)

DATE:

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)



Change Order Review Form

PR # 14 Revised locking functions

PR #14 Revised locking functions.

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

PR # 14 Revised locking functions

Date: 5/9/2025

To: Sherman Carter Barnhart Architects, PLLC

From: Michael Graf

Attn:

CC: Kenny Davis

I have reviewed and approved the attachment pricing. Your approval and signature is required in order to process this change order. Please review the pricing and sign below it is acceptable.

PR # 14 Revised locking functions.


Description	BP	Amount
C&T DESIGN & EQUIPMENT CO.,	012	0.00
CENTRAL KENTUCKY SHEET METAL	018	0.00
DIXIE ROOFING, INC.	006	0.00
ELLIOTT CONTRACTING, INC.	008	0.00
FACILITY COMMISSIONING GROUP	020	0.00
GRAYHAWK, LLC	007	0.00
HINKLE CONTRACTING COMPANY LLC	002	0.00
IRWIN INSTALLATION SOURCE	013	0.00
MARTIN FLOORING COMPANY, INC.	014	0.00
MASON STRUCTURE, INC.	004	0.00
RIMAR ELECTRIC, LLC	019	0.00
RISING SUN DEVELOPING COMPANY	021	7,033.40
ROSA MOSAIC & TILE COMPANY	022	0.00
TWIN LAKES FIRE SERVICE, LLC	017	0.00

Summary

Total

Total Days 0.00

7,033.40

Sherman Carter Barnhart Architects, PLLC	
	09JUN25
Signature	DATE:

Codell Construction Company
Michael Graf
West College Avenue
Stanton, KY 40380
mgraf@codellconstruction.com



AIA[®] Document G709[™] – 2018

Proposal Request

PROJECT: *(name and address)*

Stanton Elementary School

870 W. College Avenue
Stanton, KY 40380

OWNER: *(name and address)*

Powell County Schools

691 Breckinridge Street
Stanton, KY 40380

CONTRACT INFORMATION:

Contract For:

General Construction

Date:

09-20-2023

Architect's Project Number: 2060

Proposal Request Number:

Proposal Request Date: 04-23-2025

ARCHITECT: *(name and address)*

Sherman Carter Barnhart Architects PLLC

144 Turner Commons Way Suite 110
Lexington, KY 40508

CONTRACTOR: *(name and address)*

Codell Construction Co. (CM) -
Winchester

4475 Rockwell Road
Winchester, KY 40392

The Owner requests an itemized proposal for changes to the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. The Contractor shall submit this proposal within (0) days or notify the Architect in writing of the anticipated date of submission.

(Insert a detailed description of the proposed modifications to the Contract Documents and, if applicable, attach or reference specific exhibits.)

Change the locking function to Best 45H7T14H VIB for the following doors: 135, 155, 191, 116A, 120A, 175A, 177A. Prep doors, in the field, as required. Use escutcheon trim to cover additional prep holes, if necessary.

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE, OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

REQUESTED BY THE ARCHITECT



ARCHITECT *(Signature)*

BY: Allison Commings, AIA, Associate Principal

(Printed name, title, and license number if required)

PR# 14				
			5/21/2025	
Project: Stanton Elementary Attn- Kenny Davis				
Description: PR# 14 Provide pricing per direction in pr 14				
Item	QTY	Unit	Unit \$	Cost
Material				
45h7T14hxVIB Locksets	7	ea	\$788.00	\$5,516
Labor				
Door Prep on 4 Doors	1	lot		\$600
				\$ -
				\$ -
Summary				
				\$ -
Material	1	ea	\$5,516.00	\$ 5,516.00
Labor	1	ea	\$600.00	\$ 600.00
Tx On Material	0.06	\$		
OHP @ 15%	0.15	\$		\$ 917.40
ADD				\$7,033.40
Donnie Napier Project Manager Rising Sun Developing, Inc. 2555 Palumbo Drive, Ste 110 Lexington, KY 40509 Phone: 859-543-0205 / Fax: 859-543-0230 				

FACPAC Contract Change Order

Supplemental Information Form (Ref#

62495)

Form Status: Saved

Tier 1 Project: New Stanton Elementary School

BG Number: 21-072District: Powell County (HB678) (495)

Status: ActivePhase: Project Initiation (View Checklist)

Contract: Rosa Mosaic & Tile Co, 0022, Combination Bid (BP#10VCT, #11Tiling,

#15Terrazzo, #16Resinous Flooring)

Type: CM Bid PackageProposed

Change Order Number22-02

Time Extension RequiredYes

If Yes Number Of Days93

Date Of Change Order6/9/2025

Change Order Amount To Date

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$1,235,621.11
Net Approved COs	\$438,961.30
Remaining After Approved COs	\$796,659.81
Net All COs	\$224,117.61
Remaining After All COs	\$1,011,503.50

This Requested Change Order Amount \$0.00

+/-

Change In A/E Fee This Change Order

+/-

Change In CM Fee This Change Order

+/-

Remaining Construction Contingency

Balance

Contract Change Requested ByConstruction Manager

Contract Change Reason CodeTime Extension

Change Order Description And Justification

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.

2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

Cost Benefit To Owner
No cost from Contractor

Contract unit prices have been utilized No
to support the cost associated with this
change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which
separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor	\$0.00	0.00%
Materials	\$0.00	0.00%
Profit and Overhead	\$0.00	0.00%
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported by an alternate bid or competitive price quote	No	
Explain Why		

**Change Order Supplemental Information Form Signature
Page (Online Form Ref# 62495)**

Architect

Date

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 STANTON ELEMENTARY SCHOOL
 WEST COLLEGE AVENUE
 STANTON, KY 40380

CHANGE ORDER NUMBER: 22-02
 INITIATION DATE: 6/8/2025

TO CONTRACTOR (Name and Address)
 ROSA MOSAIC & TILE COMPANY

PROJECT NUMBERS: 000743
 CONTRACT DATE: 3/4/2024
 CONTRACT FOR: BID PACKAGE #22 (BP#10 VCT, 11 TILING, 15
 TERRAZZO, 16 RESINOUS FLOORING)

THE CONTRACT IS CHANGED AS FOLLOWS:

1. The project schedule has been affected by PR #1 - Wick Drains – adding 20 workdays which equates to 28 calendar days.
2. The project schedule has been affected by adverse weather days - 47 workdays which equates to 65 calendar days.

Substantial Completion dates extended from 8/7/2025 to 11/7/2025. Final Completion dates extended from 9/3/2025 to 12/04/2025.

The original Contract Sum was	775,265.00
Net change by previously authorized Change Orders	17,140.00
The Contract Sum prior to this Change Order was	792,405.00
The Contract Sum will be Increased by this Change Order in the amount of	0.00
The new Contract Sum including this Change Order will be	792,405.00

The Contract Time will be adjusted by 93 days.

The date of Substantial Completion as of the date of this Change Order therefore is 11/7/2025.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

ROSA MOSAIC & TILE COMPANY

CONTRACTOR (Firm Name)

ADDRESS

BY (Signature)

(Typed Name)

DATE:

SHERMAN CARTER BARNHART ARCHITECTS, PLLC

ARCHITECT (Firm Name)
 144 TURNER COMMONS WAY SUITE, 110 LEXINGTON, KY

ADDRESS

BY (Signature)

(Typed Name)

DATE:

POWELL COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
 691 BRECKINRIDGE STREET STANTON, KY 40380

ADDRESS

BY (Signature)

(Typed Name)

DATE:

AIA Document G701/CMa[™] – 1992. Copyright © 1992 by The American Institute of Architects. All rights reserved. **WARNING: This AIA[®] Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA[®] Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.**

User Notes:

(1884033357)

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025									
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1	Notice to Proceed	0 days	Mon 3/4/24	Mon 3/4/24	1	3/4															
2	Mobilization	5 days	Mon 3/4/24	Fri 3/8/24	2	0%															
3	Quick Ship Shop Drawings - Concrete Rebar	5 days	Mon 3/4/24	Fri 3/8/24	3	0%															
4	Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	Mon 3/4/24	Fri 3/8/24	4	0%															
5	Quick Ship Shop Drawings - Grout Mix Design	5 days	Mon 3/4/24	Fri 3/8/24	5	0%															
6	Quick Ship Shop Drawings - CMU	5 days	Mon 3/4/24	Fri 3/8/24	6	0%															
7	Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	Mon 3/4/24	Fri 4/5/24	7	0%															
8	Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	Mon 3/4/24	Fri 4/5/24	8	0%															
9	Quick Ship Shop Drawings - MEP underslab piping	10 days	Mon 3/4/24	Fri 3/15/24	9	0%															
10	Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	Mon 3/4/24	Fri 3/15/24	10	0%															
11	Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	Mon 3/4/24	Fri 3/15/24	11	0%															
12	Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	Mon 3/4/24	Fri 4/26/24	12	0%															
13	Submit Notice of Intent - Best Management Plan	0 days	Tue 3/5/24	Tue 3/5/24	13	3/5															
14	Install BMP mandated work	3 days	Wed 3/6/24	Fri 3/8/24	14	0%															
15	Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	Fri 3/8/24	Mon 3/11/24	15	0%															
16	Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	Mon 3/11/24	Fri 3/15/24	16	0%															
17	Install Stone(#2's capped with DGA) for construction entrance	2 days	Tue 3/12/24	Wed 3/13/24	17	0%															
18	Site Clearing/Demolition/Stockpile Topsoil	15 days	Thu 3/14/24	Wed 4/3/24	18	0%															
19	Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	Mon 3/18/24	Fri 3/22/24	19	0%															
20	Site Grading/Earthwork	65 days	Tue 3/26/24	Tue 6/25/24	20	0%															
21	A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	Mon 4/8/24	Fri 4/19/24	21	0%															
22	A/E review remainder of shop drawings	20 days	Mon 4/29/24	Fri 5/24/24	22	0%															
23	Building Pad on Grade	0 days	Tue 5/14/24	Tue 5/14/24	23	5/14															
24	Install Storm Drainage	30 days	Wed 6/5/24	Wed 7/17/24	24	0%															
25	Install Geothermal Well Field (verticals/horizontal/vault)	60 days	Wed 6/5/24	Wed 8/28/24	25	0%															
26	Install Fire Main, Vault and Hyrdants	30 days	Wed 6/26/24	Wed 8/7/24	26	0%															
27	Install Sewer line	30 days	Wed 6/26/24	Wed 8/7/24	27	0%															
28	Install Domestic Water	15 days	Thu 8/8/24	Wed 8/28/24	28	0%															
29	Install Gas	15 days	Thu 8/29/24	Thu 9/19/24	29	0%															
30	Install Grease Trap	7 days	Fri 9/20/24	Mon 9/30/24	30	0%															
31	Set Transformer/Pull Primary/Secondary Wire	10 days	Mon 12/16/24	Mon 12/30/24	31	0%															
32	Set Cooling Tower - Hook up lines	10 days	Mon 12/23/24	Tue 1/7/25	32	0%															
33	Permanent Power	0 days	Tue 1/28/25	Tue 1/28/25	33	1/28															
34	AREA A	236 days	Tue 5/14/24	Wed 4/16/25	34	0%															

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
35	Footers - Area A	23 days	Tue 5/14/24	Fri 6/14/24																						
36	ICF Stem walls- Area A	7 days	Tue 5/28/24	Wed 6/5/24																						
37	Underslab Plumbing Rough in - Area A	20 days	Wed 6/5/24	Tue 7/2/24																						
38	Underslab CMU - Area A	5 days	Mon 6/3/24	Fri 6/7/24																						
39	Stone Backfill non plumbing areas - Area A	2 days	Thu 6/20/24	Fri 6/21/24																						
40	Underslab Electrical Rough in - Area A	12 days	Mon 6/24/24	Wed 7/10/24																						
41	Stone Backfill at pumbing areas - Area A	2 days	Mon 7/1/24	Tue 7/2/24																						
42	Slab Prep 1st Floor - Area A	3 days	Thu 7/11/24	Mon 7/15/24																						
43	Slab Placement 1st Floor - Area A	1 day	Tue 7/16/24	Tue 7/16/24																						
44	Hollow Metal Doorframes installation 1st Floor - Area A	3 days	Fri 7/19/24	Tue 7/23/24																						
45	CMU Bearing Walls - Area A	25 days	Wed 7/24/24	Tue 8/27/24																						
46	ICF Walls - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
47	Plumbing Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
48	Electrical Wall Rough in - Area A	20 days	Wed 7/24/24	Tue 8/20/24																						
49	Steel Columns/Beams/Bent Plate - Area A	12 days	Wed 8/7/24	Thu 8/22/24																						
50	CMU Non Bearing Walls/Rub all walls - Area A	10 days	Wed 8/28/24	Wed 9/11/24																						
51	Set Roof Joists - Area A	15 days	Wed 8/28/24	Wed 9/18/24																						
52	Exterior Brick/Stone - Area A	35 days	Mon 9/9/24	Fri 10/25/24																						
53	Roof Deck installation/inspection - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
54	ICF Parapet Walls - Area A	7 days	Thu 9/19/24	Fri 9/27/24																						
55	Electrical Rough-In --Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
56	Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	Thu 9/19/24	Wed 11/13/24																						
57	Duct installation - Above Ceiling - Area A	35 days	Thu 9/19/24	Wed 11/6/24																						
58	Roof Wood Blocking - Area A	7 days	Mon 9/30/24	Tue 10/8/24																						
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	Mon 10/7/24	Tue 10/22/24																						
60	TPO Roof- Area A	15 days	Wed 10/9/24	Tue 10/29/24																						
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	Thu 10/10/24	Wed 11/6/24																						
62	Block Filler - Area A	10 days	Wed 10/16/24	Tue 10/29/24																						
63	Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	Wed 10/23/24	Tue 11/26/24																						
64	Clean Brick - Area A	5 days	Mon 10/28/24	Fri 11/1/24																						
65	Brick Caulking - Area A	3 days	Mon 10/28/24	Wed 10/30/24																						
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	Wed 10/30/24	Tue 11/26/24																						
67	Set Mechanical Equipment/Tie In - Area A	25 days	Wed 10/30/24	Wed 12/4/24																						
68	Metal Coping, Trim etc... - Area A	15 days	Mon 11/4/24	Fri 11/22/24																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
69	Electrical Systems/Devices - Area A	60 days	Thu 11/14/24	Mon 2/10/25																						
70	Primer/1st Coat of Paint - Walls - Area A	10 days	Wed 11/27/24	Wed 12/11/24																						
71	HVAC Controls - Area A	25 days	Thu 12/5/24	Fri 1/10/25																						
72	Ceiling Grid - Area A	12 days	Thu 12/12/24	Mon 12/30/24																						
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
74	Light Fixtures - Area A	15 days	Thu 12/19/24	Fri 1/10/25																						
75	Sprinkler Heads - Area A	12 days	Thu 12/19/24	Tue 1/7/25																						
76	Ceramic Tile - Area A	20 days	Mon 12/30/24	Mon 1/27/25																						
77	Above Ceiling Punch - Engineer - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
78	Paint - Exposed Ceilings/Floors- Area A	10 days	Mon 1/13/25	Fri 1/24/25																						
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	Tue 1/14/25	Mon 1/20/25																						
80	Ceiling Tiles - Area A	7 days	Tue 1/21/25	Wed 1/29/25																						
81	Plumbing Fixtures - Area A	12 days	Tue 1/28/25	Wed 2/12/25																						
82	Aluminum Storefront Frames and Doors - Area A	5 days	Mon 1/6/25	Fri 1/10/25																						
83	Controlled Air - Area A	0 days	Fri 1/10/25	Fri 1/10/25																						
84	VCT and Base - Area A	20 days	Tue 1/21/25	Mon 2/17/25																						
85	Toilet Partitions and Accessories - Area A	8 days	Wed 2/5/25	Fri 2/14/25																						
86	Casework/Solid Surface Sills - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
87	Final Coat Paint - Walls - Area A	10 days	Tue 2/4/25	Mon 2/17/25																						
88	Display/Tack Boards - Area A	7 days	Tue 2/18/25	Wed 2/26/25																						
89	Door Frame Paint - 1 Coats - Area A	3 days	Tue 2/18/25	Thu 2/20/25																						
90	Doors & Hardware - Area A	15 days	Tue 2/18/25	Mon 3/10/25																						
91	Interior Signage - Area A	2 days	Thu 2/27/25	Fri 2/28/25																						
92	Doorframe Paint - 2nd Coat - Area A	3 days	Tue 3/11/25	Thu 3/13/25																						
93	Install Door Glass - Area A	2 days	Tue 3/11/25	Wed 3/12/25																						
94	Pre-Clean before Architect Punchlist - Area A	5 days	Fri 3/14/25	Thu 3/20/25																						
95	Architect Punch List Review - Area A	0 days	Thu 3/20/25	Thu 3/20/25																						
96	Air Balance - Area A	5 days	Fri 3/21/25	Thu 3/27/25																						
97	Architect Punch List Distributed - Area A	2 days	Fri 3/21/25	Mon 3/24/25																						
98	Architect Punch List Worked Off by Contractors - Area A	10 days	Tue 3/25/25	Mon 4/7/25																						
99	Final Clean after Punchlist worked off - Area A	5 days	Tue 4/8/25	Mon 4/14/25																						
100	Final Review by Architect - Area A	2 days	Tue 4/15/25	Wed 4/16/25																						
101	AREA B	241 days	Mon 6/17/24	Tue 5/27/25																						
102	Footers - Area B	23 days	Mon 6/17/24	Thu 7/18/24																						

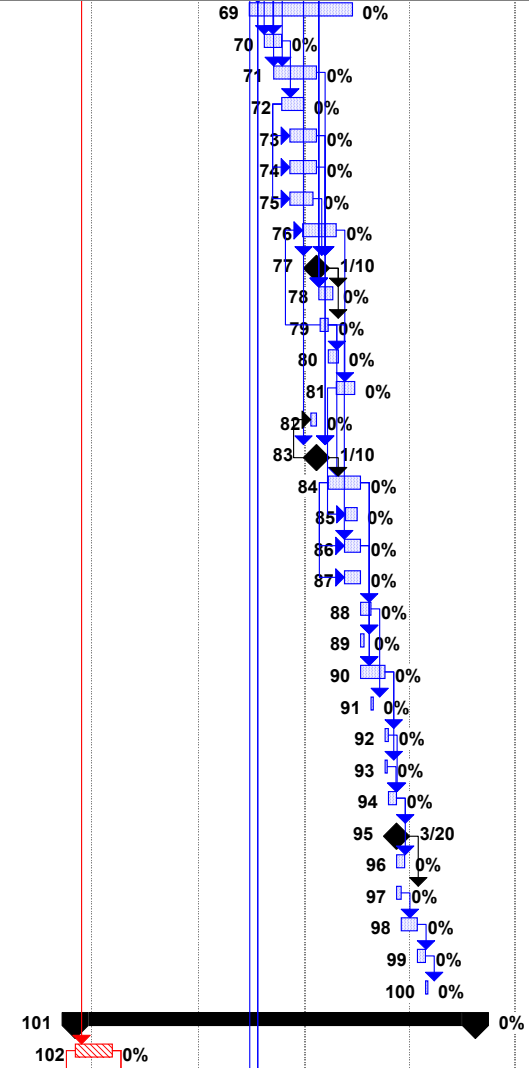

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
103	ICF Stem walls- Area B	7 days	Fri 6/28/24	Tue 7/9/24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
137	Electrical Systems/Devices - Area B	60 days	Fri 12/6/24	Mon 3/3/25																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										</

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task




Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec
171	Final Clean after Punchlist worked off - Area B	5 days	Fri 5/16/25	Thu 5/22/25								
172	Final Review by Architect - Area B	2 days	Fri 5/23/25	Tue 5/27/25								
173	AREA C	289 days	Fri 7/12/24	Thu 8/28/25								
174	Footers - Area C	28 days	Fri 7/12/24	Tue 8/20/24								
175	ICF Stem walls- Area C	10 days	Thu 7/25/24	Wed 8/7/24								
176	Underslab CMU - Area C	7 days	Mon 8/5/24	Tue 8/13/24								
177	Underslab Plumbing Rough in - Area C	25 days	Fri 8/9/24	Fri 9/13/24								
178	Stone Backfill non plumbing areas - Area C	3 days	Tue 9/3/24	Thu 9/5/24								
179	Underslab Electrical Rough in - Area C	17 days	Fri 9/6/24	Mon 9/30/24								
180	Stone Backfill at pumping areas - Area C	3 days	Thu 9/12/24	Mon 9/16/24								
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	Fri 9/20/24	Tue 9/24/24								
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	Wed 9/25/24	Wed 9/25/24								
183	Prep Slab - Pour #2 - Area C	3 days	Wed 9/25/24	Fri 9/27/24								
184	Hollow Metal Doorframes installation - Area C	3 days	Mon 9/30/24	Wed 10/2/24								
185	Slab Placement - Pour #2 - Area C	1 day	Mon 9/30/24	Mon 9/30/24								
186	Prep Slab - Pour #3 - Area C	3 days	Tue 10/1/24	Thu 10/3/24								
187	CMU Bearing Walls - Area C	55 days	Thu 10/3/24	Thu 12/19/24								
188	ICF Walls - Area C	35 days	Thu 10/3/24	Wed 11/20/24								
189	Plumbing Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
190	Electrical Wall Rough in - Area C	40 days	Thu 10/3/24	Wed 11/27/24								
191	Slab Placement - Pour #3 - Area C	1 day	Fri 10/4/24	Fri 10/4/24								
192	Steel Columns/Beams/Bent Plate - Area C	15 days	Thu 10/24/24	Wed 11/13/24								
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	Thu 11/7/24	Wed 11/20/24								
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	Fri 12/20/24	Wed 1/8/25								
195	Set Steel Joists - Area C	23 days	Fri 12/20/24	Thu 1/23/25								
196	Exterior Brick/Stone - Area C	40 days	Fri 12/20/24	Mon 2/17/25								
197	Install Ladders/Handrails Etc... - Area C	7 days	Fri 12/20/24	Tue 12/31/24								
198	Windows/Glazing/Caulking - Area C	12 days	Tue 1/21/25	Wed 2/5/25								
199	Roof Deck installation/inspection - Area C	10 days	Fri 1/24/25	Thu 2/6/25								
200	ICF Parapet Walls - Area C	7 days	Fri 1/24/25	Mon 2/3/25								
201	Electrical Rough-In - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	Fri 1/24/25	Thu 3/6/25								
203	Duct installation - Above Ceiling - Area C	25 days	Fri 1/24/25	Thu 2/27/25								
204	Prep Roof Concrete Slab - Gym - Area C	3 days	Fri 2/7/25	Tue 2/11/25								

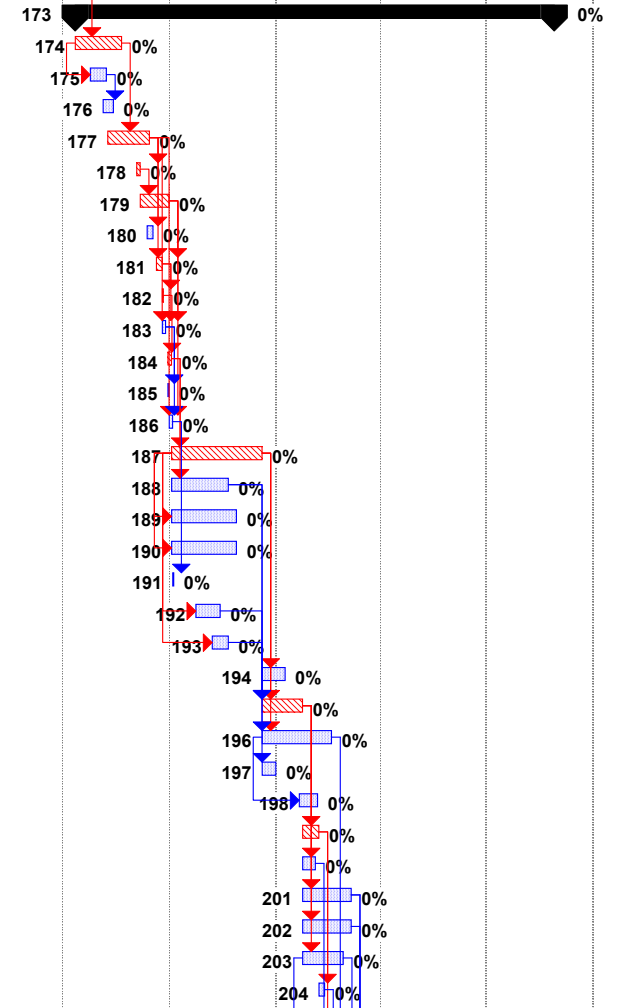

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024			Qtr 2, 2024			Qtr 3, 2024			Qtr 4, 2024			Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
205	Roof Wood Blocking - Area C	7 days	Fri 2/7/25	Mon 2/17/25																						
206	Pour Roof Concrete Slab - Gym - Area C	1 day	Wed 2/12/25	Wed 2/12/25																						
207	Sprinkler Rough-In - Above Ceiling - Area C	15 days	Fri 2/7/25	Thu 2/27/25																						
208	TPO Roof - Area C	20 days	Tue 2/18/25	Mon 3/17/25																						
209	Clean Brick - Area C	5 days	Tue 2/18/25	Mon 2/24/25																						
210	Block Filler - Area C	10 days	Tue 2/25/25	Mon 3/10/25																						
211	Brick Caulking - Area C	3 days	Tue 2/25/25	Thu 2/27/25																						
212	Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	Tue 3/11/25	Mon 4/14/25																						
213	Electrical Systems/Devices - Area C	60 days	Fri 3/7/25	Fri 5/30/25																						
214	Electrical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	Fri 3/7/25	Thu 4/3/25																						
216	Mechanical/Plumbing/Duct Insulation - Area C	15 days	Tue 3/18/25	Mon 4/7/25																						
217	Set Mechanical Equipment/Tie In - Area C	25 days	Tue 3/18/25	Mon 4/21/25																						
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	Tue 3/18/25	Mon 4/14/25																						
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	Wed 3/19/25	Thu 4/3/25																						
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	Mon 3/24/25	Fri 4/4/25																						
221	Install Light Fixtures - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	Fri 4/4/25	Thu 4/24/25																						
223	Primer/1st Coat of Paint - Walls - Area C	10 days	Tue 4/15/25	Mon 4/28/25																						
224	Kitchen Hood System - Kitchen - Area C	3 days	Fri 4/18/25	Tue 4/22/25																						
225	Set Cooler/Freezer - Kitchen - Area C	4 days	Fri 4/18/25	Wed 4/23/25																						
226	HVAC Controls - Area C	25 days	Tue 4/22/25	Tue 5/27/25																						
227	Ceiling Grid - Area C	12 days	Tue 4/29/25	Wed 5/14/25																						
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	Thu 4/24/25	Thu 4/24/25																						
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	Tue 4/29/25	Thu 5/1/25																						
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
231	Light Fixtures - Area C	15 days	Fri 5/2/25	Thu 5/22/25																						
232	Sprinkler Heads - Area C	12 days	Tue 5/6/25	Wed 5/21/25																						
233	Paint - Exposed Ceilings - Gym - Area C	10 days	Fri 5/2/25	Thu 5/15/25																						
234	Ceramic Tile - Area C	15 days	Mon 5/12/25	Mon 6/2/25																						
235	Epxoy Resin Floor - Area C	5 days	Mon 5/12/25	Fri 5/16/25																						
236	Aluminum Storefront Frames and Doors - Area C	10 days	Tue 5/13/25	Tue 5/27/25																						
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	Fri 5/16/25	Fri 5/30/25																						
238	Above Ceiling Punch - Engineer - Area C	0 days	Thu 5/22/25	Thu 5/22/25																						

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr 4, 2025															
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	Fri 5/23/25	Tue 6/3/25																							
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	Tue 5/27/25	Mon 6/2/25																							
241	Controlled Air - Area C	0 days	Tue 5/27/25	Tue 5/27/25																							
242	VCT and Base - Area C	20 days	Tue 6/3/25	Mon 6/30/25																							
243	Ceiling Tiles - Area C	7 days	Tue 6/3/25	Wed 6/11/25																							
244	Plumbing Fixtures - Area C	12 days	Tue 6/3/25	Wed 6/18/25																							
245	Epoxy Resin Floor - Kitchen - Area C	10 days	Tue 6/3/25	Mon 6/16/25																							
246	Install Basketball Goals - Gym - Area C	10 days	Mon 6/2/25	Fri 6/13/25																							
247	Install Scoreboard - Gym - Area C	3 days	Mon 6/2/25	Wed 6/4/25																							
248	Toilet Partitions and Accessories - Area C	8 days	Wed 6/11/25	Fri 6/20/25																							
249	Casework/Solid Surface Sills - Area C	10 days	Tue 6/17/25	Mon 6/30/25																							
250	Final Coat Paint - Walls - Area C	10 days	Tue 6/17/25	Mon 6/30/25																							
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym -	18 days	Mon 6/16/25	Thu 7/10/25																							
252	Kitchen Equipment - Kitchen - Area C	12 days	Tue 6/24/25	Thu 7/10/25																							
253	Display/Tack Boards - Area C	5 days	Tue 7/1/25	Tue 7/8/25																							
254	Door Frame Paint - 1 Coats - Area C	3 days	Tue 7/1/25	Thu 7/3/25																							
255	Doors & Hardware - Area C	15 days	Tue 7/1/25	Tue 7/22/25																							
256	Interior Signage - Area C	2 days	Wed 7/9/25	Thu 7/10/25																							
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	Wed 7/9/25	Tue 7/29/25																							
258	Overhead Coiling Doors - Kitchen - Area C	5 days	Fri 7/11/25	Thu 7/17/25																							
259	Install Bleachers - Area C - Gym - Area C	12 days	Fri 7/11/25	Mon 7/28/25																							
260	Sound Wall Panels - Gym - Area C	7 days	Fri 7/11/25	Mon 7/21/25																							
261	Install Athletic Equipment - Gym - Area C	3 days	Fri 7/11/25	Tue 7/15/25																							
262	Doorframe Paint - 2nd Coat - Area C	3 days	Wed 7/23/25	Fri 7/25/25																							
263	Install Door Glass - Area C	2 days	Wed 7/23/25	Thu 7/24/25																							
264	Pre-Clean before Architect Punchlist - Area C	5 days	Mon 7/28/25	Fri 8/1/25																							
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	Tue 7/29/25	Wed 8/6/25																							
266	Architect Punch List Review - Area C	0 days	Fri 8/1/25	Fri 8/1/25																							
267	Air Balance - Area C	5 days	Mon 8/4/25	Fri 8/8/25																							
268	Architect Punch List Distributed - Area C	2 days	Mon 8/4/25	Tue 8/5/25																							
269	Kitchen Hood Certificate - Area C	0 days	Tue 8/5/25	Tue 8/5/25																							
270	Architect Punch List Worked Off by Contractors - Area C	10 days	Wed 8/6/25	Tue 8/19/25																							
271	Final Clean after Punchlist worked off - Area C	5 days	Wed 8/20/25	Tue 8/26/25																							
272	Final Review by Architect - Area C	2 days	Wed 8/27/25	Thu 8/28/25																							

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical  Task  Milestone 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas

STANTON ELEMENTARY SCHOOL

ID	Task Name	Duration	Start	Finish	Qtr 1, 2024	Qtr 2, 2024	Qtr 3, 2024	Qtr 4, 2024	Qtr 1, 2025	Qtr 2, 2025	Qtr 3, 2025	Qtr
					Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct/Nov/Dec	Jan/Feb/Mar	Apr/May/Jun	Jul/Aug/Sep	Oct
273	Fine Grading/Topsoil Distribution	6 days	Tue 4/22/25	Tue 4/29/25								
274	Stone Base - Drives and Lots	10 days	Wed 4/30/25	Tue 5/13/25								
275	Exterior Lighting	25 days	Fri 5/16/25	Fri 6/20/25								
276	Concrete Curb and Gutters	12 days	Wed 5/14/25	Fri 5/30/25								
277	Site Concrete Walks	30 days	Mon 6/2/25	Mon 7/14/25								
278	Install Site Sign	10 days	Mon 6/16/25	Fri 6/27/25								
279	Install Flag Pole	2 days	Tue 7/8/25	Wed 7/9/25								
280	Chain Link Fence	3 days	Tue 7/15/25	Thu 7/17/25								
281	Install Canopies	15 days	Tue 7/15/25	Mon 8/4/25								
282	Seeding/Sod and Landscaping	20 days	Tue 7/15/25	Mon 8/11/25								
283	Exterior Paint/Caulk	10 days	Tue 7/15/25	Mon 7/28/25								
284	Paving/Striping/Wheel Stops	15 days	Tue 7/15/25	Mon 8/4/25								
285	Boiler Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
286	Sprinkler Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
287	Fire Alarm Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
288	Plumbing Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
289	Electrical Certificate	0 days	Tue 7/29/25	Tue 7/29/25								
290	Exterior Signage	3 days	Tue 8/5/25	Thu 8/7/25								
291	Architect Site Punch List Review - Site	0 days	Thu 8/7/25	Thu 8/7/25								
292	Kitchen Hood Certificate	0 days	Tue 8/5/25	Tue 8/5/25								
293	Occupancy Permit	0 days	Tue 8/5/25	Tue 8/5/25								
294	Substantial Completion	0 days	Thu 8/7/25	Thu 8/7/25								
295	Closeout and Owner Training	10 days	Fri 8/8/25	Thu 8/21/25								
296	Architect Site Punch List Distrubuted - Site	0 days	Mon 8/11/25	Mon 8/11/25								
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	Tue 8/12/25	Mon 8/25/25								
298	Final Site Review by Architect - Site	0 days	Mon 8/25/25	Mon 8/25/25								
299	Final Completion	0 days	Wed 9/3/25	Wed 9/3/25								

Stanton Elementary - REVISED FOR USACE REVIEW
Date: Fri 3/1/24 kd

Critical



Task



Milestone



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledge the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving, & Christmas



Daily Construction Report

With Labor Summary and Material
Thursday, April 11, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/11/2024

20.00
hours

66° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 19.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Cloudy	59%	7 mph	0 mph
08:53:00	64° F	Rain	70%	5 mph	0 mph
09:53:00	63° F	Rain	75%	6 mph	0 mph
10:53:00	64° F	Rain	80%	0 mph	0 mph
11:49:00	64° F	Thunderstorm	83%	5 mph	0 mph
12:30:00	62° F	Rain	93%	6 mph	0 mph
13:23:00	63° F	Rain	97%	0 mph	0 mph
14:15:00	66° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and offloaded storm structures.		5.00	20.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/11/2024

Michael Graf on 4/11/2024 07:58 AM

Lost production day (unsuitable soils), waiting on PR approval.

Michael Graf on 4/11/2024 08:07 AM



File
4/11/2024 8:07 AM
Michael Graf



File
4/11/2024 8:07 AM
Michael Graf

Michael Graf on 4/11/2024 12:26 PM



File
4/11/2024 12:26 PM
Michael Graf


Michael Graf on 4/11/2024 02:30 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, April 12, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/12/2024

0.00
hours

52° F
rain

1
notes

0
equipment

● Approved
status

Days Lost on Project: 20.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:33:00	48° F	Cloudy	86%	0 mph	0 mph
08:05:00	48° F	Cloudy	83%	10 mph	0 mph
08:31:00	49° F	Cloudy	74%	12 mph	0 mph
09:07:00	49° F	Cloudy	74%	12 mph	0 mph
09:53:00	49° F	Cloudy	74%	5 mph	0 mph
10:41:00	49° F	Cloudy	71%	9 mph	0 mph
11:22:00	50° F	Cloudy	68%	5 mph	0 mph
11:53:00	50° F	Cloudy	68%	7 mph	0 mph
12:53:00	52° F	Rain	63%	12 mph	0 mph
13:53:00	52° F	Rain	63%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 4/12/2024

Michael Graf on 4/12/2024 07:45 AM

Lost production day (unsuitable soils) waiting on PR approval.

Michael Graf on 4/12/2024 08:46 AM



File

4/12/2024 8:46 AM
Michael Graf



File

4/12/2024 8:46 AM
Michael Graf

Michael Graf on 4/12/2024 02:30 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, May 15, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 5/15/2024

20.00

hours

67° F

rain

1

notes

4

equipment

● Approved

status

Days Lost on Project: 23.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:19:00	60° F	Mist	96%	0 mph	0 mph
07:57:00	61° F	Mist	97%	3 mph	0 mph
08:44:00	61° F	Mist	93%	0 mph	0 mph
09:16:00	61° F	Cloudy	97%	0 mph	0 mph
09:53:00	63° F	Cloudy	90%	0 mph	0 mph
10:53:00	67° F	Cloudy	84%	3 mph	0 mph
11:40:00	67° F	Cloudy	76%	5 mph	0 mph
11:53:00	67° F	Cloudy	79%	0 mph	0 mph
12:53:00	68° F	Cloudy	76%	0 mph	0 mph
13:38:00	72° F	Cloudy	68%	0 mph	0 mph
13:53:00	71° F	Cloudy	68%	0 mph	0 mph
14:41:00	67° F	Rain	81%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING	Placing 57's around east side of building pad.		4.00	16.00 Hours	Approved
COMPANY (N/A)	Repairing entrance and lane with stone.				
SOLID GROUND CONSULTING (N/A)	Recommended not placing DGA due to rain.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	3.00	3.00
Roller	RISING SUN DEVELOP		1.00	3.00	3.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

Daily report for 5/15/2024

NOTES

Michael Graf on 5/15/2024 11:29 AM

Lost production due to rain, too wet to place DGA on building pad. Rising Sun was working east edge of building pad with 57 stone. Equipment was damaging the DGA already in place allowing rain water to saturate into the building pad.

Michael Graf on 5/15/2024 01:12 PM



File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf

File

5/15/2024 1:12 PM
Michael Graf


Michael Graf on 5/15/2024 02:59 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Friday, May 17, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/17/2024

31.00
hours

68° F
cloudy

1
notes

3
equipment

● Approved
status

Days Lost on Project: 24.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	63° F	Rain	93%	0 mph	0 mph
08:53:00	63° F	Rain	93%	0 mph	0 mph
09:42:00	63° F	Rain	97%	0 mph	0 mph
09:53:00	63° F	Rain	97%	0 mph	0 mph
10:53:00	66° F	Clear	90%	0 mph	0 mph
11:16:00	67° F	Clear	90%	0 mph	0 mph
11:53:00	67° F	Clear	90%	0 mph	0 mph
12:53:00	68° F	Cloudy	87%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Installing DGA on the building pad. Delivered and spread stone for material lay down area. Installed fabric on eastside of area C.		4.00	28.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Observing and testing moisture / compaction of DGA on the building pad.		1.00	3.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Roller	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED

NOTES

Daily report for 5/17/2024

Michael Graf on 5/17/2024 10:54 AM

Lost production day due to weather. Solid Ground shut down DGA install due to rain at 10:15am.



File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

File

5/17/2024 10:54 AM
Michael Graf

Michael Graf on 5/17/2024 01:04 PM



File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

File

5/17/2024 1:04 PM
Michael Graf

Michael Graf on 5/17/2024 01:36 PM



File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf

File

5/17/2024 1:36 PM
Michael Graf


Michael Graf on 5/17/2024 02:50 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

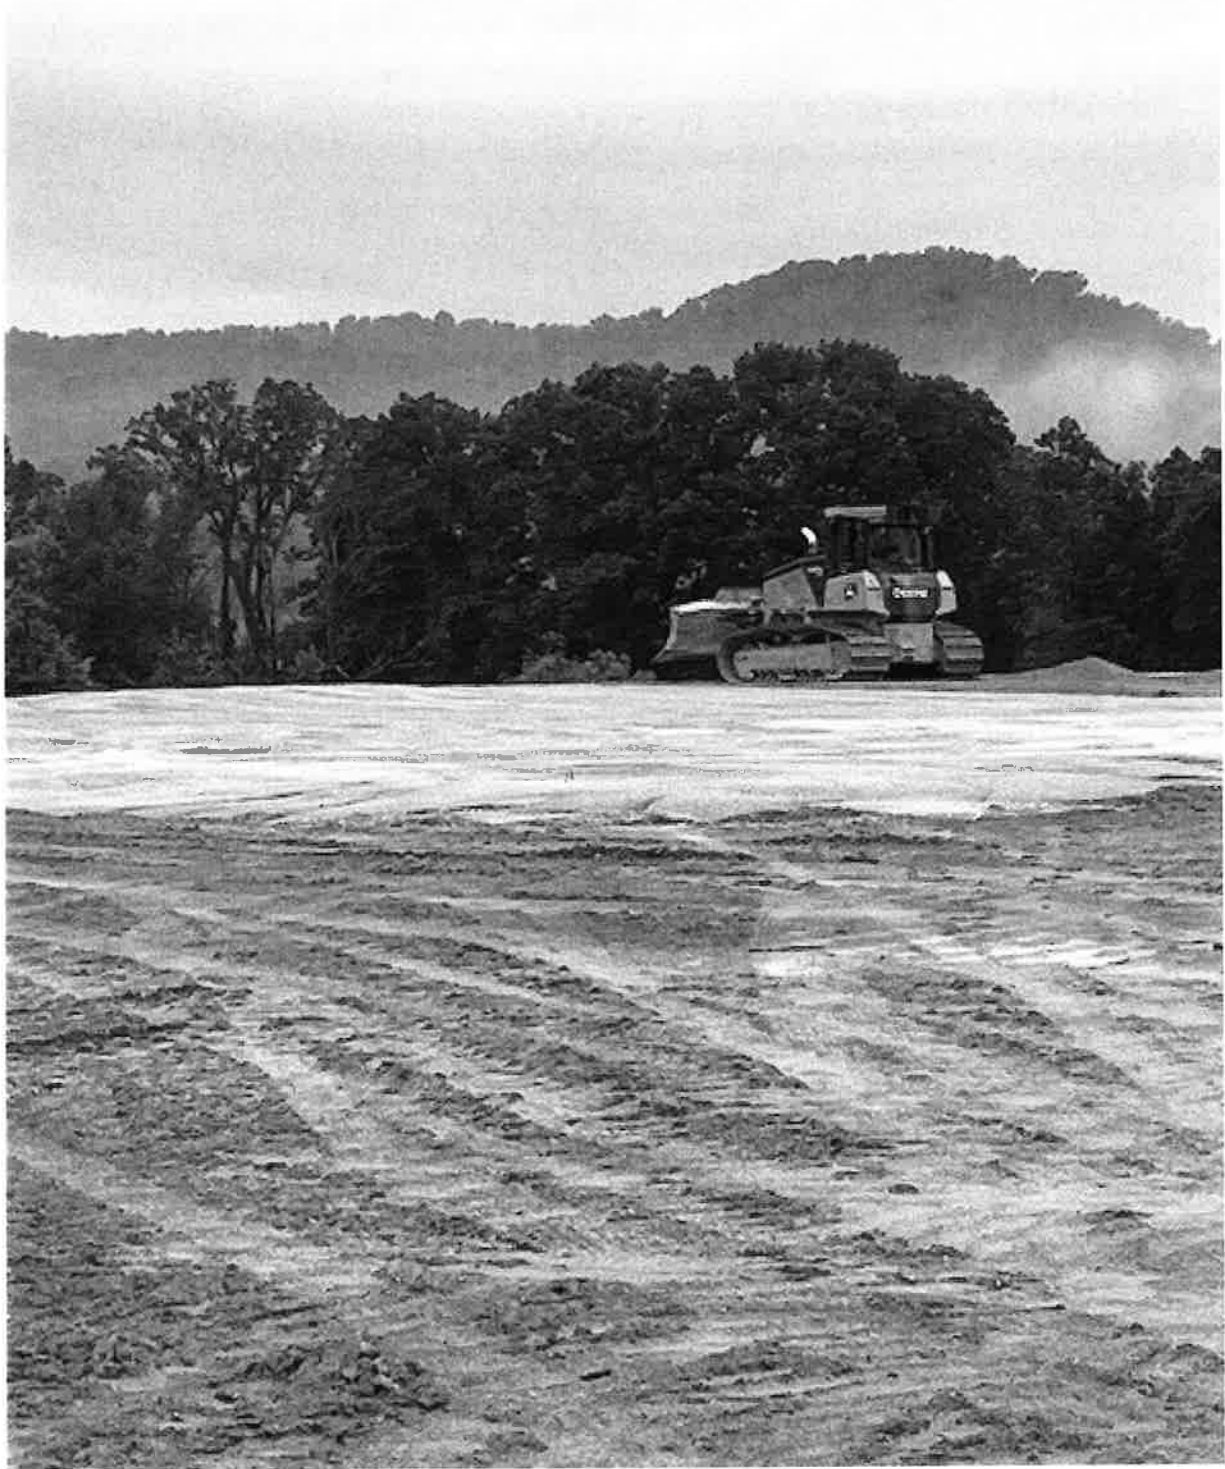



Daily Construction Report

With Labor Summary and Material
Thursday, May 23, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 5/23/2024

24.00
hours

72° F
clear

1
notes

1
equipment

● Approved
status

Days Lost on Project: 25.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	62° F	Partly Cloudy	93%	0 mph	0 mph
08:36:00	62° F	Mist	96%	0 mph	0 mph
09:24:00	63° F	Rain	93%	0 mph	0 mph
10:19:00	62° F	Thunderstorm	93%	5 mph	0 mph
11:11:00	63° F	Rain	93%	3 mph	0 mph
11:53:00	68° F	Rain	87%	0 mph	0 mph
12:17:00	67° F	Cloudy	87%	5 mph	0 mph
12:53:00	67° F	Clear	90%	5 mph	0 mph
13:53:00	72° F	Clear	82%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Delivered additional footer rebar from		6.00	24.00 Hours	Approved
DEVELOPING	MMI.				
COMPANY (N/A)	Installed jobsite signage.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 5/23/2024

Michael Graf on 5/23/2024 09:12 AM



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf



File

5/23/2024 9:11 AM
Michael Graf

Michael Graf on 5/23/2024 12:24 PM



File

5/23/2024 12:24 PM
Michael Graf



File

5/23/2024 12:24 PM
Michael Graf

Michael Graf on 5/23/2024 01:44 PM



File

5/23/2024 1:44 PM
Michael Graf

Michael Graf on 5/23/2024 02:54 PM

Lost production day due to rain.

Michael Graf on 5/23/2024 02:56 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 5/23/2024 02:57 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

Daily report for 5/24/2024

Michael Graf on 5/24/2024 11:23 AM

Lost production day due to overnight rain.

Michael Graf on 5/24/2024 12:01 PM



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf



File

5/24/2024 12:01 PM
Michael Graf

Michael Graf on 5/24/2024 02:52 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS







Daily Construction Report

With Labor Summary and Material
Wednesday, June 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/5/2024

68.00
hours

73° F
thunderstorm

1
notes

1
equipment

● Approved
status

Days Lost on Project: 27.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	69° F	Clear	93%	0 mph	0 mph
08:53:00	71° F	Clear	90%	3 mph	0 mph
09:53:00	73° F	Partly Cloudy	87%	6 mph	0 mph
10:37:00	72° F	Rain	93%	0 mph	0 mph
10:53:00	75° F	Cloudy	84%	3 mph	0 mph
11:56:00	74° F	Rain	91%	0 mph	0 mph
12:31:00	74° F	Thunderstorm	91%	5 mph	0 mph
13:22:00	74° F	Partly Cloudy	91%	0 mph	0 mph
14:14:00	74° F	Rain	94%	3 mph	0 mph
15:04:00	73° F	Thunderstorm	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		11.00	68.00 Hours	Approved
DEVELOPING	Equipment maintenance.				
COMPANY (N/A)	No work on building pad due to rain. Earthwork crew left at 11am.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 6/5/2024

Michael Graf on 6/5/2024 10:54 AM



Michael Graf on 6/5/2024 01:16 PM



Michael Graf on 6/5/2024 02:03 PM

Lost production day due to rain.

Michael Graf on 6/5/2024 02:14 PM




Michael Graf on 6/5/2024 03:29 PM



ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, June 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 6/6/2024

32.00
hours

81° F
clear

0
notes

0
equipment

● Approved
status

Days Lost on Project: 28.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	69° F	Cloudy	93%	0 mph	0 mph
08:20:00	70° F	Cloudy	90%	3 mph	0 mph
08:53:00	71° F	Cloudy	90%	0 mph	0 mph
09:36:00	73° F	Cloudy	84%	6 mph	0 mph
10:15:00	75° F	Cloudy	79%	5 mph	0 mph
11:12:00	76° F	Partly Cloudy	71%	8 mph	0 mph
11:53:00	77° F	Partly Cloudy	66%	12 mph	0 mph
12:53:00	79° F	Clear	60%	6 mph	0 mph
13:53:00	81° F	Clear	58%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN	Pre tying steel for footers.		4.00	32.00 Hours	Approved
DEVELOPING COMPANY (N/A)	Weed eating around entrance and fencing.				

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 6/6/2024

Michael Graf on 6/6/2024 10:12 AM



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf



File
6/6/2024 10:12 AM
Michael Graf

Michael Graf on 6/6/2024 03:03 PM



File
6/6/2024 3:03 PM
Michael Graf



File
6/6/2024 3:03 PM
Michael Graf

Michael Graf on 6/6/2024 03:05 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Friday, August 2, 2024

Stanton Elementary School (000743)

West College Avenue

Stanton, KY 40380

Daily report for 8/2/2024

80.00

hours

82° F

clear

2

notes

3

equipment

● Pending

status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	72° F	Clear	91%	0 mph	0 mph
08:53:00	73° F	Clear	90%	0 mph	0 mph
09:58:00	74° F	Rain	87%	7 mph	0 mph
10:29:00	73° F	Rain	90%	3 mph	0 mph
10:53:00	73° F	Rain	90%	0 mph	0 mph
11:28:00	71° F	Thunderstorm	93%	3 mph	0 mph
11:53:00	71° F	Clear	93%	3 mph	0 mph
12:53:00	76° F	Clear	85%	6 mph	0 mph
13:53:00	79° F	Clear	77%	6 mph	0 mph
14:53:00	80° F	Partly Cloudy	74%	0 mph	0 mph
15:53:00	82° F	Clear	77%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Grouting geothermal wells, 78 of 88 total.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up below slab CMU in classrooms 166, 165, 164, 162, 160. (Area B)		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough in in ICF stem walls in classrooms 166, 165, 164, 162. (Area B)		7.00	14.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Site grading by west entrance at front of property. Backfilling and compacting DGA in all rooms below mezzanine. (Area C)		5.00	10.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Dozer - D6	RISING SUN DEVELOP		1.00	2.00	2.00
Excavator	RISING SUN DEVELOP		1.00	2.00	2.00
Truck - Dump - Articulating 14ton 9-10yd,	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 8/2/2024

MATERIAL DELIVERED

NOTES

Daily report for 8/2/2024

Michael Graf on 8/2/2024 10:09 AM



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf



File
8/2/2024 10:09 AM
Michael Graf

Michael Graf on 8/2/2024 10:40 AM

Lost production day due to heavy rain, (Contractors left at 9:45AM)

Michael Graf on 8/2/2024 12:51 PM

Clark Energy power outage at 11:45AM, 500+ customers affected.

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

Michael Graf on 8/2/2024 05:09 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, August 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 8/16/2024

40.00
hours

72° F
mist

1
notes

0
equipment

● Approved
status

Days Lost on Project: 29.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	71° F	Rain	87%	0 mph	0 mph
08:42:00	70° F	Rain	93%	5 mph	0 mph
09:33:00	69° F	Rain	96%	0 mph	0 mph
10:19:00	71° F	Cloudy	93%	3 mph	0 mph
10:53:00	73° F	Partly Cloudy	90%	0 mph	0 mph
11:53:00	74° F	Cloudy	87%	0 mph	0 mph
12:45:00	71° F	Thunderstorm	96%	5 mph	0 mph
13:33:00	72° F	Mist	97%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	No work due to rain.		3.00	6.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	No work due to rain.		8.00	16.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	No work due to rain.		4.00	8.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	No work due to rain.		5.00	10.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 8/16/2024

Michael Graf on 8/16/2024 10:41 AM

Lost production day due to heavy rain.

Michael Graf on 8/16/2024 10:54 AM



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf



File

8/16/2024 10:54 AM
Michael Graf

Michael Graf on 8/16/2024 01:53 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, September 24, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 9/24/2024

158.00
hours

71° F
clear

1
notes

2
equipment

● Approved
status

Days Lost on Project: 30.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	67° F	Clear	93%	5 mph	0 mph
08:53:00	69° F	Clear	90%	3 mph	0 mph
09:53:00	70° F	Cloudy	87%	5 mph	0 mph
10:28:00	70° F	Thunderstorm	87%	3 mph	0 mph
11:20:00	67° F	Thunderstorm	93%	6 mph	0 mph
11:53:00	67° F	Rain	90%	0 mph	0 mph
12:53:00	69° F	Cloudy	87%	3 mph	0 mph
13:43:00	70° F	Mist	87%	0 mph	0 mph
14:29:00	71° F	Clear	90%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing below slab plumbing in 171 boys and 172 girls restrooms in (Area B).		5.00	10.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing and partition walls in administration area.		10.00	20.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-ins in masonry walls (Administration area).		5.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured ICF walls in (Area B) approximately 270 linear feet, 70 cubic yards.		12.00	96.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Installing ICF wall forms in (Area A). Testing and collecting concrete samples for ICF wall pour.		1.00	2.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

Daily report for 9/24/2024

NOTES

Michael Graf on 9/24/2024 09:50 AM

Contractors left at 9:30am due to heavy consistent rain.

Michael Graf on 9/24/2024 01:04 PM



File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

File

9/24/2024 1:04 PM
Michael Graf

Michael Graf on 9/24/2024 03:18 PM



File

Daily Report 2024...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, November 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/6/2024

195.00

hours

71° F

rain

2

notes

5

equipment

● Pending

status

Days Lost on Project: 32.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	68° F	Cloudy	63%	3 mph	0 mph
08:53:00	69° F	Cloudy	63%	5 mph	0 mph
09:53:00	71° F	Cloudy	61%	6 mph	0 mph
10:53:00	72° F	Cloudy	61%	3 mph	0 mph
11:53:00	74° F	Cloudy	60%	6 mph	0 mph
12:53:00	78° F	Clear	54%	7 mph	0 mph
13:53:00	75° F	Cloudy	62%	6 mph	0 mph
14:53:00	71° F	Rain	73%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing below slab plumb in (Area A)		5.00	30.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) cutting in roof drain pans in kitchen area		15.00	45.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up CMU bearing walls in North and West wing of (Area B)		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing below slab electrical in (Area A)		10.00	80.00 Hours	Approved
	(4) storm shelter remediation				
	(6) Wrecking ICF scaffold bracing and shoring (Area A)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	CENTRAL KENTUCKY		1.00	2.00	2.00
Fork Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	MASON STRUCTURE, I		1.00	2.00	2.00
Manlift - Scissor 15' -19'	MASON STRUCTURE, I		1.00	2.00	2.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

Daily report for 11/6/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 11/6/2024 11:20 AM

Lost production day. Masons left site at 10:30am due to rain.

Michael Graf on 11/6/2024 02:42 PM



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf



File
11/6/2024 2:42 PM
Michael Graf

Michael Graf on 11/6/2024 02:47 PM


CKSM left at 1pm due to rain.

Michael Graf on 11/6/2024 03:21 PM



File
Daily Report 2024....
Michael Graf

ASSIGNMENTS

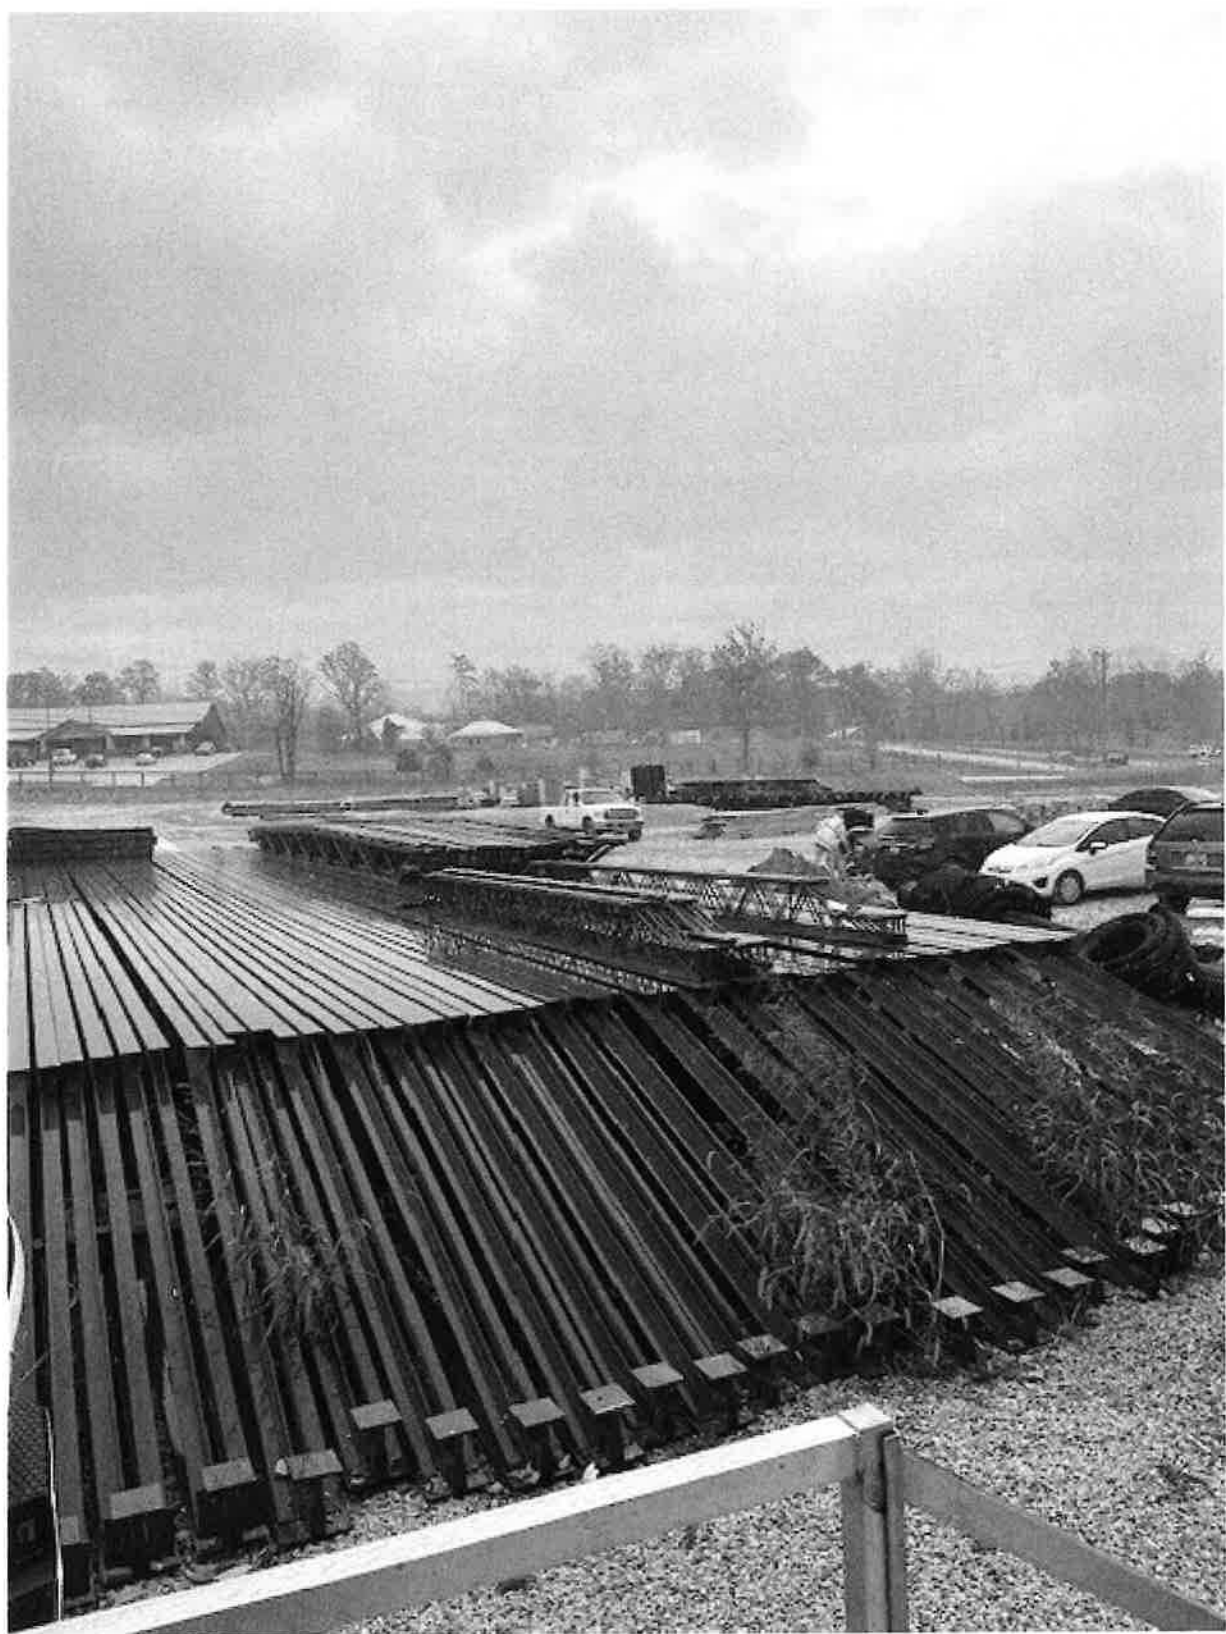



Daily Construction Report
With Labor Summary and Material
Thursday, November 7, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/7/2024

48.00
hours

67° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	64° F	Cloudy	90%	0 mph	0 mph
08:50:00	66° F	Cloudy	83%	0 mph	0 mph
09:43:00	65° F	Cloudy	90%	0 mph	0 mph
10:18:00	67° F	Cloudy	87%	0 mph	0 mph
10:53:00	66° F	Rain	90%	0 mph	0 mph
11:53:00	65° F	Cloudy	90%	0 mph	0 mph
12:53:00	66° F	Cloudy	87%	0 mph	0 mph
13:48:00	66° F	Cloudy	83%	0 mph	0 mph
13:53:00	66° F	Cloudy	84%	3 mph	0 mph
14:53:00	67° F	Cloudy	84%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RISING SUN DEVELOPING COMPANY (N/A)	Storm shelter remediation started at 11am after morning rain tapered off.		6.00	48.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Skid Steer	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Daily report for 11/7/2024

Michael Graf on 11/7/2024 08:28 AM

Lost production day, Masons left at 8am due to rain.

Steel contractors not onsite due to rain.



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf



File

11/7/2024 8:28 AM
Michael Graf


Michael Graf on 11/7/2024 03:05 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS

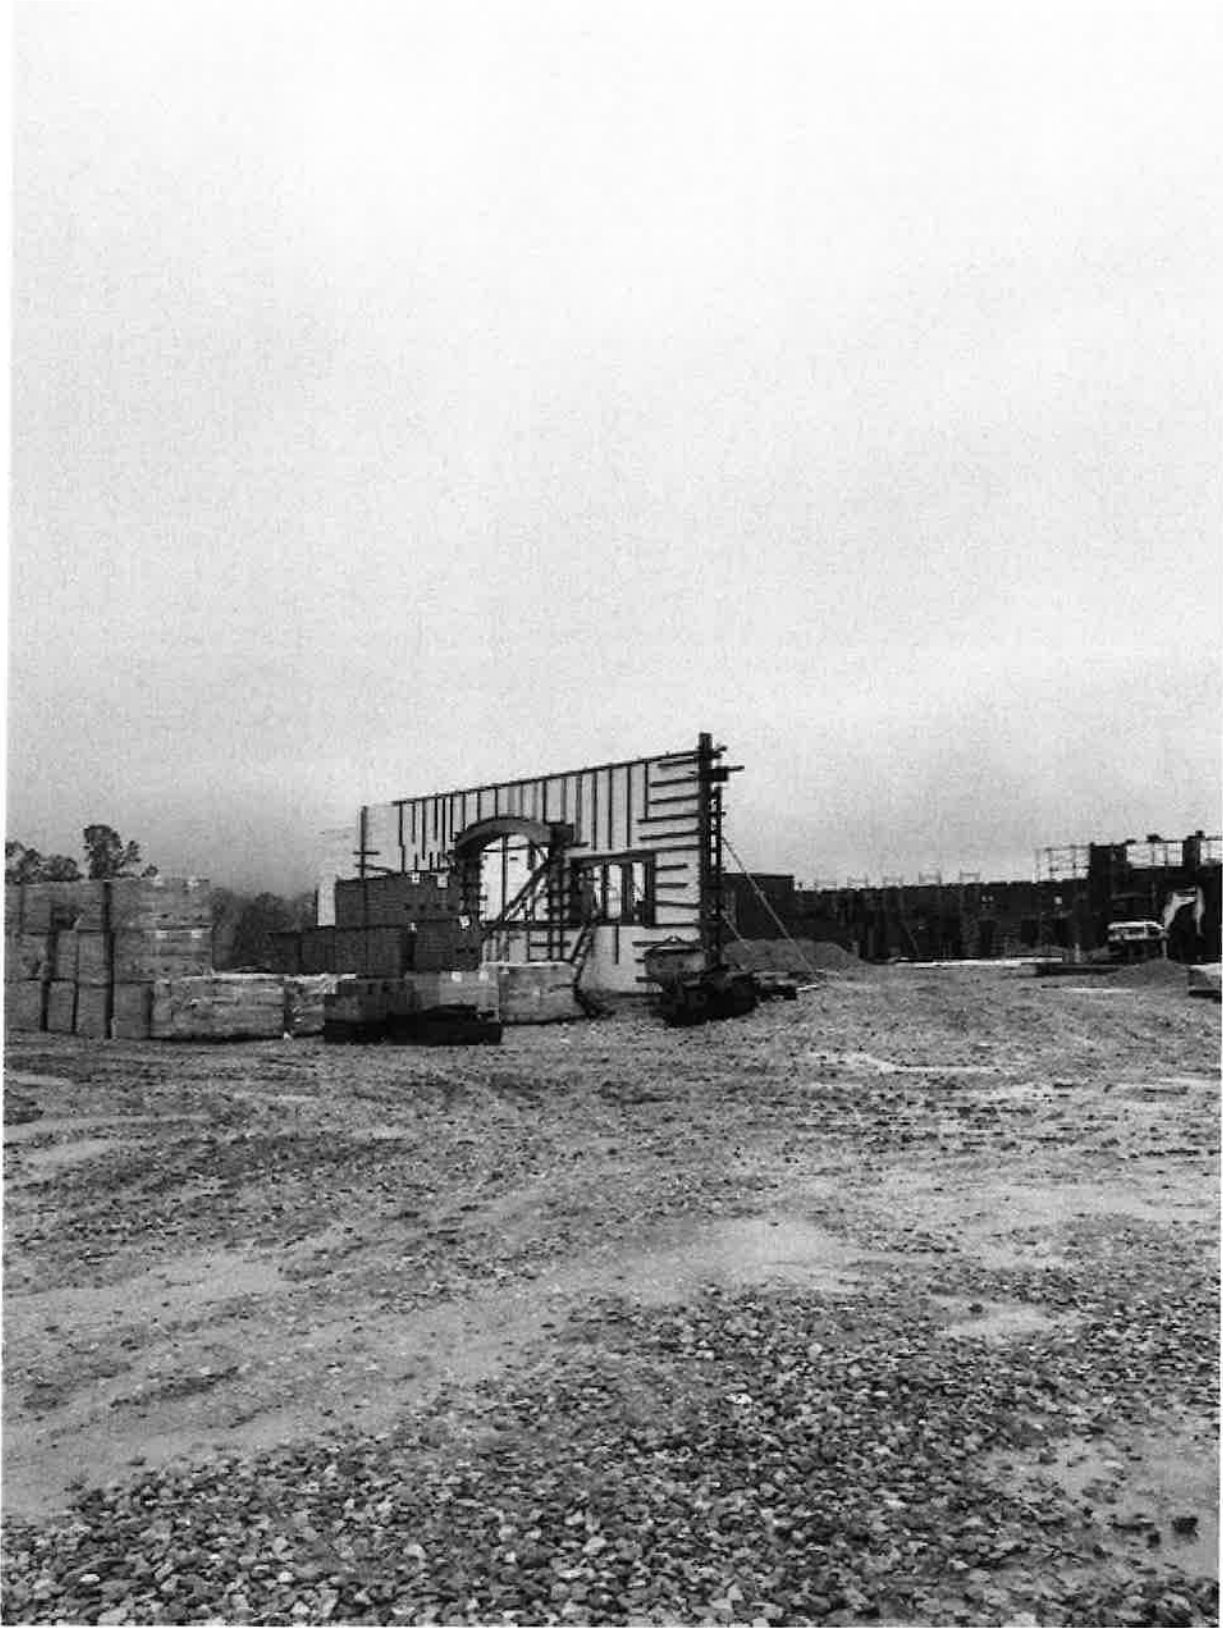



Daily Construction Report

With Labor Summary and Material
Thursday, November 14, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/14/2024

121.00
hours

52° F
rain

1
notes

2
equipment

● Approved
status

Days Lost on Project: 33.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:25:00	46° F	Rain	93%	0 mph	0 mph
08:21:00	46° F	Rain	96%	3 mph	0 mph
09:18:00	47° F	Cloudy	97%	6 mph	0 mph
10:09:00	48° F	Cloudy	93%	7 mph	0 mph
10:53:00	49° F	Cloudy	97%	3 mph	0 mph
11:29:00	49° F	Rain	93%	3 mph	0 mph
11:53:00	50° F	Rain	93%	5 mph	0 mph
12:45:00	51° F	Cloudy	92%	5 mph	0 mph
12:53:00	51° F	Rain	92%	3 mph	0 mph
13:53:00	52° F	Cloudy	93%	6 mph	0 mph
14:20:00	52° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CODELL CONSTRUCTION CO. (N/A)	Installing hangers and roof drain lines in cafeteria.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Left at 9am due to rain.		15.00	30.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Excavating remaining interior and exterior walls footers for (Area A) Poured last remaining interior and exterior footers (Area A) approximately 154 linear feet. 20 cubic yards Poured storm shelter remediation stem wall. Approximately 245 linear feet, 30 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Testing and collecting concrete sample for footers and storm shelter stem wall.		1.00	3.00 Hours	Approved

EQUIPMENT

Daily report for 11/14/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator - Mini	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00

MATERIAL DELIVERED

NOTES

Michael Graf on 11/14/2024 09:17 AM

Mason's left at 9am due to rain.

SLA not onsite due rain.

Michael Graf on 11/14/2024 09:52 AM


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf


File
11/14/2024 9:52 AM
Michael Graf

Michael Graf on 11/14/2024 01:40 PM


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf


File
11/14/2024 1:40 PM
Michael Graf

Michael Graf on 11/14/2024 03:15 PM


File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, November 21, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 11/21/2024

373.00
hours

32° F
snow

2
notes

8
equipment

● Approved
status

Days Lost on Project: 34.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	40° F	Cloudy	53%	9 mph	0 mph
08:53:00	40° F	Cloudy	55%	8 mph	0 mph
09:53:00	41° F	Cloudy	52%	5 mph	0 mph
10:53:00	41° F	Cloudy	51%	12 mph	0 mph
11:53:00	39° F	Rain	59%	13 mph	0 mph
12:47:00	34° F	Snow	86%	5 mph	0 mph
13:39:00	33° F	Snow	88%	0 mph	0 mph
14:31:00	32° F	Snow	88%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 0 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing roof drain lines in administration (Area C)		10.00	80.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	(5) Installing above ceiling ductwork in kitchen and cafeteria.		6.00	21.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing ISO and TPO over kitchen area.		2.00	8.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing dense glass on administration parapet walls.		15.00	120.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up bearing walls in west wing of (Area B).		7.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing structural embeds in clearstory bearing walls (Area B)		11.00	88.00 Hours	Approved
	(4) Installing above ceiling electrical in cafeteria (Area C).				
	(3) Installing electrical rough-in's in masonry walls in west wing of (Area B)				
	Relocating remaining HM frames and materials to gym to open up more laydown area for Dixie Roofing deliveries.				
	Installing gym / storm shelter ICF formwork and bracing.				

EQUIPMENT

Daily report for 11/21/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Manlift - Scissor 15' -19'	CENTRAL KENTUCKY S		2.00	8.00	16.00
Skid Steer	CENTRAL KENTUCKY S		1.00	6.00	6.00
Lull Lift	GRAYHAWK, LLC		1.00	3.00	3.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00
Manlift - Scissor 15' -19'	RISING SUN DEVELOP		3.00	2.00	6.00

MATERIAL DELIVERED**NOTES**


Michael Graf on 11/21/2024 11:32 AM

Dixie Roofing left at 11:30 due to heavy snow.

Michael Graf on 11/21/2024 12:45 PM

Gray Hawk left at 10:45 due to heavy snow.

Michael Graf on 11/21/2024 01:46 PM

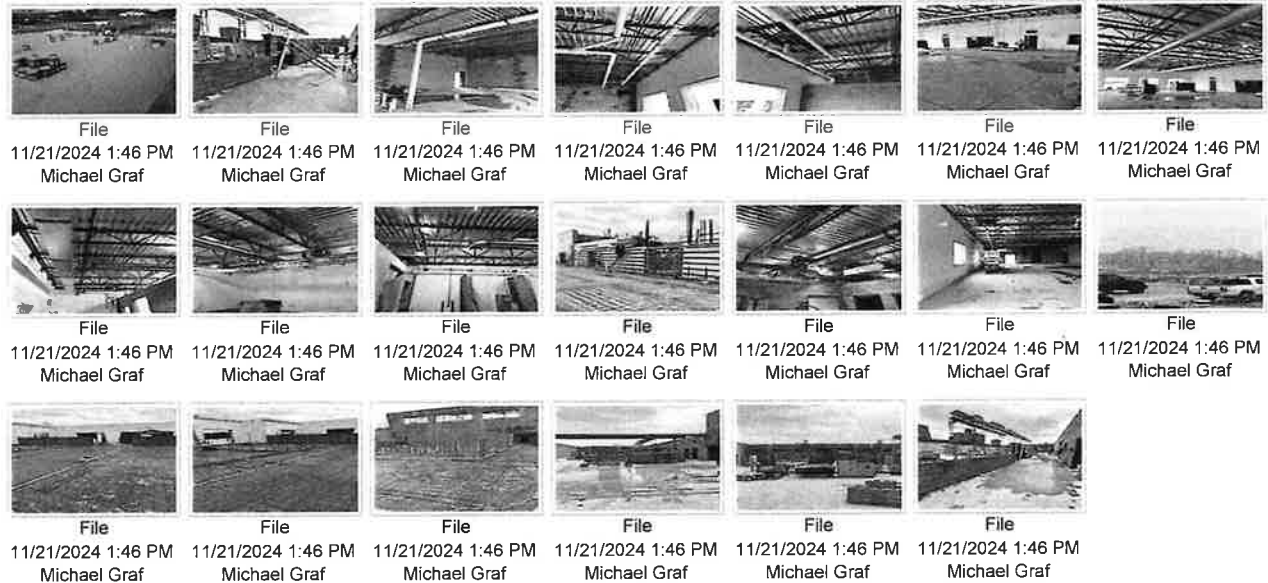

Michael Graf on 11/21/2024 03:16 PM







Daily Construction Report
With Labor Summary and Material
Thursday, December 5, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/5/2024

200.00
hours

26° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 37.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	44%	8 mph	0 mph
08:53:00	25° F	Clear	57%	6 mph	0 mph
09:53:00	24° F	Clear	50%	9 mph	0 mph
10:53:00	25° F	Cloudy	48%	14 mph	0 mph
11:53:00	25° F	Partly Cloudy	42%	6 mph	0 mph
12:53:00	25° F	Clear	44%	12 mph	0 mph
13:53:00	26° F	Clear	42%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Continuing to work on running duct and storm drain in the preschool area. Also dug out one of the storm drain mains out front to drain all the water out to prevent it from freezing and busting the pipes.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Continued to work on overhead power for preschool area.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Continued to prep the gymnasium walls to be poured and worked on shoring the wall.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 12/5/2024

Michael Graf on 6/6/2025 09:52 AM

Lost production due to freezing temperatures. No work performed by Dixie Roofing.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, December 6, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/6/2024

248.00
hours

31° F
clear

1
notes

0
equipment

● Approved
status

Days Lost on Project: 38.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:41:00	16° F	Cloudy	67%	0 mph	0 mph
08:01:00	16° F	Clear	67%	3 mph	0 mph
08:53:00	19° F	Clear	62%	0 mph	0 mph
09:53:00	22° F	Partly Cloudy	60%	0 mph	0 mph
10:53:00	26° F	Clear	52%	0 mph	0 mph
11:53:00	28° F	Clear	50%	6 mph	0 mph
12:53:00	31° F	Clear	47%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	They continued running duct and plumbing for preschool area and starting on the art room and surrounding classrooms.		8.00	64.00 Hours	Approved
CODELL CONSTRUCTION CO. (N/A)			1.00	8.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	They continued working on the roof of Area B.		6.00	48.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Today they started on running pipe for overhead power in the art room and the surrounding classrooms.		6.00	48.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Today they continued shoring up the exterior walls of the gymnasium to get ready for them to be poured.		10.00	80.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED


NOTES

Daily report for 12/6/2024

Michael Graf on 6/6/2025 09:54 AM

No work performed by Dixie Roofing due to freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Monday, December 16, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/16/2024

312.00

hours

60° F

cloudy

1

notes

6

equipment

● Approved

status

Days Lost on Project: 39.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:34:00	51° F	Cloudy	92%	6 mph	0 mph
08:26:00	51° F	Rain	96%	5 mph	0 mph
09:20:00	52° F	Mist	93%	5 mph	0 mph
09:53:00	52° F	Rain	97%	3 mph	0 mph
10:50:00	54° F	Rain	94%	7 mph	0 mph
11:40:00	54° F	Cloudy	97%	6 mph	0 mph
12:22:00	55° F	Cloudy	93%	9 mph	0 mph
12:53:00	57° F	Cloudy	87%	7 mph	0 mph
13:53:00	59° F	Cloudy	83%	3 mph	0 mph
14:53:00	60° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Resetting carriers in gang restrooms in storm shelter due to concrete slab settlement. (2) Installing above ceiling ductwork in kitchen and (Area B) (2) installing geothermal hydronic line hangers through administration corridor.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(4) Clean up (Area B) (3) Laying up partition chase walls in kitchen. (7) laying up partition chase walls (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(9) Installing above ceiling electrical rough in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Site crew installing storm lines left at 10:30 due to rain. (6) Offloaded and staged delivery of ICF forms for storm shelter. Pre-fabing additional tube steel bracing for ICF forms for storm shelter. Installing ICF form work at storm shelter.		9.00	72.00 Hours	Approved

Daily report for 12/16/2024

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		2.00	8.00	16.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	5.00	5.00
Scissor Lift	RISING SUN DEVELOP		2.00	4.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/16/2024

Michael Graf on 12/16/2024 01:58 PM



File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

File

12/16/2024 1:58 PM
Michael Graf

Michael Graf on 12/16/2024 02:01 PM



File

12/16/2024 2:01 PM
Michael Graf

File

12/16/2024 2:01 PM
Michael Graf

Michael Graf on 12/16/2024 03:37 PM

Lost production day due to rain.

Michael Graf on 12/16/2024 03:37 PM




File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material

Wednesday, December 18, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/18/2024

172.00
hours

54° F
rain

1
notes

4
equipment

● Approved
status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	48° F	Mist	96%	5 mph	0 mph
08:10:00	49° F	Rain	97%	0 mph	0 mph
09:01:00	50° F	Rain	93%	6 mph	0 mph
09:53:00	51° F	Thunderstorm	89%	0 mph	0 mph
10:41:00	52° F	Rain	97%	5 mph	0 mph
11:37:00	52° F	Rain	97%	5 mph	0 mph
12:19:00	52° F	Rain	97%	5 mph	0 mph
13:06:00	53° F	Rain	96%	7 mph	0 mph
13:53:00	54° F	Rain	93%	8 mph	0 mph
14:50:00	54° F	Rain	94%	14 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling ductwork (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing domestic water hangers in kitchen area.		3.00	24.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing perimeter gyp board at soffit location in cafeteria.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing above ceiling electrical in (area B)		6.00	12.00 Hours	Approved
	Installing ICF formwork at storm shelter.				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Scissor Lift	RISING SUN DEVELOP		1.00	2.00	2.00

Daily report for 12/18/2024

MATERIAL DELIVERED

NOTES

Michael Graf on 12/18/2024 02:52 PM
Lost production day. RSD left at 9am due to heavy rain.



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf



File
12/18/2024 2:52 PM
Michael Graf

Michael Graf on 12/18/2024 03:23 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Friday, December 20, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 12/20/2024

344.00

hours

31° F

freezing fog

0

notes

7

equipment

● Approved

status

Days Lost on Project: 40.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:08:00	37° F	Cloudy	82%	5 mph	0 mph
07:53:00	37° F	Cloudy	82%	3 mph	0 mph
08:34:00	37° F	Cloudy	82%	6 mph	0 mph
08:53:00	37° F	Cloudy	85%	5 mph	0 mph
09:53:00	38° F	Cloudy	82%	5 mph	0 mph
10:17:00	39° F	Cloudy	79%	6 mph	0 mph
10:53:00	39° F	Cloudy	82%	6 mph	0 mph
11:53:00	38° F	Rain	85%	8 mph	0 mph
12:53:00	37° F	Rain	92%	7 mph	0 mph
13:44:00	34° F	Snow	88%	8 mph	0 mph
14:40:00	31° F	Freezing Fog	92%	10 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Laying out and installing soffits in the cafeteria.		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up bearing walls in (Area A&B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(6) Installing above ceiling electrical in (Area B) (2) Installing electrical masonry wall rough-in's (Area A)		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(6) Installing bracing and shoring to ICF wall forms in storm shelter. (5) Installing storm lines (6) Installing HCP's at mezzanine.		17.00	136.00 Hours	Approved

EQUIPMENT

Daily report for 12/20/2024

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		1.00	7.00	7.00
Fork Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	7.00	21.00
Crane - Boom Truck 23 Ton	RISING SUN DEVELOP		1.00	6.00	6.00
Excavator	RISING SUN DEVELOP		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	7.00	7.00

MATERIAL DELIVERED**NOTES**

Daily report for 12/20/2024

Michael Graf on 12/20/2024 01:06 PM



File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

File

12/20/2024 1:06 PM
Michael Graf

Michael Graf on 12/20/2024 01:26 PM



File

12/20/2024 1:26 PM
Michael Graf

Michael Graf on 12/20/2024 03:11 PM



File

Daily Report 2024...
Michael Graf

Michael Graf on 12/30/2024 03:23 PM



File

Daily Report 2024...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 6, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 1/6/2025

0.00
hours

28° F
snow

1
notes

0
equipment

● Approved
status

Days Lost on Project: 43.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	33° F	Fog	92%	0 mph	0 mph
07:53:00	32° F	Fog	100%	0 mph	0 mph
08:44:00	32° F	Freezing Rain	96%	3 mph	0 mph
09:11:00	32° F	Fog	96%	3 mph	0 mph
10:02:00	32° F	Snow	92%	0 mph	0 mph
10:53:00	31° F	Cloudy	92%	9 mph	0 mph
11:30:00	31° F	Snow	92%	5 mph	0 mph
12:26:00	28° F	Snow	88%	12 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 1/6/2025 01:11 PM
Lost production day due to snow and ice.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Tuesday, January 7, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/7/2025

104.00

hours

21° F

cloudy

1

notes

2

equipment

● Approved

status

Days Lost on Project: 43.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	20° F	Cloudy	77%	0 mph	0 mph
08:53:00	20° F	Cloudy	84%	5 mph	0 mph
09:53:00	21° F	Cloudy	80%	0 mph	0 mph
10:19:00	21° F	Snow	80%	0 mph	0 mph
10:53:00	21° F	Snow	80%	5 mph	0 mph
11:53:00	21° F	Snow	84%	3 mph	0 mph
12:53:00	21° F	Snow	80%	3 mph	0 mph
13:48:00	21° F	Cloudy	79%	5 mph	0 mph
14:20:00	21° F	Cloudy	80%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing above ceiling domestic water lines in Kitchen area. (3) Installing carriers in 148 boys and 149 girls / Installing roof drain lines (Area B)		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing soffits in cafeteria.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00

MATERIAL DELIVERED

NOTES

Daily report for 1/7/2025

Michael Graf on 1/7/2025 12:34 PM

Lost production day due to snow, ice and freezing temperatures.

Michael Graf on 1/7/2025 03:09 PM



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf



File
1/7/2025 3:09 PM
Michael Graf

Michael Graf on 1/7/2025 03:10 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Wednesday, January 8, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/8/2025

136.00

hours

22° F

cloudy

0

notes

3

equipment

● Approved

status

Days Lost on Project: 44.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:50:00	19° F	Snow	86%	0 mph	0 mph
08:31:00	20° F	Snow	88%	0 mph	0 mph
09:24:00	20° F	Snow	88%	0 mph	0 mph
10:04:00	21° F	Snow	88%	0 mph	0 mph
10:53:00	22° F	Snow	92%	0 mph	0 mph
11:20:00	22° F	Snow	88%	3 mph	0 mph
12:09:00	22° F	Snow	88%	3 mph	0 mph
12:53:00	23° F	Cloudy	78%	3 mph	0 mph
13:34:00	22° F	Snow	84%	7 mph	0 mph
14:10:00	22° F	Snow	81%	6 mph	0 mph
14:53:00	22° F	Cloudy	81%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling domestic water lines in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing floor drains in mezzanine. Installing soffits in cafeteria. Staged delivery of gyp board and metal studs.		5.00	40.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Set propane tank for temporary heat. Sealing bar joist pockets in ICF exterior walls (Area C & B) Installing temp doors (plywood) at exterior door openings (Area C & B)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

Daily report for 1/8/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/8/2025 10:04 AM



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf



File
1/8/2025 10:04 AM
Michael Graf

Michael Graf on 1/8/2025 11:00 AM



File
1/8/2025 11:00 AM
Michael Graf

Michael Graf on 1/8/2025 01:48 PM



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf



File
1/8/2025 1:48 PM
Michael Graf

Michael Graf on 1/8/2025 03:18 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Thursday, January 9, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/9/2025

176.00
hours

24° F
cloudy

2
notes

3
equipment

● Approved
status

Days Lost on Project: 45.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:03:00	15° F	Cloudy	83%	3 mph	0 mph
07:53:00	16° F	Mist	84%	0 mph	0 mph
08:46:00	16° F	Mist	84%	3 mph	0 mph
09:09:00	16° F	Partly Cloudy	84%	3 mph	0 mph
09:53:00	17° F	Cloudy	80%	3 mph	0 mph
10:38:00	18° F	Cloudy	77%	3 mph	0 mph
11:33:00	18° F	Partly Cloudy	80%	3 mph	0 mph
12:04:00	22° F	Cloudy	81%	0 mph	0 mph
12:53:00	21° F	Cloudy	77%	0 mph	0 mph
13:42:00	22° F	Cloudy	77%	5 mph	0 mph
13:53:00	21° F	Cloudy	77%	0 mph	0 mph
14:53:00	24° F	Cloudy	71%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing floor drain penetrations in mezzanine.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling domestic water lines in kitchen.		5.00	40.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Installing soffits in cafeteria and kitchen.		4.00	32.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Laying up brick veneer on north facade of cafeteria. ****(Utilizing tarps, heaters and concrete blankets)****		5.00	40.00 Hours	Approved
	Sealing bar joist pockets in (Area C)				
	Building temporary doors and enclosures (Area C & B)				

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	5.00	5.00

Daily report for 1/9/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/9/2025 02:59 PM



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf



File
1/9/2025 2:59 PM
Michael Graf

Michael Graf on 1/9/2025 03:24 PM

Lost Production Day due to weather.

Michael Graf on 1/9/2025 03:25 PM


Hardy Gas delivered 800 gallons of propane.


Michael Graf on 1/9/2025 03:25 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

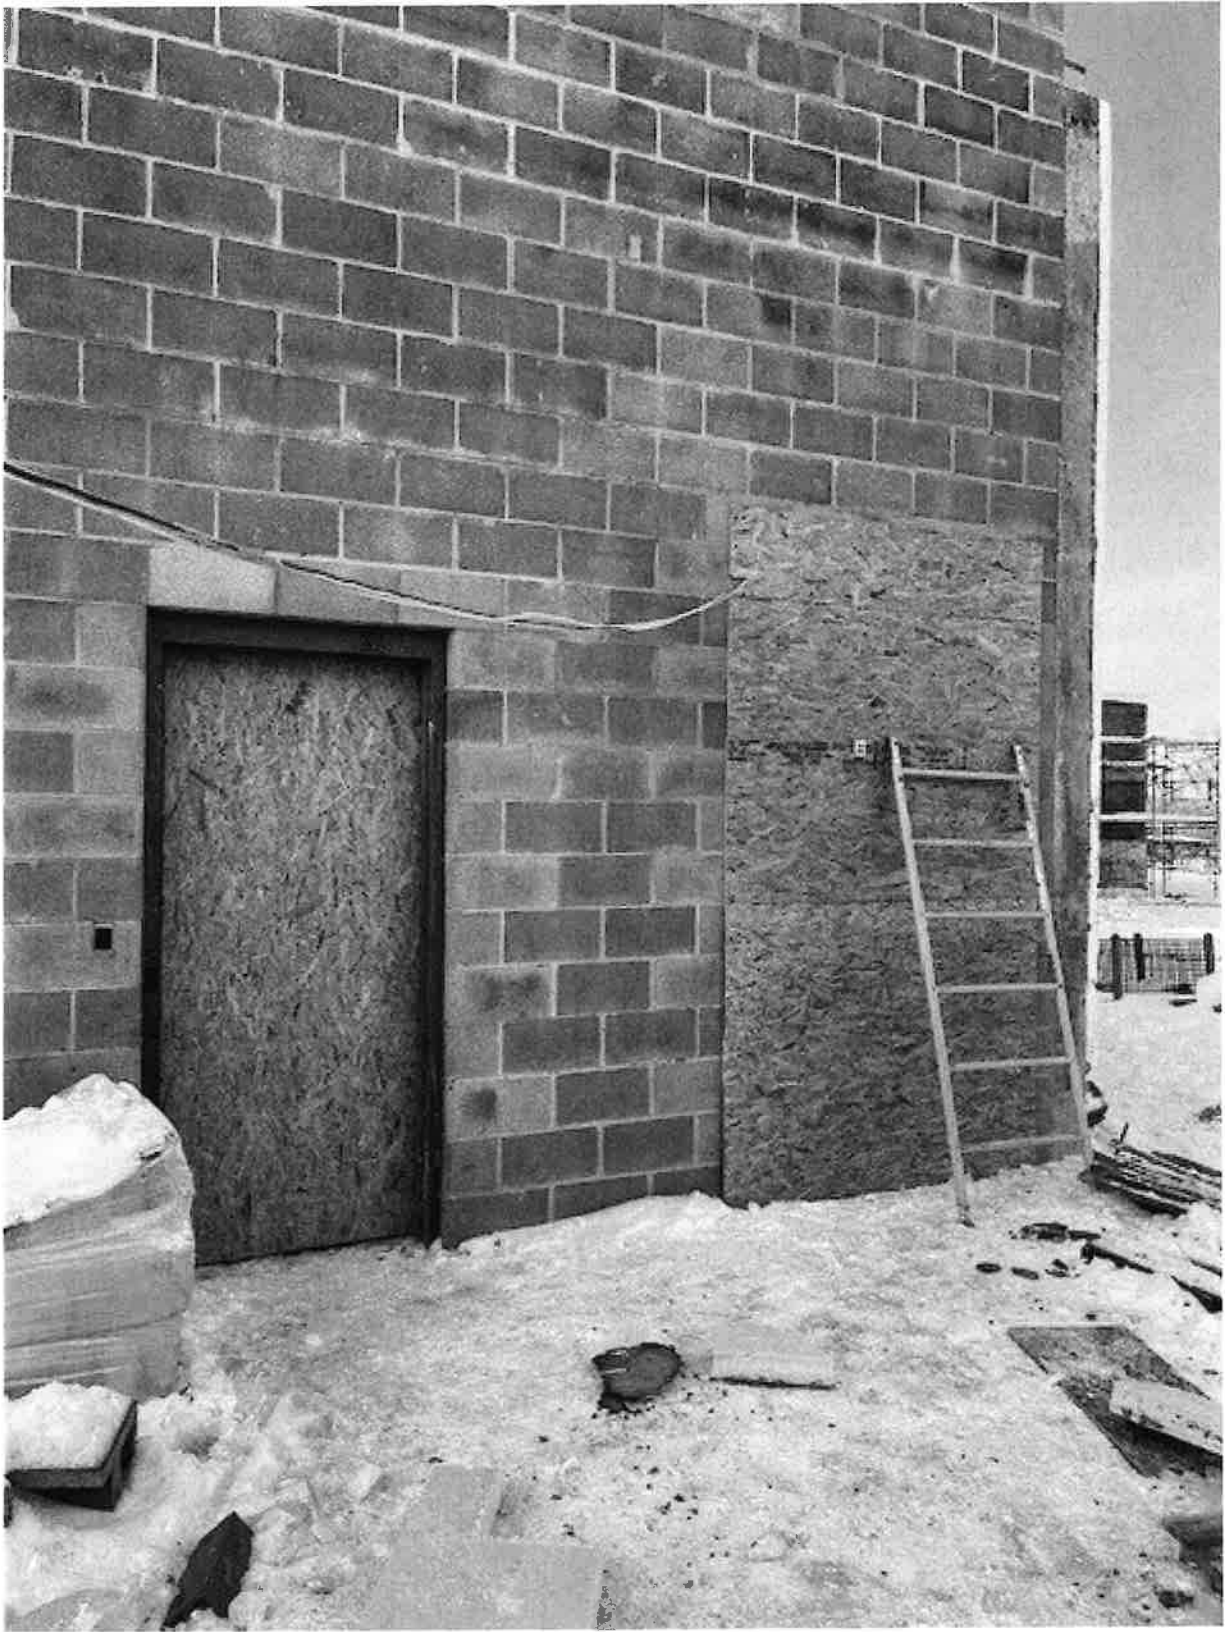



Daily Construction Report

With Labor Summary and Material
Friday, January 10, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/10/2025

174.00
hours

25° F
snow

1
notes

3
equipment

● Approved
status

Days Lost on Project: 46.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	17° F	Partly Cloudy	83%	0 mph	0 mph
08:53:00	18° F	Cloudy	84%	0 mph	0 mph
09:53:00	20° F	Cloudy	84%	0 mph	0 mph
10:53:00	22° F	Cloudy	84%	0 mph	0 mph
11:53:00	23° F	Cloudy	84%	3 mph	0 mph
12:53:00	24° F	Cloudy	81%	0 mph	0 mph
13:40:00	25° F	Snow	81%	0 mph	0 mph
14:32:00	25° F	Snow	88%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in kitchen area.		6.00	36.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Hanging gyp board in cafeteria. (3) Installing soffits in kitchen		7.00	42.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria.		8.00	56.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Sealing ICF bar joist pockets throughout the building. (Interior and exterior) (2) installing temp doors throughout building.		5.00	40.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		2.00	7.00	14.00
Scissor Lift	GRAYHAWK, LLC		3.00	7.00	21.00
Lull Lift	MASON STRUCTURE, I		1.00	7.00	7.00

MATERIAL DELIVERED

Daily report for 1/10/2025

NOTES

Michael Graf on 1/10/2025 12:43 PM



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf



File

1/10/2025 12:43 PM
Michael Graf

Michael Graf on 1/10/2025 02:58 PM



File

Daily Report 2025...
Michael Graf

Michael Graf on 1/10/2025 02:59 PM

Lost production day due to weather.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, January 13, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/13/2025

336.00
hours

40° F
cloudy

1
notes

5
equipment

● Approved
status

Days Lost on Project: 47.00

Days Lost on this Month: 8.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	35° F	Cloudy	69%	5 mph	0 mph
08:53:00	35° F	Cloudy	72%	3 mph	0 mph
09:53:00	36° F	Cloudy	73%	3 mph	0 mph
10:53:00	37° F	Cloudy	70%	3 mph	0 mph
11:53:00	38° F	Cloudy	67%	5 mph	0 mph
12:53:00	38° F	Cloudy	64%	6 mph	0 mph
13:39:00	39° F	Cloudy	62%	7 mph	0 mph
13:53:00	39° F	Cloudy	62%	0 mph	0 mph
14:53:00	40° F	Cloudy	57%	9 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling ductwork in (Area C). Installing tank regulator and connecting propane lines to temporary heating units.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Installing soffits in kitchen area. (3) Hanging gyp board in cafeteria. (2) Installing metal stud partition walls in Administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on North facade of cafeteria and kitchen.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing above ceiling whips in (Area C) (5) Installing above ceiling electrical rough-in's in (Area B)		10.00	80.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF form work over mezzanine in storm shelter.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/13/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/13/2025 02:54 PM

File
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael GrafFile
1/13/2025 2:54 PM
Michael Graf

Michael Graf on 1/13/2025 02:58 PM

Lost production day due to ice and snow on roof decking and bar joists.

Michael Graf on 1/13/2025 03:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 14, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/14/2025

352.00

hours

37° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 48.00

Days Lost on this Month: 9.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	15° F	Clear	73%	5 mph	0 mph
08:53:00	17° F	Clear	67%	5 mph	0 mph
09:53:00	20° F	Clear	59%	6 mph	0 mph
10:53:00	25° F	Clear	50%	6 mph	0 mph
11:53:00	28° F	Clear	44%	8 mph	0 mph
12:53:00	32° F	Clear	43%	6 mph	0 mph
13:53:00	35° F	Clear	39%	8 mph	0 mph
14:53:00	37° F	Cloudy	40%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling duct work (Area B)		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Installing above ceiling domestic water lines in kitchen area. (2) Installing soffits in kitchen. (2) Hanging gyp board in kitchen and cafeteria. (2) Framing metal stud partition walls in administration area.		6.00	48.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(12) Laying up brick veneer on North elevation of Administration area. (2) Rubbing out walls in west wing of (Area B)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing above ceiling whips in (Area B) Pulling wire and homeruns in kitchen / cafeteria and North wing of (Area B).		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Installing ICF formwork in storm shelter at mezzanine. (4) Job site maintenance, burning trees and brush from site demolition.		9.00	72.00 Hours	Approved

EQUIPMENT

Daily report for 1/14/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		2.00	8.00	16.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	8.00	16.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/14/2025 02:49 PM



File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

File

1/14/2025 2:49 PM
Michael Graf

Michael Graf on 1/14/2025 02:52 PM

Lost production day, Steel and roofing contractor unable to work due to ice and freezing temperatures.


Michael Graf on 1/14/2025 03:13 PM



File

Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Wednesday, January 15, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/15/2025

272.00

hours

26° F

clear

1

notes

4

equipment

● Approved

status

Days Lost on Project: 49.00

Days Lost on this Month: 10.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Clear	76%	0 mph	0 mph
08:53:00	13° F	Clear	77%	0 mph	0 mph
09:53:00	16° F	Clear	64%	0 mph	0 mph
10:53:00	19° F	Clear	56%	0 mph	0 mph
11:53:00	21° F	Clear	54%	3 mph	0 mph
12:53:00	23° F	Clear	50%	0 mph	0 mph
13:53:00	24° F	Clear	43%	0 mph	0 mph
14:53:00	26° F	Clear	46%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing above ceiling domestic water lines in the kitchen area.		7.00	56.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Installing above ceiling ductwork in (Area B) Hanging gyp board in kitchen and cafeteria. Framing metal stud partition walls in administration area.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and homeruns in cafeteria, kitchen and (Area B) Installing above ceiling whips (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Heavy equipment maintenance. (5) Installing wood blocking at parapet walls, insulating decking flutes in administration (Area B).		9.00	72.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

Daily report for 1/15/2025

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/15/2025 10:58 AM



File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf

File

1/15/2025 10:58 AM
Michael Graf


File

1/15/2025 10:58 AM
Michael Graf

Michael Graf on 1/15/2025 03:19 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/15/2025 03:19 PM



File

Daily Report 2025....
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Thursday, January 16, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/16/2025

384.00
hours

45° F
clear

1
notes

7
equipment

● Approved
status

Days Lost on Project: 50.00

Days Lost on this Month: 11.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	31° F	Cloudy	61%	7 mph	0 mph
08:53:00	32° F	Cloudy	63%	9 mph	0 mph
09:53:00	34° F	Cloudy	64%	6 mph	0 mph
10:53:00	38° F	Partly Cloudy	57%	10 mph	0 mph
11:53:00	39° F	Clear	55%	8 mph	0 mph
12:53:00	41° F	Clear	52%	13 mph	0 mph
13:53:00	43° F	Clear	51%	8 mph	0 mph
14:53:00	45° F	Clear	49%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing above ceiling domestic water lines in the kitchen area.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing above ceiling duct work in the North wing (Area B) (2) Hanging drywall in kitchen and cafeteria. (2) Laying out metal stud partition walls in North wing of (Area B). (3) Framing metal stud partition walls administration area.		7.00	56.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A)		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) Pulling wire and home runs in kitchen and cafeteria. (3) Pulling wire and home runs in North wing of (Area B) (3) Installing electrical rough-in's in CMU bearing walls (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing storm lines from building into structure MH-7A. (6) Installing and bracing ICF formwork in storm shelter.		10.00	80.00 Hours	Approved

Daily report for 1/16/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Excavator	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/16/2025 02:27 PM



Michael Graf on 1/16/2025 03:16 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/16/2025 03:19 PM

Lost production day due to Ice and snow.

ASSIGNMENTS





Daily Construction Report
With Labor Summary and Material
Friday, January 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/17/2025

443.00
hours

48° F
clear

0
notes

8
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 12.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	28° F	Clear	85%	0 mph	0 mph
08:53:00	30° F	Clear	85%	3 mph	0 mph
09:53:00	32° F	Clear	78%	6 mph	0 mph
10:53:00	36° F	Clear	69%	5 mph	0 mph
11:53:00	40° F	Clear	59%	3 mph	0 mph
12:53:00	43° F	Clear	51%	5 mph	0 mph
13:53:00	46° F	Clear	42%	5 mph	0 mph
14:53:00	48° F	Clear	37%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/17/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing Domestic water lines in the kitchen area. Installing above ceiling hanger and ductwork in the North and West wings of (Area B).		8.00	64.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Installing ISO and TPO over north side of administration area.		6.00	48.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Framing metal stud partition walls in the administration area. (4) Hanging drywall the kitchen and cafeteria areas.		9.00	72.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up CMU bearing walls in (Area A) Grouting bearing walls. Approximately 7 cubic yards.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(3) installing electrical rough-in's in masonry walls (Area A) (2) Installing electrical rough-in's in metal stud partition walls in administration area. (2) Pulling wire in the kitchen and cafeteria area (2) Pulling wire and home runs in North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing ICF formwork and bracing in storm shelter area. Installed curb inlet 4D.		9.00	72.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Inspecting steel decking in west wing of (Area B) Testing grout samples.		1.00	3.00 Hours	Approved


EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY SHEET METAL, INC		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Fork Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Lull Lift	MASON STRUCTURE, INC		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Crane - Boom Truck 10 Ton	RISING SUN DEVELOPING COMPANY		1.00	5.00	5.00
Excavator	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOPING COMPANY		1.00	8.00	8.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/17/2025

Michael Graf on 1/17/2025 01:02 PM



File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

File

1/17/2025 1:02 PM
Michael Graf

Michael Graf on 1/17/2025 02:50 PM



File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf

File

1/17/2025 2:50 PM
Michael Graf


Michael Graf on 1/17/2025 03:18 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS

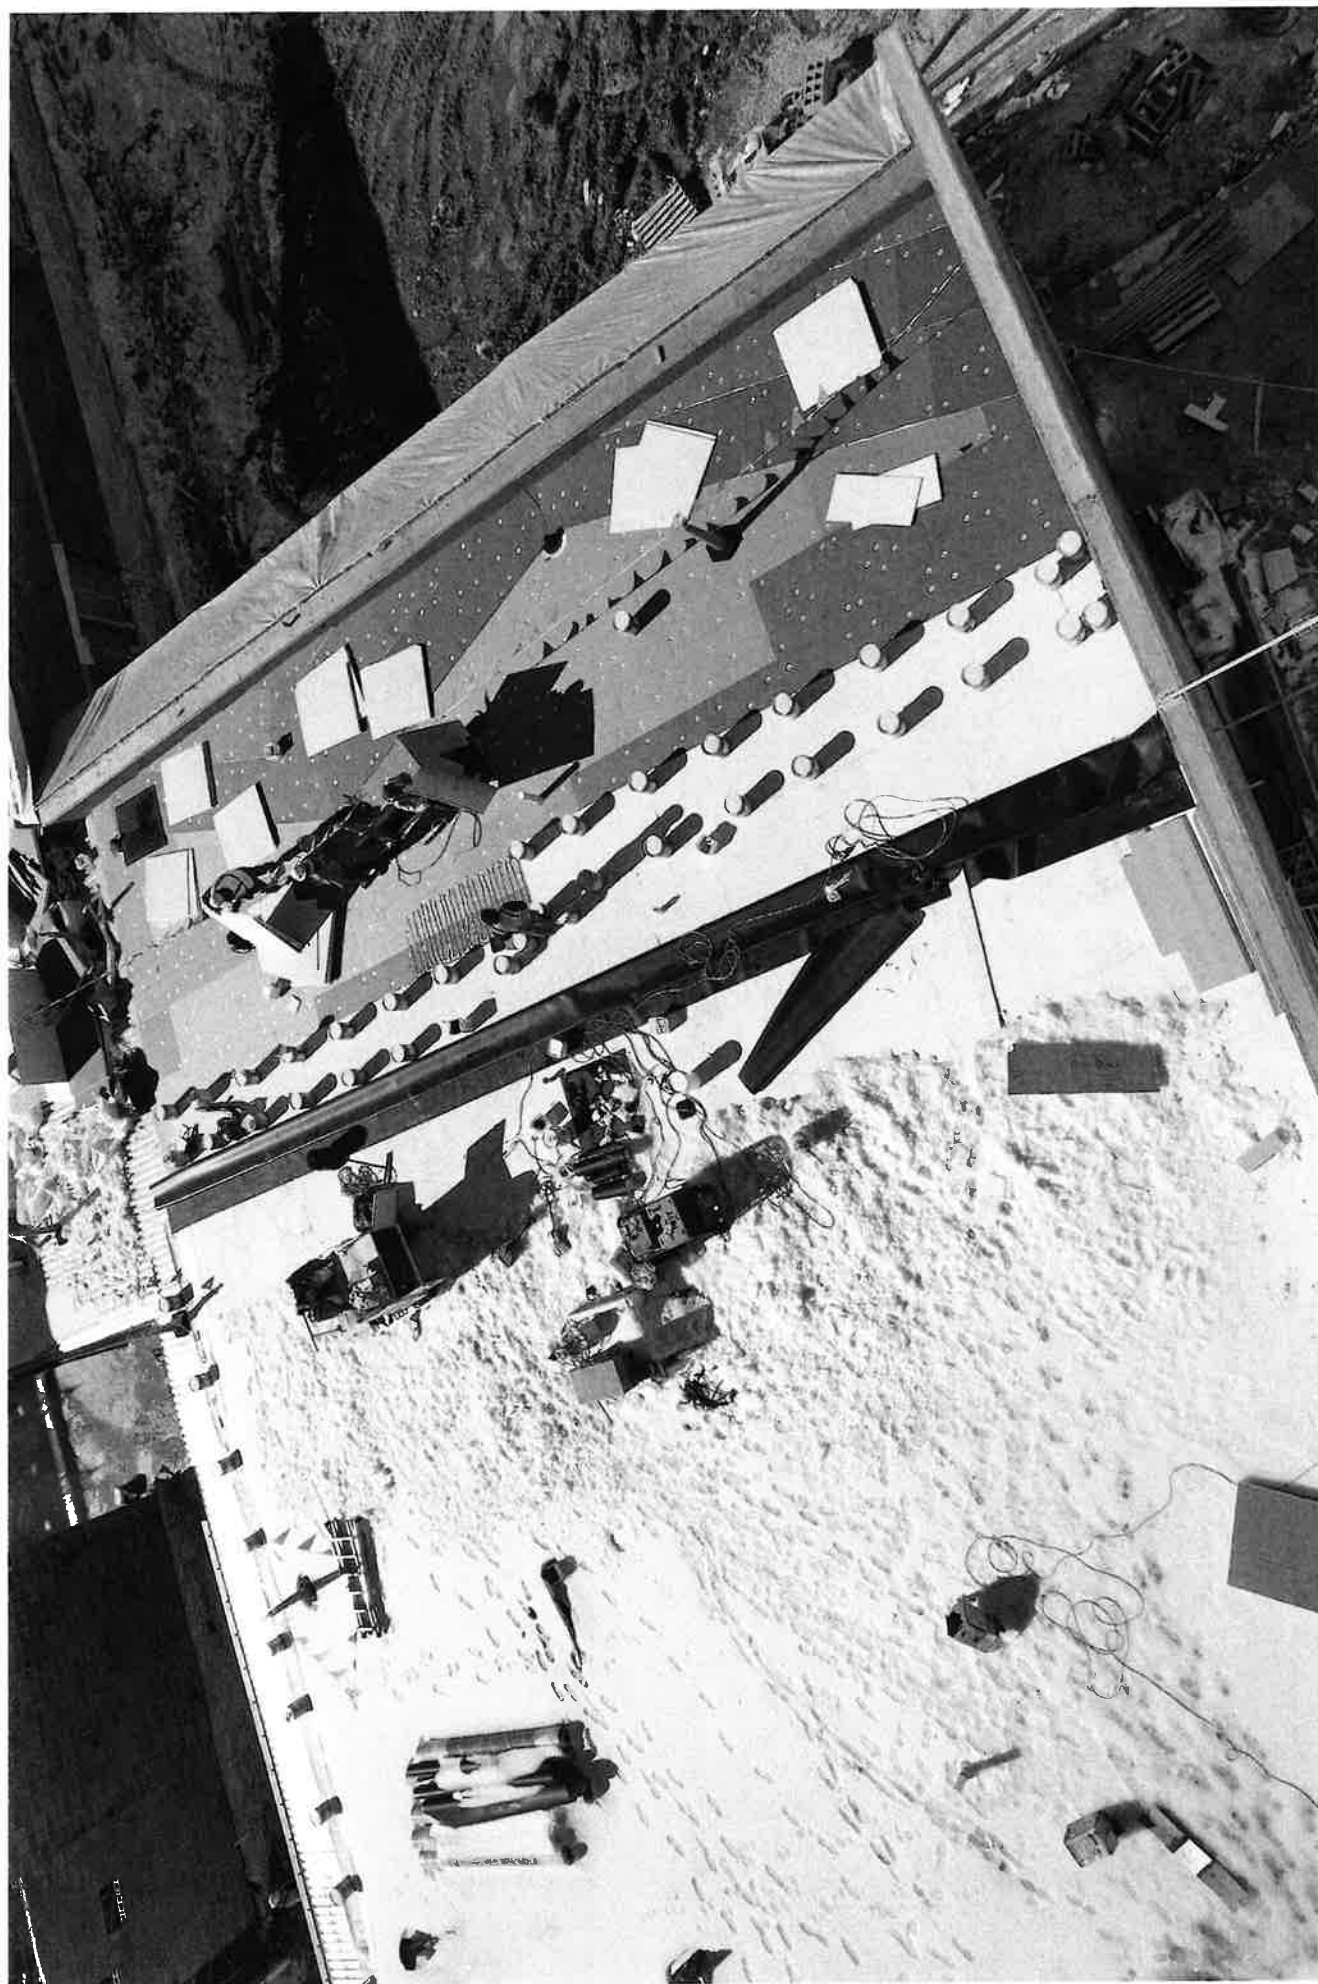



Daily Construction Report

With Labor Summary and Material
Monday, January 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/20/2025

264.00
hours

13° F
clear

1
notes

4
equipment

● Approved
status

Days Lost on Project: 52.00

Days Lost on this Month: 13.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	3° F	Partly Cloudy	76%	6 mph	0 mph
08:08:00	3° F	Cloudy	76%	5 mph	0 mph
08:53:00	4° F	Partly Cloudy	72%	0 mph	0 mph
09:53:00	5° F	Partly Cloudy	65%	3 mph	0 mph
10:00:00	6° F	Cloudy	66%	3 mph	0 mph
10:53:00	6° F	Cloudy	66%	0 mph	0 mph
11:53:00	9° F	Snow	66%	6 mph	0 mph
12:53:00	8° F	Cloudy	66%	3 mph	0 mph
13:05:00	12° F	Partly Cloudy	61%	0 mph	0 mph
13:53:00	11° F	Clear	60%	6 mph	0 mph
14:53:00	13° F	Clear	55%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(5) Installing geothermal hydronic lines in (area C) (4) Insulating domestic water lines in kitchen area. (2) Installing above ceiling ductwork in North wing of (Area B)		11.00	88.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in kitchen and cafeteria. (2) Topping out masonry walls in kitchen area. (3) Framing metal stud partition walls in administration and pre-school areas.		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in the kitchen, cafeteria, Administration areas.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building clean-up		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 1/20/2025 01:04 PM

Lost production day due to freezing temperatures.

Michael Graf on 1/20/2025 01:54 PM

File
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael GrafFile
1/20/2025 1:54 PM
Michael Graf

Michael Graf on 1/20/2025 03:29 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**





Daily Construction Report

With Labor Summary and Material
Tuesday, January 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/21/2025

280.00
hours

17° F
haze

1
notes

4
equipment

● Approved
status

Days Lost on Project: 53.00

Days Lost on this Month: 14.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	8° F	Cloudy	72%	3 mph	0 mph
08:53:00	9° F	Cloudy	72%	0 mph	0 mph
09:53:00	11° F	Cloudy	70%	0 mph	0 mph
10:53:00	14° F	Cloudy	55%	3 mph	0 mph
11:53:00	14° F	Cloudy	58%	0 mph	0 mph
12:53:00	16° F	Cloudy	51%	8 mph	0 mph
13:53:00	17° F	Cloudy	58%	8 mph	0 mph
14:53:00	17° F	Haze	67%	6 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Installing Above ceiling domestic water in Administration area. (2) Installing geothermal hydronic lines in Pre-school area. (4) Installing above ceiling ductwork in North wing of (Area B).		9.00	72.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(6) Framing metal stud partition walls in administration and pre-school areas. (3) Finishing drywall in kitchen and cafeteria (3) Topping out walls in kitchen area.		12.00	96.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Pulling wire and home runs in kitchen and cafeteria areas. (4) Installing above ceiling electrical in administration area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Setting HM door frames in Administration area. (2) Clean-up.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY :		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/21/2025 09:49 AM



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf



File
1/21/2025 9:49 AM
Michael Graf

Michael Graf on 1/21/2025 01:07 PM

Held monthly progress meeting with owner, design team and contractors.

Michael Graf on 1/21/2025 04:00 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, January 22, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/22/2025

312.00
hours

23° F
clear

2
notes

4
equipment

● Approved
status

Days Lost on Project: 54.00

Days Lost on this Month: 15.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	1° F	Clear	75%	3 mph	0 mph
08:53:00	4° F	Clear	80%	0 mph	0 mph
09:53:00	6° F	Clear	66%	0 mph	0 mph
10:53:00	10° F	Clear	69%	3 mph	0 mph
11:53:00	14° F	Clear	61%	0 mph	0 mph
12:53:00	18° F	Clear	47%	5 mph	0 mph
13:53:00	22° F	Clear	43%	5 mph	0 mph
14:53:00	23° F	Clear	38%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating roof drain lines in kitchen and cafeteria areas. (3) Installing geothermal hydronic lines in pre-school area. (4) Installing kitchen equipment hoods in kitchen. (5) Installing above ceiling ductwork in administration area.		15.00	120.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(5) Finishing drywall in kitchen and cafeteria areas. (6) Framing metal stud partition walls in administration and pre-school areas.		11.00	88.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Pulling wire and home runs in kitchen, cafeteria and administration areas.		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Building and site clean-up. Setting HM frames in administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

Daily report for 1/22/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED

NOTES

Michael Graf on 1/22/2025 08:53 AM
Atlas onsite to field measure for casework in kitchen, administration and preschool areas.

Michael Graf on 1/22/2025 02:12 PM
Lost production day due to Ice and freezing temperatures.

Michael Graf on 1/22/2025 02:29 PM



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf



File
1/22/2025 2:29 PM
Michael Graf

Michael Graf on 1/22/2025 03:19 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS

Daily report for 1/23/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Insulating above ceiling roof leader lines. (4) Installing geothermal hydronic lines in the pre-school area. (4) Installing kitchen equipment hoods (2) Installing plumbing rough ins in metal stud partition walls in administration and pre-school areas.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in the kitchen and cafeteria areas. (6) Framing metal stud partition walls in the administration and pre-school areas. (2) Framing up metal stud partition walls in Art room (Area B) (1) Cleanup		13.00	104.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up exterior brick on north facade of (Area C).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(5) Installing electrical rough in's in metal stud partition walls in administration and pre-school areas, (4) Pulling home runs and wire in kitchen, cafeteria and North wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Poured final lift on ICF storm shelter walls. Approximately 150 cubic yards.		6.00	48.00 Hours	Approved
SOLID GROUND CONSULTING (N/A)	Collecting and testing concrete samples from ICF stem wall pour.		1.00	4.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		4.00	8.00	32.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Lull Lift	MASON STRUCTURE, I		1.00	6.00	6.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Concrete Pump 110'	RISING SUN DEVELOP		1.00	6.00	6.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/23/2025

Michael Graf on 1/23/2025 02:27 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/23/2025 02:44 PM

						
File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf
						
File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf
						
File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	File 1/23/2025 2:44 PM Michael Graf	

Michael Graf on 1/23/2025 03:17 PM



File
Daily Report 2025...
Michael Graf

Michael Graf on 1/23/2025 03:37 PM



File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Friday, January 24, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/24/2025

368.00
hours

29° F
cloudy

1
notes

0
equipment

☒ Approved
status

Days Lost on Project: 56.00

Days Lost on this Month: 17.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	23° F	Cloudy	81%	6 mph	0 mph
08:53:00	22° F	Cloudy	77%	6 mph	0 mph
09:06:00	22° F	Cloudy	74%	5 mph	0 mph
09:53:00	23° F	Cloudy	74%	5 mph	0 mph
10:53:00	24° F	Cloudy	71%	3 mph	0 mph
11:43:00	24° F	Cloudy	74%	3 mph	0 mph
12:29:00	26° F	Cloudy	68%	5 mph	0 mph
12:53:00	27° F	Cloudy	66%	3 mph	0 mph
13:53:00	29° F	Cloudy	61%	7 mph	0 mph
14:53:00	29° F	Cloudy	56%	0 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/24/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Installing geothermal hydronic lines (Area C) (3) Installing domestic water lines in Administration and pr-school areas. (3) Installing kitchen equipment hoods in kitchen.		8.00	64.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(4) Finishing drywall in kitchen and cafeteria. (9) Framing up metal stud partition walls and soffits in administration, pre-school and North wing of (Area B).		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick on west facade of cafeteria and north facade of pre-school wing.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. Pulling wire and home runs in North wing of (Area B) and kitchen area.		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Installing wood blocking in partition walls in administration and pre-school areas. Installing HM frames in the administration area.		5.00	40.00 Hours	Approved

EQUIPMENT

MATERIAL DELIVERED

NOTES

Daily report for 1/24/2025

Michael Graf on 1/24/2025 01:57 PM

Lost production day due to freezing temperatures and ice.

Michael Graf on 1/24/2025 01:59 PM

File
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael GrafFile
1/24/2025 1:59 PM
Michael Graf


Michael Graf on 1/24/2025 03:18 PM

File
1/24/2025 3:18 PM
Michael GrafFile
1/24/2025 3:18 PM
Michael Graf

Michael Graf on 1/24/2025 03:18 PM

File
Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, January 31, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 1/31/2025

448.00

hours

54° F

cloudy

2

notes

6

equipment

● Approved

status

Days Lost on Project: 57.00

Days Lost on this Month: 18.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:38:00	53° F	Rain	93%	6 mph	0 mph
07:53:00	54° F	Rain	90%	13 mph	0 mph
08:53:00	55° F	Rain	93%	9 mph	0 mph
09:34:00	55° F	Rain	93%	10 mph	0 mph
09:53:00	56° F	Rain	90%	12 mph	0 mph
10:53:00	57° F	Rain	89%	12 mph	0 mph
11:53:00	58° F	Rain	87%	12 mph	0 mph
12:53:00	57° F	Rain	87%	7 mph	0 mph
13:53:00	56° F	Rain	87%	9 mph	0 mph
14:50:00	54° F	Cloudy	94%	7 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 1/31/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Setting carriers in west wing rest rooms (Area B) (4) Insulating domestic water lines in kitchen area. (4) Installing above ceiling ductwork in West wing of (Area B)		11.00	88.00 Hours	Approved
DIXIE ROOFING, INC. (N/A)	Staging delivery of roofing insulation. Investigating major roof leaks throughout the administration and pre-school areas.		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(2) Final sanding of drywall in kitchen and cafeteria. (4) Framing up metal stud partition walls and soffits in North wing (Area B) (4) Hanging drywall on exterior ICF walls and interior soffits.		10.00	80.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up restroom partition walls in west wing of (Area B).		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(2) Installing electrical rough-in's in metal stud partition walls in administration and pre-school areas. (4) Installing electrical rough-in's in masonry walls in west wing od (Area B) (3) Installing above ceiling electrical in West Wing of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Equipment maintenance. (5) Wrecking bracing and shoring from storm shelter ICF walls.		7.00	56.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Daily report for 1/31/2025

Michael Graf on 1/31/2025 12:32 PM

Lost production day due rain. (No work performed by Dixie Roofing or SLA)

Michael Graf on 1/31/2025 12:48 PM



File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

File

1/31/2025 12:48 PM
Michael Graf

Michael Graf on 1/31/2025 01:01 PM

Expansion foam applied to admin, and pre-school decking in an effort to keep rainwater diverted.



File

1/31/2025 1:01 PM
Michael Graf

File

1/31/2025 1:01 PM
Michael Graf

Michael Graf on 1/31/2025 03:21 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Tuesday, February 11, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/11/2025

32.00
hours

32° F
mist

1
notes

1
equipment

● Approved
status

Days Lost on Project: 58.00

Days Lost on this Month: 6.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:30:00	29° F	Snow	96%	6 mph	0 mph
08:05:00	29° F	Snow	96%	5 mph	0 mph
08:53:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:12:00	30° F	Freezing Rain	96%	3 mph	0 mph
09:53:00	31° F	Freezing Rain	96%	3 mph	0 mph
10:32:00	31° F	Freezing Rain	96%	5 mph	0 mph
11:13:00	31° F	Freezing Rain	100%	6 mph	0 mph
12:01:00	32° F	Freezing Rain	96%	3 mph	0 mph
12:53:00	32° F	Mist	96%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
RIMAR ELECTRIC, LLC (N/A)	Pulling wire in administration area. Running conduit in (Area A)		4.00	32.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	RIMAR ELECTRIC, LLC		2.00	4.00	8.00

MATERIAL DELIVERED

NOTES

Daily report for 2/11/2025

Michael Graf on 2/11/2025 01:10 PM

Lost production day due to heavy snow.

Michael Graf on 2/11/2025 01:17 PM



File

Daily Report 2025...
Michael Graf

ASSIGNMENTS



Daily Construction Report
With Labor Summary and Material
Wednesday, February 12, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/12/2025

376.00
hours

39° F
mist

1
notes

6
equipment

● Approved
status

Days Lost on Project: 59.00

Days Lost on this Month: 7.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	33° F	Fog	96%	3 mph	0 mph
08:35:00	33° F	Fog	96%	6 mph	0 mph
09:28:00	33° F	Fog	100%	6 mph	0 mph
10:22:00	35° F	Fog	96%	3 mph	0 mph
11:19:00	36° F	Mist	96%	0 mph	0 mph
12:13:00	36° F	Fog	100%	0 mph	0 mph
13:09:00	38° F	Mist	97%	3 mph	0 mph
13:56:00	38° F	Rain	100%	3 mph	0 mph
14:49:00	39° F	Mist	100%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 2/12/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(4) Installing above ceiling ductwork North and West wing (Area B) (4) Running geothermal hydronic lines to (Area B) (5) installing domestic water in North and West wing of (Area B)		13.00	104.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Framing metal stud partition walls (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Laying up CMU partition walls in West wing of (Area B) (5) Taking remaining partitions to deck in Discovery Zone 163, North wing (Area B) (2) Rubbing out masonry walls (Area A&B) (4) Wrecking scaffolding from 12" storm shelter bearing wall install.		14.00	112.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Running electrical conduit in West wing (Area B) (3) Pulling wire in administration area. (2) Installing temp lighting in (Area A)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing ICF bar joist pockets throughout (Area B) (2) Grouting under ICF louver blockouts in storm shelter. (2) Slab demo in 192 Girls due to slab settlement.		6.00	48.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Installing CMU block fill Drywall primer in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY !		3.00	8.00	24.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		8.00	8.00	64.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 2/12/2025

Michael Graf on 2/12/2025 02:22 PM



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf



File
2/12/2025 2:22 PM
Michael Graf

Michael Graf on 2/12/2025 03:09 PM




File
Daily Report 2025...
Michael Graf

Michael Graf on 2/13/2025 09:58 AM

Lost production day due to Ice and rain.

ASSIGNMENTS





Daily Construction Report

With Labor Summary and Material
Monday, February 17, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/17/2025

288.00

hours

31° F

clear

1

notes

6

equipment

● Approved

status

Days Lost on Project: 60.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	9 mph	0 mph
08:53:00	22° F	Cloudy	65%	7 mph	0 mph
09:53:00	25° F	Cloudy	60%	7 mph	0 mph
10:53:00	25° F	Cloudy	60%	6 mph	0 mph
11:53:00	26° F	Cloudy	63%	7 mph	0 mph
12:53:00	26° F	Cloudy	63%	3 mph	0 mph
13:21:00	28° F	Partly Cloudy	63%	0 mph	0 mph
13:53:00	29° F	Clear	58%	0 mph	0 mph
14:53:00	31° F	Clear	51%	8 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing framing out masonry walls to deck, gyp board and insulation in (Area A & B)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Wrecking scaffolding west wing (Area B). Building exterior scaffolding stone and brick install.		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Rasping ICF foam for 12" CMU bearing wall clearance in Lobby 101. (2) Sealing exterior ICF wall bar joists pockets. (5) Installing roof drain framing and decking at clearstory.		10.00	80.00 Hours	Approved

Daily report for 2/17/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY I		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/17/2025 01:14 PM

File
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael GrafFile
2/17/2025 1:14 PM
Michael Graf

Michael Graf on 2/17/2025 01:20 PM

Lost production day due to snow and ice.

Michael Graf on 2/17/2025 03:22 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Tuesday, February 18, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/18/2025

304.00

hours

28° F

cloudy

2

notes

7

equipment

Approved

status

Days Lost on Project: 61.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	22° F	Cloudy	68%	0 mph	0 mph
08:53:00	24° F	Cloudy	62%	0 mph	0 mph
09:53:00	25° F	Clear	65%	0 mph	0 mph
10:53:00	25° F	Cloudy	68%	3 mph	0 mph
11:53:00	26° F	Cloudy	65%	3 mph	0 mph
12:22:00	26° F	Snow	71%	3 mph	0 mph
12:53:00	27° F	Cloudy	68%	0 mph	0 mph
13:32:00	28° F	Cloudy	65%	3 mph	0 mph
14:14:00	29° F	Cloudy	66%	5 mph	0 mph
14:53:00	28° F	Cloudy	65%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing ductwork in North and West wings of (Area B)		5.00	40.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing domestic water in (Area A)		3.00	24.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Framing up metal stud partition walls and soffits (Area A). (2) Rubbing out masonry walls in (Area A) (2) cleanup (5) Laying up exterior brick facade west side of (Area B).		9.00	72.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Installing electrical rough-in's in metal stud partition walls (Area A) Running above ceiling conduit in West wing (Area B) Pulling wire in (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(3) Installing temp enclosures in clearstory window openings. (2) Sealing exterior ICF wall bar joists pockets. (5) Setting storm shelter bar joists.		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying primer coat on kitchen and cafeteria gyp board soffits and walls.		2.00	16.00 Hours	Approved

Daily report for 2/18/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		5.00	8.00	40.00
Scissor Lift	GRAYHAWK, LLC		5.00	8.00	40.00
Fork Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Lull Lift	MASON STRUCTURE, I		1.00	8.00	8.00
Scissor Lift	RIMAR ELECTRIC, LLC		3.00	8.00	24.00
10 Ton Crane	RISING SUN DEVELOP		1.00	8.00	8.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/18/2025 12:26 PM



Michael Graf on 2/18/2025 03:32 PM

Held monthly progress meeting with owners, design team and contractors.


Michael Graf on 2/18/2025 03:32 PM

Lost production day due to freezing temperatures and snow.

Michael Graf on 2/18/2025 03:33 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily Report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 2.00

WEATHER

Total Rainfall: 0" Total Snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost Productivity: 1 Days

Company (Crew)	Work Description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES

Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Wednesday, February 19, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/19/2025

0.00
hours

18° F
cloudy

1
notes

0
equipment

● Approved
status

Days Lost on Project: 62.00

Days Lost on this Month: 3.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:35:00	14° F	Snow	84%	3 mph	0 mph
07:53:00	14° F	Snow	84%	5 mph	0 mph
08:37:00	14° F	Snow	84%	5 mph	0 mph
09:10:00	14° F	Snow	84%	5 mph	0 mph
10:00:00	14° F	Snow	80%	0 mph	0 mph
10:53:00	15° F	Cloudy	80%	0 mph	0 mph
11:20:00	16° F	Cloudy	77%	0 mph	0 mph
11:53:00	16° F	Cloudy	77%	3 mph	0 mph
12:21:00	17° F	Snow	73%	5 mph	0 mph
13:08:00	18° F	Cloudy	71%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status

EQUIPMENT

MATERIAL DELIVERED

NOTES


Michael Graf on 2/19/2025 01:36 PM

Lost production day due to heavy snow and freezing temperatures.

Michael Graf on 2/19/2025 01:36 PM



File
Daily Report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Thursday, February 20, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/20/2025

208.00

hours

18° F

cloudy

1

notes

3

equipment

● Pending

status

Days Lost on Project: 63.00

Days Lost on this Month: 4.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:14:00	14° F	Snow	84%	5 mph	0 mph
08:08:00	14° F	Snow	84%	7 mph	0 mph
08:53:00	14° F	Snow	84%	6 mph	0 mph
09:37:00	15° F	Snow	76%	5 mph	0 mph
09:53:00	15° F	Snow	76%	6 mph	0 mph
10:53:00	17° F	Snow	70%	5 mph	0 mph
11:53:00	17° F	Snow	61%	8 mph	0 mph
12:29:00	17° F	Snow	61%	9 mph	0 mph
13:23:00	19° F	Snow	62%	9 mph	0 mph
14:14:00	18° F	Cloudy	53%	14 mph	0 mph
14:53:00	18° F	Cloudy	53%	13 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Hours

Company (Crew)	Work description	Location	Workers	Qty.	Status
GRAYHAWK, LLC (N/A)	Installing insulation and hanging gyp board west wing (Area B).		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Laying up brick veneer on north facade of (Area B).		8.00	64.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(2) Sealing exterior ICF wall bar joist pockets. (5) Forming and prepping mezzanine HCP's for topping coat. (3) Installing wood blocking in pre-school metal stud partition walls, (Area C). (2) Clean up		12.00	96.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying 1st finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/20/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	GRAYHAWK, LLC		2.00	8.00	16.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Lull Lift	RISING SUN DEVELOP		1.00	3.00	3.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/20/2025 01:51 PM

File
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael GrafFile
2/20/2025 1:51 PM
Michael Graf

Michael Graf on 2/20/2025 03:14 PM

Lost production day due to snow and freezing temperatures.

Michael Graf on 2/20/2025 03:16 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report

With Labor Summary and Material
Friday, February 21, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 2/21/2025

304.00

hours

23° F

cloudy

1

notes

5

equipment

● Approved

status

Days Lost on Project: 64.00

Days Lost on this Month: 5.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:53:00	11° F	Cloudy	76%	3 mph	0 mph
08:53:00	12° F	Cloudy	73%	0 mph	0 mph
09:53:00	13° F	Snow	73%	0 mph	0 mph
10:53:00	15° F	Cloudy	73%	0 mph	0 mph
11:53:00	18° F	Cloudy	67%	0 mph	0 mph
12:53:00	20° F	Cloudy	67%	0 mph	0 mph
13:53:00	21° F	Cloudy	68%	3 mph	0 mph
14:53:00	23° F	Cloudy	62%	0 mph	0 mph
15:53:00	23° F	Cloudy	62%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Installing roof drain lines in (Area A)		3.00	24.00 Hours	Approved
GRAYHAWK, LLC (N/A)	Installing floor drains in mezzanine (Area C)		4.00	32.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	Topping out masonry walls in (Area A)		8.00	64.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	Laying up brick on north facade of (Area B)		9.00	72.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(4) Installing cable trays in (Area B) (5) Pulling wire in west wing of (Area B)		12.00	96.00 Hours	Approved
	(2) Sealing exterior ICF wall bar joist pockets. (5) Prepping mezzanine HCP's for topping coat. (2) clean up. (3) installing metal stud partition walls wood blocking (Pre school)				
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying initial finish coat in kitchen and cafeteria.		2.00	16.00 Hours	Approved

EQUIPMENT

Daily report for 2/21/2025

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY S		1.00	8.00	8.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	4.00	4.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	4.00	4.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 2/21/2025 08:43 AM


File
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael GrafFile
2/21/2025 8:43 AM
Michael Graf

Michael Graf on 2/22/2025 01:16 PM

Lost production day due to ice and freezing temperatures.

Michael Graf on 2/22/2025 01:17 PM

File
Daily Report 2025...
Michael Graf**ASSIGNMENTS**



Daily Construction Report
With Labor Summary and Material
Thursday, April 3, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/3/2025

528.00
hours

63° F
thunderstorm

2
notes

6
equipment

● Approved
status

Days Lost on Project: 65.00

Days Lost on this Month: 1.00

WEATHER

Total rainfall: 3" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:47:00	63° F	Thunderstorm	94%	12 mph	0 mph
08:30:00	63° F	Rain	97%	0 mph	0 mph
09:19:00	63° F	Rain	97%	5 mph	0 mph
09:53:00	63° F	Rain	97%	7 mph	0 mph
10:46:00	63° F	Rain	97%	9 mph	0 mph
11:35:00	63° F	Thunderstorm	93%	12 mph	0 mph
11:53:00	63° F	Rain	93%	9 mph	0 mph
12:53:00	63° F	Rain	97%	0 mph	0 mph
13:46:00	63° F	Rain	97%	0 mph	0 mph
14:39:00	63° F	Thunderstorm	97%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Daily report for 4/3/2025

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(3) Insulating domestic water lines. (4) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (2) Installing plumbing rough-in's in CMU partition walls (Area A) (6) Installing above ceiling ductwork in (Area A). (2) Sealing duct penetrations.		17.00	136.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area B) (5) Topping out masonry walls in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(6) Tuck point and infilling corridor steel lintel beams. (2) Rubbing out masonry walls ahead of painters (Area A) (1) Weekly cleanup. (1) Material handler		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) Weekly cleanup.		11.00	88.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	(5) Weekly Cleanup (2) Prefabricating radius forms for sidewalks. (3) Sanding and repairing HM frames		10.00	80.00 Hours	Approved
SPRAY FOAM TECHNOLOGIES OF KY (N/A)	Applying block fill in (Area A & B)		4.00	32.00 Hours	Approved
TWIN LAKES FIRE SERVICE, LLC (N/A)	Installing fire suppression mains to administration and pre-school areas from mezzanine.		2.00	16.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00
Lull Lift	RISING SUN DEVELOP		1.00	2.00	2.00

MATERIAL DELIVERED**NOTES**

Daily report for 4/3/2025

Michael Graf on 4/3/2025 11:43 AM

Unable to upload progress photos due to technical issues. Bill Arnold has been made aware of this issue.

Michael Graf on 4/3/2025 11:45 AM

(Lost Production Day) Elliott Contracting, Dixie Roofing unable to work due to weather conditions.

Michael Graf on 4/3/2025 03:19 PM




File

Daily report 2025...

Michael Graf

ASSIGNMENTS



Daily Construction Report

With Labor Summary and Material
Friday, April 4, 2025

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/4/2025

360.00
hours

65° F
rain

1
notes

5
equipment

● Approved
status

Days Lost on Project: 66.00

Days Lost on this Month: 2.00

WEATHER

Total rainfall: 1" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:01:00	59° F	Cloudy	93%	6 mph	0 mph
07:53:00	60° F	Rain	93%	5 mph	0 mph
08:35:00	59° F	Thunderstorm	96%	3 mph	0 mph
09:27:00	59° F	Thunderstorm	96%	5 mph	0 mph
10:19:00	60° F	Rain	96%	6 mph	0 mph
10:53:00	61° F	Rain	97%	3 mph	0 mph
14:21:00	65° F	Rain	93%	3 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	(2) Slab demo in kitchen RR 186 for new grease sanitary tie in location. (4) Installing plumbing rough-in's in CMU partition walls (Area A) (5) Installing above ceiling ductwork in (Area A). (1) Sealing duct penetrations.		12.00	96.00 Hours	Approved
GRAYHAWK, LLC (N/A)	(3) Finishing drywall in (Area A & B) (5) Hanging drywall in (Area A). (4) Finishing drywall Administration and pre-school Area C.		12.00	96.00 Hours	Approved
MASON STRUCTURE, INC. (N/A)	(3) Tuck point and infilling corridor steel lintel beams. (1) Rubbing out masonry walls ahead of painters (Area A) (1) Rubbing out masonry walls under mezzanine. (4) Infilling bar joist pockets (Area A)		10.00	80.00 Hours	Approved
RIMAR ELECTRIC, LLC (N/A)	(1) Material handler (4) Pulling wire (Area A) (5) Installing above ceiling electrical in (Area A&B). (2) ICF wall electrical rough-in storm shelter		11.00	88.00 Hours	Approved

Daily report for 4/4/2025

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Scissor Lift	CENTRAL KENTUCKY		1.00	8.00	8.00
Skid Steer	CENTRAL KENTUCKY		1.00	1.00	1.00
Scissor Lift	GRAYHAWK, LLC		3.00	8.00	24.00
Lull Lift	MASON STRUCTURE, I		1.00	3.00	3.00
Scissor Lift	RIMAR ELECTRIC, LLC		5.00	8.00	40.00

MATERIAL DELIVERED**NOTES**

Michael Graf on 4/4/2025 01:13 PM


File
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael GrafFile
4/4/2025 1:13 PM
Michael Graf

Michael Graf on 4/4/2025 03:13 PM

Elliott contracting, Dixie Roofing and RSD - (Lost production day due to weather.)

Michael Graf on 4/4/2025 03:14 PM

File
Daily report 2025...
Michael Graf



Daily Construction Report

With Labor Summary and Material
Wednesday, April 10, 2024

Stanton Elementary School (000743)

West College Avenue
Stanton, KY 40380

Daily report for 4/10/2024

17.00
hours

68° F
cloudy

1
notes

1
equipment

● Approved
status

Days Lost on Project: 18.00

Days Lost on this Month: 16.00

WEATHER

Total rainfall: 0" Total snowfall: 0"

Time	Temperature	Conditions	Humidity	Wind	Gusts
07:04:00	55° F	Rain	93%	0 mph	0 mph
07:53:00	55° F	Mist	96%	3 mph	0 mph
08:18:00	55° F	Mist	96%	3 mph	0 mph
08:53:00	56° F	Cloudy	93%	3 mph	0 mph
09:53:00	57° F	Rain	93%	3 mph	0 mph
10:53:00	57° F	Cloudy	93%	3 mph	0 mph
11:32:00	58° F	Rain	97%	3 mph	0 mph
11:53:00	60° F	Cloudy	90%	0 mph	0 mph
12:53:00	64° F	Cloudy	80%	3 mph	0 mph
13:53:00	68° F	Cloudy	70%	5 mph	0 mph

DETAILED LABOR

Lost productivity: 1 Days

Company (Crew)	Work description	Location	Workers	Qty.	Status
CENTRAL KENTUCKY SHEET METAL, INC (N/A)	Tied in holding tank to field office.		2.00	2.00 Hours	Approved
RISING SUN DEVELOPING COMPANY (N/A)	Delivered and off loaded storm structures.		5.00	15.00 Hours	Approved

EQUIPMENT

Equipment	Company	Crew	Qty.	Hours	Total Hours
Excavator	RISING SUN DEVELOP		1.00	1.00	1.00

MATERIAL DELIVERED

NOTES

Daily report for 4/10/2024

Michael Graf on 4/10/2024 07:45 AM

Lost production day (Unsuitable Soils), waiting on PR approval.

Michael Graf on 4/10/2024 07:46 AM



File
4/10/2024 7:46 AM
Michael Graf



File
4/10/2024 7:46 AM
Michael Graf

Michael Graf on 4/10/2024 08:38 AM



File
4/10/2024 8:38 AM
Michael Graf



File
4/10/2024 8:38 AM
Michael Graf

Michael Graf on 4/10/2024 02:41 PM



File
Daily Report 2024...
Michael Graf

ASSIGNMENTS



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
1	✓ Notice to Proceed	0 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	0 days	1 day	
2	✓ Mobilization	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
3	✓ Quick Ship Shop Drawings - Concrete Rebar	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
4	✓ Quick Ship Shop Drawings - Concrete Mix Design/ICF	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
5	✓ Quick Ship Shop Drawings - Grout Mix Design	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
6	✓ Quick Ship Shop Drawings - CMU	5 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	0 days	-4 days	
7	✓ Quick Ship Shop Drawings - Structural Steel/Miscellaneous Steel	25 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 4/5/24	Tue 3/5/24	Tue 3/5/24	1 day	-23 days	
8	✓ Quick Ship Shop Drawings - Joists/Decking/Hollow Core Planks	25 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/5/24	Mon 3/4/24	Mon 3/4/24	0 days	-24 days	
9	✓ Quick Ship Shop Drawings - MEP underslab piping	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
10	✓ Quick Ship Shop Drawings - MEP -pipe,duct,conduit etc...	10 days	1 day	Mon 3/4/24	Tue 3/5/24	Tue 3/5/24	Fri 3/15/24	Tue 3/5/24	Tue 3/5/24	1 day	-8 days	
11	✓ Quick Ship Shop Drawings - Hollow Metal Door and Window Frames	10 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	0 days	-9 days	
12	✓ Shop Drawings - Exclude Quick Ship Shop Drawings	40 days	1 day	Mon 3/4/24	Mon 3/4/24	Mon 3/4/24	Fri 4/26/24	Mon 3/4/24	Mon 3/4/24	0 days	-39 days	
13	✓ Submit Notice of Intent - Best Management Plan	0 days	1 day	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	Tue 3/5/24	Mon 3/4/24	Mon 3/4/24	-2 days	-1 day	
14	✓ Install BMP mandated work	3 days	1 day	Wed 3/6/24	Thu 3/7/24	Thu 3/7/24	Fri 3/8/24	Thu 3/7/24	Thu 3/7/24	1 day	-1 day	
15	✓ Install Temporary Job site Fencing/Gates/Temporary construction entrance	2 days	0 days	Fri 3/8/24	Mon 3/4/24	Mon 3/4/24	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	-4 days	-5 days	
16	✓ Architect/Engineer Review of rebar, concrete design, grout, & CMU shops	5 days	0 days	Mon 3/11/24	Mon 3/4/24	Mon 3/4/24	Fri 3/15/24	Mon 3/4/24	Mon 3/4/24	-5 days	-9 days	
17	✓ Install Stone(#2's capped with DGA) for construction entrance	2 days	0 days	Tue 3/12/24	Mon 3/11/24	Mon 3/11/24	Wed 3/13/24	Mon 3/11/24	Mon 3/11/24	-1 day	-2 days	
18	✓ Site Clearing/Demolition/Stockpile Topsoil	15 days	0 days	Thu 3/14/24	Mon 3/11/24	Mon 3/11/24	Wed 4/3/24	Mon 3/11/24	Mon 3/11/24	-3 days	-17 days	
19	✓ Architect/Engineer Review - Hollow Metal Door frames & MEP pipe, conduit etc...	5 days	0 days	Mon 3/18/24	Mon 3/4/24	Mon 3/4/24	Fri 3/22/24	Mon 3/4/24	Mon 3/4/24	-10 days	-14 days	
20	✓ Site Grading/Earthwork	86 days	0 days	Tue 3/26/24	Mon 3/18/24	Mon 3/18/24	Thu 7/25/24	Mon 3/18/24	Mon 3/18/24	-6 days	-91 days	
21	✓ A/E review Steel/Joists/Deck Quick Ship Shop Drawings	10 days	0 days	Mon 4/8/24	Tue 3/5/24	Tue 3/5/24	Fri 4/19/24	Tue 3/5/24	Tue 3/5/24	-24 days	-33 days	
22	✓ A/E review remainder of shop drawings	20 days	0 days	Mon 4/29/24	Tue 3/5/24	Tue 3/5/24	Fri 5/24/24	Tue 3/5/24	Tue 3/5/24	-39 days	-58 days	
23	✓ Building Pad on Grade	0 days	1 day	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	Thu 6/13/24	0 days	1 day	
24	✓ Install Storm Drainage	30 days	1 day	Fri 7/5/24	Tue 12/9/25	Tue 12/9/25	Thu 8/15/24	Tue 12/9/25	Tue 12/9/25	364 days	335 days	
25	✓ Install Geothermal Well Field (verticals/horizontals/vault)	60 days	1 day	Fri 7/5/24	Wed 7/10/24	Wed 7/10/24	Fri 9/27/24	Wed 7/10/24	Wed 7/10/24	3 days	-56 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
26	Install Fire Main, Vault and Hydrants	30 days	30 days	Fri 7/26/24	Tue 3/19/24	NA	Fri 9/6/24	Mon 4/29/24	NA	-91 days	-91 days	
27	✓ Install Sewer line	30 days	0 days	Fri 7/26/24	Tue 6/25/24	Tue 6/25/24	Fri 9/6/24	Tue 6/25/24	Tue 6/25/24	-22 days	-51 days	
28	Install Domestic Water	15 days	15 days	Mon 9/9/24	Wed 6/26/24	NA	Fri 9/27/24	Wed 7/17/24	NA	-51 days	-51 days	
29	Install Gas	15 days	15 days	Mon 9/30/24	Thu 7/18/24	NA	Fri 10/18/24	Wed 8/7/24	NA	-51 days	-51 days	
30	✓ Install Grease Trap	7 days	1 day	Mon 10/21/24	Wed 4/2/25	Wed 4/2/25	Tue 10/29/24	Wed 4/2/25	Wed 4/2/25	114 days	108 days	
31	Set Transformer/Pull Primary/Secondary Wire	10 days	10 days	Thu 1/16/25	Fri 9/6/24	NA	Wed 1/29/25	Thu 9/19/24	NA	-91 days	-91 days	
32	Set Cooling Tower - Hook up lines	10 days	10 days	Thu 1/23/25	Fri 11/1/24	NA	Wed 2/5/25	Thu 11/14/24	NA	-56 days	-56 days	
33	Permanent Power	0 days	0 days	Wed 2/26/25	Thu 10/17/24	NA	Wed 2/26/25	Thu 10/17/24	NA	-91 days	-91 days	
34	AREA A	236 days	236 days	Thu 6/13/24	Thu 6/13/24	Wed 7/17/24	Thu 5/15/25	Thu 5/15/25	NA	0 days	0 days	
35	✓ Footers - Area A	23 days	1 day	Thu 6/13/24	Wed 7/17/24	Wed 7/17/24	Tue 7/16/24	Wed 7/17/24	Wed 7/17/24	23 days	1 day	
36	✓ ICF Stem walls- Area A	7 days	0 days	Wed 6/26/24	Mon 7/22/24	Mon 7/22/24	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	17 days	11 days	
37	✓ Underslab Plumbing Rough in - Area A	20 days	0 days	Fri 7/5/24	Mon 7/22/24	Mon 7/22/24	Thu 8/1/24	Mon 7/22/24	Mon 7/22/24	11 days	-8 days	
38	✓ Underslab CMU - Area A	5 days	1 day	Tue 7/2/24	Tue 8/13/24	Tue 8/13/24	Tue 7/9/24	Tue 8/13/24	Tue 8/13/24	29 days	25 days	
39	✓ Stone Backfill non plumbing areas - Area A	2 days	1 day	Mon 7/22/24	Mon 11/11/24	Mon 11/11/24	Tue 7/23/24	Mon 11/11/24	Mon 11/11/24	79 days	78 days	
40	✓ Underslab Electrical Rough in - Area A	12 days	0 days	Wed 7/24/24	Mon 11/4/24	Mon 11/4/24	Thu 8/8/24	Mon 11/4/24	Mon 11/4/24	72 days	61 days	
41	✓ Stone Backfill at pumbing areas - Area A	2 days	1 day	Wed 7/31/24	Wed 11/20/24	Wed 11/20/24	Thu 8/1/24	Wed 11/20/24	Wed 11/20/24	79 days	78 days	
42	✓ Slab Prep 1st Floor - Area A	3 days	0 days	Fri 8/9/24	Wed 11/20/24	Wed 11/20/24	Tue 8/13/24	Wed 11/20/24	Wed 11/20/24	72 days	70 days	
43	✓ Slab Placement 1st Floor - Area A	1 day	0 days	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	Wed 8/14/24	Tue 11/26/24	Tue 11/26/24	73 days	73 days	
44	✓ Hollow Metal Doorframes installation 1st Floor - Area A	3 days	0 days	Mon 8/19/24	Tue 10/29/24	Tue 10/29/24	Wed 8/21/24	Tue 10/29/24	Tue 10/29/24	50 days	48 days	
45	✓ CMU Bearing Walls - Area A	25 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/26/24	Mon 11/11/24	Mon 11/11/24	56 days	32 days	
46	✓ ICF Walls - Area A	20 days	0 days	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
47	✓ Plumbing Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Thu 12/19/24	Thu 12/19/24	Thu 9/19/24	Thu 12/19/24	Thu 12/19/24	83 days	64 days	
48	✓ Electrical Wall Rough in - Area A	20 days	1 day	Thu 8/22/24	Mon 11/11/24	Mon 11/11/24	Thu 9/19/24	Mon 11/11/24	Mon 11/11/24	56 days	37 days	
49	✓ Steel Columns/Beams/Bent Plate - Area A	12 days	0 days	Fri 9/6/24	Tue 11/12/24	Tue 11/12/24	Mon 9/23/24	Tue 11/12/24	Tue 11/12/24	47 days	36 days	
50	✓ CMU Non Bearing Walls/Rub all walls - Area A	10 days	0 days	Fri 9/27/24	Tue 12/17/24	Tue 12/17/24	Thu 10/10/24	Tue 12/17/24	Tue 12/17/24	56 days	47 days	
51	✓ Set Roof Joists - Area A	15 days	1 day	Fri 9/27/24	Wed 1/29/25	Wed 1/29/25	Thu 10/17/24	Wed 1/29/25	Wed 1/29/25	85 days	71 days	
52	✓ Exterior Brick/Stone - Area A	35 days	1 day	Tue 10/8/24	Mon 3/17/25	Mon 3/17/25	Mon 11/25/24	Mon 3/17/25	Mon 3/17/25	111 days	77 days	
53	✓ Roof Deck installation/inspection - Area A	7 days	0 days	Fri 10/18/24	Fri 2/7/25	Fri 2/7/25	Mon 10/28/24	Fri 2/7/25	Fri 2/7/25	77 days	71 days	
54	✓ ICF Parapet Walls - Area A	7 days	0 days	Fri 10/18/24	Tue 12/3/24	Tue 12/3/24	Mon 10/28/24	Tue 12/3/24	Tue 12/3/24	31 days	25 days	
55	✓ Electrical Rough-In --Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
56	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area A	40 days	0 days	Fri 10/18/24	Mon 2/10/25	Mon 2/10/25	Fri 12/13/24	Mon 2/10/25	Mon 2/10/25	78 days	39 days	
57	✓ Duct installation - Above Ceiling - Area A	35 days	1 day	Fri 10/18/24	Mon 3/3/25	Mon 3/3/25	Fri 12/6/24	Mon 3/3/25	Mon 3/3/25	93 days	59 days	
58	✓ Roof Wood Blocking - Area A	7 days	0 days	Tue 10/29/24	Wed 2/5/25	Wed 2/5/25	Wed 11/6/24	Wed 2/5/25	Wed 2/5/25	68 days	62 days	
59	Windows/Glazing/Sunshades/Caulking - Area A	12 days	12 days	Tue 11/5/24	Mon 4/14/25	NA	Wed 11/20/24	Tue 4/29/25	NA	111 days	111 days	
60	✓ TPO Roof- Area A	15 days	0 days	Thu 11/7/24	Mon 2/10/25	Mon 2/10/25	Wed 11/27/24	Mon 2/10/25	Mon 2/10/25	64 days	50 days	
61	Sprinkler Rough-In - Above Ceiling - Area A	20 days	20 days	Fri 11/8/24	Thu 5/15/25	Thu 5/15/25	Fri 12/6/24	Thu 6/12/25	NA	131 days	131 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
62	Block Filler - Area A	10 days	10 days	Thu 11/14/24	Mon 2/17/25	NA	Wed 11/27/24	Fri 2/28/25	NA	64 days	64 days	
63	✓ Gypsum Board walls/soffits - Hang/Finish - Area A	25 days	0 days	Thu 11/21/24	Mon 2/10/25	Mon 2/10/25	Fri 12/27/24	Mon 2/10/25	Mon 2/10/25	54 days	30 days	
64	✓ Clean Brick - Area A	5 days	0 days	Tue 11/26/24	Mon 3/24/25	Mon 3/24/25	Tue 12/3/24	Mon 3/24/25	Mon 3/24/25	81 days	77 days	
65	Brick Caulking - Area A	3 days	3 days	Tue 11/26/24	Tue 3/18/25	NA	Fri 11/29/24	Thu 3/20/25	NA	77 days	77 days	
66	Mechanical/Plumbing/Duct Insulation - Area A	20 days	20 days	Fri 11/29/24	Thu 5/15/25	Thu 5/15/25	Fri 12/27/24	Thu 6/12/25	NA	117 days	117 days	
67	Set Mechanical Equipment/Tie In - Area A	25 days	25 days	Fri 11/29/24	Thu 5/1/25	Thu 5/1/25	Mon 1/6/25	Thu 6/5/25	NA	107 days	107 days	
68	Metal Coping, Trim etc... - Area A	15 days	15 days	Wed 12/4/24	Wed 5/14/25	Wed 5/14/25	Tue 12/24/24	Wed 6/4/25	NA	113 days	113 days	
69	Electrical Systems/Devices - Area A	60 days	60 days	Mon 12/16/24	Tue 2/11/25	NA	Tue 3/11/25	Mon 5/5/25	NA	39 days	39 days	
70	Primer/1st Coat of Paint - Walls - Area A	10 days	10 days	Mon 12/30/24	Tue 3/4/25	Tue 3/4/25	Mon 1/13/25	Mon 3/17/25	NA	45 days	45 days	
71	HVAC Controls - Area A	25 days	25 days	Tue 1/7/25	Fri 6/13/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
72	Ceiling Grid - Area A	12 days	12 days	Tue 1/14/25	Tue 3/18/25	NA	Wed 1/29/25	Wed 4/2/25	NA	45 days	45 days	
73	Grilles, Registers, Diffusers, Labeling - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
74	Light Fixtures - Area A	15 days	15 days	Tue 1/21/25	Tue 3/25/25	NA	Mon 2/10/25	Mon 4/14/25	NA	45 days	45 days	
75	Sprinkler Heads - Area A	12 days	12 days	Tue 1/21/25	Tue 3/25/25	NA	Wed 2/5/25	Wed 4/9/25	NA	45 days	45 days	
76	Ceramic Tile - Area A	20 days	20 days	Wed 1/29/25	Fri 5/23/25	NA	Tue 2/25/25	Fri 6/20/25	NA	82 days	82 days	
77	Above Ceiling Punch - Engineer - Area A	0 days	0 days	Mon 2/10/25	Thu 6/5/25	NA	Mon 2/10/25	Thu 6/5/25	NA	82 days	82 days	
78	Paint - Exposed Ceilings/Floors- Area A	10 days	10 days	Tue 2/11/25	Fri 6/13/25	NA	Mon 2/24/25	Thu 6/26/25	NA	87 days	87 days	
79	Work off Above Ceiling Punchlist - Contractors - Area A	5 days	5 days	Wed 2/12/25	Mon 6/9/25	NA	Tue 2/18/25	Fri 6/13/25	NA	82 days	82 days	
80	Ceiling Tiles - Area A	7 days	7 days	Wed 2/19/25	Mon 6/16/25	NA	Thu 2/27/25	Tue 6/24/25	NA	82 days	82 days	
81	Plumbing Fixtures - Area A	12 days	12 days	Wed 2/26/25	Mon 6/23/25	NA	Thu 3/13/25	Wed 7/9/25	NA	82 days	82 days	
82	Aluminum Storefront Frames and Doors - Area A	5 days	5 days	Tue 2/4/25	Mon 7/14/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
83	Controlled Air - Area A	0 days	0 days	Mon 2/10/25	Fri 7/18/25	NA	Mon 2/10/25	Fri 7/18/25	NA	112 days	112 days	
84	VCT and Base - Area A	20 days	20 days	Wed 2/19/25	Mon 7/21/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
85	Toilet Partitions and Accessories - Area A	8 days	8 days	Thu 3/6/25	Tue 7/1/25	NA	Mon 3/17/25	Fri 7/11/25	NA	82 days	82 days	
86	Casework/Solid Surface Sills - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
87	Final Coat Paint - Walls - Area A	10 days	10 days	Wed 3/5/25	Mon 8/4/25	NA	Tue 3/18/25	Fri 8/15/25	NA	106 days	106 days	
88	Display/Tack Boards - Area A	7 days	7 days	Wed 3/19/25	Mon 8/18/25	NA	Thu 3/27/25	Tue 8/26/25	NA	106 days	106 days	
89	Door Frame Paint - 1 Coats - Area A	3 days	3 days	Wed 3/19/25	Mon 4/21/25	Mon 4/21/25	Fri 3/21/25	Wed 8/20/25	NA	23 days	106 days	
90	Doors & Hardware - Area A	15 days	15 days	Wed 3/19/25	Mon 8/18/25	NA	Tue 4/8/25	Mon 9/8/25	NA	106 days	106 days	
91	Interior Signage - Area A	2 days	2 days	Fri 3/28/25	Wed 8/27/25	NA	Mon 3/31/25	Thu 8/28/25	NA	106 days	106 days	
92	Doorframe Paint - 2nd Coat - Area A	3 days	3 days	Wed 4/9/25	Tue 9/9/25	NA	Fri 4/11/25	Thu 9/11/25	NA	106 days	106 days	
93	Install Door Glass - Area A	2 days	2 days	Wed 4/9/25	Tue 9/9/25	NA	Thu 4/10/25	Wed 9/10/25	NA	106 days	106 days	
94	Pre-Clean before Architect Punchlist - Area A	5 days	5 days	Mon 4/14/25	Fri 9/12/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
95	Architect Punch List Review - Area A	0 days	0 days	Fri 4/18/25	Thu 9/18/25	NA	Fri 4/18/25	Thu 9/18/25	NA	106 days	106 days	
96	Air Balance - Area A	5 days	5 days	Mon 4/21/25	Fri 9/19/25	NA	Fri 4/25/25	Thu 9/25/25	NA	106 days	106 days	
97	Architect Punch List Distributed - Area A	2 days	2 days	Mon 4/21/25	Fri 9/19/25	NA	Tue 4/22/25	Mon 9/22/25	NA	106 days	106 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

|||||

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
98	Architect Punch List Worked Off by Contractors - Area A	10 days	10 days	Wed 4/23/25	Tue 9/23/25	NA	Tue 5/6/25	Mon 10/6/25	NA	106 days	106 days	
99	Final Clean after Punchlist worked off - Area A	5 days	5 days	Wed 5/7/25	Tue 10/7/25	NA	Tue 5/13/25	Mon 10/13/25	NA	106 days	106 days	
100	Final Review by Architect - Area A	2 days	2 days	Wed 5/14/25	Tue 10/14/25	NA	Thu 5/15/25	Wed 10/15/25	NA	106 days	106 days	
101	AREA B	241 days	241 days	Wed 7/17/24	Tue 7/9/24	Tue 7/9/24	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
102	✓ Footers - Area B	23 days	0 days	Wed 7/17/24	Mon 7/15/24	Mon 7/15/24	Fri 8/16/24	Mon 7/15/24	Mon 7/15/24	-2 days	-24 days	
103	✓ ICF Stem walls- Area B	7 days	0 days	Tue 7/30/24	Tue 7/23/24	Tue 7/23/24	Wed 8/7/24	Tue 7/23/24	Tue 7/23/24	-5 days	-11 days	
104	✓ Underslab Plumbing Rough in - Area B	20 days	0 days	Wed 8/7/24	Tue 7/9/24	Tue 7/9/24	Wed 9/4/24	Tue 7/9/24	Tue 7/9/24	-21 days	-40 days	
105	✓ Underslab CMU - Area B	5 days	1 day	Mon 8/5/24	Fri 8/2/24	Fri 8/2/24	Fri 8/9/24	Fri 8/2/24	Fri 8/2/24	-1 day	-5 days	
106	✓ Stone Backfill non plumbing areas - Area B	2 days	0 days	Thu 8/22/24	Thu 8/15/24	Thu 8/15/24	Fri 8/23/24	Thu 8/15/24	Thu 8/15/24	-5 days	-6 days	
107	✓ Underslab Electrical Rough in - Area B	12 days	0 days	Mon 8/26/24	Thu 8/1/24	Thu 8/1/24	Wed 9/11/24	Thu 8/1/24	Thu 8/1/24	-17 days	-28 days	
108	✓ Stone Backfill at pumbing areas - Area B	2 days	0 days	Tue 9/3/24	Thu 8/22/24	Thu 8/22/24	Wed 9/4/24	Thu 8/22/24	Thu 8/22/24	-7 days	-8 days	
109	✓ Slab Prep 1st Floor - Area B	3 days	0 days	Thu 9/12/24	Mon 8/19/24	Mon 8/19/24	Mon 9/16/24	Mon 8/19/24	Mon 8/19/24	-17 days	-19 days	
110	✓ Slab Placement 1st Floor - Area B	1 day	0 days	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	Tue 9/17/24	Wed 8/28/24	Wed 8/28/24	-13 days	-13 days	
111	✓ Hollow Metal Doorframes installation 1st Floor - Area B	3 days	0 days	Fri 9/20/24	Mon 9/30/24	Mon 9/30/24	Tue 9/24/24	Mon 9/30/24	Mon 9/30/24	6 days	4 days	
112	✓ CMU Bearing Walls - Area B	30 days	0 days	Wed 9/25/24	Mon 9/30/24	Mon 9/30/24	Tue 11/5/24	Mon 9/30/24	Mon 9/30/24	3 days	-26 days	
113	✓ ICF Walls - Area B	20 days	0 days	Wed 9/25/24	Tue 9/3/24	Tue 9/3/24	Tue 10/22/24	Tue 9/3/24	Tue 9/3/24	-16 days	-35 days	
114	✓ Plumbing Wall Rough in - Area B	20 days	1 day	Wed 9/25/24	Wed 10/2/24	Wed 10/2/24	Tue 10/22/24	Wed 10/2/24	Wed 10/2/24	5 days	-14 days	
115	✓ Electrical Wall Rough in - Area B	20 days	0 days	Wed 9/25/24	Thu 9/26/24	Thu 9/26/24	Tue 10/22/24	Thu 9/26/24	Thu 9/26/24	1 day	-18 days	
116	✓ Steel Columns/Beams/Bent Plate - Area B	12 days	0 days	Wed 10/9/24	Tue 9/3/24	Tue 9/3/24	Thu 10/24/24	Tue 9/3/24	Tue 9/3/24	-26 days	-37 days	
117	✓ CMU Non Bearing Walls/Rub all walls - Area B	10 days	0 days	Wed 11/6/24	Thu 9/26/24	Thu 9/26/24	Tue 11/19/24	Thu 9/26/24	Thu 9/26/24	-29 days	-38 days	
118	✓ Set Steel Joists - Area B	15 days	0 days	Wed 11/6/24	Thu 10/31/24	Thu 10/31/24	Tue 11/26/24	Thu 10/31/24	Thu 10/31/24	-4 days	-18 days	
119	✓ Exterior Brick/Stone - Area B	25 days	0 days	Fri 11/15/24	Thu 10/10/24	Thu 10/10/24	Fri 12/20/24	Thu 10/10/24	Thu 10/10/24	-26 days	-50 days	
120	✓ Roof Deck installation/inspection - Area B	7 days	0 days	Wed 11/27/24	Tue 11/12/24	Tue 11/12/24	Fri 12/6/24	Tue 11/12/24	Tue 11/12/24	-11 days	-17 days	
121	✓ ICF Parapet Walls - Area B	7 days	0 days	Wed 11/27/24	Tue 9/24/24	Tue 9/24/24	Fri 12/6/24	Tue 9/24/24	Tue 9/24/24	-46 days	-52 days	
122	✓ Roof Wood Blocking - Area B	7 days	0 days	Mon 12/9/24	Mon 11/18/24	Mon 11/18/24	Tue 12/17/24	Mon 11/18/24	Mon 11/18/24	-14 days	-20 days	
123	✓ Windows/Glazing/Caulking - Area B	12 days	1 day	Mon 12/16/24	Wed 3/26/25	Wed 3/26/25	Thu 1/2/25	Wed 3/26/25	Wed 3/26/25	70 days	59 days	
124	✓ Duct installation - Above Ceiling - Area B	35 days	0 days	Mon 12/9/24	Mon 12/2/24	Mon 12/2/24	Tue 1/28/25	Mon 12/2/24	Mon 12/2/24	-5 days	-39 days	
125	✓ TPO Roof - Area B	15 days	0 days	Wed 12/18/24	Mon 12/2/24	Mon 12/2/24	Thu 1/9/25	Mon 12/2/24	Mon 12/2/24	-12 days	-26 days	
126	✓ Clean Brick - Area B	5 days	1 day	Mon 12/23/24	Mon 3/10/25	Mon 3/10/25	Mon 12/30/24	Mon 3/10/25	Mon 3/10/25	53 days	49 days	
127	✓ Brick Caulking - Area B	3 days	3 days	Mon 12/23/24	Fri 10/11/24	NA	Thu 12/26/24	Tue 10/15/24	NA	-50 days	-50 days	
128	✓ Electrical Rough-In - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Mon 12/9/24	Mon 12/9/24	Tue 2/11/25	Mon 12/9/24	Mon 12/9/24	-5 days	-44 days	
129	✓ Mechanical/Plumbing Rough in - Above Ceiling - Area B	40 days	0 days	Mon 12/16/24	Tue 12/10/24	Tue 12/10/24	Tue 2/11/25	Tue 12/10/24	Tue 12/10/24	-4 days	-43 days	
130	✓ Block Filler - Area B	10 days	1 day	Thu 12/26/24	Mon 3/24/25	Mon 3/24/25	Thu 1/9/25	Mon 3/24/25	Mon 3/24/25	61 days	52 days	
131	✓ Gypsum Board walls/soffits - Hang/Finish - Area B	25 days	0 days	Fri 1/3/25	Mon 1/27/25	Mon 1/27/25	Thu 2/6/25	Mon 1/27/25	Mon 1/27/25	16 days	-8 days	
132	✓ Install Clearstory Windows - Area B	5 days	9 days	Fri 1/3/25	Tue 5/20/25	Tue 5/20/25	Thu 1/9/25	Mon 6/2/25	Mon 6/2/25	97 days	101 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

■■■■■■■■■■

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
133	Sprinkler Rough-In - Above Ceiling - Area B	20 days	20 days	Tue 12/31/24	Thu 5/15/25	Thu 5/15/25	Tue 1/28/25	Thu 6/12/25	NA	96 days	96 days	
134	Mechanical/Plumbing/Duct Insulation - Area B	20 days	20 days	Fri 1/10/25	Thu 5/15/25	Thu 5/15/25	Thu 2/6/25	Thu 6/12/25	NA	89 days	89 days	
135	Set Mechanical Equipment/Tie In - Area B	25 days	25 days	Fri 1/10/25	Mon 5/19/25	Mon 5/19/25	Thu 2/13/25	Mon 6/23/25	NA	91 days	91 days	
136	Metal Coping, Trim etc... - Area B	15 days	15 days	Fri 1/10/25	Wed 5/14/25	Wed 5/14/25	Thu 1/30/25	Wed 6/4/25	NA	88 days	88 days	
137	Electrical Systems/Devices - Area B	60 days	60 days	Wed 1/8/25	Mon 5/19/25	Mon 5/19/25	Tue 4/1/25	Tue 8/12/25	NA	93 days	93 days	
138	✓ Primer/1st Coat of Paint - Walls - Area B	10 days	0 days	Fri 2/7/25	Mon 3/24/25	Mon 3/24/25	Thu 2/20/25	Mon 3/24/25	Mon 3/24/25	31 days	22 days	
139	HVAC Controls - Area B	25 days	25 days	Fri 2/14/25	Tue 6/24/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
140	Ceiling Grid - Area B	12 days	12 days	Fri 2/21/25	Tue 5/27/25	Tue 5/27/25	Mon 3/10/25	Wed 6/11/25	NA	66 days	66 days	
141	Grilles, Registers, Diffusers, Labeling - Area B	15 days	15 days	Fri 2/28/25	Mon 6/2/25	Mon 6/2/25	Thu 3/20/25	Mon 6/23/25	NA	65 days	66 days	
142	Light Fixtures - Area B	15 days	15 days	Fri 2/28/25	Tue 6/3/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
143	Sprinkler Heads - Area B	12 days	12 days	Fri 2/28/25	Mon 5/5/25	Mon 5/5/25	Mon 3/17/25	Wed 6/18/25	NA	46 days	66 days	
144	Ceramic Tile - Area B	20 days	20 days	Mon 3/10/25	Wed 6/11/25	NA	Fri 4/4/25	Wed 7/9/25	NA	66 days	66 days	
145	Aluminum Storefront Frames and Doors - Area B	5 days	5 days	Fri 3/14/25	Tue 5/20/25	Tue 5/20/25	Thu 3/20/25	Tue 7/29/25	NA	47 days	91 days	
146	Controlled Air - Area B	0 days	0 days	Thu 3/20/25	Tue 7/29/25	NA	Thu 3/20/25	Tue 7/29/25	NA	91 days	91 days	
147	Above Ceiling Punch - Engineer - Area B	0 days	0 days	Thu 3/20/25	Mon 6/23/25	NA	Thu 3/20/25	Mon 6/23/25	NA	66 days	66 days	
148	Paint - Exposed Ceilings/Floors- Area B	10 days	10 days	Fri 3/21/25	Tue 6/24/25	NA	Thu 4/3/25	Tue 7/8/25	NA	66 days	66 days	
149	Work off Above Ceiling Punchlist - Contractors - Area B	5 days	5 days	Mon 3/24/25	Wed 6/25/25	NA	Fri 3/28/25	Tue 7/1/25	NA	66 days	66 days	
150	VCT and Base - Area B	20 days	20 days	Mon 3/31/25	Wed 7/30/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
151	Ceiling Tiles - Area B	7 days	7 days	Mon 3/31/25	Thu 5/1/25	Thu 5/1/25	Tue 4/8/25	Fri 7/11/25	NA	23 days	66 days	
152	Install Acoustical Clouds - Area B	10 days	10 days	Mon 3/31/25	Wed 7/2/25	NA	Fri 4/11/25	Wed 7/16/25	NA	66 days	66 days	
153	Plumbing Fixtures - Area B	12 days	12 days	Mon 4/7/25	Thu 7/10/25	NA	Tue 4/22/25	Fri 7/25/25	NA	66 days	66 days	
154	Casework/Solid Surface Sills - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
155	Final Coat Paint - Walls - Area B	10 days	10 days	Mon 4/14/25	Wed 8/13/25	NA	Fri 4/25/25	Tue 8/26/25	NA	85 days	85 days	
156	Toilet Partitions and Accessories - Area B	8 days	8 days	Tue 4/15/25	Fri 7/18/25	NA	Thu 4/24/25	Tue 7/29/25	NA	66 days	66 days	
157	Display/Tack Boards - Area B	7 days	7 days	Mon 4/28/25	Wed 8/27/25	NA	Tue 5/6/25	Fri 9/5/25	NA	85 days	85 days	
158	✓ Door Frame Paint - 1 Coats - Area B	3 days	0 days	Mon 4/28/25	Thu 4/10/25	Thu 4/10/25	Wed 4/30/25	Thu 6/5/25	Thu 6/5/25	-12 days	25 days	
159	Doors & Hardware - Area B	15 days	15 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/16/25	Wed 9/17/25	NA	85 days	85 days	
160	✓ Install Overhead Door - Area B	3 days	0 days	Mon 4/28/25	Thu 5/1/25	Thu 5/1/25	Wed 4/30/25	Fri 5/2/25	Fri 5/2/25	3 days	2 days	
161	Install Decorative Wall Treatment - Area B	10 days	10 days	Mon 4/28/25	Wed 8/27/25	NA	Fri 5/9/25	Wed 9/10/25	NA	85 days	85 days	
162	Install Owner Supplied Graphics - Area B	6 days	6 days	Mon 4/28/25	Wed 8/27/25	NA	Mon 5/5/25	Thu 9/4/25	NA	85 days	85 days	
163	Interior Signage - Area B	2 days	2 days	Wed 5/7/25	Mon 9/8/25	NA	Thu 5/8/25	Tue 9/9/25	NA	85 days	85 days	
164	Doorframe Paint - 2nd Coat - Area B	3 days	3 days	Mon 5/19/25	Thu 9/18/25	NA	Wed 5/21/25	Mon 9/22/25	NA	85 days	85 days	
165	Install Door Glass - Area B	2 days	2 days	Mon 5/19/25	Thu 9/18/25	NA	Tue 5/20/25	Fri 9/19/25	NA	85 days	85 days	
166	Pre-Clean before Architect Punchlist - Area B	5 days	5 days	Thu 5/22/25	Tue 9/23/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
167	Architect Punch List Review - Area B	0 days	0 days	Thu 5/29/25	Mon 9/29/25	NA	Thu 5/29/25	Mon 9/29/25	NA	85 days	85 days	
168	Air Balance - Area B	5 days	5 days	Fri 5/30/25	Tue 9/30/25	NA	Thu 6/5/25	Mon 10/6/25	NA	85 days	85 days	
169	Architect Punch List Distributed - Area B	2 days	2 days	Fri 5/30/25	Tue 9/30/25	NA	Mon 6/2/25	Wed 10/1/25	NA	85 days	85 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ◆

Critical

1290110101010101

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.



STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
170	Architect Punch List Worked Off by Contractors - Area B	10 days	10 days	Tue 6/3/25	Thu 10/2/25	NA	Mon 6/16/25	Wed 10/15/25	NA	85 days	85 days	
171	Final Clean after Punchlist worked off - Area B	5 days	5 days	Tue 6/17/25	Thu 10/16/25	NA	Mon 6/23/25	Wed 10/22/25	NA	85 days	85 days	
172	Final Review by Architect - Area B	2 days	2 days	Tue 6/24/25	Thu 10/23/25	NA	Wed 6/25/25	Fri 10/24/25	NA	85 days	85 days	
173	AREA C	289 days	289 days	Mon 8/12/24	Mon 4/29/24	Mon 4/29/24	Mon 9/29/25	Mon 6/16/25	NA	-73 days	-73 days	
174	Footers - Area C	32 days	0 days	Mon 8/12/24	Mon 6/10/24	Mon 6/10/24	Wed 9/25/24	Mon 6/10/24	Mon 6/10/24	-44 days	-75 days	
175	ICF Stem walls- Area C	10 days	1 day	Fri 8/23/24	Mon 7/1/24	Mon 7/1/24	Fri 9/6/24	Mon 7/1/24	Mon 7/1/24	-38 days	-47 days	
176	Underslab CMU - Area C	7 days	1 day	Wed 9/4/24	Fri 7/19/24	Fri 7/19/24	Thu 9/12/24	Fri 7/19/24	Fri 7/19/24	-32 days	-38 days	
177	Underslab Plumbing Rough in - Area C	28 days	0 days	Mon 9/16/24	Mon 4/29/24	Mon 4/29/24	Wed 10/23/24	Mon 4/29/24	Mon 4/29/24	-97 days	-124 days	
178	Stone Backfill non plumbing areas - Area C	3 days	0 days	Fri 10/11/24	Mon 8/5/24	Mon 8/5/24	Tue 10/15/24	Mon 8/5/24	Mon 8/5/24	-48 days	-50 days	
179	Underslab Electrical Rough in - Area C	17 days	0 days	Wed 10/16/24	Wed 7/24/24	Wed 7/24/24	Thu 11/7/24	Wed 7/24/24	Wed 7/24/24	-59 days	-75 days	
180	Stone Backfill at pumbing areas - Area C	3 days	0 days	Tue 10/22/24	Mon 8/5/24	Mon 8/5/24	Thu 10/24/24	Mon 8/5/24	Mon 8/5/24	-55 days	-57 days	
181	Slab Prep 1st Floor - Pour #1 - Area C	3 days	0 days	Wed 10/30/24	Tue 8/6/24	Tue 8/6/24	Fri 11/1/24	Tue 8/6/24	Tue 8/6/24	-60 days	-62 days	
182	Slab Placement 1st Floor - Pour #1 - Area C	1 day	0 days	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	Mon 11/4/24	Thu 8/8/24	Thu 8/8/24	-61 days	-61 days	
183	Prep Slab - Pour #2 - Area C	3 days	0 days	Mon 11/4/24	Tue 8/20/24	Tue 8/20/24	Wed 11/6/24	Tue 8/20/24	Tue 8/20/24	-53 days	-55 days	
184	Hollow Metal Doorframes installation - Area C	3 days	0 days	Thu 11/7/24	Tue 8/13/24	Tue 8/13/24	Mon 11/11/24	Tue 8/13/24	Tue 8/13/24	-61 days	-63 days	
185	Slab Placement - Pour #2 - Area C	1 day	0 days	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	Thu 11/7/24	Fri 8/23/24	Fri 8/23/24	-53 days	-53 days	
186	Prep Slab - Pour #3 - Area C	3 days	0 days	Fri 11/8/24	Tue 8/27/24	Tue 8/27/24	Tue 11/12/24	Tue 8/27/24	Tue 8/27/24	-52 days	-54 days	
187	CMU Bearing Walls - Area C	60 days	0 days	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 2/6/25	Thu 8/15/24	Thu 8/15/24	-62 days	-121 days	
188	ICF Walls - Area C	35 days	0 days	Tue 11/12/24	Tue 8/13/24	Tue 8/13/24	Thu 1/2/25	Tue 8/13/24	Tue 8/13/24	-64 days	-98 days	
189	Plumbing Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Mon 8/19/24	Mon 8/19/24	Thu 1/9/25	Mon 8/19/24	Mon 8/19/24	-60 days	-99 days	
190	Electrical Wall Rough in - Area C	40 days	1 day	Tue 11/12/24	Thu 8/15/24	Thu 8/15/24	Thu 1/9/25	Thu 8/15/24	Thu 8/15/24	-62 days	-101 days	
191	Slab Placement - Pour #3 - Area C	1 day	0 days	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	Wed 11/13/24	Thu 9/5/24	Thu 9/5/24	-49 days	-49 days	
192	Steel Columns/Beams/Bent Plate - Area C	15 days	1 day	Wed 12/4/24	Wed 9/11/24	Wed 9/11/24	Tue 12/24/24	Wed 9/11/24	Wed 9/11/24	-59 days	-73 days	
193	Steel Beams/Hollow Core Plans/Topping - Mezzanine Level - Area C	10 days	1 day	Wed 12/18/24	Thu 12/12/24	Thu 12/12/24	Thu 1/2/25	Thu 12/12/24	Thu 12/12/24	-4 days	-13 days	
194	CMU Non Bearing Walls/Rub all walls - Area C	12 days	0 days	Fri 2/7/25	Mon 9/23/24	Mon 9/23/24	Mon 2/24/25	Mon 9/23/24	Mon 9/23/24	-96 days	-107 days	
195	Set Steel Joists - Area C	47 days	0 days	Fri 2/7/25	Tue 10/29/24	Tue 10/29/24	Mon 4/14/25	Tue 10/29/24	Tue 10/29/24	-70 days	-116 days	
196	Exterior Brick/Stone - Area C	40 days	0 days	Fri 2/7/25	Mon 12/23/24	Mon 12/23/24	Thu 4/3/25	Mon 12/23/24	Mon 12/23/24	-32 days	-71 days	
197	Install Ladders/Handrails Etc... - Area C	7 days	7 days	Fri 1/31/25	Tue 1/14/25	NA	Mon 2/10/25	Wed 1/22/25	NA	-13 days	-13 days	
198	Windows/Glazing/Caulking - Area C	12 days	1 day	Fri 3/7/25	Wed 3/26/25	Wed 3/26/25	Mon 3/24/25	Wed 3/26/25	Wed 3/26/25	13 days	2 days	
199	Roof Deck installation/inspection - Area C	10 days	0 days	Tue 4/15/25	Fri 11/1/24	Fri 11/1/24	Mon 4/28/25	Fri 11/1/24	Fri 11/1/24	-114 days	-123 days	
200	ICF Parapet Walls - Area C	7 days	0 days	Tue 4/15/25	Tue 8/13/24	Tue 8/13/24	Wed 4/23/25	Tue 8/13/24	Tue 8/13/24	-171 days	-177 days	
201	Electrical Rough-In - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Wed 11/20/24	Wed 11/20/24	Tue 5/27/25	Wed 11/20/24	Wed 11/20/24	-101 days	-130 days	
202	Mechanical/Plumbing Rough in - Above Ceiling - Area C	30 days	0 days	Tue 4/15/25	Mon 11/4/24	Mon 11/4/24	Tue 5/27/25	Mon 11/4/24	Mon 11/4/24	-113 days	-142 days	
203	Duct installation - Above Ceiling - Area C	25 days	0 days	Tue 4/15/25	Wed 11/13/24	Wed 11/13/24	Mon 5/19/25	Wed 11/13/24	Wed 11/13/24	-106 days	-130 days	
204	Prep Roof Concrete Slab - Gym - Area C	3 days	0 days	Tue 4/29/25	Mon 3/3/25	Mon 3/3/25	Thu 5/1/25	Mon 3/3/25	Mon 3/3/25	-41 days	-43 days	

Slanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task

Milestone ♦

Critical

1111111111111111

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
205	✓ Roof Wood Blocking - Area C	7 days	0 days	Tue 4/29/25	Tue 11/12/24	Tue 11/12/24	Wed 5/7/25	Tue 11/12/24	Tue 11/12/24	-117 days	-123 days	
206	✓ Pour Roof Concrete Slab - Gym - Area C	1 day	0 days	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	Fri 5/2/25	Tue 3/11/25	Tue 3/11/25	-38 days	-38 days	
207	✓ Sprinkler Rough-In - Above Ceiling - Area C	15 days	1 day	Tue 4/29/25	Thu 3/20/25	Thu 3/20/25	Mon 5/19/25	Thu 3/20/25	Thu 3/20/25	-28 days	-42 days	
208	✓ TPO Roof - Area C	28 days	0 days	Thu 5/8/25	Tue 11/19/24	Tue 11/19/24	Tue 6/17/25	Tue 11/19/24	Tue 11/19/24	-119 days	-146 days	
209	✓ Clean Brick - Area C	10 days	0 days	Fri 4/4/25	Mon 3/10/25	Mon 3/10/25	Thu 4/17/25	Mon 3/10/25	Mon 3/10/25	-19 days	-28 days	
210	✓ Block Filler - Area C	10 days	1 day	Thu 5/15/25	Mon 2/10/25	Mon 2/10/25	Thu 5/29/25	Mon 2/10/25	Mon 2/10/25	-68 days	-77 days	
211	Brick Caulking - Area C	3 days	3 days	Fri 4/18/25	Tue 3/11/25	NA	Tue 4/22/25	Thu 3/13/25	NA	-28 days	-28 days	
212	✓ Gypsum Board walls/soffits - Hang/Finish - Area C	25 days	0 days	Wed 6/11/25	Tue 12/17/24	Tue 12/17/24	Wed 7/16/25	Tue 12/17/24	Tue 12/17/24	-123 days	-147 days	
213	Electrical Systems/Devices - Area C	60 days	60 days	Wed 5/28/25	Thu 4/24/25	Thu 4/24/25	Wed 8/20/25	Fri 7/18/25	NA	-23 days	-23 days	
214	Electrical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Sun 6/1/25	Sun 6/1/25	Tue 6/24/25	Fri 6/27/25	NA	3 days	3 days	
215	Duct/Plumbing/Mechanical Rough in above ceiling - Gym - Area C	20 days	20 days	Wed 5/28/25	Mon 5/19/25	Mon 5/19/25	Tue 6/24/25	Mon 6/16/25	NA	-6 days	-6 days	
216	✓ Mechanical/Plumbing/Duct Insulation - Area C	15 days	0 days	Wed 6/18/25	Mon 2/3/25	Mon 2/3/25	Wed 7/9/25	Mon 2/3/25	Mon 2/3/25	-96 days	-110 days	
217	Set Mechanical Equipment/Tie In - Area C	25 days	25 days	Wed 6/18/25	Mon 5/19/25	Mon 5/19/25	Wed 7/23/25	Mon 6/23/25	NA	-21 days	-21 days	
218	Metal Wall Panels, Coping, Trim etc... - Area C	20 days	20 days	Wed 6/18/25	Wed 11/20/24	NA	Wed 7/16/25	Wed 12/18/24	NA	-146 days	-146 days	
219	Sprinkler Rough in/Heads - Gym - Area C	12 days	12 days	Mon 6/9/25	Wed 5/14/25	Wed 5/14/25	Tue 6/24/25	Mon 6/16/25	NA	-17 days	-6 days	
220	Insulation for Duct/Plumbing/Rough in above ceiling - Gym - Area C	10 days	10 days	Thu 6/12/25	Wed 6/4/25	NA	Wed 6/25/25	Tue 6/17/25	NA	-6 days	-6 days	
221	Install Light Fixtures - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/30/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
222	Blockfill/1st and Final Coat Paint - Walls - Gym - Area C	15 days	15 days	Wed 6/25/25	Mon 6/2/25	Mon 6/2/25	Wed 7/16/25	Mon 7/21/25	NA	-17 days	3 days	
223	Primer/1st Coat of Paint - Walls - Area C	10 days	10 days	Thu 7/17/25	Mon 2/17/25	Mon 2/17/25	Wed 7/30/25	Fri 2/28/25	NA	-106 days	-106 days	
224	✓ Kitchen Hood System - Kitchen - Area C	3 days	0 days	Tue 7/22/25	Tue 1/28/25	Tue 1/28/25	Thu 7/24/25	Tue 1/28/25	Tue 1/28/25	-123 days	-125 days	
225	✓ Set Cooler/Freezer - Kitchen - Area C	4 days	4 days	Tue 7/22/25	Tue 4/29/25	Tue 4/29/25	Fri 7/25/25	Fri 5/2/25	Fri 5/2/25	-58 days	-58 days	
226	HVAC Controls - Area C	25 days	25 days	Thu 7/24/25	Tue 6/24/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
227	Ceiling Grid - Area C	12 days	12 days	Thu 7/31/25	Mon 3/3/25	NA	Fri 8/15/25	Tue 3/18/25	NA	-106 days	-106 days	
228	Above Ceiling Punchlist - Design Team - Gym - Area C	0 days	0 days	Wed 7/16/25	Mon 7/21/25	NA	Wed 7/16/25	Mon 7/21/25	NA	3 days	3 days	
229	Work off Above Ceiling Punchlist - Contractors - Gym - Area C	3 days	3 days	Mon 7/21/25	Thu 7/24/25	NA	Wed 7/23/25	Mon 7/28/25	NA	3 days	3 days	
230	Grilles, Registers, Diffusers, Labeling - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
231	Light Fixtures - Area C	15 days	15 days	Tue 8/5/25	Thu 3/6/25	NA	Mon 8/25/25	Wed 3/26/25	NA	-106 days	-106 days	
232	Sprinkler Heads - Area C	12 days	12 days	Thu 8/7/25	Wed 5/14/25	Wed 5/14/25	Fri 8/22/25	Fri 5/30/25	NA	-59 days	-59 days	
233	Paint - Exposed Ceilings - Gym - Area C	10 days	10 days	Thu 7/24/25	Tue 7/29/25	NA	Wed 8/6/25	Mon 8/11/25	NA	3 days	3 days	
234	Ceramic Tile - Area C	15 days	15 days	Wed 8/13/25	Wed 6/11/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
235	Epoxy Resin Floor - Area C	5 days	5 days	Wed 8/13/25	Wed 6/11/25	NA	Tue 8/19/25	Tue 6/17/25	NA	-44 days	-44 days	
236	Aluminum Storefront Frames and Doors - Area C	10 days	10 days	Thu 8/14/25	Wed 7/16/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
237	Install Spray Applied Cellulosic Insulation - Gym - Area C	10 days	10 days	Thu 8/7/25	Tue 8/12/25	NA	Wed 8/20/25	Mon 8/25/25	NA	3 days	3 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task  Milestone  Critical 

Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
238	Above Ceiling Punch - Engineer - Area C	0 days	0 days	Mon 8/25/25	Mon 6/23/25	NA	Mon 8/25/25	Mon 6/23/25	NA	-44 days	-44 days	
239	Paint - Exposed Ceilings/Floors- Area C	7 days	7 days	Tue 8/26/25	Tue 6/24/25	NA	Thu 9/4/25	Wed 7/2/25	NA	-44 days	-44 days	
240	Work off Above Ceiling Punchlist - Contractors - Area C	5 days	5 days	Wed 8/27/25	Wed 6/25/25	NA	Wed 9/3/25	Tue 7/1/25	NA	-44 days	-44 days	
241	Controlled Air - Area C	0 days	0 days	Wed 8/27/25	Tue 7/29/25	NA	Wed 8/27/25	Tue 7/29/25	NA	-21 days	-21 days	
242	VCT and Base - Area C	20 days	20 days	Thu 9/4/25	Wed 7/30/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
243	Ceiling Tiles - Area C	7 days	7 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/12/25	Fri 7/11/25	NA	-44 days	-44 days	
244	Plumbing Fixtures - Area C	12 days	12 days	Thu 9/4/25	Wed 7/2/25	NA	Fri 9/19/25	Fri 7/18/25	NA	-44 days	-44 days	
245	Epoxy Resin Floor - Kitchen - Area C	10 days	10 days	Thu 9/4/25	Wed 7/2/25	NA	Wed 9/17/25	Wed 7/16/25	NA	-44 days	-44 days	
246	Install Basketball Goals - Gym - Area C	10 days	10 days	Thu 8/21/25	Tue 8/26/25	NA	Thu 9/4/25	Tue 9/9/25	NA	3 days	3 days	
247	Install Scoreboard - Gym - Area C	3 days	3 days	Thu 8/21/25	Tue 8/26/25	NA	Mon 8/25/25	Thu 8/28/25	NA	3 days	3 days	
248	Toilet Partitions and Accessories - Area C	8 days	8 days	Fri 9/12/25	Fri 7/11/25	NA	Tue 9/23/25	Tue 7/22/25	NA	-44 days	-44 days	
249	Casework/Solid Surface Sills - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
250	Final Coat Paint - Walls - Area C	10 days	10 days	Thu 9/18/25	Wed 8/13/25	NA	Wed 10/1/25	Tue 8/26/25	NA	-25 days	-25 days	
251	Install Wood Floor (Install entire floor but sand/finish under bleacher only) - Gym - Area C	18 days	18 days	Fri 9/5/25	Wed 9/10/25	NA	Tue 9/30/25	Fri 10/3/25	NA	3 days	3 days	
252	Kitchen Equipment - Kitchen - Area C	12 days	12 days	Thu 9/25/25	Thu 7/24/25	NA	Fri 10/10/25	Fri 8/8/25	NA	-44 days	-44 days	
253	Display/Tack Boards - Area C	5 days	5 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/8/25	Wed 9/3/25	NA	-25 days	-25 days	
254	Door Frame Paint - 1 Coats - Area C	3 days	3 days	Thu 10/2/25	Wed 8/27/25	NA	Mon 10/6/25	Fri 8/29/25	NA	-25 days	-25 days	
255	Doors & Hardware - Area C	15 days	15 days	Thu 10/2/25	Wed 8/27/25	NA	Wed 10/22/25	Wed 9/17/25	NA	-25 days	-25 days	
256	Interior Signage - Area C	2 days	2 days	Thu 10/9/25	Thu 9/4/25	NA	Fri 10/10/25	Fri 9/5/25	NA	-25 days	-25 days	
257	Kitchen Equipment MEP Hookup - Kitchen - Area C	15 days	15 days	Thu 10/9/25	Thu 8/7/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
258	Overhead Coiling Doors - Kitchen - Area C	5 days	5 days	Mon 10/13/25	Mon 8/11/25	NA	Fri 10/17/25	Fri 8/15/25	NA	-44 days	-44 days	
259	Install Bleachers - Area C - Gym - Area C	12 days	12 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/16/25	Tue 10/21/25	NA	3 days	3 days	
260	Sound Wall Panels - Gym - Area C	7 days	7 days	Wed 10/1/25	Mon 10/6/25	NA	Thu 10/9/25	Tue 10/14/25	NA	3 days	3 days	
261	Install Athletic Equipment - Gym - Area C	3 days	3 days	Wed 10/1/25	Mon 10/6/25	NA	Fri 10/3/25	Wed 10/8/25	NA	3 days	3 days	
262	Doorframe Paint - 2nd Coat - Area C	3 days	3 days	Thu 10/23/25	Thu 9/18/25	NA	Mon 10/27/25	Mon 9/22/25	NA	-25 days	-25 days	
263	Install Door Glass - Area C	2 days	2 days	Thu 10/23/25	Thu 9/18/25	NA	Fri 10/24/25	Fri 9/19/25	NA	-25 days	-25 days	
264	Pre-Clean before Architect Punchlist - Area C	5 days	5 days	Tue 10/28/25	Tue 9/23/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
265	Seal and Stripe Gym Wood Floor -- Gym - Area C	7 days	7 days	Fri 10/17/25	Wed 10/22/25	NA	Mon 10/27/25	Thu 10/30/25	NA	3 days	3 days	
266	Architect Punch List Review - Area C	0 days	0 days	Mon 11/3/25	Mon 9/29/25	NA	Mon 11/3/25	Mon 9/29/25	NA	-25 days	-25 days	
267	Air Balance - Area C	5 days	5 days	Tue 11/4/25	Tue 9/30/25	NA	Mon 11/10/25	Mon 10/6/25	NA	-25 days	-25 days	
268	Architect Punch List Distributed - Area C	2 days	2 days	Tue 11/4/25	Tue 9/30/25	NA	Wed 11/5/25	Wed 10/1/25	NA	-25 days	-25 days	
269	Kitchen Hood Certificate - Area C	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
270	Architect Punch List Worked Off by Contractors - Area C	10 days	10 days	Thu 11/6/25	Thu 10/2/25	NA	Wed 11/19/25	Wed 10/15/25	NA	-25 days	-25 days	
271	Final Clean after Punchlist worked off - Area C	5 days	5 days	Thu 11/20/25	Thu 10/16/25	NA	Wed 11/26/25	Wed 10/22/25	NA	-25 days	-25 days	
272	Final Review by Architect - Area C	2 days	2 days	Fri 11/28/25	Thu 10/23/25	NA	Mon 12/1/25	Fri 10/24/25	NA	-25 days	-25 days	

Stanton Elementary School - Updated June 2025 MMM
Date: Tue 6/10/25 KD

Task



Milestone ◆

Critical



Items incidental to each task shown are to be incorporated into this schedule. This schedule is based on working days and acknowledges the following holidays: New Years Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day & Christmas Day.

STANTON ELEMENTARY SCHOOL

ID	Task Name	Baseline Duration	Duration	Baseline Start	Start	Actual Start	Baseline Finish	Finish	Actual Finish	Start Variance	Finish Variance	2019
273	Fine Grading/Topsoil Distribution	6 days	6 days	Thu 7/24/25	Fri 12/27/24	NA	Thu 7/31/25	Mon 1/6/25	NA	-146 days	-146 days	
274	Stone Base - Drives and Lots	10 days	10 days	Fri 8/1/25	Tue 1/7/25	NA	Thu 8/14/25	Mon 1/20/25	NA	-146 days	-146 days	
275	Exterior Lighting	25 days	25 days	Tue 8/19/25	Tue 3/18/25	NA	Tue 9/23/25	Mon 4/21/25	NA	-108 days	-108 days	
276	Concrete Curb and Gutters	12 days	12 days	Fri 8/15/25	Tue 1/21/25	NA	Tue 9/2/25	Wed 2/5/25	NA	-146 days	-146 days	
277	Site Concrete Walks	30 days	30 days	Wed 9/3/25	Tue 4/1/25	Tue 4/1/25	Tue 10/14/25	Mon 5/12/25	NA	-108 days	-108 days	
278	Install Site Sign	10 days	10 days	Wed 9/17/25	Tue 4/15/25	NA	Tue 9/30/25	Mon 4/28/25	NA	-108 days	-108 days	
279	Install Flag Pole	2 days	2 days	Wed 10/8/25	Tue 5/6/25	NA	Thu 10/9/25	Wed 5/7/25	NA	-108 days	-108 days	
280	Chain Link Fence	3 days	3 days	Wed 10/15/25	Tue 5/13/25	NA	Fri 10/17/25	Thu 5/15/25	NA	-108 days	-108 days	
281	✓ Install Canopies	15 days	0 days	Wed 10/15/25	Tue 4/1/25	Tue 4/1/25	Tue 11/4/25	Tue 4/1/25	Tue 4/1/25	-138 days	-152 days	
282	Seeding/Sod and Landscaping	20 days	20 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
283	Exterior Paint/Caulk	10 days	10 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 10/28/25	Tue 5/27/25	NA	-108 days	-108 days	
284	Paving/Striping/Wheel Stops	15 days	15 days	Wed 10/15/25	Tue 5/13/25	NA	Tue 11/4/25	Tue 6/3/25	NA	-108 days	-108 days	
285	Boiler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
286	Sprinkler Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
287	Fire Alarm Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
288	Plumbing Certificate	0 days	0 days	Wed 10/29/25	Wed 8/27/25	NA	Wed 10/29/25	Wed 8/27/25	NA	-44 days	-44 days	
289	Electrical Certificate	0 days	0 days	Wed 10/29/25	Tue 10/21/25	NA	Wed 10/29/25	Tue 10/21/25	NA	-6 days	-6 days	
290	Exterior Signage	3 days	3 days	Wed 11/5/25	Wed 6/4/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
291	Architect Site Punch List Review - Site	0 days	0 days	Fri 11/7/25	Fri 6/6/25	NA	Fri 11/7/25	Fri 6/6/25	NA	-108 days	-108 days	
292	Kitchen Hood Certificate	0 days	0 days	Wed 11/5/25	Thu 9/4/25	NA	Wed 11/5/25	Thu 9/4/25	NA	-44 days	-44 days	
293	Occupancy Permit	0 days	0 days	Wed 11/5/25	Tue 10/21/25	NA	Wed 11/5/25	Tue 10/21/25	NA	-11 days	-11 days	
294	Substantial Completion	0 days	0 days	Fri 11/7/25	Tue 10/21/25	NA	Fri 11/7/25	Tue 10/21/25	NA	-13 days	-13 days	
295	Closeout and Owner Training	10 days	10 days	Mon 11/10/25	Wed 10/22/25	NA	Fri 11/21/25	Tue 11/4/25	NA	-13 days	-13 days	
296	Architect Site Punch List Distrubuted - Site	0 days	0 days	Tue 11/11/25	Tue 6/10/25	NA	Tue 11/11/25	Tue 6/10/25	NA	-108 days	-108 days	
297	Architect Site Punch List Worked Off by Contractors - Site	10 days	10 days	Wed 11/12/25	Wed 6/11/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
298	Final Site Review by Architect - Site	0 days	0 days	Tue 11/25/25	Tue 6/24/25	NA	Tue 11/25/25	Tue 6/24/25	NA	-108 days	-108 days	
299	Final Completion	0 days	0 days	Thu 12/4/25	Fri 11/14/25	NA	Thu 12/4/25	Fri 11/14/25	NA	-13 days	-13 days	
