




HARDIN COUNTY SCHOOLS
HELPING CHILDREN SUCCEED

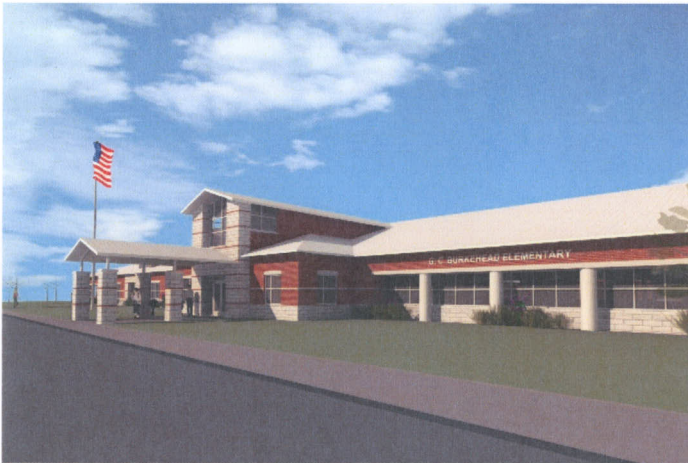

May 2014 Board Update

Hardin County Board of Education

GC Burkhead Elementary School



MURPHY • GRAVES • TRIMBLE, PLLC
ARCHITECTURE | PLANNING | INTERIORS

Overview

Budget:

Original Construction Cost: \$15,817,590.00

Present Construction Cost: \$15,817,590.00

Schedule:

Original Substantial Completion: 06/30/15

Final Completion: 07/30/15



The following notes highlight the activities over the last Thirty (30) days of the project:

Meetings

Pre-Construction Meeting took place on April 29th, 2014.

Shop Drawings

Fifty Five (55) Shop Drawings have been received from DW Wilburn and are being reviewed by the Design Team.

RFI'S

Nine (9) RFI's have been received and are being reviewed and responded to by the Design Team

ASI's

No ASI's have been issued to date

Construction Last 30 Days

Silt Fence / Erosion Control in place

Building pad at Sub-grade

Removal and stockpile of topsoil

Construction Snapshot next 30 Days

Building Pad complete

Foundations Started

Underground Utilities (water/electric)

Storm Drainage Started

