



HARDIN COUNTY SCHOOLS EARLY COLLEGE AND CAREER CENTER

SCB Project No. 1309

Construction Update **June 4, 2014**



Original Construction Cost:	\$15,362,000.00
Present Construction Cost:	\$15,495,343.00 (<i>Revised by Change Order No. 4</i>)

Original Completion Dates	
Substantial Completion:	July 1, 2014
Final Completion:	August 1, 2014

Anticipated Completion Dates	
Substantial Completion:	July 1, 2014
Final Completion:	August 1, 2014

Progress Report

Past Two Weeks Progress:

1. Continued paving, curbs, and sidewalks
2. Completed CMU on Upper Level
3. Completed brick veneer on building
4. Continued roofing, flashing, curbs, and pipe penetrations
5. Completed GWB on Upper Level
6. Completed Hollow Metal doors and frames
7. Continued visual display boards following painter
8. Completed stainless steel wainscot at Culinary Arts
9. Completed locker installation
10. Continued painting
11. Continued ceiling grid
12. Continued polished concrete floor system at Upper Level
13. Continued window installation
14. Completed hydronic piping at Upper Level
15. Factory started heat pumps by Trane
16. Continued duct work on Upper Level
17. Continued electrical devices, light fixtures, and hook up roof top units
18. Continued building racks and data closets
19. Completed operable panel partitions
20. Continued HVAC controls
21. Continued fire suppression at Upper Level

Next Two Weeks Progress:

1. Complete brick at sign wall
2. Complete roofing and walk pads
3. Continue sheet metal
4. Complete ceiling grid
5. Continue painting
6. Continue windows
7. Start aluminum doors
8. Install brackets for the sunshades
9. Complete plumbing fixtures at restrooms
10. Continue sidewalks, curbs, and paving
11. Place topsoil at islands and around building
12. Start trees at island

Lower Level

1



1




3



2



Upper Level

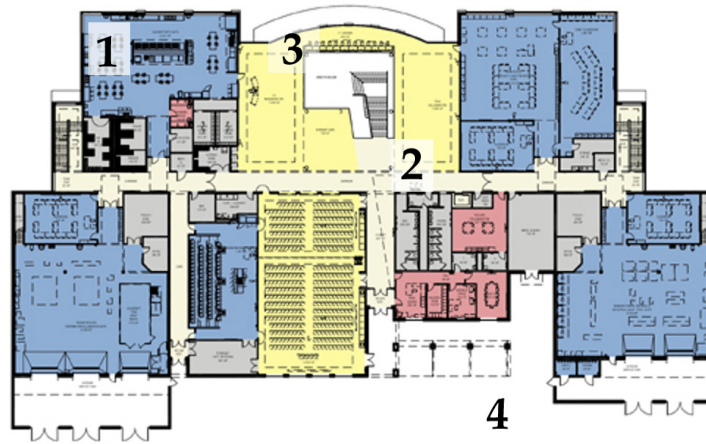

1



2



3



4

