




HARDIN COUNTY SCHOOLS  
HELPING CHILDREN SUCCEED

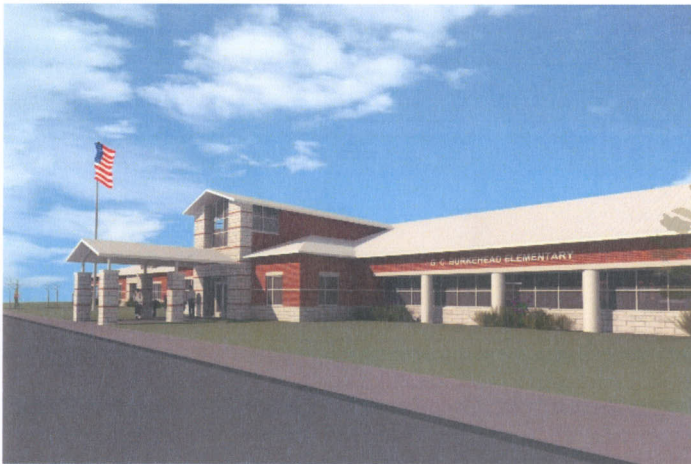

May 2015 Board Update

Hardin County Board of Education

---

GC Burkhead Elementary School



MURPHY • GRAVES • TRIMBLE, PLLC  
ARCHITECTURE | PLANNING | INTERIORS

# Overview

---

## **Budget:**

Original Construction Cost: \$15,817,590.00  
Change Orders: \$1,600 in credit  
Present Construction Cost: \$15,818,990.00

## **Schedule:**

Original Substantial Completion: 06/30/15  
Final Completion: 07/30/15

---

The following notes highlight the activities over the last Thirty (30) days of the project:

## **Meetings**

Progress Meetings took place on April 16, 2015 and April 30, 2015 (See attached meeting minutes).  
Door Hardware Pre-installation meeting took place on April 16, 2015 (See attached meeting minutes).

## **Shop Drawings**

Two (2) shop drawing was submitted.

## **RFI's**

Three (3) RFI's have been received and responded to by the Design Team.

## **ASI's**

Three (3) ASI's have been issued to date.

## **Attachments:**

1. Progress Meeting Notes (4/16/15)
2. Door Hardware Pre-Install Notes
3. Marcum Construction Report
4. MGT Field Report
5. Progress Meeting Notes(4/30/15)

# Schedule

---

## **Construction Last 15 Days: (see attached Field Report)**

Geothermal and building loops flushed and treated.  
Hoods installed in kitchen.  
Installing duct in Main hallway.  
Complete duct in gym.  
Kiln hood installed.  
Duct work installed in Media center and Cafeteria.  
Electric continues in area A.  
Masonry work on main building is complete.  
Masonry work complete at maintenance building.  
Beginning masonry punch work.  
2<sup>nd</sup> entry road graded installing curbs.  
Completing curbs in rear parking area.  
Sidewalks continue.  
Canopies complete.  
Basketball rims installed.  
Painting continues.  
Ceramic Tile continues in area A.  
Drywall complete in areas D and C.  
Soffits continue in area B.  
Roof soffits continue.

## **Construction Snapshot next 15 Days:**

All Geothermal mains and taps complete.  
Hose kits complete (geo).  
Finish Ductwork in area A.  
All roof-top units installed.  
Roof work complete.  
Install border cuts in ceilings areas B,C and D.  
Complete drywall hanging.  
Complete tile work.  
Light gauge trusses set on Maintenance building.  
Complete curbs.  
Complete paint in areas B2, C, D.  
Complete casework in areas B2, C, D.  
Begin installation of VET.  
Complete caulking in areas B, C and D.  
Rework insulation following soffits.



**HARDIN COUNTY SCHOOLS**  
HELPING CHILDREN SUCCEED



May 2015 Board Update  
Hardin County Board of Education

---

**New Highland Elementary Secure Vestibule Upgrade**



**MURPHY · GRAVES · TRIMBLE, PLLC**  
ARCHITECTURE | PLANNING | INTERIORS

# Overview

---

## Budget:

Original Construction Cost: \$36,000

Present Construction Cost: n/a

## Schedule:

DD and CD Approval: 5/21/2015

BG-2, BG-3 Approval: 5/21/2015

---

The following notes highlight the activities over the last Thirty (30) days of the project:

## Meetings

n/a

## Shop Drawings

n/a

## RFI'S

n/a

## ASI's

n/a

# Schedule

---

## Last 30 Days:

Provide Design Development and Construction Documents for approval.

BG-2, BG-3 for approval.

## Next 30 Days:

Submit documents and BG's to KDE for approval.



**HARDIN COUNTY SCHOOLS**  
HELPING CHILDREN SUCCEED



May 2015 Board Update  
Hardin County Board of Education

---

**North Park Elementary Secure Vestibule Upgrade**



**MURPHY • GRAVES • TRIMBLE, PLLC**  
ARCHITECTURE | PLANNING | INTERIORS



# Overview

---

## Budget:

Original Construction Cost: \$80,000

Present Construction Cost: n/a

## Schedule:

DD and CD Approval: 5/21/2015

BG-2, BG-3 Approval: 5/21/2015

---

The following notes highlight the activities over the last Thirty (30) days of the project:

### Meetings

MGT met Mr. Milby and the principal to discuss the design development of the project.

### Shop Drawings

n/a

### RFI'S

n/a

### ASI's

n/a

# Schedule

---

## Last 30 Days:

Provide Design Development and Construction Documents for approval.

BG-2, BG-3 for approval.

## Next 30 Days:

Submit documents and BG's to KDE for approval.
