



Cecilia Valley Elementary



Construction Update

June 9, 2017

Original Construction Cost:	\$15,510,000.00
Present Construction Cost:	\$15,517,604.00 (Revised by Change Order No. 03)

Original Completion Dates	
Substantial Completion:	September 1, 2017
Final Completion:	October 1, 2017

Anticipated Completion Dates	
Substantial Completion:	September 19, 2017 (Revised by Change Order No. 3)*
Final Completion:	October 19, 2017 (Revised by Change Order No. 3)*

*ITC advises of weather delay request for previous two months to be submitted.



Change Order Summary

<u>Change Order</u>	<u>Amount</u>	<u>Status</u>	<u>Rvsd. Contract Amount</u>
Change Order No. 01	\$3,765.00	BOE Approved	\$15,513,765.00
Change Order No. 02	\$0.00**	BOE Approved	\$15,513,765.00
Change Order No. 03	\$3,839.00	BOE Approved	\$15,517,604.00
Change Order No. 04	\$33,737.00	BOE Approved	\$15,551,341.00

Summary

- Exterior face brick veneer ongoing.
- Exterior storefronts windows commenced.
- Interior cast stone / brick veneer commenced.
- Interior CMU nearly complete.
- ICF parapets have commenced.
- Metal roof decking nearly complete.
- Metal trusses at clerestory installed.
- Clerestory secondary framing commenced.
- Roofing of ground floor areas is dried-in and nears completion.
- Roofing of second floor areas has commenced.
- Kitchen M/E rough-in ongoing
- 2nd floor M/E rough-in ongoing
- Piping insulation has commenced.
- 2nd floor fire suppression sprinklering ongoing.
- Pump station nearly complete
- Storm system piping nearly complete
- Special Inspections ongoing. No outstanding issues.




Cafeteria / Entry / Gym



Gym / Art / FMD / Stair "B"



Gym / Art beyond

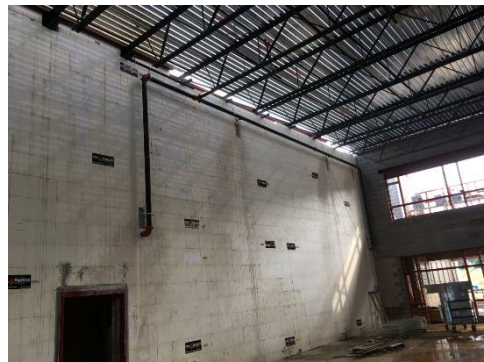

Cafeteria



Entry Vestibule at Front



2nd Floor Classroom
