



BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE



PREVIOUS TWO WEEKS:

- Retaining wall excavation completed to edge of building (kitchen).
- Forming next Gymnasium retaining wall section (north wall).
- Floor Slab placed in lower level classroom wing and storm shelter.
- ICF walls installed in partial upper level classroom wing.
- Electrical rough-in lower level classroom wing and storm shelter.
- Electrical rough-in at the next Gymnasium retaining wall section.
- Plumbing underground in lower level classroom wing and storm shelter.
- Week of 7/5/21, retaining wall foundation rebar was removed due to heavy rains and mud slides which covered the installed rebar. The majority of the week was spent pumping and mucking mud from the area.
- All day rain days occurred on 7/1/21 and 7/11/21.

FORECASTED WORK:

- Place retaining wall foundation Friday 7/16/21 from Gymnasium to SW corner of Kitchen.
- Place next 50' of Gymnasium retaining wall and structural piers.
- Anticipate interior footers in lower and upper level classroom wings.
- Anticipate slab prep for remainder of Lower Level classroom wing.
- Joists are being delivered for Gym and Commons areas.
- Masonry loadbearing walls in lower level classroom wing and storm shelter.
- Once loadbearing walls are to Upper Level, joist/deck and ICF will follow.



BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE





BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

CONSTRUCTION PROGRESS – SITE & BUILDING PROGRESS
NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE





BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

CONSTRUCTION PROGRESS – SITE & BUILDING PROGRESS
NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE





BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

CONSTRUCTION PROGRESS – SITE & BUILDING PROGRESS

NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE





BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021


DRONE AERIAL FOOTAGE – BRET HIGHLEY – JULY 22ND, 2021
NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE



Use of the Soil Stabilization Allowance to Date:

Since the last board meeting use of the Soil Allowance has not been needed – the remaining balance of the allowance is \$175,697.06.

Billing towards the Allowance will be made to account for some work at the building retaining wall foundation. Pricing will be reviewed at the next Board Meeting once prepared.

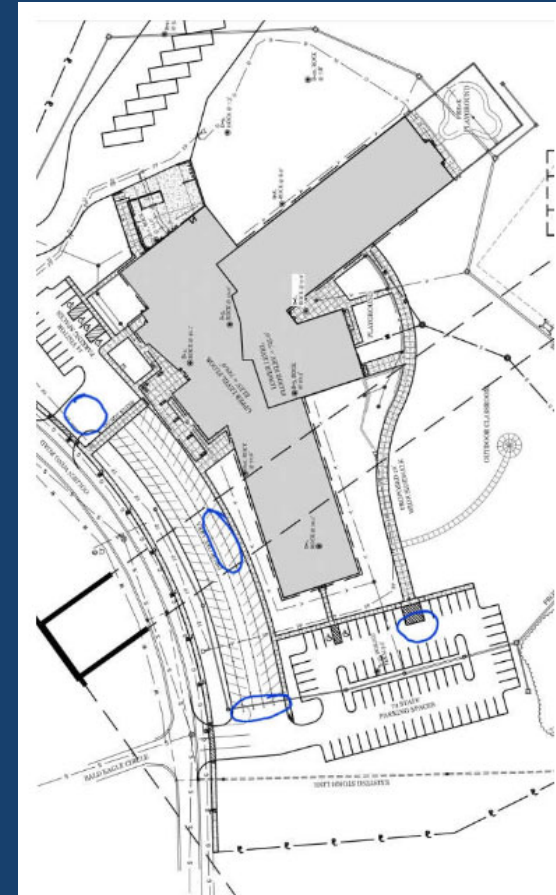

BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE



Upcoming Change Order – HBC Required Changes to School Design:

Update on Cost Changes

Redlee Construction has submitted pricing for the remaining changes related to HBC required revisions:

To be submitted at next Board Meeting:


1.) The South Stair Extension

- Submitted pricing is currently under review – Proposed Cost: \$9,769.25. Revisions are underway to account for unit costs.

For Board Approval Tonight:

2.) The Door Changes at the Main Building

On Agenda for Review Tonight – Change Order 5 Cost - \$29,070.01

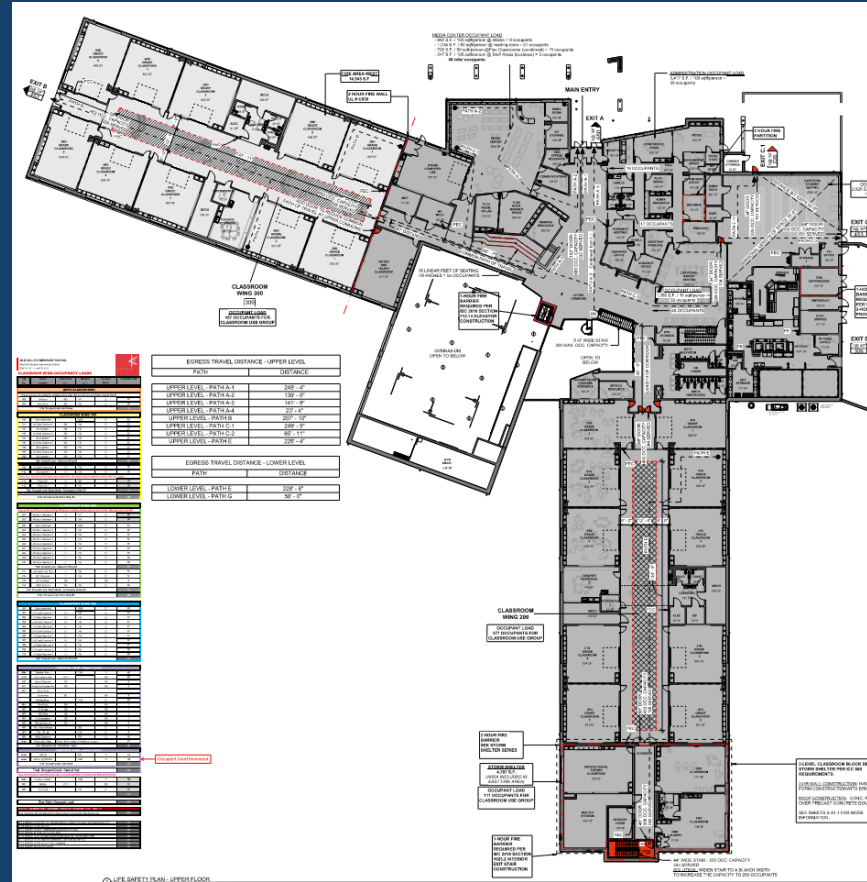

BULLITT COUNTY PUBLIC SCHOOLS
BOARD OF EDUCATION – JULY 26, 2021

NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE

