



studio kremer architects

October 23, 2023 Design and Construction Update





Current Status

Close-Out Paperwork is being reviewed and executed.

Board Consent Items

Substantial Completion Certificate - Calhoun


Change Order #21

*Final Allowance Rectification
Soils and Geothermal*



Football Stadiums - Substantial Completion



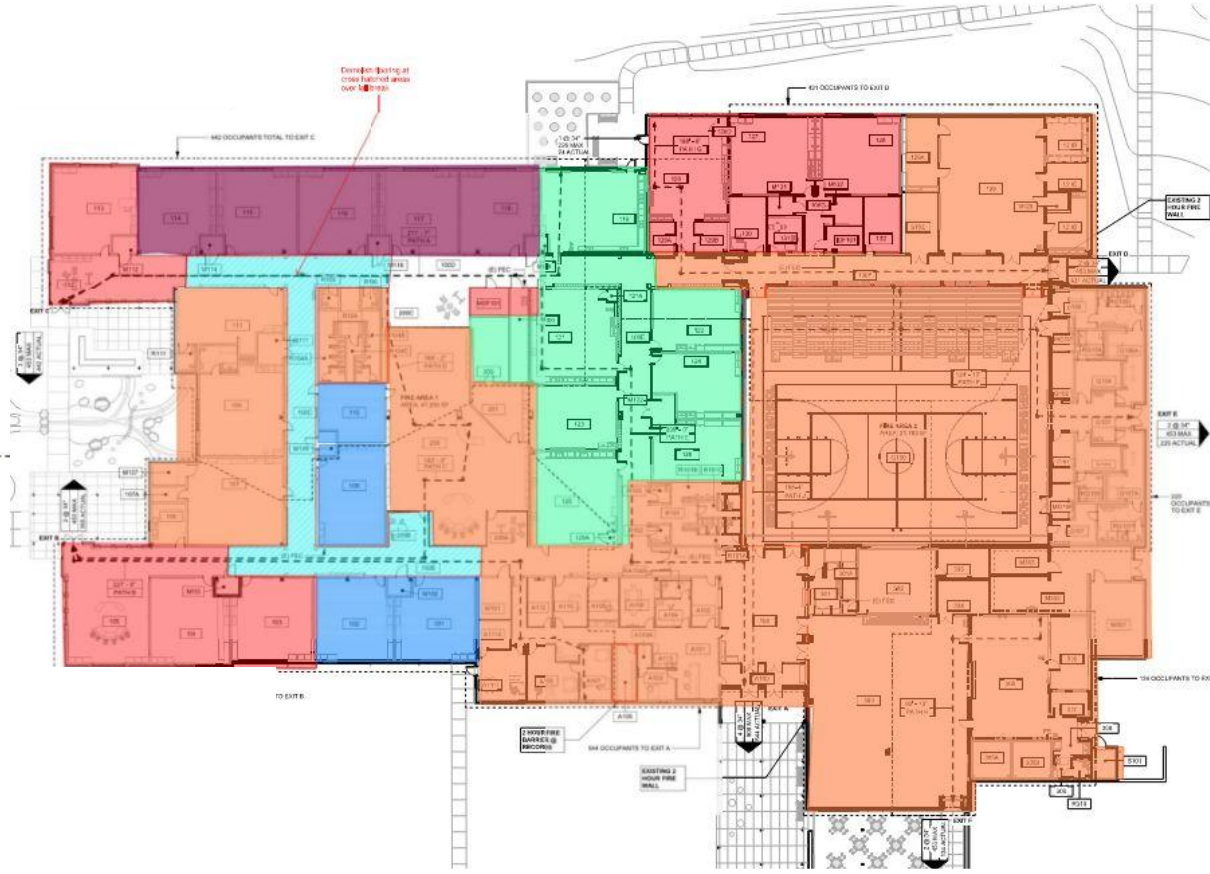

- July 17th - January 12th
- January 12th 2024 - March 11th
- March 12th - May 17th
- May 18th 2024 - First Day of Sch August 2024
- May 18th - Christmas Break 2024



Bernheim Middle School - Construction





Bernheim Middle School - Construction





Bernheim Middle School - Construction





Bernheim Middle School - Construction



Board Consent Items

Upcoming consent items for November 13th Worksession

V/E Change Order Credit to the General Construction Contract that reflect results of the V/E Effort that will be added to Construction Contingency. Change Order had to be prepared after all DPOs were executed to realize any material savings.

Interior Finishing Change Order

A Change Order for addressing the interior finish where existing brick was removed will be on the next Board agenda. The Design Team recommends new drywall finishes in the spaces where this occurs.



Bernheim Middle School - Construction





Bullitt East High School - Construction Documents





Bullitt East High School - Construction Documents



BEHS Fine Arts - Design and Bid Schedule:

- **October 23rd - BOARD MEETING** - Request Approval of 100% CDs and Release for Bid

November 1st - Release for Bid

Increasing length of the Bid Period to work around Thanksgiving and make sure Bidders have time to review Documents.

December 1st - Bid Opening

- **December 11th – BOARD MEETING** - Request Approval of Award of Contract
- **December 18th – BOARD MEETING** - *Back-Up Board Meeting Day if any Dates listed here get pushed*



Bullitt East High School - Construction Documents
