



FIELD OBSERVATION REPORT

Central Hardin High School – Phase 2, 2019111 -CA8

Date: 10/24/2025 Time: 12:30 PM

Weather: Clear

Observed by: Joseph Jones, AIA

Report No: 33

Trades Observed on Site: General Trades, Framers, Flooring Installers, Plumbers, HVAC, Electricians,

1. Work observed in Progress

- a) The Area J second floor punch list was being corrected.
- b) The floors which needed repair in two of the classrooms on the second floor had been repaired.
- c) The first floor of Area J was being made ready for a punch list inspection on 10-16-2025.
- d) Work was ongoing for the soffit of the Area J overhang.
- e) Rubber flooring was being installed on the first floor of Area J.
- f) Preparations were started to seal off the connecting corridors from Area J to Area H.

2. General Observations

- a) The elevations of Area J with the exposed weather barrier have been measured for the metal panel system. Each panel will have an exact location for placement on the exterior.



- b) Windows in Area J have been installed, and sealant has been applied at all sides.

We are still waiting on pricing to stain some of the bricks to match surrounding bricks.



- c) Gill reported that the wallboard backup for the Area J soffit will pause until the fireproofing contractor returns to spray fire resistive material on the structure for the overhang.


We are still waiting on pricing to replace the angle supporting the brick on the overhang.



- d) The store front window system at the connecting corridor was in place.



- e) The original connecting corridor to Area H had been sealed off from Area J.

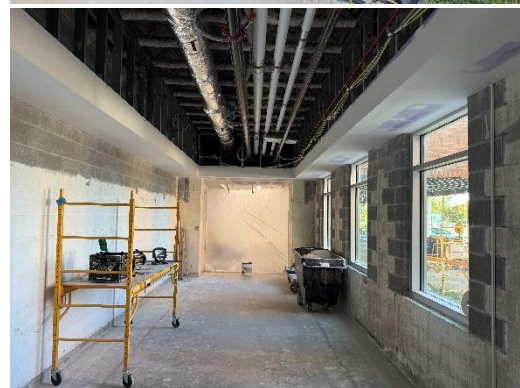

- f) On the first floor of Area J, rubber flooring was being installed in the corridors.



- g) Most of the finishes and accessories are in place on the first floor of Area J.




- h) Display boards and the digital displays were installed on the first floor of Area J




- i) Most ceilings, flooring and wall base were installed on the first floor of Area J.



- j) The installation of rubber flooring on the first floor of Area J was nearing completion.

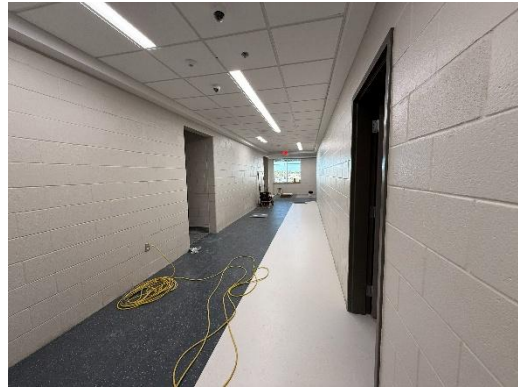


- k) The toilets rooms on the first floor of Area J appeared to be complete except for final cleaning.

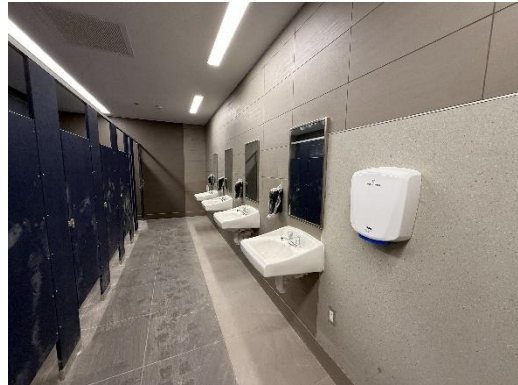

- l) Once flooring is installed, wall base will be installed.



- m) The flooring and treads were installed for the north stair in Area J. The south stair will be the last area to be completed.

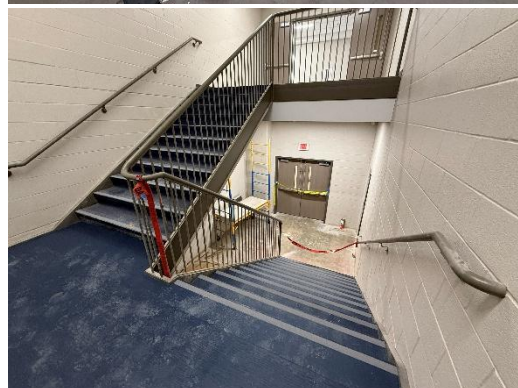

- n) Repairs to the two south classrooms on the second floor were completed. The repairs were almost not perceptible.
- o) The work noted in the punch list for the second floor appeared to be mostly complete.
- p) The mason had repaired the block walls where the original and new block presented uneven appearance.
- q) Pipes and conduits through the second floor slab were properly sealed with fire resistant sealants.



- r) Walls in the storage rooms that had not been properly prepped were corrected.



- s) This opening to the connecting corridor to Area H will be sealed before students occupy Area J.



- t) The mechanical room had been cleaned up, and the equipment appeared to be operational.



- u) Refer to STW's punchlist inspection for electrical and mechanical items needing correction.



3. Stored Material Observed:

- a) Concrete accessories.
- b) Brick, CMUs and accessories.
- c) Sanitary, domestic water piping and fittings, fixtures
- d) Windows.
- e) Paint.
- f) Wallboard, metal framing and accessories.
- g) Ceiling grid and tile.
- h) Sheet metal panels.
- i) Electrical conduits, wiring and fittings.
- j) Metal Framing.

4. Follow up items:

- a) Monitor floor prep costs on a time and materials basis.
- b) Note changes on the As-Built Drawings.

Follow up by:

☐ Architect, ☐ Owner, ☐ MEP Engineer, ☐ Structural Engineer,
☐ Civil Engineer ☒ Construction Manager, ☐ Other

Respectfully submitted,

JRA Architects
Joseph Jones, AIA,
Construction Contract Administrator

Cc: 2019111, CA8, HCS, Codell, B+K, STW, EDG, JRA
