APPLICATION AND CERTIFICATE FOR PAYMENT

Invoice #: Elizabethtown Ind. Board of Education **Project** 25-011 T K Stone Middle School GC KY Contract For: **Bid Division** CONTRACTOR'S APPLICATION FOR PAYMENT **DEDUCTIONS** \$0.00 Contract Sum To Date \$0.00 Retainage @ 10.00% Total Retainage Total Earned Less Retainage \$0.00 \$0.00 Current Payment Due

Contract Date Builders & Monagers Application is made for payment, as shown below, in connection with the Contract. Continuation Sheet is attached \$1,564,340.00 Original Contract Sum Net Change By Change Order

Application No...

Period To 11/5/2025

Net Change Orders \$0.00 The undersigned Contractor certifies that to the best of the Contractor's knowledge,

\$0.00

\$0.00

information, and belief, the work covered by this Application for Payment has been completed in accordance with the Contract Documents. That all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due.

ALLIANCE CORPORATION CONTRACTOR

ARCHIPECT'S CERTIFICATÉ FOR PAYMENT

In accordance with the Contract Documents, based on on-site observations and the data comprising the above application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information, and belief, the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor

AMOUNT CERTIFIED \$143,153,54

To Owner:

Attention:

TOTAL

Change Order Summary

Change Orders approved in

previous months by Owner

Approved This Month

219 Helm Street

Elizabethtown, KY 42701

ADDITIONS

Subscribed and sworn to before me this day of

1070

State of:

Bv:

Notary Public:

My Commission

Architects C

County of:

\$0.00

\$1,564,340.00

\$480,988.81

\$48.098.90

\$48,098.90

\$432,889.91

\$289,736.37

\$143,153.54

ALLIANCE CORPORATION CM Approval:

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment, and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

CONTINUATION SHEET

Application and Certification for Payment, containing

Contractor's signed certification is attached.

In tabulations below, amounts are stated to the nearest dollar.

Use Column I on Contracts where variable retainage for line items may apply.

Invoice #:

Contract: 25-011 T K Stone Middle School GC

Application No.:

6

Application Date: 11/5/2025

To:

Architect's Project No.:

\mathbf{A}	B	C	D	E	F	G		H	
tem	Description of Work	Scheduled	Work Co	mpleted	Materials	Total	%	Balance	Retainage
No.		Value	From Previous Application (D+E)	This Period In Place	Presently Stored	Completed and Stored To Date	(G/C)	Ta Finish (C-G)	
					(Not in D or E)	(D+E+F)			
1	T K Stone Middle School GC	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
2	****Division 1*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
	Insurance and Bonds	47,333.00	47,333.00	0.00	0.00	47,333.00	100.00%	0.00	
- 1	General Conditions	381,767.00	87,806.41	0.00	0.00	87,806.41	23.00%	293,960.59	
- 1	Temoprary Fencing	8,500.00	4,250.00	0.00	0.00	4,250.00	50.00%	4,250.00	
	Barrier Allowance (300 Carpenter Hours)	13,500.00	2,520.00	0.00	0.00	2,520.00	18.67%	10,980.00	
	Barrier Allowance (300 Laborer Hours)	13,500.00	0.00	0.00	0.00	0.00	0.00%	13,500.00	
- 1	Barrier Allowance (Material)	10,000.00	206.49	0.00	0.00	206.49	2.06%	9,793.51	
- 1	Dumpster Allowance	60,000.00	9,469.43	0.00	0.00	9,469.43	15.78%	50,530.57	
- 1	Material Allowance	15,000.00	1,450.60	0.00	0.00	1,450.60	9.67%	13,549.40	
- 1	Laborer Allowance	9,000.00	0.00	0.00	0.00	0.00	0.00%	9,000.00	
- 1	Stone Allowance (1500 Tons)	52,500.00	0.00	0.00	0.00	0.00	0.00%	52,500.00	
- 1	Carpenter Allowance	9,000.00	2,160.00	0.00	0.00	2,160.00	24.00%	6,840.00	
- 1	Cleanup	2,500.00	375.00	0.00	0.00	375.00	15.00%	2,125.00	
- 1	Closeout	2,750.00	0.00	0.00	0.00	0.00	0.00%	2,750.00	
- 1	Submittals	2,500.00	2,125.00	0.00	0.00	2,125.00	85.00%	375.00	
17	Mobilization	15,000.00	11,250.00	0.00	0.00	11,250.00	75.00%	3,750.00	
18	****Division 2*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
19	Selective Structure Demolition Material	115,685.00	34,705.50	17,352.75	0.00	52,058.25	45.00%	63,626.75	
20	Selective Structure Demolition Labor	236,906.00	71,071.80	35,535.90	0.00	106,607.70	45.00%	130,298.30	
21	Shoring Material	5,500.00	1,100.00	1,375.00	0.00	2,475.00	45.00%	3,025.00	
- 1	Shoring Labor	6,500.00	1,300.00	1,625.00	0.00	2,925.00	45.00%	3,575.00	
	****Division 6*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
- 1	Rough Carpentry Material	42,932.00	12,879.60	6,439.80	0.00	19,319.40	45.00%	23,612.60	
- 1	Rough Carpentry Labor	101,837.00	30,551.10	15,275.55	0.00	45,826.65	45.00%	56,010.35	
	****Division 7*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
- 1	Expanison Joint Cover Assemblies Material	15,000.00	0.00	0.00	0.00	0.00	0.00%	15,000.00	
- 1	Expanison Joint Cover Assemblies Labor	6,000.00	0.00	0.00	0.00	0.00	0.00%	6,000.00	
- 1	****Division 10*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
- 1	Metal Lockers Labor	25,900.00	0.00	0.00	0.00	0.00	0.00%	25,900.00	

CONTINUATION SHEET

Application and Certification for Payment, containing

Contractor's signed certification is attached.

In tabulations below, amounts are stated to the nearest dollar.

Use Column I on Contracts where variable retainage for line items may apply.

Invoice #:

1070

Contract: 25-011 T K Stone Middle School GC

Application No.:

6

Application Date: 11/5/2025

To:

Architect's Project No.:


Α	B	C	D Work Co	E	F	G	9/	Palanas	Retainage
tem No.	Description of Work	Scheduled Value	From Previous Application (D+E)	This Period In Place	Materials Presently Stored	Total Completed and Stored To Date	% (G/C)	Balance To Finish (C-G)	Ketainag
					(Not in D or E)	(D+E+F)			
31	Aluminum Canopy - Material	40,092.00	0.00	0.00	0.00	0.00	0.00%	40,092.00	
32	Aluminum Canopy - Labor	24,247.00	0.00	0.00	0.00	0.00	0.00%	24,247.00	
33	Aluminum Canopy - Misc.	13,050.00	0.00	0.00	0.00	0.00	0.00%	13,050.00	
	Flagpole Material	7,641.00	1,375.38	0.00	0.00	1,375.38	18.00%	6,265.62	
	Flagpole Labor	1,350.00	0.00	0.00	0.00	0.00	0.00%	1,350.00	
	****Division 12*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
- 1	Roller Window Shades Material	60,720.00	0.00	0.00	0.00	0.00	0.00%	60,720.00	
	Roller Window Shades Labor	8,719.00	0.00	0.00	0.00	0.00	0.00%	8,719.00	
	****Division 32*****	0.00	0.00	0.00	0.00	0.00	0.00%	0.00	
	Chain Link Fences & Gates Material	162,911.00		81,455.50	0.00	81,455.50	50.00%	81,455.50	
	Chain Link Fences & Gates Labor	46,500.00	1	0.00	0.00	0.00	0.00%	46,500.00	
		4.		ď					
	Grand Totals	1,564,340.00	321,929.31	159,059.50	0.00	480,988.81	30.75%	1,083,351.19	48,0

APPLICATION AND CERTIFICATE FOR PAYMENT

TO(OWNER):	Elizabethtown Independent District Board of Education	PROJECT:	T K Stone Middle School Renovation Elizabethtown, KY		APPLICATION NO: 6 PERIOD FROM: 10/1/2025 TO: 10/30/2025	
ATTENTION:	Paul Mullins	CONTRACT FOR:	Doors and Hardware	CONTRACT DATE:	22-Jan-25	ALLIANCE
		BID DIV:	080			Builders & Managers
CONTRACTOR	S APPLICATION FOR PAYMENT			Application is made for Payment as shown		
CHANGE ORDE				with the Contract Continuation Sheet attach The present status of the this Contract is as		
Change Orders previous months		DEDUCTIONS		ORIGINAL CONTRACT SUM		\$40,502.00
TOTAL				Net change by Change Orders		\$942.00
Approved this m	onth \$942.00			CONTRACT SUM TO DATE		\$41,444.00
				TOTAL COMPLETED & STORED TO DAT	E (Sheet 2)	\$2,836.01
				RETAINAGE @ 10%		\$283.60
				TOTAL EARNED LESS RETAINAGE		\$2,552.41
				LESS PREVIOUS CERTIFICATES (CONTI	RACT ONLY)	
Net Change by 0	Change Orders \$942.00	\$0.00	\$942.00	CURRENT PAYMENT DUE		\$793.82
information and has been comple amounts have be Payment were is	d contractor certifies that to the best of his belief the Work covered by this Applicatio eted and in accordance with the Contract een paid by him for Work for which previous usued and payments received from the Ow herein is now due.	n for Payment Documents, that all us Certificates for	t	Subscribed and sworn to before me this 2	3rd day of October, 2025 Reptucky County of: 9/4/2029 County of:	Jefferson
CONTRACTOR: By: ARCHITECT'S C	The Atlas Companies LEATIFICATE FOR PAYMENT	Date:	10/23/2025	ARCHITECT'S CERTIFICATION: ROSS T. By: CM APPROVAL: ALLIANCE CORPORATI	Wall	Date: 11/10/25
In accordance w	ith the Contract Decuments, based on an	site observation and	I the data comprising	Dalton Jackson		Date: 11/5/202

This certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or contractor under this Contract.

the above application, the Architect certifies to the Owner that the Work has progressed to the point indicated: that to the best of his knowledge, information and belief, the quality of the Work is in accordance with the Contract Documents and the Contractor is entitled to payment of the AMOUNT CERTIFIED.



CC	NTINUATION SHEET NO. 2 APPLICATION NO. <u>6</u>	T K STONE MIDDLE SCHOOL RENO	*D* WORK	*E* COMPLETED	*F* · MATERIALS	*G* TOTAL COMPLETED	*H*	* *
ITEM #	DESCRIPTION OF WORK	SCHEDULED VALUE	FROM PREV. APPLIC.(D+E)	THIS PERIOD	STORED (NOT IN D OR E)		% G/C	BALANCE TO FINISH C-G
1 2 3	Building Area A Installation	\$8,434.49				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$8,434.49 \$0.00
4 5 6	Building Area B Installation	\$11,808.29		\$477.00		\$0.00 \$477.00 \$0.00	4%	\$0.00 \$11,331.29 \$0.00
7 8 9	Building Area C Installation	\$6,747.59				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$6,747.59 \$0.00
10 11 12	Building Area D Installation	\$1,686.90				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$1,686.90 \$0.00
13 14 15	Building Area E Installation	\$5,060.70				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$5,060.70 \$0.00
	Bond Submittals	\$1,953.99 \$405.02	\$1,953.99	\$405.02		\$0.00 \$1,953.99 \$405.02	100% 100%	\$0.00 \$0.00 \$0.00
19	Cleanup O&M Manuals Closeout Documents	\$405.02 \$3,000.00 \$1,000.00				\$0.00 \$0.00 \$0.00	0% 0% 0%	\$405.02 \$3,000.00 \$1,000.00
22 23 24 25 26 27 28 29 30 31 32 33 34 35 36 37 38 39 40	CO# PR#005 Door Closers	\$942.00						
	TOTALS	\$41,444.00 \$0.	00 \$1,953.99	\$882.02	\$0.00	\$2,836.01	7%	\$37,665.99

	CONTINUATION SHEET NO. 3 APPLICATION NO.		OOL RENO *D*	*E*	OWNER PURCH	IASE ORDERS	S ONLY *H*
ITEM #	DESCRIPTION	SUPPLIER	P.O. AMOUNT	PREVIOUS PAYMENTS	INVOICES DUE THIS MONTH (ATTACHED)	TOTAL TO DATE (E +F)	BALANCE TO FINISH (D - G)
1 2 3 4 5	81113 HM Doors/ Frames	Atlas Enterprises Atlas Enterprises Atlas Enterprises	\$17,985.87 \$14,180.36 \$30,886.54	\$17,985.87 \$14,180.36 \$19,143.25	\$10,777.75	\$17,985.87 \$14,180.36 \$29,921.00	\$0.00 \$0.00 \$965.54
6 7 8 9	Building Area B 81113 HM Doors/ Frames 81416 Wood Doors 87100 L/S Finish Hardware	Atlas Enterprises Atlas Enterprises Atlas Enterprises	\$25,180.70 \$18,907.15 \$43,241.16	\$25,180.70 \$18,907.15 \$26,800.55	\$15,088.85	\$25,180.70 \$18,907.15 \$41,889.40	\$0.00 \$0.00 \$1,351.76
11 12 13 14	81113 HM Doors/ Frames	Atlas Enterprises Atlas Enterprises Atlas Enterprises	\$14,388.69 \$11,816.96 \$24,709.23	\$14,388.69 \$11,816.96 \$15,314.60	\$8,622.20	\$14,388.69 \$11,816.96 \$23,936.80	\$0.00 \$0.00 \$772.43
15 16 17 18 19 20	81113 HM Doors/ Frames 81416 Wood Doors	Atlas Enterprises Atlas Enterprises Atlas Enterprises	\$3,597.18 \$2,363.40 \$6,177.31	\$3,597.18 \$2,363.40 \$3,828.65	\$2,155.55	\$3,597.18 \$2,363.40 \$5,984.20	\$0.00 \$0.00 \$193.11
21 22 23 24		Atlas Enterprises	\$10,791.52 \$0.00 \$18,531.93	\$10,791.52 \$11,485.95	\$6,466.65	\$10,791.52 \$17,952.60	\$0.00 \$579.33
25 26 27 28 29							
30 31 32 33 34							
35 36 37 38 39 40							
	TOTALS		\$242,758.00	\$195,784.83	\$43,111.00	\$238,895.83	\$3,862.17

INVOICE

Atlas Enterprises

5101 Commerce Crossings Drive Louisville, KY 40229

Invoice Date: 10/22/2025 Invoice #: 1226622

Due Date: 10/22/2025

Purchase Order #: 9-63885

Elizabethtown Independent Schools c/o 116 East College Street Glasgow, KY 42141

Customer #: EL0010

Contract ID: KY-25-00601 Billing: Varies

TK Stone Middle School

	DESC	CRIPTION	LABOR	MATERIAL	TOTAL
02-08-7000	Hardware	STRD DEP	0.00	1,936.00	1,936.00
		Total Amount Billed	0.00	1,936.00	1,936.00
		Amount due this Invoice			1,936.00

INVOICE

Atlas Enterprises

5101 Commerce Crossings Drive Louisville, KY 40229

Invoice Date: 10/20/2025 Invoice #: 1226557

Due Date: 10/20/2025

Purchase Order #: 9-63885

Elizabethtown Independent Schools c/o 116 East College Street Glasgow, KY 42141

Customer #: EL0010

Contract ID: KY-25-00601 Billing: Varies

TK Stone Middle School

	DESC	CRIPTION	LABOR	MATERIAL	TOTAL
02-08-7000	Hardware	STRD DEP	0.00	1,231.00	1,231.00
		Total Amount Billed	0.00	1,231.00	1,231.00
		Amount due this Invoice			1,231.00

INVOICE

Atlas Enterprises

5101 Commerce Crossings Drive Louisville, KY 40229

Invoice Date: 9/30/2025 Invoice #: 1226130

Due Date: 9/30/2025

Purchase Order #: 9-63885


Elizabethtown Independent Schools c/o 116 East College Street Glasgow, KY 42141

Customer #: EL0010

Contract ID: KY-25-00601 Billing: Varies

TK Stone Middle School

	DESC	RIPTION	LABOR	MATERIAL	TOTAL
02-08-7000	Hardware	STRD DEP	0.00	39,944.00	39,944.00
		Total Amount Billed	0.00	39,944.00	39,944.00
		Amount due this Invoice		- =	39,944.00

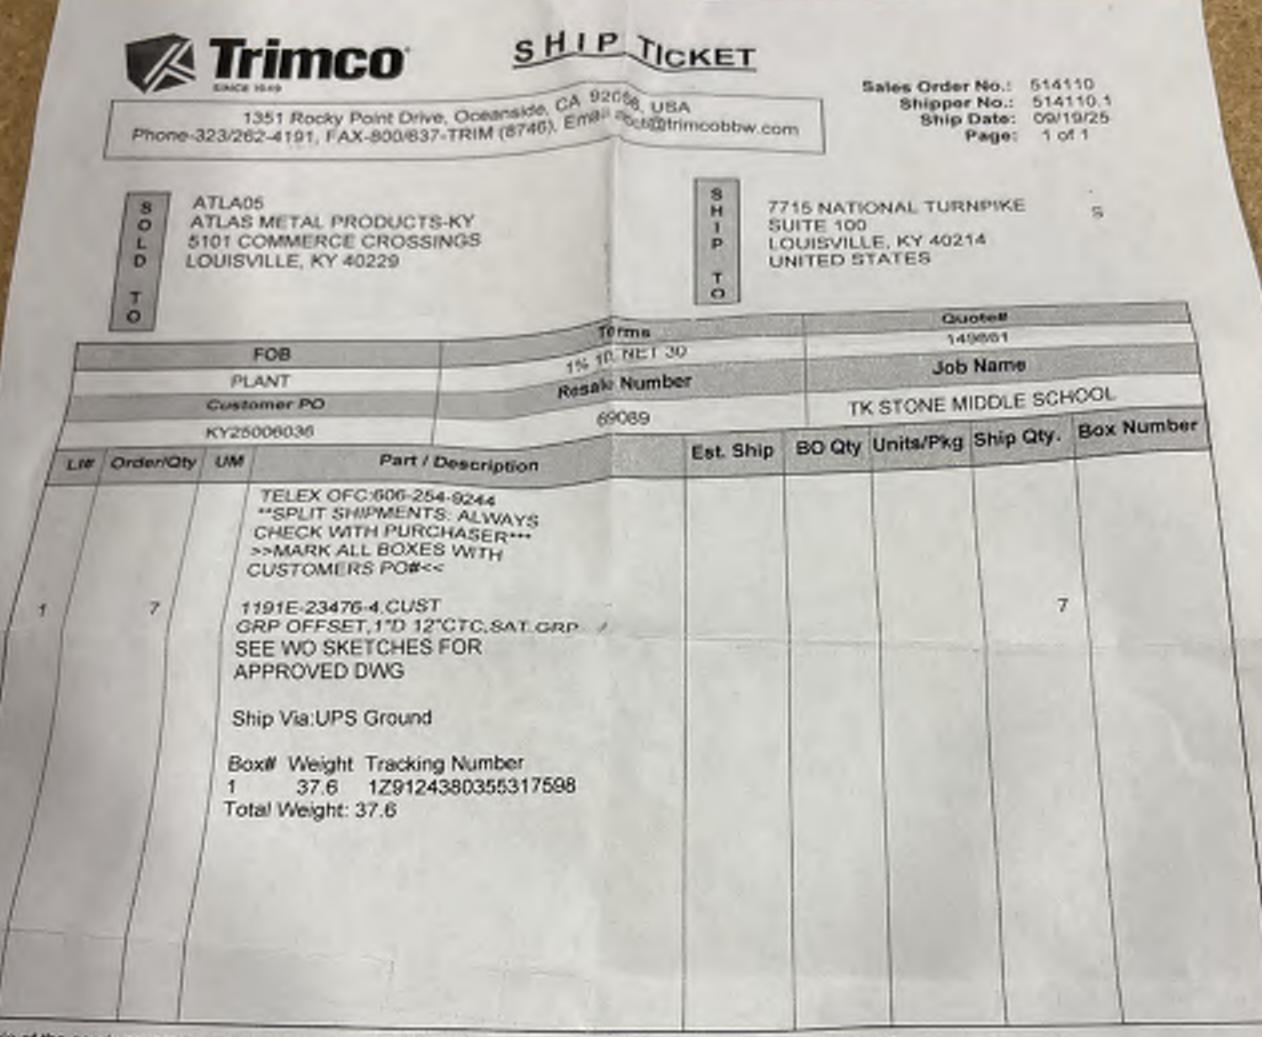

The sale of the goods covered hereby is expressly subject to the buyer's assent to the terms and conditions set forth hereof.

Acceptance

If the Terms and Conditions of the acknowledgment differ in any way from the terms and conditions of Buyer's order, this acknowledgment will be construed as a "COUNTEROFFER" and will not be effective as an acceptance of Buyer's terms and conditions which conflict herewith. The terms and conditions contained herein will be the complete and exclusive statement of the terms of the agreement between the parties. Buyer's acceptance of the goods sold hereunder will manifest Buyer's assent to the Terms and conditions hereof. No addition to or modification of any of these Terms and Conditions will be effective unless made in writing and signed by Selfer.

GENERAL

Prices - Prices and terms of sale are subject to change without notice. The price list is only a quotation and is neither an offer to sell nor an acceptance of an offer to buy the goods covered hereby. Sale of the goods covered by this order acknowledgment will be subject to the following terms and conditions. Taxes- If under any law now or hereafter passed, the seller is required to pay a tax on sales, or on an excise tax the amount of these taxes will be added to the invoice value. Delivery - Seller shall not be finished to the invoice value. not be fiable for any delay in delivery, or failure to deliver, due to any cause beyond the Seiler's control, including but not limited to fires, floods, strikes, or other labor disputes, accidents to machinery, act of sabotage, riots, precedence or priorities granted at the request or for the benefit, directly or indirectly, of the federal rules or egulations thereof. Credit - Acceptance of orders and delivenes thereof shall at all times be subject to our approval of credit. Shipments - Goods in transit are at the sk of purchaser. All shipments are F.O.B. shipping point via cheapest routing will carrier chosen by us. Please consult your current price book for pre-paid freight rms. Cancellations -Orders for goods, accepted by us, are noncancellable exolor with our prior written consent and subject to a service charge expressed in such nsent. Returned Goods - No credit will be issued for returned goods unless such return is authorized. Please consult current price book for all terms and conditions. inimum values for prepaid shipments are subject to change. Please consult yoursp to date price list for the correct amounts.

SPECIAL GOODS

is order contains any items that are were made to your specifications we are unable to accept cancellations or changes to that item without a charged based on mes incurred. Special order products, being a non-stock item cannot be returned for credit.





item	T		YTITYAUD		1		
	1	Onder	8/0	3Np.	Unit	Part Number/Revision	Description
001	8	10		10	EA	195-12-W-IND	SW SET, 195-12-W IND SAGGED
						City 10	Din E3A000
1	1						
/							
/							

COMMENTS: Discrepancies must be reported to GRI within ten (10) days of delivery.

BASCI .

- 1010

- 108

- 111

100

PON KY26 - 608 - 633
ROSS 862 - 6780
ATLAS METAL PRODUCTS - 5775 MATIONAL TURNINKE
LOUISVILLE KY 40 UPS GROUND SAGALL OF STATE - 1851 And the state of t 340 PANTY ALF 1:6365634 REF 2:0276683 BULLING (3) 215843 F.Q.O. Po 001

dormakaba

09/30/2025 21:17:24

Page

Date 1/5

PL No.

2103474990



Sold-To: ATLAS METAL PRODUCTS CO

Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

Carrier: ECHO GLOBAL LOGISTICS INC.

	Orderitam no	Gry This	Material no	manufakten	City	Gry Shipped to date	Oty Backord.
POI	Otoernani	Shipment	Customer Material no		-	1	0
KY25-006-019	1303130796/1000	J1	7000217	3R02101LDLHR9630 CONFIGURABLE PANIC EXIT DEVICES			
KY25-006-019	1303130795/2000	14	7000217	3R02101LD/SNBLHRB630 CONFIGURABLE PANIC EXIT DEVICES	4	4	0
KY25-006-019	1303130795/3000	1	7000217	3R02103LD/SNB2003CRHRB630 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
KY25-006-019	1303130795/4000	/3	7000217	3R02103LD/SNB4903ALHRB630 CONFIGURABLE PANIC EXIT DEVICES		3 3	0
KY25-006-019	1303130795/5000	V/3	7000217	3R02103LD/SNB4903ARHRB630 CONFIGURABLE PANIC EXIT DEVICE	s	3	0
KY25-006-019	1303130795/6000	1	7000217	3R02108LD/SNBV4908DRHRB6304 CONFIGURABLE PANIC EXIT DEVICE	ES	1	1

dormakaba ⋈

Date

09/30/2025 21:17:24

Page 2/5

PL No.

2103474990



Sold-To: ATLAS METAL PRODUCTS GO

Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

Carrier: ECHO GLOBAL LOGISTICS INC

POF	Ordenitem no	Oty This Shipment	Material no Customer Material no	Description	City	Oty Shipped to date	Ony Beskord.
KY25-005-019	1303130795/7000	1	7000217	3R0FL2103SNB4903DLHRB6304 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
KY25-006-019	1303130795/8000	1	7000217	3R0FL2103SNB4903DRHRB6304 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
CY25-006-019	1303130795/9000	1/2	7000217	3R0FL2214LBR/SNB4914ALHRB630 CONFIGURABLE PANIC EXIT DEVICES	2	2	0
Y25-006-019	1303130795/10000	/2	7000217	3R0FL2214LBR/SNB4914ARHRB630 CONFIGURABLE PANIC EXIT DEVICES		2 2	0
Y25-006-019	1303130795/11000	12	7000217	3R0FL2801LBR/SNBLHRB6302-6 CONFIGURABLE PANIC EXIT DEVICES		2	2 0
Y25-006-019	1303130795/12000	1/2	7000217	3R0FL2801LBR/SNBRHRB6302-6 CONFIGURABLE PANIC EXIT DEVICE	s	2	2 0

dormakaba 🚧

PL No.

09/30/2025 21:17:24 Date 3/5 Page

2103474990

Sold-To: ATLAS METAL PRODUCTS CO

Carrier: ECHO GLOBAL LOGISTICS INC.

Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

Order/frem no	Oty This Shipment	Material no Customer Material no	Description 0		Ony Shipped to dete	Gry Backord.
1303130795/13000	√,	7000217	3R0FL2801LBR/SNBLHRB630 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
1303130795/14000	1/2	7000217	3R0FL2801LBR/SNBLHR8630 CONFIGURABLE PANIC EXIT DEVICES	2	2	0
1303130795/15000	1	7000217	3R0FL2801LBR/SNBLHRB6308 CONFIGURABLE PANIC EXIT DEVICES	3	1	0
1303130796/16000	d	7000217	3R0FL2803LBR/SNB4903DRHRB630 CONFIGURABLE PANIC EXIT DEVICE	s	1	1 0
1303130795/17000	√ ₂	7000217	3R0FL2803LBR/SNB4903DRHRB830 CONFIGURABLE PANIC EXIT DEVIC	ES	2	2 0
1303130795/18000	1.	7000217	3R0FL2803LBR/SNB4903DRHRB630	8	1	1
	1303130795/13000	1303130795/13000 1 1303130795/14000 2 1303130795/15000 1 1303130795/15000 1	1303130795/13000	1303130795/14000	1303130795/17000	1303130795/17000

dormakaba∞

Date Page 09/30/2025 21:17:24

nge 4/5

PL No.

2103474990



Sold-To: ATLAS METAL PRODUCTS CO

Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100 LOUISVILLE KY 40214 Carrier: ECHO GLOBAL LOGISTICS INC.

POI	Order/tem no.	Oty This Snipment	Material no Customer Staterial no	Description	Oty Indened	Gry Shipped to date	Backord.
				CONFIGURABLE PANIC EXIT DEVICES			
KY25-006-019	1303130795/19000	1	7000217	3R0MLR2103SNB4903ARHRB630 CONFIGURABLE PANIC EXIT DEVICES	-1	1	0
Y25-006-019	1303130795/20000	1/2	7000217	3ROMLR/TS2103SNBRHRB630 CONFIGURABLE PANIC EXIT DEVICES	2	2	0
25-006-019	1303130795/21000	Si	7000217	3ROMLR/TS23032003CRHRB830S982 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
25-006-019	1303130795/22000	-	7000217	3ROMLR/TS23032003CRHRB630S9824 CONFIGURABLE PANIC EXIT DEVICES		1 1	0
25-006-019	1303130795/23000	<i>J</i> ₂	7000217	3R0TS2101LD/SNBLHRB630 CONFIGURABLE PANIC EXIT DEVICE	s	2	2 0

dormakaba

09/30/2025 21:17:24

Page 5/5

Date

PL No.

2103474990



Sold-To: ATLAS METAL PRODUCTS CO

Ship-To: THE ATLAS COMPANIES - THE DEPOT

7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

Carrier: ECHO GLOBAL LOGISTICS INC.

POF	OrderStem no	Oty This	Material no Customer Material no	Description	Ony Ordered	City Shipped to date	Gty Backerd-
KY25-006-019	1303130796/24000	Shipment 8	721803360	EPT-5 POWER TRANSFER 02189-06-00	8	8	0
KY25-006-019	1303130795/25000	0	7000283	FUMOKR8226898MCS CONFIGURABLE RM MULLION	6	0	6
CY25-006-019	1303130795/26000	/6	7000217	RPST989 CONFIGURABLE PANIC EXIT DEVICE	S 6	6	0
Tracking number 00785133952							



dormakaba

Date

10/01/2025 00:08:25

Page 1/3

PL No. 2103474991



Sold-To: ATLAS METAL PRODUCTS CO

Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

CATTHET: ECHO GLOBAL LOGISTICS INC.

POF	Ordecitem no	Ony This Shipment	Material no Customer Material no	Description	ky (to date	Ghy Backoré.
Mark for: TK STON JOB: KY-25-006 KY25-006-031	1303130969/1000	/2	7000217	3R02401LD/SNBLHRB630S301 CONFIGURABLE PANIC EXIT DEVICES	2	2	0
CY25-006-031	1303130969/2000	1	7000217	3R02401LD/SNBRHRB630S301 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
CY25-006-031	1303130969/3000	-/1	7000217	3ROMLR2403SNBRHRB630S301 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
Y25-006-031	1303130969/4000	0	7000217	3ROMLR2403SNBLHRB630S9884 CONFIGURABLE PANIC EXIT DEVICES	1	1 0	1
/25-006-031	1303130969/5000	0	7000217	3R0MLR2403SNBLHRB630S9884 CONFIGURABLE PANIC EXIT DEVICES	5	1	0 1
25-006-031	1303130969/6000	-	7000217	3R0MLR/TS2103SNBRHRB630		1	1

dormakaba

10/01/2025 00:00:25

Page

Date 2/3

2103474991 PL No.



Sold-To: ATLAS METAL PRODUCTS CO Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

No of Packages: 2

Carrier: ECHO GLOBAL LOGISTICS INC

POP	Ordertters no	Oty This Shipment	Material no Customer Material no	Description	Dity C	by Shipped to date	City Backord.
				CONFIGURABLE PANIC EXIT DEVICES			
KY25-006-031	1303130969/7000	\frac{1}{1}	7000217	3ROMLR/TS2403SNBRHRB630S301 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
CY25-006-031	1303130969/8000	1	7000217	3R0TS2101LD/SNBLHRB630 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
Y25-006-031	1303130969/9000	1	7000217	3R0TS2401LD/SNBLHRB630S301 CONFIGURABLE PANIC EXIT DEVICES	4	4	0
25-006-031	1303130969/10000	√3	7000217	3R0TS2401LD/SNBRHRB630S301 CONFIGURABLE PANIC EXIT DEVICES	3	3	3 0
25-006-031	1303130969/11000	J13	721803360	EPT-5 POWER TRANSFER 02189-06-0	0 1	3	13 0

PL No. 2103474991

A MANAGEMENT AND A STATE OF THE STATE OF THE

Packing list

dormakaba 🗺

Date Page 10/01/2025 00:06:25

3/3

Sold-To:

ATLAS METAL PRODUCTS CO Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100 LOUISVILLE KY 40214

Carrier: ECHO GLOBAL LOGISTICS INC.

No of Packages: 2


nov	Ordentters no	Gty This Shipment	Material no Customer Material no	Description	Gfy Ordered	Oty Shipped to date	Gry Backord
KY25-006-031	1303130969/12000	1	7000283	RM0KR8226898MCS CONFIGURABLE RM MULLION	7	7	0
Y25-006-031	1303130969/13000	17	7000217	CONFIGURABLE PANIC EXIT DEVICES	7	7	0

Tracking number

1520404062





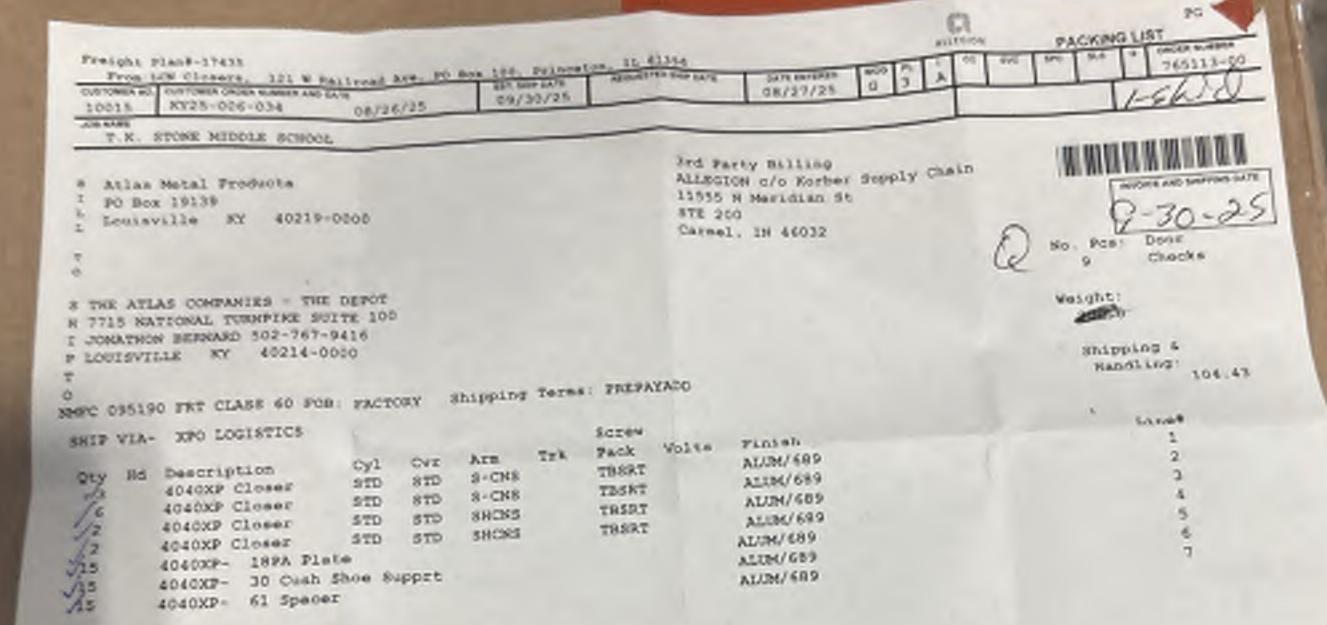

LCN Closers

COMPANIES THE DEPOT REPOT 100 NAL TURNPIKE SUITE 100 NAL TURNPIKE SUITE 100 NATE 100

CLOSEPS

the sources, subject to restriction by Eastern Weighing and important Bureau, Sentime Veryloop and Imperiors Sureau scounding to agreement. Apart, Per





Door and Hardware Systems, Inc. 17 Silver Street Rochester, NY 14611

TEL: 585-235-8543 www.dhsr-seal.com

Delivery Ticket


Date	8.0, No.
8/27/2025	13658

Atlas Companies 5101 Commerce Crossings Drive Louisville, KY 40229 Ship To

The Atlas Companies - The Depot 7715 National Tumpike, Ste 100 Louisville, KY 40214 ATTN: Jonathan Bernard 502-767-9416

MARK	P.O. No.	8'-0 BK			
-	006-020-032	TK Stone ES - Elizabethtown, KY			
Ordered	PO#KY25-006-020	Description			
1 Sh	I/2" inserts O#KY25-006-032 MS SA-75 Mullion Seal 7'-0 MS SA-75 Mullion Seal 8'-0 ip UPS Ground Oversize x It-of-state sale) BK			







Tenma

H

Phone-323/262-4191, FAX-800/637-TRIM (8746). Email 8005@httmootsbw.com

Sales Order No.: 514112 Ship Date: 10/13/25 Page: 1652

ATLA05 0 ATLAS METAL PRODUCTS-KY 5101 COMMERCE CROSSINGS D LOUISVILLE, KY 40229

0

ATLAS METAL PROD-KY 7715 NATIONAL TURNPIKE to FOURDAILTE KA 40514 UNITED STATES

E		PL	ANT	1% 10. 3 Resale N	SET 30			9665 1681		
1			oner PO 006028		600ea Job			Job Name		
LIM	Orderion			Description TK STOR			TK STONE MIDDLE 36			
5 6 20 H	10 10 2 4	1 0 8	TELEX OFC:606:25 "SPLIT SHIPMENT CHECK WITH PURK SMARK ALL BOXE CUSTOMERS POW- 1082-6S:630 CYLINDRICAL LOCI 1283-6S:626 ADJ. HLDR WIADJU SEE WO SKETCHES APPROVED DWG 1283-6S-1S:627 SHIM 1283 ALUMINI Dimension: 8:00 x 32 191E-23476-4:CUS SRP OFFSET, 1*D 12 X3275-CSK:630	S: ALWAYS CHASER*** S WITH K-GRD 6" W IST STRK S FOR UM 1" 75	Est Ship	BO ON	Unita/Pag	Ship Oty.	Box Number	
		S	OCK PLT .050 Simension: 8.00 x 32 hip Via:UPS Ground ox# Weight Trackin	1						

The sale of the goods covered hereby is expressly subject to the buyer's assent to the terms and conditions set forth hereof.

Acceptance

If the Terms and Conditions of the acknowledgment differ in any way from the terms and conditions of Buyer's order, this acknowledgment will be construed as a "COUNTEROFFER" and will not be effective as an acceptance of Buyer's terms and conditions which conflict herewith. The terms and conditions contained herein will be the complete and exclusive statement of the terms of the agreement between the parties. Buyer's acceptance of the goods sold hereunder will manifest Buyer's assert to the Terms and conditions hereof. No addition to or modification of any of these Terms and Conditions will be effective unless made in writing and signed by Seller.

Prices and terms of sale are subject to change without notice. The price list is only a quotation and is neither an offer to sell nor an acceptance of an offer to buy the goods covered hereby. Sale of the goods covered by this order acknowledgment will be subject to the following terms and conditions. Taxes—If under any law now. or hereafter passed, the seller is required to pay a tax on sales, or on an excise tax, the amount of these taxes will be added to the invoice value. Delivery - Seller shall not be liable for any delay in delivery, or failure to deliver, due to any cause beyond the Seller's control, including but not limited to fires, floods, strikes, or other labor disputes, accidents to machinery, act of sabotage, nots, precedence or priorities granted at the request or for the benefit, directly or indirectly, of the federal rules or regulations thereof. Credit - Acceptance of orders and deliveries thereof shall at all times be subject to our approval of credit. Shipments - Goods in transit are at the risk of purchaser. All shipments are F.O.B. shipping point via cheapest routing with carrier chosen by us. Please consult your current price book for pre-paid freight. terms. Cancellations -Orders for goods, accepted by us, are noncancellable except with our prior written consent and subject to a service charge expressed in such consent. Returned Goods - No credit will be issued for returned goods unless such return is authorized. Please consult current price book for all terms and conditions. "Minimum values for prepaid shipments are subject to change. Please consult your up to date price list for the correct amounts.

SPECIAL GOODS

If this order contains any items that are were made to your specifications we are unable to accept cancellations or changes to that item without a charged based on expenes incurred. Special order products, being a non-stock item cannot be returned for credit.





dormakaba 🕍

Date

10/20/2025 10:23:06

Page

1/6

PL No. 2103509783


Sold-To: ATLAS METAL PRODUCTS CO Ship-To: THE ATLAS COMPANIES - THE DEPOT

7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

Carrier: FEDERAL EXPRESS CORPORATION

PO#	Orden/tern no	Qhy This Shipment	Material no Customer Material no	Description Ovcored		shipped date	Dacword.	
CY25-006-019	1303130796/1000	0	7000217	GONFIGURABLE PANIC EXIT DEVICES				
CY25-005-019	1303130795/2000	0	7000217	3R02101LD/SNBLHRB630 CONFIGURABLE PANIC EXIT DEVICES	4	4		
Y25-006-019	1303130795/3000	0	7000217	3R02103LD/SNB2003CRHRB630 CONFIGURABLE PANIC EXIT DEVICES	1	,		0
Y25-006-019	1303130795/4000	0	7000217	3R02103LD/SNB4903ALHRB830 CONFIGURABLE PANIC EXIT DEVICES	3		3	0
y25-006-019	1303130795/5000	0	7000217	3R02103LD/SNB4903ARHRB630 CONFIGURABLE PANIC EXIT DEVICES		3	3	0
Y25-006-019	1303130795/6000	0	7000217	3R02108LD/SNBV4908DRHRB6304 CONFIGURABLE PANIC EXIT DEVICE	S	1		

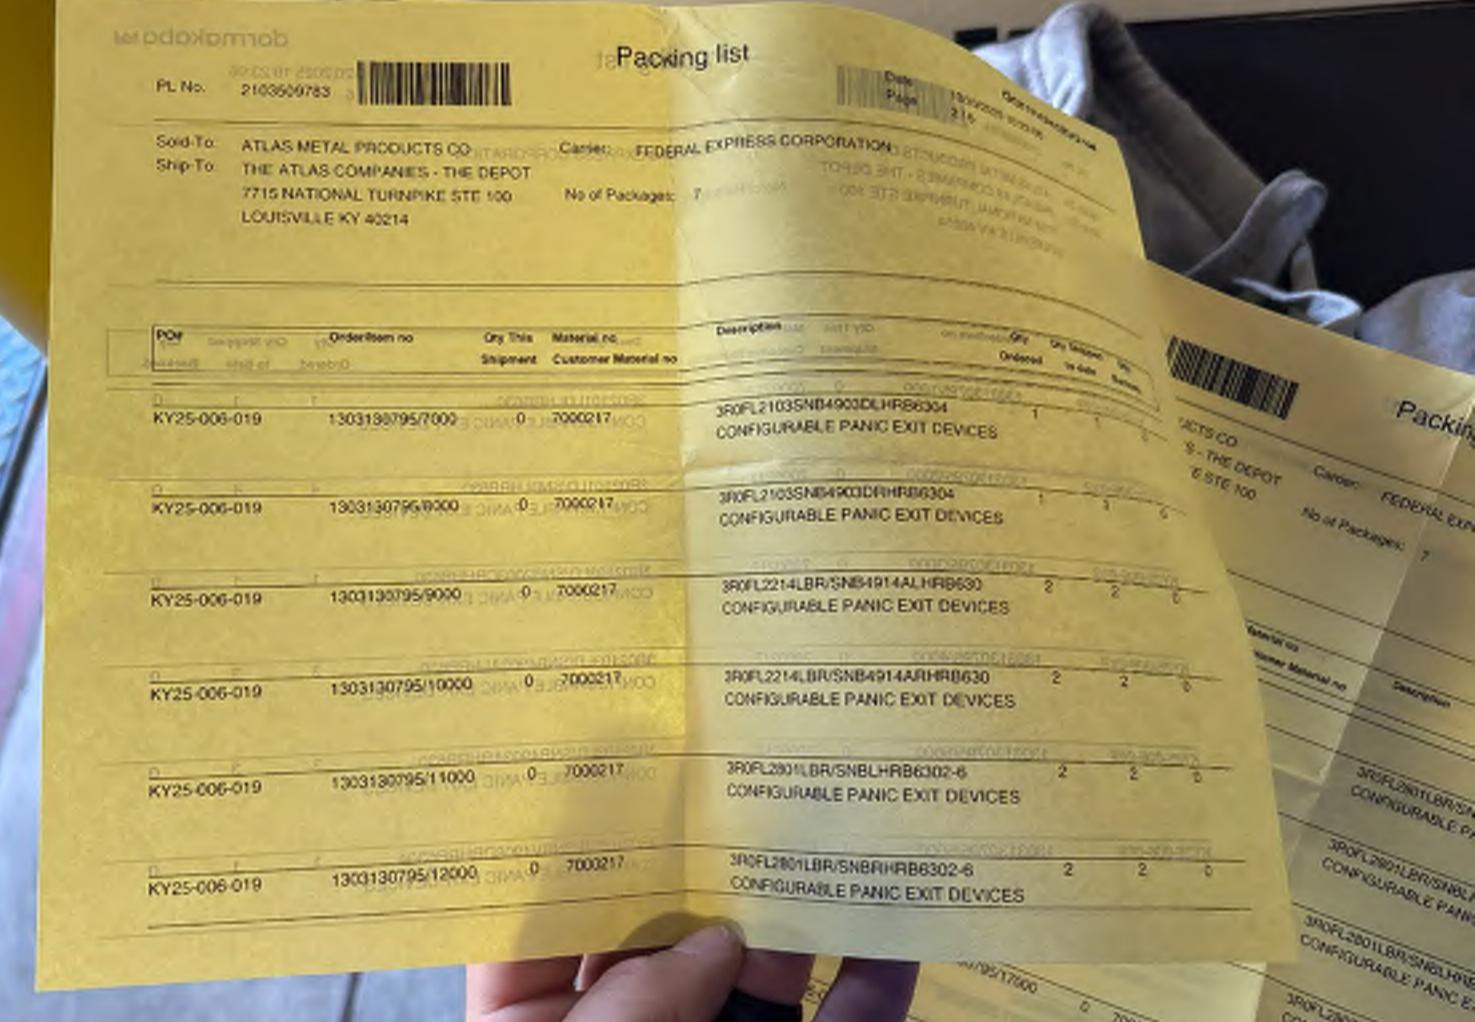

SOMESTINGADLE PAINC EXIT

COMPRESSOR BRANCHER BY

Man Langa Rep Sylla and a Change of

7000217

PL No. 2103509783 Packing list dormakabana Sold-To: ATLAS METAL PRODUCTS CO Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100 No of Packages: 7

dormakabawa

P 1009-019	Orden/kers no	City This Material no Shipment Costomer Material	Description 10	Gry Ordered	Ony Shipped to date	CRY
KY25-008-019	1303130795/13000	0 7000217	3R0FL280TLBR/SNBLHR9630 CONFIGURABLE PANIC EXIT DEVICES		1	Beckerd,
KY25-006-019	1303130795/14000	0 7000217	SROFL2001LBR/SNBLHRB630 CONFIGURABLE PANIC EXIT DEVICES		2	0
KY25-006-019	SECTION OF VICES	0 7000217	GONFIGURABLE PANIC EXIT DEVICES	1	1.	0
	1303130795/16000	0 7000217	3R0FL2803LBR/SNB4903DRHRB630 CONFIGURABLE PANIC EXIT DEVICES	1	1	0
KY25-006-019	1303130795/17000	0 7000217	3R0FL2803LBR/SNB4903DRHRB630 CONFIGURABLE PANIC EXIT DEVICE	2	5	0
Y25-006-019	1303130795/18000	0 7000217	3R0FL2803LBR/SNB4903DRHRB6308	1	-	0

dormakaba

Paching list

10/20/2025 10:23:06

Date 4/6 Page

2103509783 PL No.

Sold-To: ATLAS METAL PRODUCTS CO

Ship-To: THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100

LOUISVILLE KY 40214

Garrier: FEDERAL EXPESS CORPORATION

No of Packages 7

POF	Order@tern no	Oty This Shipment	Material no. Customer Material no.	Oscription Otty Onder		ty Shipped to date	Oty Backord.
A. Carlo				CONFIGURABLE PANIC EXIT DEVICES			
KY25 006-019	1303130795/19000	0	7000217	CONFIGURABLE PANIC EXIT DEVICES	1	1	0
KY25-006-019	1303130795/20000	2/403	7000217	SROMLR/TS2103SNBRHR8630 CONFIGURABLE PANIC EXIT DEVICES	2	2	0
CY25-006-019	1303130795/21000	0	7000217	ONFIGURABLE PANIC EXIT DEVICES	1	1	0
CY25-006-019	1303130795/22000	0	7000217	CONFIGURABLE PANIC EXIT DEVICES	1	1	0
(Y25-006-019	1303130796/23000		7000217	CONFIGURABLE PANIC EXIT DEVICES			- 6

RIMANUSAN PRIMES CONFIGURABLE PIN MUL

Vist

COMPIGURABLE PANIC EXIT

dormakaba

PL No. 2103509783 6

Packing list

dormakaba∞

Date

10/20/2025 10:23:06

Page 5/6

THE ATLAS COMPANIES - THE DEPOT 7715 NATIONAL TURNPIKE STE 100


LOUISVILLE KY 40214

Sold-To: ATLAS METAL PRODUCTS CO Carrier: FEDERAL EXPRESS CORPORATION

No of Packages: 7

POP beggin	Order/Item no	Oty This Shipment	Material no Customer Material no	Description	Ordered	Oty Shipped to date	Oty Backord.
KY25-006-019	1303130795/24000	0	721803360	EPT-5 POWER TRANSFER 02189-06-00	8	8	0
KY25-006-019	1303130795/25000	6	7000283	RM0KR8226898MCS CONFIGURABLE RM MULLION	6	6	0
KY25-006-019	1303130795/26000	0	7000217	RPST989 CONFIGURABLE PANIC EXIT DEVICES	6	6	0

Tracking number	
394418200721	
394418203157	
394418203087	
394418203000	
394418203709	



Packing list

Pt. No. 2103509783

dormakabass

10/20/2025 10:20:06

6/6

Dote-

Page

Client#: 1411671 64ATLASMET

ACORD...

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY) 10/23/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer any rights to the certificate holder in lieu of such endorsement(s).

and commonly decomed and common and make the and common and and a	• ,					
PRODUCER	CONTACT NAME:					
McGriff, a MMA LLC Company	PHONE (A/C, No, Ext): 502 489-5900 FAX (A/C, No): 86	68812184				
2600 Eastpoint Parkway	E-MAIL ADDRESS: LouisvilleCL1@McGriff.com					
Louisville, KY 40223	INSURER(S) AFFORDING COVERAGE INSURER A : FCCI Insurance Company					
502 489-5900						
INSURED	INSURER B : ClearPath Insurance Company	16273				
L R Construction Inc dba Atlas	INSURER C: The Cincinnati Insurance Company	10677				
Enterprises	INSURER D:					
5101 Commerce Crossings Drive	INSURER E:					
Louisville, KY 40229-2100	INSURER F:					

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

	CCLUSIONS AND CONDITIONS OF SUCH					ivio.	
INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	S
Α	X COMMERCIAL GENERAL LIABILITY		CPP10010208500	06/01/2025	06/01/2026	EACH OCCURRENCE	\$1,000,000
	CLAIMS-MADE X OCCUR					DAMAGE TO RENTED PREMISES (Ea occurrence)	\$100,000
						MED EXP (Any one person)	\$5,000
						PERSONAL & ADV INJURY	\$1,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:					GENERAL AGGREGATE	\$2,000,000
	POLICY PRO- JECT LOC					PRODUCTS - COMP/OP AGG	\$2,000,000
	OTHER:						\$
Α	AUTOMOBILE LIABILITY		CA10000292310	06/01/2025	06/01/2026	COMBINED SINGLE LIMIT (Ea accident)	\$1,000,000
	X ANY AUTO					BODILY INJURY (Per person)	\$
	OWNED SCHEDULED AUTOS					BODILY INJURY (Per accident)	\$
	X HIRED AUTOS ONLY X NON-OWNED AUTOS ONLY					PROPERTY DAMAGE (Per accident)	\$
							\$
Α	X UMBRELLA LIAB X OCCUR		UMB10007771403	06/01/2025	06/01/2026	EACH OCCURRENCE	\$5,000,000
	EXCESS LIAB CLAIMS-MADE					AGGREGATE	\$5,000,000
	DED X RETENTION \$10000						\$
В	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY		WC11019671	06/01/2025	06/01/2026	X PER STATUTE OTH-	
	ANY PROPRIETOR/PARTNER/EXECUTIVE	N/A				E.L. EACH ACCIDENT	\$2,000,000
	(Mandatory in NH)	13/ A				E.L. DISEASE - EA EMPLOYEE	\$2,000,000
	If yes, describe under DESCRIPTION OF OPERATIONS below					E.L. DISEASE - POLICY LIMIT	\$2,000,000
С	XS over \$5M Umb		EXS0654863	06/01/2025	06/01/2026	\$4,000,000	
Α	Leased/Rent Equi		CPP10010208500	06/01/2025	06/01/2026	\$250,000 Lim;\$1,000) Ded
_							

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

RE: Job # KY-25-00601, Job Name: TK Stone Middle School - Hardware, Amount: \$43,111.00, Stored Location:

7715 National Turnpike, Louisville, KY 40214.

CERTIFICATE H	OLDER
----------------------	-------


Elizabethtown Independent Schools %116 East College Street Glasgow, KY 42141 CANCELLATION

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

BHU

© 1988-2015 ACORD CORPORATION. All rights reserved.



the AMOUNT CERTIFIED.

APPLICATION AND CERTIFICATE FOR PAYMENT

TO (OWNER): Elizabethtown Independent District PROJECT: T K Stone Middle School Renovation 323 Morningside Drive Board of Education Elizabethtown, KY 42701 ATTENTION: Paul Mullins CONTRACT FOR: BP #084: Aluminum Entrances & Storefronts BID DIV: 074264-084313-084500-087100-088000 CONTRACTORS APPLICATION FOR PAYMENT **CHANGE ORDER SUMMARY** Change Orders approved in **ADDITIONS** DEDUCTIONS previous months by Owner \$0.00 TOTAL \$0.00 \$919.00 \$0.00 Approved this month \$919.00 \$0.00 \$919.00 **Net Change by Change Orders** The undersigned contractor certifies that to the best of his knowledge, information and belief the Work covered by this Application for Payment has been completed and in accordance with the Contract Documents, that all amounts have been paid by him for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due, CONTRACTOR: CENTRAL KENTUCKY GLASS COMPANY Date: 10/27/2025 Donnie E. Martin, Executive Vice President ARCHITECT'S CERTIFICATE FOR PAYMENT In accordance with the Contract Documents, based on on-site observation and the data comprising the above application, the Architect certifies to the Owner that the Work has progressed to the point indicated: that to the best of his knowledge, information and belief, the quality of the

Work is in accordance with the Contract Documents and the Contractor is entitled to payment of

APPLICATION NO: THREE (3) PERIOD FROM: 10/27/25

TO: 10/30/25

CONTRACT DATE: January 22, 2025

BG # 24-207 | RTA # 23016 PROJECT NO:



Application is made for Payment as shown below in connection with the Contract Continuation Sheet attached, The present status of the this Contract is as follows: ORIGINAL CONTRACT SUM \$227,760.00 \$919.00 Net change by Change Orders \$228,679.00 CONTRACT SUM TO DATE TOTAL COMPLETED & STORED TO DATE (Sheet 2) \$36,455.00 RETAINAGE @ 10% \$3,645.50 TOTAL EARNED LESS RETAINAGE \$32,809.50 LESS PREVIOUS CERTIFICATES (CONTRACT ONLY) \$19,300.50

Subscribed and sworn to before me this 27th day of October, 202 State of: KENTUCKY Notary Public:	KATHIE LEE Notary Public - State At Large CRENT OCK A Notary ID # KYNP83175 My Commission Expires 12-18-2027
My Commission expires: 12/18/2027	Coding of a 12 To A Daniel
ARCHITECT'S CERTIFICATION: ROSS TARRANT AR	CHITECTS

(my Walls

CM APPROVAL: ALLIANCE CORPORATION

Dalton Jackson

CURRENT PAYMENT DUE

Date 11/5/2025

\$13,509.00

This certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or contractor under this Contract.

A	LICATION NO. THREE (3) *B*	*C*	*D* *E* WORK COMPLETED		*F*	*G* TOTAL	*H*	* *
ITEM #	DESCRIPTION OF WORK	SCHEDULED VALUE	FROM PREVIOUS APPLICATION (D+E)	THIS PERIOD	MATERIALS STORED (NOT IN D OR E)	COMPLETED AND STORED TO DATE (D+E+F)	% (G ÷ C)	BALANCE TO FINISH (C-G)
1	Administration / Project Management	\$6,040.00	\$1,205.00	\$0.00	\$0.00	\$1,205.00	20%	\$4,835.00
2	G & A Insurance / Project Insurance	\$4,220.00	\$845.00	\$0.00	\$0.00	\$845.00	20%	\$3,375.00
3	Payment & Performance Bond / Bond Fees	\$13,300.00	\$13,300.00	\$0.00	\$0.00	\$13,300.00	100%	\$0.00
4	Submittals / Shop Drawings	\$2,280.00	\$2,280.00	\$0.00	\$0.00	\$2,280.00	100%	\$0.00
5	Engineering / Delegated-Design Submittals	\$4,880.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$4,880.00
6	O&M Manuals / Close-out / Warranties	\$4,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$4,000.00
7	Mobilization	\$1,500.00	\$0.00	\$225.00	\$0.00	\$225.00	15%	\$1,275.00
8	Demobilization	\$500.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$500.00
9	Aluminum Storefronts (Fabrication Labor)	\$17,370.00	\$0.00	\$3,475.00	\$0.00	\$3,475.00	20%	\$13,895.00
10	Aluminum Entrances (Fabrication Labor)	\$12,580.00	\$0.00	\$1,885.00	\$0.00	\$1,885.00	15%	\$10,695.00
11	Aluminum Curtain Walls (Fabrication Labor)	\$1,370.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$1,370.00
12	Translucent Panels (Fabrication Labor)	\$6,710.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$6,710.00
13	Aluminum Storefronts-Entrances (Install Labor) [Area A]	\$8,430.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$8,430.00
14	Aluminum Storefronts-Entrances (Install Labor) [Area C]	\$18,150.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$18,150.00
15	Aluminum Storefronts-Entrances (Install Labor) [Area E]	\$5,840.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,840.00
16	Aluminum Curtain Walls (Install Labor) [Area B]	\$1,880.00	\$0.00	\$0.00	\$0.00		0%	\$1,880.00
17	Glass / Glazing (Install Labor) [Area A]	\$3,030.00	\$0.00	\$0.00	\$0.00		0%	\$3,030.00
18	Glass / Glazing (Install Labor) [Area B]	\$370.00	\$0.00	\$0.00	\$0.00		0%	\$370.00
19	Glass / Glazing (Install Labor) [Area C]	\$6,660.00	\$0.00	\$0.00	\$0.00		0%	\$6,660.00
20	Glass / Glazing (Install Labor) [Area E]	\$2,060.00	\$0.00	\$0.00	\$0.00		0%	\$2,060.00
21	MCM Wall Panels-Insul (Installation Labor) [Area A]	\$7,390.00	\$0.00	\$0.00	\$0.00		0%	\$7,390.00
22	MCM Wall Panels-Insul (Installation Labor) [Area C]	\$18,960.00	\$0.00	\$0.00	\$0.00		0%	\$18,960.00
23	Translucent Panels (Installation Labor) [Area C]	\$1,710.00	\$0.00	\$0.00	\$0.00		0%	\$1,710.00
24	Translucent Panels (Installation Labor) [Area E]	\$26,680.00	\$0.00	\$0.00	\$0.00		0%	\$26,680.00
25	Management of Direct Purchases	\$30,450.00	\$3,815.00	\$7,810.00	\$0.00		38%	\$18,825.00
26	Misc. Materials & Labor (Shims, anchors, sealants, etc.)	\$570.00	\$0.00	\$0.00	\$0.00		0%	\$570.00
27	Field Measuring / Progress Meetings	\$3,250.00	\$0.00	\$650.00	\$0.00		20%	\$2,600.00
28	Delivery / Distribution of Materials	\$1,400.00	\$0.00	\$0.00	\$0.00		0%	\$1,400.00
29	Equipment: Rental / Transport / Amort & Deprec	\$9,640.00	\$0.00	\$965.00	\$0.00		10%	\$8,675.00
30	Project Site Cleanup	\$2,280.00	·	\$0.00	\$0.00		0%	\$2,280.00
31	Final Cleaning	\$3,070.00		\$0.00	\$0.00		0%	\$3,070.00
32	Project Punchlist	\$550.00		\$0.00	\$0.00		0%	\$550.00
33	Safety	\$640.00	\$0.00	\$0.00	\$0.00		0%	\$640.00
34	CO#008: PR #010 (Vestibule locks)	\$919.00		\$0.00	\$0.00		0%	\$919.00
-	TOTALS	\$228,679.00	\$21,445.00	\$15,010.00	\$0.00	\$36,455.00	15.94%	\$192,224.00

	TINUATION SHEET NO. 3 LICATION NO. THREE (3)	TKS	Stone Middle	School Reno	vation	OWNER PURCHAS	E ORDERS ONL
A TEM #	*B* Owner PO #10-63887 DESCRIPTION	*C* SUPPLIER	*D* P.O. AMOUNT	*E* PREVIOUS PAYMENTS	*F* INVOICES DUE THIS MONTH (ATTACHED)	*G* TOTAL TO DATE (E +F)	*H* BALANCE TO FINISH (D - G)
1	Aluminum-framed Storefronts	CKG Supply	\$93,990.00	\$50,879.00	\$32,881.00	\$83,760.00	\$10,230.00
2	Hardware (Aluminum Doors)	CKG Supply	\$60,580.00	\$0.00	\$43,406.00	\$43,406.00	\$17,174.00
3	MCM-ACM Wall Panels	CKG Supply	\$66,756.00	\$0.00	\$27,831.00	\$27,831.00	\$38,925.00
4	Glazing; Translucent Wall Panels	CKG Supply	\$184,684.00	\$0.00	\$0.00	\$0.00	\$184,684.0
					5)		

\$406,010.00

TOTALS

\$50,879.00 \$104,118.00

\$154,997.00

\$251,013.00



1123 Versailles Rd

Lexington KY 40508

Voice: 859-231-6024 Fax: 859-255-7317

C/O Central Kentucky Glass

Customer ID

Etown Ind Bd of Ed

Sales Rep ID

MCM-ACM Wall Panels (stored offsite)

Bill To:
Elizabethtown Independent Board of Ed

日 日 月	V	U			
Invoice	Nun	nber:	20	025-0	33-S
Invoice	Date	٠.	\circ	ct 27	2025

INIVALAE

Page:

	000
Payment Terms	
Net 30 Davs	

Ship Date

Due Date

	11/26/25
Description	Amount
Aluminum Entrances (stored offsite)	32,881.00
Hardware (Aluminum Doors) (stored offsite)	43,406.00
MCM-ACM Wall Panels (stored offsite)	27,831.00

Customer PO

10-63887

Shipping Method

Ship to:

T.K. Stone Middle School

APPROVED Central Kentucky Glass Co By: M Date: 10/21/2025

Subtotal	104,118.00
Sales Tax	
Total Invoice Amount	104,118.00
Payment/Credit Applied	
TOTAL	104,118.00

Check/Credit Memo No:



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY) 10/24/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

	APPTICIA I TE MINISTER.	DEVISION NUMBER	
Lexington	KY 40508	INSURER F:	
		INSURER E :	
1123 Versailles Rd		INSURER D:	
Central Ky Glass Co Inc		INSURER C:	
INSURED		INSURER B: Kentucky AGC	
Campbellsville	KY 42718	INSURER A: Grange Property & Casualty Insurance Company	11982
		INSURER(S) AFFORDING COVERAGE	NAIC#
311 E Broadway		ADDRESS: mail@burkholdercompany.com	
Burkholder Insurance		[M/C, ND, EXI].	65-6696
PRODUCER		CONTACT NAME: Kathy Lawson	

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR			ADDL	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	s	
-111	×	COMMERCIAL GENERAL LIABILITY			· · · · · · · · · · · · · · · · · · ·			\$	1,000,000
	Ť	CLAIMS-MADE X OCCUR					DAMAGE TO RENTED PREMISES (Ea occurrence)	\$	1,000,000
	×	SPC					MED EXP (Any one person)	\$	10,000
Α				CPP2796073	11/08/2024	11/08/2025	PERSONAL & ADV INJURY	\$	1,000,000
	GEN	"L AGGREGATE LIMIT APPLIES PER:					GENERAL AGGREGATE	\$	2,000,000
	-	POLICY X PRO-					PRODUCTS - COMP/OP AGG	s	2,000,000
		OTHER:						5	
	AUT	OMOBILE LIABILITY		 			COMBINED SINGLE LIMIT (Ea accident)	\$	1,000,000
		ANY AUTO					BODILY INJURY (Per person)	\$	
Α	_	OWNED SCHEDULED AUTOS		CA2796074	11/08/2024	11/08/2025	BODILY INJURY (Per accident)	\$	
' '	×	HIRED NON-OWNED AUTOS ONLY					PROPERTY DAMAGE (Per accident)	S	
		AUTOS ONE!						\$	
	×	UMBRELLA LIAB OCCUR	ļ —				EACH OCCURRENCE	\$	5,000,000
A	-	EXCESS LIAB CLAIMS-MADE		CUP2796075	11/08/2024	11/08/2025	AGGREGATE	\$	5,000,000
	\vdash	DED RETENTION\$	1			The state of the s	***************************************	\$	
		KERS COMPENSATION					PER OTH- STATUTE ER		
	r	PROPRIETOR/PARTNER/EXECUTIVE				0.0000	E.L EACH ACCIDENT	\$	4,000,000
В	OFFI	CER/MEMBER EXCLUDED?	N/A	000369	01/01/2025	01/01/2026	E.L. DISEASE - EA EMPLOYEE	s	4,000,000
	fves	s, describe under CRIPTION OF OPERATIONS below					E.L. DISEASE - POLICY LIMIT	\$	4,000,000
Α		ored Material-\$104,118.00 e below		CPP2796073	11/08/2024	11/08/2025			see below

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Job: TK Stone Middle School Renovation, 323 Morningside Drive, Elizabethtown, KY


\$32,881.00 Aluminum Entrances; \$43,406.00 Hardware (Aluminum Doors); \$27,831.00 (MCM-ACM Wall Panels); Stored Material is assigned to Elizabethtown Independent Board of Education

Material is stored at 1123 Versailles Road, Lexington, KY 40508.

CERTIFICATE HOLDER		CANCELLATION
Elizabethtown Independent Board of Education		SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
219 Helm Street		AUTHORIZED REPRESENTATIVE
, Elizabethtown	KY 42701	Kathy Lawson

© 1988-2015 ACORD CORPORATION. All rights reserved.




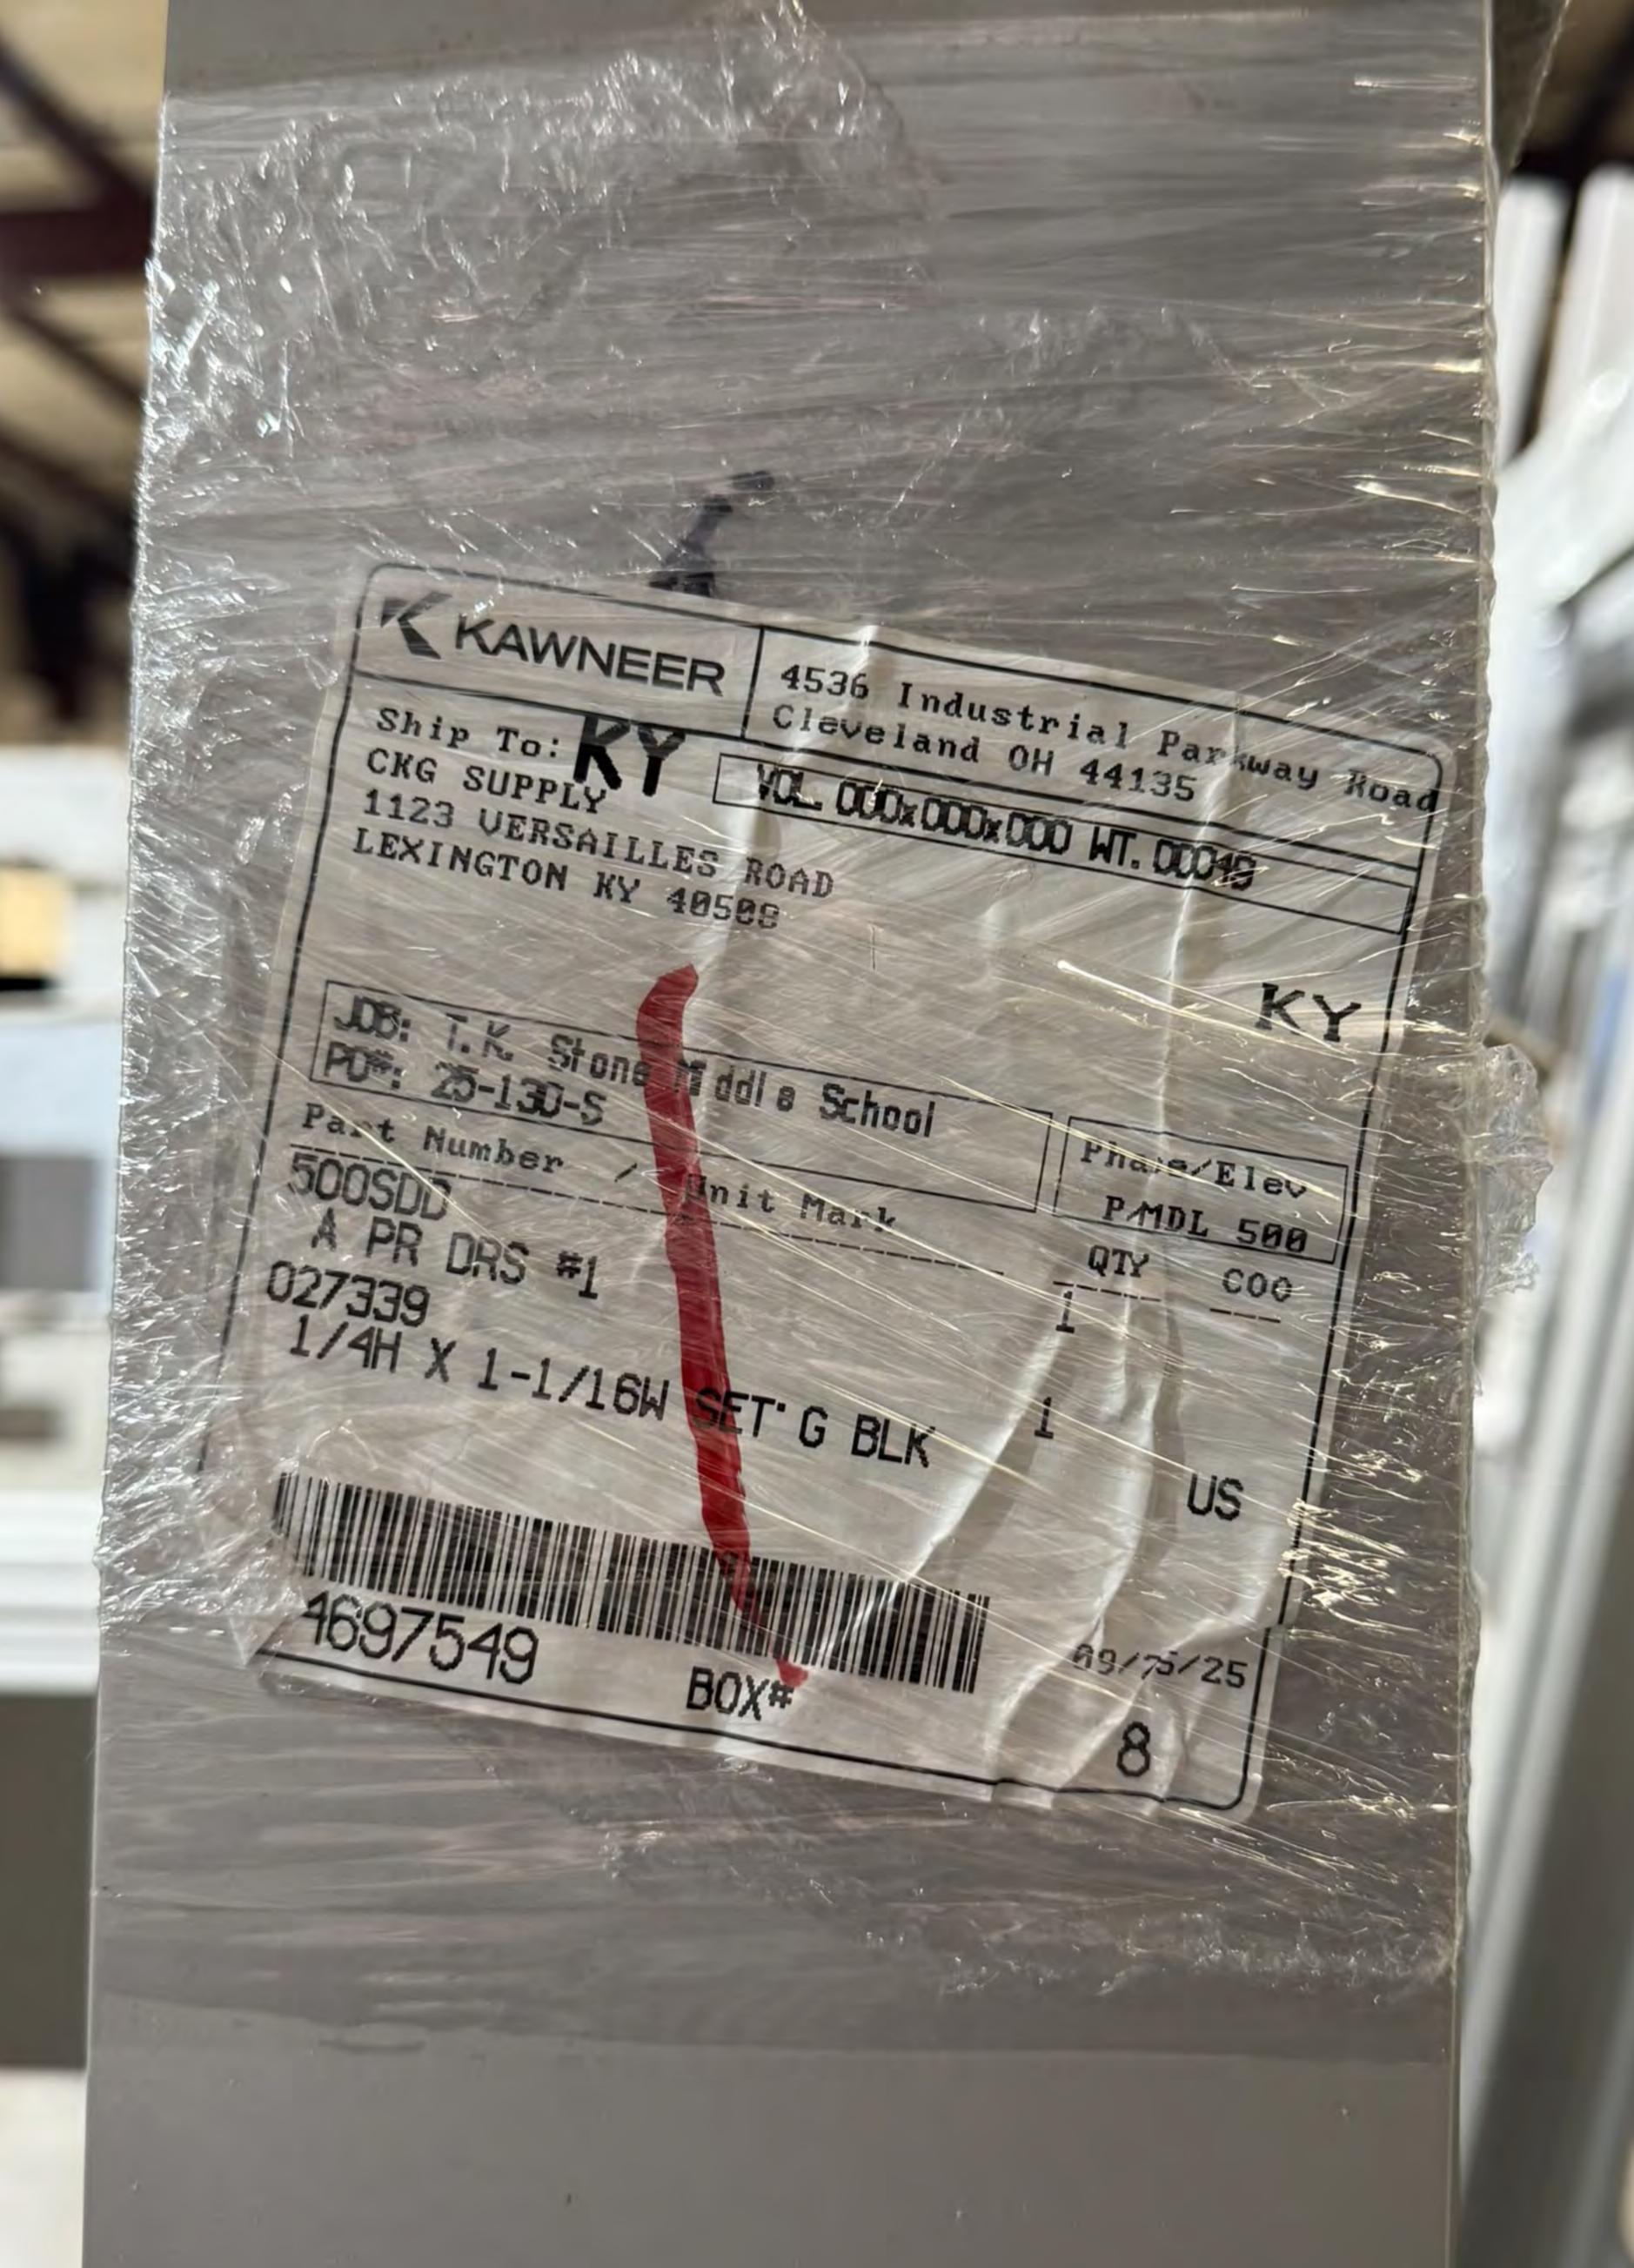








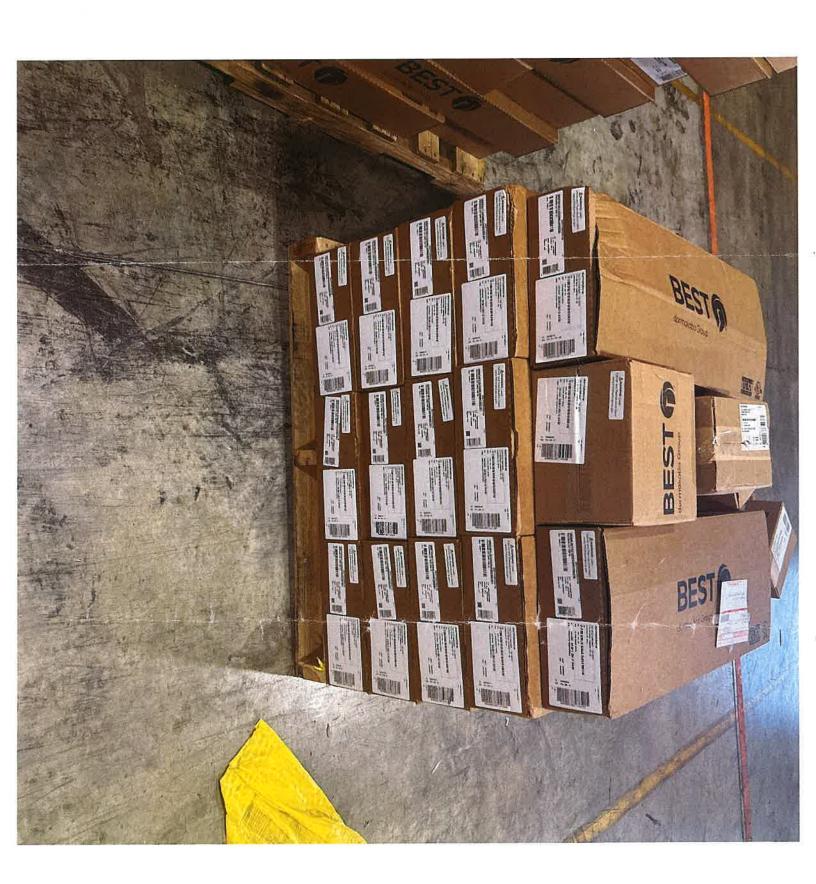



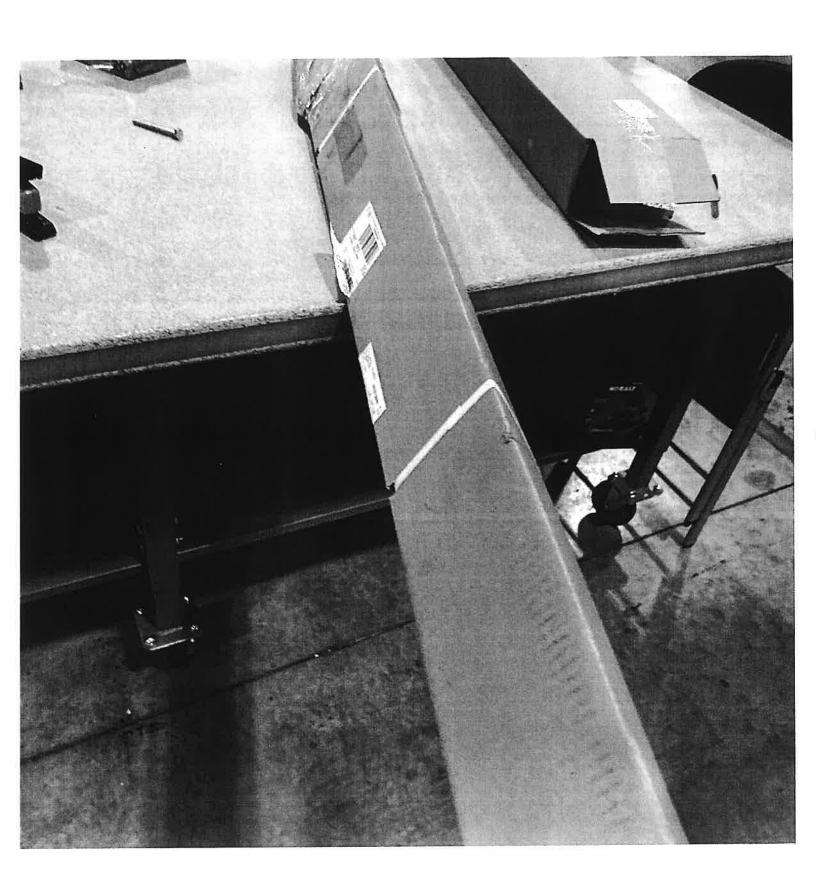





the AMOUNT CERTIFIED.

APPLICATION AND CERTIFICATE FOR PAYMENT

TO(OWNER):	Elizabethtown Independent District Board of Education		T K Stone Middle School Renovation Elizabethtown, KY	APPLICATION NO:	A
ATTENTION:	Paul Mullins	CONTRACT FOR:		CONTRACT DATE:	ALLIANCE
		BID DIV:	095 Ceilings		Builders & Managers
CONTRACTOR	S APPLICATION FOR PAYMENT			Application is made for Payment as shown below in connection with the Contract Continuation Sheet attached.	
CHANGE ORDE	TENN TO THE PERSON OF THE PERS			The present status of the this Contract is as follows:	
Change Orders a previous months		DEDUCTIONS		ORIGINAL CONTRACT SUM	\$165,000.00
TOTAL				Net change by Change Orders	\$0.00
Approved this m	nonth	***************************************		CONTRACT SUM TO DATE	\$165,000.00
				TOTAL COMPLETED & STORED TO DATE (Sheet 2)	\$114,645.00
				RETAINAGE @ 10%	\$11,464.50
				TOTAL EARNED LESS RETAINAGE	\$103,180.50
				LESS PREVIOUS CERTIFICATES (CONTRACT ONLY)	\$100,399.50
Net Change by 0	Change Orders \$0.00	\$0.00	\$0.00	CURRENT PAYMENT DUE	\$2,781.00
information and has been comple amounts have b Payment were is	d contractor certifies that to the best of his belief the Work covered by this Applicatio eted and in accordance with the Contract een paid by him for Work for which previo ssued and payments received from the Ov herein is now due.	n for Payment Documents, that all us Certificates for	ıt	Subscribed and sworn to before me this 13 day of October 2025 State of:Kentucky Notary Public: My Commission expires: 01-16-23 County of: Adair County of: Adair	
CONTRACTOR By:	Bennett's Contracting, Inc.	Date:/	0/13/25	ARCHITECT'S CERTIFICATION: ROSS TARRANT ARCHITECTS By:	Date:11/10/25
ARCHITECT'S	CERTIFICATE FOR PAYMENT		' /	CM APPROVAL: ALLIANCE CORPORATION	
In accordance w	vith the Contract Documents, based on on			_{By:} Dalton Jackson	Date:
point indicated:	cation, the Architect certifies to the Owner that to the best of his knowledge, informat rdance with the Contract Documents and t	ion and belief, the qu	uality of the	This certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the contractor named herein. Issuance, payment and acceptance of payment	



are without prejudice to any rights of the Owner or contractor under this Contract.

co	NTINUATION SHEET NO. 2 APPLICATION NO. 5	T K STONE MIDDLE SCHOOL REN		*E* COMPLETED	*F*	*G* TOTAL	*H*	*[* BALANCE
ITEM #	DESCRIPTION OF WORK	SCHEDULED VALUE	FROM PREV. APPLIC.(D+E)	THIS PERIOD	MATERIALS STORED (NOT IN D OR E)	& STORED D+E+F	% G/C	TO FINISH C-G
	BOND COST	\$3,100.00	\$3,100.00	\$0.00	\$0.00	\$3,100.00	100%	\$0.00
	SUBMITTALS	\$1,650.00	\$1,650,00	\$0.00	\$0,00	\$1,650.00	100%	\$0.00
3	CEILING TILE MATERIAL	\$31,970.00	\$31,970.00	\$0.00	\$0.00	\$31,970,00	100%	\$0.00
4	CEILING GRID MATERIAL	\$46,920.00	\$46,920.00	\$0.00	\$0.00	\$46,920.00	100%	\$0.00
5	CEILING GRID LABOR	\$19,700.00	\$6,895.00	\$0.00	\$0.00	\$6,895.00	35%	\$12,805.00
-	CEILING GRID LABOR	\$8,000.00	\$0.00	\$2,800.00	\$0.00	\$2,800.00	35%	\$5,200.00
	CLEANUP	\$1,650.00	\$412.50	\$165.00	\$0.00	\$577.50	35%	\$1,072.50
8	SPRAY INSULATION	\$1,880.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$11,880.00
_	•	\$19,900.00	\$19,900.00	\$0.00	\$0.00	\$19,900.00	100%	\$0.00
9	WALL PANEL MATERIAL		\$0.00	\$0.00	\$0.00	\$0.00	0%	\$3,000.00
10	WALL PANEL LABOR	\$3,000.00		\$0.00	\$0.00	\$0.00	0%	\$5,400.00
	EQUIPMENT	\$5,400.00	\$0.00			\$600.00	30%	\$1,400.00
	SUPERVISION	\$2,000.00	\$500.00	\$100.00	\$0.00 \$0.00	\$82.50	25%	\$247.50
	DELIVERY LABOR	\$330.00	\$82.50	\$0.00		\$150.00	30%	\$350.00
	MISC LABOR/GENERAL CONDITIONS	\$500.00	\$125.00	\$25.00	\$0.00			
	ALLOWANCE	\$5,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,000.00
16	O&M MANUALS	\$3,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$3,000.00
	CLOSEOUTS	\$1,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$1,000.00
18							#DIV/0!	\$0.00
19							#DIV/0!	\$0.00
20							#DIV/0!	\$0.00
21							#DIV/0!	\$0.00
22							#DIV/0!	\$0.00
23							#DIV/0!	\$0.00
24							#DIV/0!	\$0,00
25							#DIV/0!	\$0.00
26						\$0.00	#DIV/0!	\$0.00
27		•					#DIV/0!	\$0.00
28						\$0.00	#DIV/0!	\$0.00
29						\$0.00	#DIV/0!	\$0.00
30						\$0.00	#DIV/0!	\$0.00
31						\$0.00	#DIV/0!	\$0.00
32						\$0.00	#DIV/0!	\$0.00
33						\$0.00	#DIV/0!	\$0.00
34						\$0.00	#DIV/0!	\$0.00
35						\$0.00	#DIV/0!	\$0.00
36						\$0.00	#DIV/0!	\$0.00
37							#DIV/0!	\$0.00
38							#DIV/0!	\$0.00
39						•	#DIV/0!	\$0.00
40							#DIV/0!	\$0.00
	TOTALS	\$165,000.00 \$0.00	\$111,555.00	\$3,090.00	\$0.00	\$114,645.00	69%	\$50,355.00

	CONTINUATION SHEET NO. 3 T I		OOL RENO 5 *D*	*E*	OWNER PURCHASE ORDERS ONLY *F* *G* *H*			
ITEM #	DESCRIPTION	SUPPLIER	P.O. AMOUNT	PREVIOUS PAYMENTS	INVOICES DUE THIS MONTH (ATTACHED)	TOTAL TO DATE (E +F)	BALANCE TO FINISH (D - G)	
1 2 3 4 5 6 7 8 9	THE PARTY OF THE P					\$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	\$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00 \$0.00	
11 12 13 14 15 16 17 18								
20 21 22 23 24 25 26								
27 28 29 30 31 32 33								
35 36 37 38 39 40			***************************************					
	TOTALS		\$0.00	\$0.0	0 \$0.00	\$0.00	\$0.00	

RELEASE AND WAIVER OF LIENS

(To be submitted by Supplier or Sub-contractor of Subcontractor)

ALLIANCE CORPORATION (hereinafter ALLIANCE) is the Construction Manager for the construction of the TK Stone Middle School AC. (Hereinafter THE WORK) for Elizabethtown Independent Schools (hereinafter OWNER).

Bennett's Contracting, Inc. (hereinafter SUBCONTRACTOR) is a SUBCONTRACTOR of ALLIANCE for THE WORK.

The undersigned has furnished materials and/or labor to SUBCONTRACTOR for THE WORK, and which have been incorporated into THE WORK.

As an inducement to ALLIANCE to make progress payments to SUBCONTRACTOR, the undersigned hereby waives each and every right which it has to assert Mechanics or Materialman's Liens against THE WORK, and/or against funds of OWNER available for payment for THE WORK, and waives each and every right, claim or demand of any kind which it has against ALLIANCE, and/or ALLIANCE'S surety on its payment and performance bond, and against OWNER, for materials furnished and sold to SUBCONTRACTOR with respect to THE WORK, before October 25, 2025.

It is further understood that ALLIANCE is expected to and will rely upon this Waiver in making progress payments to SUBCONTRACTOR.

IN TESTIMONY WHEREOF, witness the signature of the undersigned. This __13_ day of __October__ 2025.

Contractor: Bennett's Contracting, Inc.

By:

Title President
Date: Jol 13 25

STATE OF Kentucky
COUNTY OF Adair
Subscribed, sworn to and acknowledged before me by Alisa King
as President (title or office) for and on behalf of Bennett's

Contracting, Inc.

NOTARY PUBLIC STATE AT LARGE
My Commission Expires: 01-16-28

OFFICIAL SEAL
JEMMIFER WALL
NOTARY PUBLIC - KENTUCKY
STATE AFFI ARGE
My Comm. Septima Jun, 18, 2028
Commission 8 CYMP. 50

APPLICATION AND CERTIFICATE FOR PAYMENT

Work is in accordance with the Contract Documents and the Contractor is entitled to payment of

the AMOUNT CERTIFIED.

TO(OWNER):	Elizabethtown Independent District Board of Education		T K Stone Middle School Renovation Elizabethtown, KY	APPLICATION NO: PERIOD FROM:10/1/202 TO:10/31/202	5
ATTENTION:	Paul Mullins	CONTRACT FOR:		CONTRACT DATE:	ALLIANCE CORPORATION
		BID DIV:	BP 092		Builders & Managers
CONTRACTOR	S APPLICATION FOR PAYMENT	• •		Application is made for Payment as shown below in connection	
CHANGE ORDE		7.		with the Contract Continuation Sheet attached. The present status of the this Contract is as follows:	
Change Orders previous months		S DEDUCTIONS		ORIGINAL CONTRACT SUM	\$369,000.00
TOTAL				Net change by Change Orders	\$0.00
Approved this m	onth			CONTRACT SUM TO DATE	\$369,000.00
				TOTAL COMPLETED & STORED TO DATE (Sheet 2)	\$99,974.00
				RETAINAGE @ 10%	\$9,997.40
				TOTAL EARNED LESS RETAINAGE	\$89,976.60
				LESS PREVIOUS CERTIFICATES (CONTRACT ONLY)	\$81,606.60
Net Change by (Change Orders \$0.00	\$0.00	\$0.00	CURRENT PAYMENT DUE	\$8,370.00
information and has been comple amounts have be Payment were is	d contractor certifies that to the best of hi belief the Work covered by this Applicati- eted and in accordance with the Contrac- een paid by him for Work for which previ- ssued and payments received from the O herein is now due.	on for Payment t Documents, that all ous Certificates for		Subscribed and sworn to before me this16th day of October State of:Kentucky Notary Public: My Commission expires:7/20/2027	MELEN MELEN
CONTRACTOR:	Grayhawk LLC	Date:_10/	16/2025	ARCHITECT'S CENTIFICATION ROSS TARRANT ARCHITECTS OF By:	pag-02-11/10/25 3
ARCHITECT'S C	CERTIFICATE FOR PAYMENT			CM APPROVAL: ALLIANCE CORPORATION	Washington XO
	rith the Contract Documents, based on or eation, the Architect certifies to the Owner			By: Dalton Jackson	Date: <u>11/5/2</u> 025
	hat to the best of his knowledge, informa	-	Ŧ	This certificate is not negotiable. The AMOUNT CERTIFIED is payable	only

to the contractor named herein. Issuance, payment and acceptance of payment

are without prejudice to any rights of the Owner or contractor under this Contract.

cc	ONTINUATION SHEET NO. 2 APPLICATION NO5	T K STONE MIDDLE SCHOOL RENO	*D* WORK	*E* COMPLETED	*F* MATERIALS	*G* TOTAL COMPLETED	*H*	* *
ITEM	DESCRIPTION	SCHEDULED	FROM PREV.	THIS	STORED (NOT	& STORED	%	BALANCE TO FINISH
#	OF WORK	VALUE	APPLIC.(D+E)	PERIOD	IN D OR E)	D+E+F	G/C	C-G
1	METAL FRAMING LABOR	\$90,000.00	\$17,000.00	\$4,000.00		\$21,000.00	23%	\$69,000.00
	GYPSUM DRYWALL LABOR	\$69,000.00	\$9,000.00	\$1,500.00		\$10,500.00	15%	\$58,500.00
	INSULATION	\$20,000.00	\$3,000.00	\$1,000.00		\$4,000.00	20%	\$16,000.00
	FINISHING	\$25,000.00	\$3,000.00	\$1,000.00		\$4,000.00	16%	\$21,000.00
	SUPERVISION	\$15,000.00	\$3,000.00	\$1,000.00		\$4,000.00	27%	\$11,000.00
6	CLEAN UP	\$3,690.00				\$0.00	0%	\$3,690.00
7	MOBILIZATION	\$10,000.00	\$10,000.00			\$10,000.00	100%	\$0.00
8	TOOLS	\$20,000.00	\$1,000.00	\$800.00		\$1,800.00	9%	\$18,200.00
9	FIELD APPLIED EIFS LABOR	\$24,000.00				\$0.00	0%	\$24,000.00
10	FIELD APPLIED EIFS MATERIAL	\$14,000.00				\$0.00	0%	\$14,000.00
11	SUBMITTALS	\$3,120.00	\$3,120.00			\$3,120.00	100%	\$0.00
12	CAULKING	\$5,500.00	\$500.00	\$0.00		\$500.00	9%	\$5,000.00
13	SHOP DRAWINGS	\$3,690.00	\$3,690.00	•		\$3,690.00	100%	\$0.00
14	ENGINEERING	\$500.00	\$500.00			\$500.00	100%	\$0.00
15	TRUSS FABRICATION LABOR	\$3,550.00				\$0.00	0%	\$3,550.00
16	TRUSS FABRICATION MATERIAL	*	\$20,340.00			\$20,340.00	100%	\$0.00
17	TRUSS ERECTION LABOR	\$18,773.00	\$5,632.00			\$5,632.00	30%	\$13,141.00
	TRUSS ERECTION MATERIAL	\$8,850.00	\$2,655.00			\$2,655.00	30%	\$6,195.00
	TRUSS FREIGHT	\$2,500.00	\$750.00			\$750.00	30%	\$1,750.00
	O&M MANUALS	\$3,000.00	\$1.00.00			\$0.00	0%	\$3,000.00
	CLOSEOUT WARRANTIES	\$1,000.00				\$0.00	0%	\$1,000.00
	BOND	\$7,487.00	\$7,487.00			\$7,487.00	100%	\$0.00
23		4.1.5.155	41,101.00			47,107.00	100,0	Ψ0.00
24								
25								
26								
27								
28								
29								
30								
31								
32								
33								
34								
35								
36								
37								
38								
39								
40								
_	TOTALS	\$369,000.00 \$0.	00 \$90,674.00	\$9,300.00	\$0.00	\$99,974.00	27%	\$269,026.00

TOTALS

	CONTINUATION SHEET NO. 3	T K STONE MIDDLE SC			OWNER PURCH		
ITEM #	APPLICATION NO.	SUPPLIER	3*D* P.O. AMOUNT	*E* PREVIOUS PAYMENTS	*F* INVOICES DUE THIS MONTH (ATTACHED)	*G* TOTAL TO DATE (E +F)	*H* BALANCE TO FINISH (D - G)
1		FBM	\$67,000.00	\$11,101.97	\$5,908.66	\$17,010.63	\$49,989.37
2 3					\$10,908.66 -dj	\$22,010.63 -d	j \$44,989.37 -
4							
5							
6 7							
8							
9							
10							
11 12							
13							
14							
15 16							
17							
18							
19							
20 21							
22							
23							
24 25	Lumm	\dots					
26	Invoice # 999 -	\$1,644.39					
27	Invoice # 1009 -						
28 29	Invoice # 912 -						
30	Invoice # 903 - Invoice # 868 -						
31	Invoice # 919 -						
32	Invoice # 920 -	\$ 672.94					
33 34	}	\$10,908.66 -DJ ქ					
35	· · · · · · · · · · · · · · · · · · ·	mmm					
36							
37							
38 39							
40							

\$67,000.00

\$11,101.97

\$5,908.66 \$17,010.63 \$49,989.37



Foundation Building Materials

Return Service Requested

Bill To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION C/O GRAYHAWK LOUISVILLE 2424 MERCHANT ST ELIZABETHTOWN KY 42701-9999

INVOICE

Invoice Number	Invoice Date	Due Date
389000999-00	09/23/2025	10/30/2025
Custome	r PO	Placed By
11-638	89	DAVID
Term	S	Page #
NET 30	NET 30TH	



PLEASE REMIT ALL PAYMENTS TO FOUNDATION BUILDING MATERIALS **6872 PAYSPHERE CIR** CHICAGO, IL 60674-6872

Ship To: DOP-TKSM

TK STONE MIDDLE SCHOOL ***DOP ORDERS ONLY** 323 MORNINGSIDE DR ELIZABETHTOWN, KY 42701-1739 (502) 499-4044

Shipping Instr	uctions		Reference			
09/22/2025	Greene, Marla	Besten, Alex	Our Truck	09/23/2025	PO 4859-0030	
Order Date	Order Taken By	Sales Rep	Ship Via	Ship Date	Job Number / Name	

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM		Net unt Due
12.00	12.00	PC	S362S162-43-12 18GA 3 5/8" STUD 1 5/8FL 12FT	0.144	1,171.00 14.052	MLF PC	1006	168.62
22.00	22.00	SHT	FRPLY58CDX-MSF 5/8" FIRE RATED CDX PLYWOOD 4X8 (19/32")	0.704	1,581.15 50.597	MSF SHT	1066	1,113,13
32.00	32.00	PC	T362T125-43-10 18GA 3 5/8" TRACK 1 1/4" LEG 10FT	0.320	977.00 9.770	MLF PC	1006	312.64

Subtotal

1,594.39

Trans Chg 50 Taxes 50.00 0.00

Total

1,644.39

Total Steel MLF Invoiced

0.464 MLF

Please reference the Invoice number with your payment

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions http://www.fbmsales.com/FBM-CREDIT California Customers; Title passes F.O.B. warehouse on pickups. Title passes F.O.B. curbside before stocking and spreading when delivered.

Manage your orders and account at MyFBM.com

Thank you for your Business

approved CT



Foundation Building Materials Return Service Requested

Bill To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION
C/O GRAYHAWK LOUISVILLE
2424 MERCHANT ST
ELIZABETHTOWN KY 42701-9999

INVOICE

Invoice Number	Invoice Date	Due Date
389001009-00	89001009-00 09/26/2025	
Custome	Placed By	
11-638	89	ERIK
Term	S	Page #
NET 30	TH	1 of 1



PLEASE REMIT ALL PAYMENTS TO

FOUNDATION BUILDING MATERIALS
6872 PAYSPHERE CIR
CHICAGO, IL 60674-6872

Ship To: DOP-TKSM

TK STONE MIDDLE SCHOOL
DOP ORDERS ONLY
323 MORNINGSIDE DR
ELIZABETHTOWN, KY 42701-1739
(502) 499-4044

Order Date	Order Taken By	Sales Rep	Ship Via	Ship Date	Job Number / Name	
09/26/2025	Greene, Marla	Besten, Alex	Our Truck	09/26/2025	PO 4859-0031	
Shipping Instru	ictions		Reference			

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM		Net unt Due
6.00	6.00	PC	S362S162-43-16 18GA 3 5/8" STUD 1 5/8FL 16FT	0.096	1,171.00 18.736	MLF PC	1006	112.42
6.00	6.00	PC	S362S162-43-14 18GA 3 5/8" STUD 1 5/8FL 14FT	0.084	1,171.00 16.394	MLF PC	1006	98.36

 Subtotal
 210.78

 Taxes
 0.00

 Total
 210.78

Total Steel MLF Invoiced

0.180 MLF

Please reference the Invoice number with your payment

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions http://www.fbmsales.com/FBM-CREDIT. California Customers: Title passes F.O.B. warehouse on pickups. Title passes F.O.B. curbside before stocking and spreading when delivered.

Manage your orders and account at MyFBM.com

Thank you for your Business

approved CT



Foundation Building Materials

Return Service Requested

BIII To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION C/O GRAYHAWK LOUISVILLE 2424 MERCHANT ST ELIZABETHTOWN KY 42701-9999

INVOICE

Invoice Number	Invoice Date	Due Date
389000912-00 08/29/2025		09/30/2025
Custome	Placed By	
11-638	89	DAVID
Term	S	Page #
NET 30	TH	1 of 1



PLEASE REMIT ALL PAYMENTS TO

FOUNDATION BUILDING MATERIALS
6872 PAYSPHERE CIR
CHICAGO, IL 60674-6872

Ship To: DOP-TKSM

TK STONE MIDDLE SCHOOL
DOP ORDERS ONLY
323 MORNINGSIDE DR
ELIZABETHTOWN, KY 42701-1739
(502) 499-4044

Order Date	Order Taken By	Sales Rep	Ship Via	Ship Date	Job Number / Name	
08/22/2025	Greene, Marla	Besten, Alex	Our Truck	08/29/2025	PO 4859-0019	
Shipping Instru	uctions		Reference			

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM	Net Amount Due
	*						
7.00	7.00	SHT	D58MM10-CT 5/8" 4X10' M2TECH MOLD RES CERTAINTEED	0.280	595.00 23.800	MSF	166.60
4.00	4.00	SHT	DCB5808-N 5/8" 4X8' CEMENT BOARD NATIONAL GYP PERMABAS	0.128 E	1,175.00 37.600	MSF SHT	150.40
22.00	22.00	PC	TTX-9110 TRIMTEX 10' 5/8" TEAR AWAY L BEAD (50/CTN)	0.220	205.00 2.050	MLF PC	45.10
35.00	35.00	PC	DWBSC10 NO-COAT OUTSIDE 90 10' CORNER BEAD (50/CTN)	0.350	554.00 5.540	MLF PC	193.90
10.00	10.00	BOX	LITENBB4.5 NGC PROFORM LITE BLUE 4.5GAL BOX JT0082	10.000	15.95	вох	159.50

 Subtotal
 715.50

 Trans Chg 50
 50.00

 Taxes
 0.00

 Total
 765.50

Total Drywall MSF Invoiced

0.408 MSF

Please reference the Invoice number with your payment

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions http://www.fbmsales.com/FBM-CREDIT California Customers: Title passes F.O.B. warehouse on pickups, Title passes F.O.B. curbside before stocking and spreading when delivered.

Thank you for your Business

Manage your orders and account at MyFBM.com



Foundation Building Materials

Return Service Requested

BIII To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION C/O GRAYHAWK LOUISVILLE 2424 MERCHANT ST ELIZABETHTOWN KY 42701-9999

INVOICE

Invoice Number	Involce Date	Due Date
389000903-00 08/29/2025		09/30/2025
Custome	Placed By	
11-638	89	David
Term	8	Page #
NET 30	TH	1 of 1



PLEASE REMIT ALL PAYMENTS TO

FOUNDATION BUILDING MATERIALS
6872 PAYSPHERE CIR
CHICAGO, IL 60674-6872

Ship To : DOP-TKSM

TK STONE MIDDLE SCHOOL
DOP ORDERS ONLY
323 MORNINGSIDE DR
ELIZABETHTOWN, KY 42701-1739
(502) 499-4044

Order Date	Order Taken By	Sales Rep	Ship Via	Ship Date	Job Number / Name	
08/20/2025	Greene, Marla	Besten, Alex	Our Truck	08/29/2025	PO 4859-0018	
Shipping Instru	ıctlons		Reference			

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM	Net Amount Due
140.00	140.00	SHT	D58MMAR10-CT 5/8" 4X10' M2TECH ABUSE RESISTANT - CERTAINTEE	5.600	805.00	MSF	4,508.00
15.00	15.00	BAG	R11U-1696-OC R11U 16X96 UNFACED M41Q SOUND(170.67) 5/UNIT	2.560	32.200 385.00 65.708	SHT MSF BAG	985.62
5.00	5.00	RL	DWT250N NATIONAL DW JOINT TAPE 250' (20/CTN)	5.000	4.55	RL	22.75

 Subtotal
 5,516.37

 Trans Chg 50
 50.00

 Taxes
 0.00

 Total
 5,566.37

Total Drywall MSF Invoiced

Please reference the Invoice number with your payment

5.600 MSF

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions https://www.fbmsales.com/FBM-CREDIT. California Customers: Title passes F.O.B. warehouse on pickups. Title passes F.O.B. curbside before stocking and spreading when delivered.

Manage your orders and account at MyFBM.com



Foundation Building Materials

Return Service Requested

Bill To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION C/O GRAYHAWK LOUISVILLE 2424 MERCHANT ST ELIZABETHTOWN KY 42701-9999

INVOICE

Invoice Number	Invoice Date	Due Date
389000868-00	09/30/2025	
Custome	Placed By	
11-638	889	DAVID
Tem	S	Page #
NET 30)TH	1 of 1



PLEASE REMIT ALL PAYMENTS TO

FOUNDATION BUILDING MATERIALS
6872 PAYSPHERE CIR
CHICAGO, IL 60674-6872

Ship To: DOP-TKSM

TK STONE MIDDLE SCHOOL
DOP ORDERS ONLY
323 MORNINGSIDE DR
ELIZABETHTOWN, KY 42701-1739
(502) 499-4044

08/14/2025	Greene, Marla	Besten, Alex	Our Truck	08/18/2025	PO 4859-0017	
Shipping Insti	ructions		Reference			

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM	Net Amount Due
60.00	60.00	SHT	D58F10-GE 5/8" 4X10' FC TYPE X	2.400	460.00 18.400	MSF SHT	1,104.00
10.00	10.00	RL	DWT250N NATIONAL DW JOINT TAPE 250' (20/CTN)	10.000	4.55	RL	45.50
4.00	4.00	PAIL	APN5 NGC PROFORM ALL PURPOSE 61.7LB PAIL JT0070 E (BLACK)	4.000 BLACK	23.95	PAIL	95.80
10.00	10.00	BAG	R11U-1696-OC R11U 16X96 UNFACED M41Q SOUND(170.67) 5/UNIT	1.707	385.00 65.708	MSF BAG	657.08
					Trai	Subtotal	1,902.38 50.00

 Subtotal
 1,902.38

 Trans Chg 50
 50.00

 Taxes
 0.00

 Total
 1,952.38

Please reference the Invoice number with your payment

2.400 MSF

Total Drywall MSF Invoiced

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions https://www.fbmsales.com/FBM-CREDIT California Customers: Title passes F.O.B. warehouse on pickups. Title passes F.O.B. curbside before stocking and spreading when delivered.

Manage your orders and account at MyFBM.com



Foundation Building Materials

Return Service Requested

BIII To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION
C/O GRAYHAWK LOUISVILLE
2424 MERCHANT ST
ELIZABETHTOWN KY 42701-9999

INVOICE

invoice Number	Invoice Date	Due Date
389000919-00 08/26/2025		09/30/2025
Custome	r PO	Placed By
11-638	89	DAVID
Term	S	Page #
NET 30	TH	1 of 1



PLEASE REMIT ALL PAYMENTS TO

FOUNDATION BUILDING MATERIALS
6872 PAYSPHERE CIR
CHICAGO, IL 60674-6872

Ship To: DOP-TKSM

TK STONE MIDDLE SCHOOL
DOP ORDERS ONLY
323 MORNINGSIDE DR
ELIZABETHTOWN, KY 42701-1739
(502) 499-4044

Order Date	Order Taken By	Sales Rep	Ship Via	Ship Date	Job Number / Name
08/25/2025	Greene, Marla	Besten, Alex	Our Truck	08/26/2025	PO 4859-0020
Shipping Instru	uctions		Reference		

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM	Net Amount Due
10.00	10.00	PC	T362TX125-18-10 20GA EQ 18M 3 5/8 DW TRK 10FT	0.100	463.00 4.630	MLF PC	46.30

 Subtotal
 46.30

 Trans Chg 50
 50.00

 Taxes
 0.00

 Total
 96.30

Total Steel MLF Invoiced

0.100 MLF

Please reference the invoice number with your payment

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions http://www.tbmsales.com/FBM-CREDIT California Customers: Title passes F.O.B. warehouse on pickups. Title passes F.O.B. curbside before stocking and spreading when delivered.

Manage your orders and account at MyFBM.com



Foundation Building Materials

Return Service Requested

Bill To: 100128174

ELIZABETHTOWN BOARD OF EDUCATION C/O GRAYHAWK LOUISVILLE 2424 MERCHANT ST ELIZABETHTOWN KY 42701-9999

INVOICE

Invoice Number	Invoice Date	Due Date
389000920-00 08/26/2025		09/30/2025
Custome	r PO	Placed By
11-638	89	DAVID
Term	S	Page #
NET 30)TH	1 of 1



PLEASE REMIT ALL PAYMENTS TO

FOUNDATION BUILDING MATERIALS
6872 PAYSPHERE CIR
CHICAGO, IL 60674-6872

Ship To: DOP-TKSM

TK STONE MIDDLE SCHOOL
DOP ORDERS ONLY
323 MORNINGSIDE DR
ELIZABETHTOWN, KY 42701-1739
(502) 499-4044

Shipping Instr	ructions		Reference			
08/25/2025	Greene, Marla	Besten, Alex	Our Truck	08/26/2025	PO 4859-0021	
Order Date	Order Taken By	Sales Rep	Ship Via	Ship Date	Job Number / Name	

Qty Ordered	Qty Shipped	Sell Unit	Product and Description	Price Unit Qty	Unit Price	Price UOM	Net Amount Due
5.00	5.00	BAG	R11U-1696-OC R11U 16X96 UNFACED M41Q SOUND(170.67) 5/UNIT	0.853	385.00 65.708	MSF BAG	328.54
20.00	20.00	SHT	D58F08-GE 5/8" 4X8' FC TYPE X	0.640	460.00 14.720	MSF SHT	294.40

 Subtotal
 622.94

 Trans Chg 50
 50.00

 Taxes
 0.00

 Total
 672.94

Total Drywall MSF Invoiced

0.640 MSF

Please reference the Involce number with your payment

A finance charge of 1-1/2% per month (18% per year) will be charged on all past due accounts. All invoices are subject to a surcharge fee of 2% of the total amount charged if paid by a credit card. ALL claims and returned goods MUST be accompanied with the appropriate paperwork. Job access is the contractor's responsibility including ingress and egress. Subject to FBM Terms and Conditions http://www.fbmsales.com/FBM-CREDIT California Customers: Title passes F.O.B. warehouse on pickups. Title passes F.O.B. curbside before stocking and spreading when delivered.

Manage your orders and account at MyFBM.com

		DDO IFOT THE			1	PAGE 01 OF 01 PAGE
	Alliance Corporation 116 E Collge Street	PROJECT: TK StoneMiddle School	APPLICATION NO.:	3 Dis	stribution to:	COMPRESSION OF STREET
			Invoice #			
	Glasgow, KY 42142		PERIOD TO:	10/17/2025		OWNER
			SCF Job#	2412200182		OWNER
FROM CONTRACTOR:	Spectra Contract Flooring			BP096		ARCHITECT
on on the order	5644 Shepherdsville Road	VIA ARCHITECT:	PROJECT NOS.:	DI 000		CONTRACTOR
	Louisville, KY 40228		sub Contract No.:			
	Louisville, NT 40220		CONTRACT DATE:		_	
CONTRACT FOR:	Commercial Flooring					
CONTRACTOR'S AP	PLICATION FOR PAYMENT					
Application is made for navment	as shown below, in connection with the Contract.		The undersigned Contractor certifies that to the best of the	Contractor's knowledge	infor-	
Continuation Sheet, AIA Docume	as shown below, in connection with the Contract.		mation and belief the Work covered by this Application for	Payment has been comp	leted	
- Tooding	in 6700, is attached.		in accordance with the Contract Documents, that all amour	its have been paid by the		
1. ORIGINAL CONTRACT SUM		//-	Contractor for Work for which previous Certificates for Pay	ment were issued and na	nv-	
		<u>\$154,803.00</u>	ments received from the Owner, and that current payment	shown herein is now due.		
2. Net change by Change Orde	rs		CONTRACTOR: Spectra Contract Flooring		0	
		#400 000 00 "				
		\$198,889.00 - dj	By:	Date	e:	10/17/25
3. CONTRACT SUM TO DATE (Line 1 +/- 2)	\$353,692.00 - dj - \$154,803.00 -	6			
4. TOTAL COMPLETED & STOR	RED TO DATE	\$37,519.00	State of Kentucky, County of Jefferson			
(Column G on G703)		907,018.00	Cotambert 1	+ DOOS Karen	Marie S	Simpson
. RETAINAGE:		\$3,281.90	Notory Public:	Notary Public.	Commonw	ealth of Kentucky
a. 10% of Completed Work		1 110 (min 2002)	Show of the state	Commi	ission # KY	NP104879
(Columns D + E on G703) b. 10% of Stored Material			My commission expires:	Expirati	on date. S	/16/2029
(Column F on G703)			my transmission expires.		AND THE PARTY	The state of the s
(Column F on G/03)				Charles of the same		
		\$470.00	ARCHITECT'S CERTIFICATE FOR PA	VMENT		
Total Retainage (Line 5a + 5b o	or	\$470.00	ARCHITECT'S GERTIFICATE FOR PA	YMENT		
Total Retainage (Line 5a + 5b of Total in Column I of G703		\$470.00	In accordance with the Contract Documents, based on on-s	ite observations and the	data	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAINED			In accordance with the Contract Documents, based on on-s comprising this application, the Architect certifies to the Own	ite observations and the ner that to the best of the		
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAIL (Line 4 less Line 5 Total)	NAGE	\$470.00 \$33,767.10	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a	ite observations and the ner that to the best of the progressed as indicated	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETA (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICA	NAGE		In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents.	ite observations and the ner that to the best of the progressed as indicated	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETA (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICA (Line 6 from prior Certificate)	NAGE	\$33,767.10 \$29,537.10	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a	ite observations and the ner that to the best of the progressed as indicated	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETA (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICA	NAGE	\$33,767.1 <u>0</u>	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has quality of the Work is in accordance with the Contract Document of the AMOUNT CERTIFIED. AMOUNT CERTIFIED	ite observations and the oner that to the best of the progressed as indicated, ments, and the Contracto	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE	NAGE TES FOR PAYMENT	\$33,767.10 \$29,537.10 \$4,230.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount if incompanies on this Application and on the Continuation Sheet	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contracto	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETA (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICA (Line 6 from prior Certificate)	NAGE TES FOR PAYMENT	\$33,767.10 \$29,537.10	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount all figures on this Application and on the Continuation Sheet conform to impain ount certified.)	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contracto	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETA (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICA (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI	NAGE TES FOR PAYMENT	\$33,767.10 \$29,537.10 \$4,230.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount if incompanies on this Application and on the Continuation Sheet	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contracto	the	
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6)	TES FOR PAYMENT DING RETAINAGE	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount in the amount in the Continuation Sheet conform to the amount certified.) ARCHITECT:	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contracto	the	444605
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in	NAGE TES FOR PAYMENT	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount if gures on this Application and on the Continuation Sheet conform to the amount certified.) ARCHITECT:	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in evious months by Owner	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount in the Amount on the Continuation Sheet conform to the amount certified.) ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED.	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to Date:	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in evious months by Owner otal approved this Month	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount if it is amount certified.) ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to Date: It is payable only to the Contractor of payment are without	the r	11/10/25
Total Retainage (Line 5a + 5b or Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in revious months by Owner otal approved this Month	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount in the Amount on the Continuation Sheet conform to the amount certified.) ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED.	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to Date: It is payable only to the Contractor of payment are without	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in evious months by Owner otal approved this Month	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00 \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount lifegures on this Application and on the Continuation Sheet conform to the amount certified ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of prejudice to any rights of the Owner or Contractor under this	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to Date: It is payable only to the Contractor of payment are without	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in evious months by Owner otal approved this Month	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00 \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount if it is amount certified.) ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to Date: It is payable only to the Contractor of payment are without	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in evious months by Owner otal approved this Month	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00 \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has quality of the Work is in accordance with the Contract Document is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount lifegures on this Application and on the Continuation Sheet conform to the amount certified ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of prejudice to any rights of the Owner or Contractor under this	ite observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor and applied for. Initial that are changed to Date: It is payable only to the Contractor of payment are without	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6)	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$33,767.10 \$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00 \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount all figures on this Application and on the Continuation Sheet conform to the amount certified ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of prejudice to any rights of the Owner or Contractor under this OWNER: By:	ite observations and the observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor of the applied for. Initial that are changed to Date: Dispayable only to the Contract.	the r	11/10/25
Total Retainage (Line 5a + 5b of Total in Column I of G703 TOTAL EARNED LESS RETA (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICA (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY obtail changes approved in revious months by Owner obtail approved this Month hange Order 1	INAGE TES FOR PAYMENT DING RETAINAGE ADDITIONS \$1,0	\$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00 \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents is entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount all figures on this Application and on the Continuation Sheet conform to fine amount certified.) ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of prejudice to any rights of the Owner or Contractor under this OWNER: By: CONSTRUCTION MANAGER:	ite observations and the observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor of the applied for. Initial that are changed to Date: Dispayable only to the Contract.	the r	
Total Retainage (Line 5a + 5b or Total in Column I of G703 TOTAL EARNED LESS RETAI (Line 4 less Line 5 Total) LESS PREVIOUS CERTIFICAI (Line 6 from prior Certificate) CURRENT PAYMENT DUE BALANCE TO FINISH, INCLUI (Line 3 less Line 6) CHANGE ORDER SUMMARY otal changes approved in revious months by Owner otal approved this Month	TES FOR PAYMENT DING RETAINAGE ADDITIONS	\$29,537.10 \$4,230.00 \$121,035.90 DEDUCTIONS \$0.00 \$0.00 \$0.00	In accordance with the Contract Documents, based on on-scomprising this application, the Architect certifies to the Own Architect's knowledge, information and belief the Work has a quality of the Work is in accordance with the Contract Documents entitled to payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED (Attach explanation if amount certified differs from the amount all figures on this Application and on the Continuation Sheet conform to the amount certified ARCHITECT: By: This certificate is not negotiable. The AMOUNT CERTIFIED tractor named herein. Issuance, payment and acceptance of prejudice to any rights of the Owner or Contractor under this OWNER: By:	ite observations and the observations and the observations and the observations and the best of the progressed as indicated, ments, and the Contractor of the applied for. Initial that are changed to Date: Dispayable only to the Contract.	the r	11/10/25

CONTINUATION SHEET

APPLICATION AND CERTIFICATE FOR PAYMENT

In tabulations below, amounts may be stated to the nearest dollar.

Contractor's signed Certification is attached.

TO:

Alliance Corporation

From: Spectra Contract Flooring

APPLICATION NO.:

APPLICATION DATE: PERIOD TO:

10/17/25 10/31/25

3

(DESCRIPTION OF WORK Bond Submittals	SCHEDULED VALUE	WORK COMPLETED			G	Н	1	J
					MATERIALO		2000		-
(FROM PREV. APPLICATION (D+E)	THIS PERIOD	MATERIALS PRESENTLY STORED (NOT IN D OR E)	TOTAL COMPLETED & STORED TO DATE	% (G / C)	BALANCE TO FINISH (C-G)	RETAINAGE
(Submittale	\$1,480.00	\$1,480.00		IN D OR E)	(D+E+F)	72227		10%
(\$3,939.00	\$3,939.00			\$1,480.00	100%	\$0.00	\$148.0
	Clean up	\$3,939.00	\$0.00			\$3,939.00	100%	\$0.00	\$393.9
	Closeout Documents	\$1,000.00	\$0.00			\$0.00	0%	\$3,939.00	\$0.0
	O&M Manuals	\$3,000.00	\$0.00			\$0.00	0%	\$1,000.00	\$0.0
- 5	Safety/Engineering	\$3,000.00	\$2,000.00			\$0.00	0%	\$3,000.00	\$0.0
\	Varehouse and Logistics	\$6,000.00	\$4,500.00			\$2,000.00	67%	\$1,000.00	\$200.0
1	st Floor Area A - Carpet Tile	\$4,700.00	\$0.00		£4 700 00	\$4,500.00	75%	\$1,500.00	\$450.0
1	st Floor Area A - Carpet Tile Labor	\$2,500.00	\$0.00		\$4,700.00	\$4,700.00	100%	\$0.00	\$470.0
1	st Floor Area A - SVT Labor	\$6,500.00	\$0.00			\$0.00	0%	\$2,500.00	\$0.0
1	st Floor Area A - Base Labor	\$2,500.00	\$0.00			\$0.00	0%	\$6,500.00	\$0.0
1	st Floor Area A - Floor Prep	\$5,000.00	\$0.00			\$0.00	0%	\$2,500.00	\$0.0
1	st Floor Area B - SVT Labor	\$9,500.00	\$0.00			\$0.00	0%	\$5,000.00	\$0.00
1	st Floor Area B - Base Labor	\$2,000.00	\$0.00			\$0.00	0%	\$9,500.00	\$0.0
1	st Floor Area B - Floor Prep	\$5,500.00	\$0.00			\$0.00	0%	\$2,000.00	\$0.0
	st Floor Area C - SVT Labor	\$6,500.00	\$0.00			\$0.00	0%	\$5,500.00	\$0.00
1	st Floor Area C - Res. Tile Labor	\$10,500.00	\$0.00			\$0.00	0%	\$6,500.00	\$0.00
1	st Floor Area C - Base Labor	\$2,250.00	\$0.00			\$0.00	0%	\$10,500.00	\$0.00
	1st Floor Area C - Floor Prep	\$7,500.00	\$0.00			\$0.00	0%	\$2,250.00	\$0.00
2	nd Floor Area A - SVT Labor	\$7,750.00				\$0.00	0%	\$7,500.00	\$0.00
2	nd Floor Area A - Base Labor	\$1,500.00	\$0.00			\$0.00	0%	\$7,750.00	\$0.00
2	nd Floor Area A - Floor Prep	\$4,395.00	\$0.00			\$0.00	0%	\$1,500.00	\$0.00
2	nd Floor Area B - SVT Labor	\$11,500.00	\$0.00			\$0.00	0%	\$4,395.00	\$0.00
2	nd Floor Area B - Base Labor	\$2,400.00	\$11,500.00			\$11,500.00	100%	\$0.00	\$1,150.00
2	nd Floor Area B - Floor Prep	\$7,000.00	\$2,400.00			\$2,400.00	100%	\$0.00	\$240.00
2	nd Floor Area C - SVT Labor		\$7,000.00			\$7,000.00	100%	\$0.00	\$700.00
21	nd Floor Area C - Res. Tile Labor	\$9,250.00	\$0.00			\$0.00	0%	\$9,250.00	\$0.00
21	nd Floor Area C - Base Labor	\$4,200.00	\$0.00			\$0.00	0%	\$4,200.00	\$0.00
21	nd Floor Area C - Floor Prep	\$2,000.00	\$0.00			\$0.00	0%	\$2,000.00	\$0.00
S	eps Labor	\$2,500.00	\$0.00			\$0.00	0%	\$2,500.00	\$0.00
	oor Protection Labor	\$8,500.00	\$0.00			\$0.00	0%	\$8,500.00	\$0.00
	O #1 - RFP #2 - 6th Grade wing flooring -dj	\$6,500.00	\$0.00			\$0.00	0%	\$6,500.00	\$0.00
	S #1 TAT #2 Our Crade wing nooning aj	\$198,889.00 - dj						\$198,889.00 - cj	40.00
+									
Pa	ge Total	\$154,803.00	\$22,840,00	20.05					
Pro	ject Total	\$154,803.00	\$32,819.00 \$32,819.00	\$0.00 \$0.00	\$4,700.00 \$4,700.00	\$37,519.00 \$37,519.00	24% 24%	\$117,284.00	\$3,751.90

Spectra | contract flooring

CONDITIONAL WAIVER AND RELEASE PROGRESS PAYMENT

Upon receipt by the undersigned of a check from Alliance Corporation \$4,230.00 payable to Spectra Contract Flooring, and when the check has been properly endorsed and has been paid by the bank upon which it is drawn, this document shall become effective to release any mechanic's lien, stop notice, or bond right the undersigned has on the job of TK StoneMiddle School located at Elizabethtown, KY to the following extent. This release covers progress payment for labor, service equipment, material furnished to **Alliance Corporation** through October 17, 2025 only does not cover retention retained before or after the release date; extras furnished before the release date for which payment has not been received; extras or items furnished after the release date. Rights based upon work performed or items furnished under a written change order which has been fully executed by the parties prior to the release date are covered by this release unless specifically reserved by the claimant in this release. This release of any mechanic's lien, stop notice, or bond right shall not otherwise affect the contract rights, including rights between parties to the contract based upon a rescission, abandonment, or breach of the contract, or the right of the undersigned to receive compensation for furnished labor, services, equipment, or material covered by this release if that furnished labor, services, equipment, or material was not compensated by the progress payment. Before any recipient of this document relies on it, said party should verify evidence of payment to the undersigned.

DATE:

October 17, 2025

Spectra Contract Flooring

State of KY , County of Jefferson Subscribed and sworn to before me this

Notory Public:

My commission expires:

CT 3005

Karen Marie Simpson
Notary Public, Commonwealth of Kentucky
Commission # KYNP104879

Expiration date. 9/16/2029

SUBCONTRACTOR AFFIDAVIT & CONDITIONAL WAIVER & RELEASE OF LIENS

Spectra Contract Flooring	3	herinafter ("Subcontractor") ha	aving a contract with	
for the work of (project)	TK StoneMiddle School		address) Elizabethtown, KY	Alliance Corporation
whereof (Owner)		is or	the Owner and O	and have a second
and/or furnished materials,	equipment and/or machinery or has	fabricated materials especially f	for this project.	see, has performed work
Materials				
	t the following shows the names of	OVOD poroon furnishing		
amount, if any, which is due	t the following shows the names of e e, or to become due to them. If all ma	sterial is paid in full places state	ery, material or fuel to said Subcont	ractor, giving the
Name		Material	as such.	
		material		Amount Due
all materials are pd				
Lahar				
Labor Said affiant further save that	the feller in the state of			
which is due, or to become of	the following shows the names of edue, to them. If all labor is paid in full	very unpaid laborer in the emplo	by of said Subcontractor, giving the	amount, if any,
Name		in produce didice as such.	Amount Due	
			Amount Due	
"NONE"				
Subcontractors				
	the fellowing of the			
if any which is due, or to be	the following shows the names of ev	very Subcontractor, if any, under	r a contract with the principal contra	actor, giving the amount,
any, which is due, or to bec	come due, to them. If all Subcontract	tors are paid in full or if none are	contracted, please state as such.	
Name				
Titaling .			Amount Due	
all subs are pd				
Conditional Lien Waiver				
	ractor of a check in the amount of			
Subcontractor waives and rel	eases all rights to liens and claims a	\$4,230.00 and wh	hen said check is paid by the bank	upon which it is drawn,
naterials, equipment and/or r	machinery, or for especially fabricate	igainst ti .		200 0
STEEL TO THE STATE OF THE STATE	and the copediany raphicate	id materials for the project furnis	sned to the Owner to the extent of t	he payment received.
I, Chris Johns		being VP of Sales and Ope	erations of Country	
o hereby acknowledge the fo	oregoing in full and certify that this is	a true and accurate statement	erations of Spectra	Contract Flooring
	,	a true and accurate statement.		
()				
ignature				
				A
tate Of: Kentucky		Subscribed and sworn to before	me this day o	1 /ht 2025
ounty Of: Jefferson		XX	day o	1
		1 Jac	A Cimpson	~
	1	Notary Public	Karen Marie Simpson Notary Public, Commonwealth of Ker	ntucky
			COMMISSION & Letter 19.10.	
			- 1 Non data 0/48/2029	4 7

Ohio Valley DPO Invoice Summary Oct. 2025 -DJ

Less Previous \$0.00

Total Completed and Stored to Date \$22,180.00

```
Invoice # 216104 - $20,270.80

Invoice # 221005 - $ 1,909.20

$22,180.00 Total due -DJ
```

Balance to Finish \$10,147.00

Unio valley Flooring

INVOICE#	PAGE#
216104	

INVOICE DATE	SHIP DATE	SHIP VIA					210104	1
08/27/25	0000000	Jiii VIA	F.O.B.	ACCT#	YOUR P.O.#	TERMS	OUR DESCRIPTION	
00/21/20	08/27/25	OUR TRUCK	REG. TRUCK	04444		,	OUR REF#	ORDER#
	SCAC APST	LL06 (LOUISV		044444	13-63894	C NET 30	9728424	240455
			ILLE LOCAL)	044440	SPECTRA			019456
BILL TO:							LP/LOU/	MS

ELIZABETHTOWN INDEPENDENT BOARD OF EDUCATION 219 HELM STREET ELIZABETHTOWN KY 42701 SHIP TO:

OVF CONTRACT SALES
***BILL-TO SAME AS SHIP-TO
LOUISVILLE KY 40213

2004	ITEM NUMBER		SERIAL#	DESCRIPTION	QUANTITY	QUANTITY	QUANTITY	T		
0001				******SEND ORDER AND INVOICE TO:	ORDERED	SHIPPED	B/O	UM	PRICE	AMOUNT
0002				SPECTRA/DIVERZIFY						
0003				5644 SHEPHERDSVILLE RD						
0004				LOUISVILLE RD						
0005				LOUISVILLE, KY 40228						
0006				**EMAIL COPY OF INVOICE TO:						
0010	TAR400368326	1		KAREN.SIMPSON@SPECTRACF.COM						
		100		HAMMERED SPECKLED RUBBER 24X24	88.00	00.00				
0011				MT RAINER HRTSPVE7 3.2MM	00.00	88.00		EA	26,600	2,340.80
0020	7474			SPA 1197358 / 1						-10.000
0020	TAR400368369	1		HAMMERED SPECKLED RUBBER 24X24	NATION SECTION					
and the				CAPE HATTERAS HRTSPVK5 3.2MM	101.00	101.00		EA	26.600	
0021				SPA 1197358 / 1					20.000	2,686.60
1030	TAR400368322	1								
				HAMMERED SPECKLED RUBBER 24X24	569.00	569.00				
031				SPOKANE WARM HRTSPVE3 3.2MM	0.000000	505.00		EA	26.600	15,135.40
966				SPA 1197358 / 1						
none.				Delivery Charge:						
				Bill of Lading# 136908913879 Manifest# 0136908						108.00

Branch LOU

REMIT TO:

TOTAL PRICE \$

20,270.80

TOTAL AMOUNT DUE \$

20,270.80

Mobile friendly OVF Online is available now at https://online.ovf.com

Please return this portion with your remittance.

ELIZABETHTOWN INDEPENDENT

LOU

ACCT# INVOICE# DATE
044444 216104 08/27/25

TOTAL PRICE \$

20,270.80

OHIO VALLEY FLOORING 3079 SOLUTIONS CENTER CHICAGO IL 60677-3000

TOTAL AMOUNT DUE \$

20,270.80

Ohio Valley Flooring

THIS IS AN INVOICE

INVOICE#	PAGE#
221005	1

INVOICE DATE								
INVOICE DATE	SHIP DATE	SHIP VIA	F.O.B.	ACCT#	YOUR P.O.#	TERMS	OUR REF#	ORDER#
09/17/25	09/17/25	OUR TRUCK	REG. TRUCK	044444	40.00004		Social States	
	SCAC APST	1105 (10110)		000000000000000000000000000000000000000	13-63894	C NET 30	9739821	026309
	OUND AT OT	LL05 (LOUISVI	LLE LOCAL)	044440	SPECTA		LP/LOU/	MS

BILL TO:

ELIZABETHTOWN INDEPENDENT BOARD OF EDUCATION 219 HELM STREET ELIZABETHTOWN KY 42701 SHIP TO:

OVF CONTRACT SALES
***BILL-TO SAME AS SHIP-TO
LOUISVILLE KY 40213

0001	ITEM NUMBER	SERIAL#	DESCRIPTION	QUANTITY ORDERED	QUANTITY	QUANTITY B/O	UM	PRICE	AMOUNT
0002 0003 0004 0005 0006			SEND ORDER AND INVOICE TO: SPECTRA CONTRACT FLOORING 5644 SHEPHERDSVILLE RD LOUISVILLE, KY 40228 SEND INVOICE TO KAREN,SIMPSO	*****					
0010 T	AR440145160	1	RUBBER COVE GREY DC 48 4 X 120 1/8 TOE	19.00	19.00		СТ	94.800	1,801.2
9966			Delivery Charge: Bill of Lading# 137017915367 Manifesti	= # 0137017					108,0

Branch LOU

REMIT TO:

TOTAL PRICE \$

1,909,20

TOTAL AMOUNT DUE \$

1,909.20

Mobile friendly OVF Online is available now at https://online.ovf.com

Please return this portion with your remittance.

ELIZABETHTOWN INDEPENDENT

LOU

ACCT# INVOICE# DATE
044444 221005 09/17/25

TOTAL PRICE \$

1,909.20

OHIO VALLEY FLOORING 3079 SOLUTIONS CENTER CHICAGO IL 60677-3000

TOTAL AMOUNT DUE \$

1,909.20

EVIDENCE OF COMMERCIAL PROPERTY INSURANCE

DATE (MM/DO/YYYY) 10/20/2025

THIS EVIDENCE OF COMMERCIAL PROPERTY INSURANCE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS

PRODUCER NAME, CONTACT PERSON AND ADDRESS), AUTHORIZED REPRESENTATIVE				COMPANY NAME AND AD			NAIC NO: 19437	
CONTACT PERSON AND ADDRESS Willis Towers Watson Nort					Lexington Insurance Company				
c/o 26 Century Blvd					100 Summer St				
P.O. Box 305191					Boston, MA 02	1102106			
Nashville, TN 372305191	USA								
FAX (A/C, No): 1-888-467-2378	E-MAIL AOORESS: certificates@wtwco.co	6	IF MULTIP	LE COMPANIES	COMPLETE SE	PARATE FORM FOR EACH			
CODE:	SUB CODE:				POLICY TYPE				
AGENCY CUSTOMER ID 4:					Commercial Prope	rty			
NAMED INSURED AND ADDRESS Spectra Holdings, Inc.					LOAN NUMBER		P	OLICY NUMBER	
Spectra Holdings, Inc. 5670 Shepherdsville Road							0	11144832	
Louisville, KY 40218					EFFECTIVE DATE	EXPIRATIO	NOATE	CONTINUED UNTIL	
					07/01/2025	07/01/2	026	TERMINATED IF CHECKED	
ADDITIONAL NAMED INSURED(S)					THIS REPLACES PRIOR E	VIDENCE DATE	D:		
DDODEDTY INFORMATIO	M (ACODD 101 may be attached if				o in required) 🖾 🖭	III DING OF	RIPIN N	ESS PERSONAL PROPERTY	
LOCATION / DESCRIPTION	N (ACORD 101 may be attached if	mọi	9 3	pac	e is required) as Bo	ILDING OF	1 60 003111	ESS PERISONAL PROFEST	
LOCATION, DESCRIPTION									
ANY REQUIREMENT, TERM O	E LISTED BELOW HAVE BEEN ISSUED R CONDITION OF ANY CONTRACT OR I, THE INSURANCE AFFORDED BY THE	HTC	ER C	COC	UMENT WITH RESPECT	TO WHICH TH	IS EVIDENCE	OF PROPERTY INSURANCE MAY	
	HOWN MAY HAVE BEEN REDUCED BY				S.				
COVERAGE INFORMATIO			SIC		BROAD X SPE	CIAL			
COMMERCIAL PROPERTY COV	ERAGE AMOUNT OF INSURANCE \$,000	÷	T-			DED: 10,000	
		YES	NO	N/A			1		
BUSINESS INCOME IN R	ENTAL VALUE	X		_	If YES, LIMIT, Includ			ual Loss Sustained; # of months.	
BLANKET COVERAGE		X			If YES, indicate value(s)		perty identified	above \$	
TERRORISM COVERAGE		X			Attach Disclosure Notice	*DEC			
IS THERE A TERRORISM-S	PECIFIC EXCLUSION?		X	_					
IS DOMESTIC TERRORISM	EXCLUDED?		X						
LIMITED FUNGUS COVERAGE			X		If YES, LIM T			DED	
FUNGUS EXCLUSION II "YES".	specify organization's form used)	X		╙					
REPLACEMENT COST		X							
AGREED VALUE		X							
COINSURANCE				×	If YES				
EQUIPMENT BREAKDOWN (II A	pplicable	X			If YES LIMIT Include			DED 50,000	
ORDINANCE OR LAW - Covera	ge for loss to undamaged portion of bldg	X			If YES, LIMIT: include			DED: 50,000	
- Demoli	tion Costs	X			If YES, LIMIT: 10,000			DED: 50,000	
- Incr. C	ost of Construction	X		1	If YES, LIMIT: 10,000			DED: 50,000	
EARTH MOVEMENT (If Applicab	le)	X		1	If YES, LIMIT: 60,000			DED: 100,000	
FLOOD (If Applicable)		X			If YES, LIMIT: 60,000			DED: 100,000	
WIND / HAIL INCL YES	□ NO Subject to Different Provisions:	×			II YES, LIMIT: 60,000	,000		DED: 50,000	
	NO Subject to Different Provisions: DGATION IN FAVOR OF MORTGAGE	×			If YES, LIMIT: include	nd.		DED: 50,000	
HOLDER PRIOR TO LOSS				_					
SHOULD ANY OF THE	ABOVE DESCRIBED POLICIES E	3E	CAN	ICE	LLED BEFORE THE	EXPIRATION	N DATE T	HEREOF, NOTICE WILL BE	
	ANCE WITH THE POLICY PROVISIO								
ADDITIONAL INTEREST									
CONTRACT OF SALE	LENDER'S LOSS PAYABLE LOSS	S PAY	/EE		LENDER SERVICING AGEN	IT NAME AND AL	ODRESS		
MORTGAGEE									
NAME AND ADDRESS									
Elizabethtown Independe	nt Board of Education				AUTHORIZED REPRESENT				
323 Morningside Drive					Patricia 0	- Free			
Elizabethtown, KY 42701						-			

© 2003-2015 ACORD CORPORATION. All rights reserved.

AGENCY CUSTOMER ID:	
LOC#	



ADDITIONAL REMARKS SCHEDULE

Page 2 of 2

AGENCY Willis Towers Watson Northeast,	Inc	NAMED HSURED Spectra Holdings, Inc. 5670 Shepherdsville Road			
POLICY NUMBER See Page 1		Louisville, KY 40218			
CARRIER	NAIC CODE				
See Page 1	See Page 1	1 EFFECTIVE DATE: See Page 1			
ADDITIONAL REMARKS					
THIS ADDITIONAL REMARKS FORM IS FORM NUMBER: 28 FORM 1		operty			
Sublimits -					
Earthquake in CA: \$10,000,000					
Installation Floater - Stored					
Stored Materials includes Prop \$1,000,000 / \$10,000 Deductibl		Care, Custody or Control of the Named Insured; Limit			

Deductibles =

Inland Transit \$1,000,000 per occurrence

Earthquake in CA: 5% per unit / \$100,000 minimum
Earthquake in PNW: 2% per unit / \$100,000 minimum
Flood Zones A/V: 3% per unit / \$250,000 minimum
Mammed Windstorm in Tier 1 Counties: 5% per unit / \$100,000 minimum (Tri-County, FL); 3% per unit / \$100,000 minimum
(All other FL counties); 2% per unit / \$100,000 minimum (All other Tier 1 counties)

Project name Vel TK Stone Middle School / Diverzify job Number: 2412200182 Stored Material Description: Flooring material Stored Material Value: \$25,000

Address Stored Materials are Located 5644 Shepherdsville Road Louisville, KY 40228

ACORD 101 (2008/01)

© 2008 ACORD CORPORATION. All rights reserved.

Coverage / Policy	% Participation	\$ Participation	Insurer/Paper	Policy #
Primary \$10M	30.00%	\$3,000,000	Lexington Insurance Company	11144832
Primary \$10M	20.00%	\$2,000,000	Beazley Excess and Surplus Insurance Inc	D233C1250801
Primary \$10M	20.80%	\$2,080,000	Allied World Assurance Company	0310-7409-1A
Primary \$25M	9.20%	\$2,300,000	Lloyds QBE	B1230AP06336A2
Primary \$25M	20.00%	\$5,000,000	Lloyds Brit	B1230AP06336B2
\$15M x \$10M	16.67%	\$2,500,000	Arch Specialty Insurance Company	ESP7303053-09
\$15M x \$10M	33.33%	\$5,000,000	AXIS Surplus insurance Company	P-001-000891773 01
\$15M x \$10M	20.80%	\$3,120,000	StarStone Specialty Insurance Company	CSP00143919P-0
\$35M x \$25M	15.00%	\$5,250,000	RSUI Indemnity Company	NHD953159
\$35M x \$25M	26.43%	\$9,250,000	Starr Insurance Companies	25SLCFM1225810
\$35M x \$25M	17.29%	\$6,050,000	Kinsale Insurance Company	0100381530-0
\$35M x \$25M	17.00%	\$5,950,000	StarStone Specialty Insurance Company	CSP00143920P-0
\$35M x \$25M	14.29%	\$5,000,000	SRU - Various	CMS-250169 IND-250169 BRA-250169 SSC0005597 42-AIP-000135-0 GOT-250169
\$35M x \$25M	10.00%	\$3,500,000	Lloyds Fidelis	B1230AP06336C2
\$40M x \$60M	15.00%	\$6,000,000	Starr Insurance Companies	25SLCFM1225810
\$40M x \$60M	12.50%	\$5,000,000	StarStone Specialty Insurance Company	CSP00143921P-0
\$40M x \$60M	15.50%	\$6,200,000	Trisura Specialty Insurance Company	TR25-25-XSP-085
\$40M x \$60M	20.00%	\$8,000,000	Nautilus Insurance Company / WR Berkley Corp	ZB936K25A000
\$40M x \$60M	37.00%	\$14,800,000	Lloyds Fidelis	B1230AP06336D2
\$15M x \$100M	100.00%	\$15,000,000	Homeland Insurance Company of NY	795030309
Boiler	100.00%	\$100,000,000	National Fire Insurance of Hartford	7034127151
Terrorism	100.00%	\$60,000,000	Liberty Surplus Insurance Corporation	5N523600001

APPLICATION AND CERTIFICATE FOR PAYMENT

TO(OWNER):	Elizabethtown Independent District Board of Education	PROJECT	T K Stone Middle School Renovation Elizabethtown, KY		NO: 5 DM: 10/1/2025 TO: 10/30/2025
ATTENTION:	Paul Mullins	CONTRACT FOR	Miscellaneous Specialties	CONTRACT DATE: 22-Jan-	-25 ALLIANCE
		BID DIV	100		Builders & Managers
CONTRACTOR	S APPLICATION FOR PAYMENT			Application is made for Payment as shown below in connection	1
CHANGE ORDE		-		with the Contract Continuation Sheet attached. The present status of the this Contract is as follows:	
Change Orders previous months		S DEDUCTIONS	3	ORIGINAL CONTRACT SUM	\$42,263.00
TOTAL				Net change by Change Orders	\$0.00
Approved this m	nonth			CONTRACT SUM TO DATE	\$42,263.00
				TOTAL COMPLETED & STORED TO DATE (Sheet 2)	\$1,141.27
				RETAINAGE @ 10%	\$114.13
				TOTAL EARNED LESS RETAINAGE	\$1,027.14
				LESS PREVIOUS CERTIFICATES (CONTRACT ONLY)	\$1,027.14
Net Change by 0	Change Orders \$0.00	\$0.00	\$0.00	CURRENT PAYMENT DUE	\$0.00
information and has been comple amounts have be Payment were is payment shown	d contractor certifies that to the best of his belief the Work covered by this Application eted and in accordance with the Contract een paid by him for Work for which previous assued and payments received from the Online	on for Payment Documents, that all ous Certificates for	nt	State of: Notary Public: My Commission expires 9/4/20	October, 2025 County of: D29 County of:
By:	The Atlas Companies	Date:	_ _10/23/2025	By:	Date: 11/10/25
ARCHITECT'S	CERTIFICATE FOR PAYMENT			CM APPROVAL: ALLIANCE CORPORATION	11/5/202
the above applic	with the Contract Documents, based on or cation, the Architect certifies to the Owner that to the best of his knowledge, informa	that the Work has p	rogressed to the	By: Dalton Jackson This certificate is not negotiable. The AMOUNT CERTIFIED is	Date: 11/5/202

to the contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or contractor under this Contract.

Brad Hollenkamp
Notary Public
State at Large, Kentucky
My Commission Expires on 9/4/29

the AMOUNT CERTIFIED.

Work is in accordance with the Contract Documents and the Contractor is entitled to payment of

CC	NTINUATION SHEET NO. 2 APPLICATION NO. <u>5</u>	T K STONE MIDDLE SCHOOL RENO	*D* WORK	*E* COMPLETED	*F*	*G* TOTAL	*H*	* *
ITEM #	DESCRIPTION OF WORK	SCHEDULED VALUE	FROM PREV APPLIC (D+E)	THIS PERIOD	MATERIALS STORED (NOT IN D OR E)	COMPLETED & STORED D+E+F	% G/C	BALANCE TO FINISH C-G
1 2 3	Building Area A Installation	\$12,602.11			-	\$0.00 \$0.00 \$0.00	0%	\$0.00 \$12,602.11 \$0.00
4 5 6	Building Area B Installation	\$14,589.38				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$14,589.38 \$0.00
7 8 9	Building Area C Installation	\$8,632.43				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$8,632.43 \$0.00
10 11 12	Building Area D Installation	\$301.70				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$301.70 \$0.00
13 14 15	Building Area E Installation	\$75.42				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$75.42 \$0.00
16 17 18	Building Area F Installation	\$75.42				\$0.00 \$0.00 \$0.00	0%	\$0.00 \$75.42 \$0.00
19 20 21	Bond Submittals Cleanup	\$1,141.27 \$422.63 \$422.63	\$1,141.27			\$1,141.27 \$0.00 \$0.00	100% 0% 0%	\$0.00 \$422.63 \$422.63
	O&M Manuals Closeout Documents	\$3,000.00 \$1,000.00				\$0.00 \$0.00	0% 0%	\$3,000.00 \$1,000.00
26 27 28 29								
30 31 32 33								
34 35 36								
37 38 39 40								
	TOTALS	\$42,263.00 \$0	.00 \$1,141.27	\$0.00	\$0.00	\$1,141.27	3%	\$41,121.73

		INUATION SHEET NO. 3 T K STONE MIDDLE SCHOOL RENO APPLICATION NO. 5 *D* *E*				OWNER PURCHASE ORDERS ONLY *F* *G* *H*			
ITEM #	DESCRIPTION	SUPPLIER	P.O. AMOUNT	PREVIOUS PAYMENTS	INVOICES DUE THIS MONTH (ATTACHED)	TOTAL TO DATE (E +F)	BALANCE TO FINISH (D - G)		
	Building Area A								
2	101101 Visual Display Boards	Atlas Enterprises	\$5,818.39	\$5,818.39		\$5,818.39	\$0.00		
3	101424 Signs	Atlas Enterprises	\$15,817 . 27			\$0.00	\$15,817.27		
4	101550 Toilet Compartments	Atlas Enterprises	\$5,359.31			\$0.00	\$5,359.31		
5	102601 Wall Protection	Atlas Enterprises	\$4,625.56	\$4,625.56		\$4,625.56	\$0.00		
6	102800 Toilet Accessories	Atlas Enterprises	\$2,083.28	\$1,710.00	\$373.28	\$2,083.28	\$0.00		
7	104400 Fire Protection	Atlas Enterprises	\$284.81	\$284.81		\$284.81	\$0.00		
8	105723 Closet and Utility Shelvi	nç Atlas Enterprises	\$312.27		\$312.27	\$312.27	\$0.00		
9									
10	Building Area B								
11	101101 Visual Display Boards	Atlas Enterprises	\$16,000.58	\$16,000.58		\$16,000.58	\$0.00		
12	101424 Signs	Atlas Enterprises	\$7,029.90			\$0.00	\$7,029.90		
13	101550 Toilet Compartments	Atlas Enterprises	\$12,058.43			\$0.00	\$12,058.43		
14	102601 Wall Protection	Atlas Enterprises	\$308.37			\$0.00	\$308.37		
15	102800 Toilet Accessories	Atlas Enterprises	\$4,687.38	\$3,847.50	\$839.88	\$4,687.38	\$0.00		
16	104400 Fire Protection	Atlas Enterprises	\$854.42	\$854.42		\$854.42	\$0.00		
17									
18	Building Area C								
19	101101 Visual Display Boards	Atlas Enterprises	\$7,273.00	\$7,273.00		\$7,273.00	\$0.00		
20	101424 Signs	Atlas Enterprises	\$5,272.42			\$0.00	\$5,272.42		
21		Atlas Enterprises	\$9,378.78			\$0.00	\$9,378.78		
22	102601 Wall Protection	Atlas Enterprises	\$1,233.47	\$939.44		\$939.44	\$294.03		
23	102260 Operable Wall	Atlas Enterprises	\$33,585.73			\$0.00	\$33,585.73		
24	102800 Toilet Accessories	Atlas Enterprises	\$3,645.74	\$2,992.50	\$653.24	\$3,645.74	\$0.00		
25									
26	Building Area D								
27	101424 Signs	Atlas Enterprises	\$3,514.94			\$0.00	\$3,514.94		
28									
29	Building Area E								
30	101424 Signs	Atlas Enterprises	\$1,757.47			\$0.00	\$1,757.47		
31									
32	Building Area F								
33	101424 Signs	Atlas Enterprises	\$1,757.48			\$0.00	\$1,757.48		
34									
35									
36									
37									
38									
39									
40									
	TOTALS		\$142,659.00	\$44,346.20	\$2,178.67	\$46,524.87	\$96,134.13		

INVOICE

Atlas Enterprises

5101 Commerce Crossings Drive Louisville, KY 40229

Invoice Date: 9/29/2025 Invoice #: 1226106

Due Date: 9/29/2025

Purchase Order #: 15-63898

Elizabethtown Independent Schools c/o 116 East College Street Glasgow, KY 42141

Customer #: EL0010

Contract ID: KY-25-00603 Billing: Varies

TK Stone Middle School

	DESCRIPTION	LABOR	MATERIAL	TOTAL
02-10-8000	Div 10 Miscellaneous	0.00	312.27	312.27
	Total Amount Billed	0.00	312.27	312.27
	Amount due this Invoice		-	312.27

INVOICE

Atlas Enterprises

5101 Commerce Crossings Drive Louisville, KY 40229

Invoice Date: 9/29/2025 Invoice #: 1226105

Due Date: 9/29/2025

Purchase Order #: 15-63898

Elizabethtown Independent Schools c/o 116 East College Street Glasgow, KY 42141

Customer #: EL0010


Contract ID: KY-25-00603 Billing: Varies

TK Stone Middle School

	DESCRIPTION	LABOR	MATERIAL	TOTAL
02-10-2800	Toilet Accessories	0.00	1,866.40	1,866.40
	Total Amount Billed	0.00	1,866.40	1,866.40
	Amount due this Invoice			1,866.40





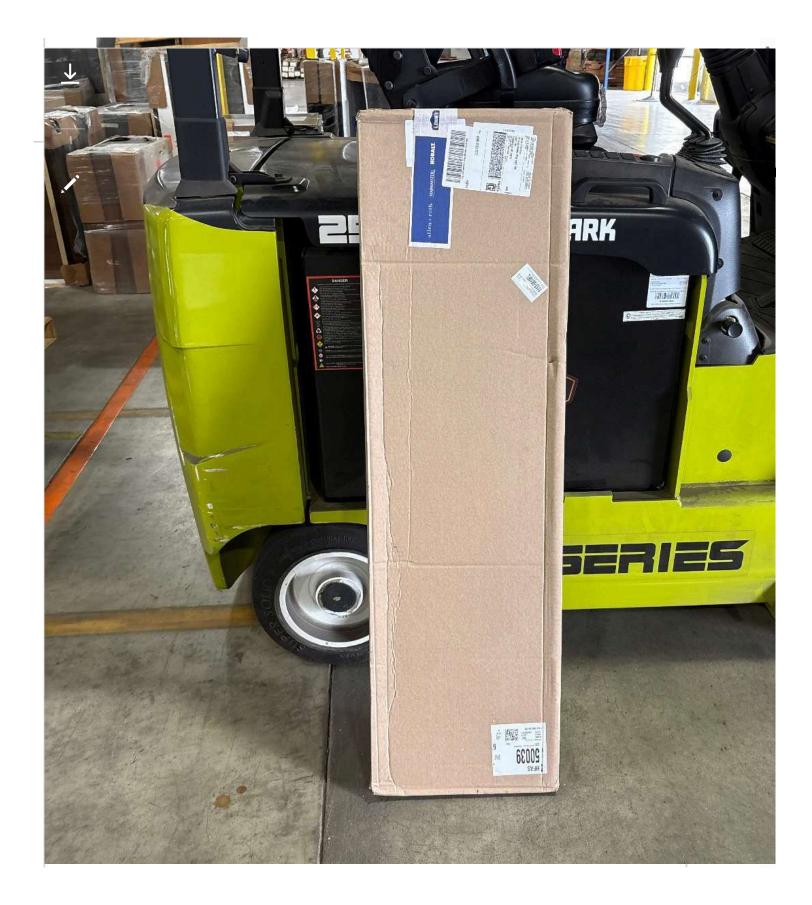

Client#: 1411671 64ATLASMET

ACORD...

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY) 10/23/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer any rights to the certificate holder in lieu of such endorsement(s).

and to mind the control of the contr	• • • • • • • • • • • • • • • • • • • •					
PRODUCER	CONTACT NAME:					
McGriff, a MMA LLC Company	PHONE (A/C, No, Ext): 502 489-5900 FAX (A/C, No): 866881					
2600 Eastpoint Parkway	E-MAIL ADDRESS: LouisvilleCL1@McGriff.com					
Louisville, KY 40223	INSURER(S) AFFORDING COVERAGE					
502 489-5900	INSURER A: FCCI Insurance Company					
INSURED	INSURER B : ClearPath Insurance Company	16273				
Atlas Metal Products Co Inc	INSURER C: The Cincinnati Insurance Company	10677				
5101 Commerce Crossings Drive	INSURER D:					
Louisville, KY 40229-2100	INSURER E:					
	INSURER F:					

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

	CCLUSIONS AND CONDITIONS OF SUCH					ivio.	
INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	S
Α	X COMMERCIAL GENERAL LIABILITY		CPP10010208500	06/01/2025	06/01/2026	EACH OCCURRENCE	\$1,000,000
	CLAIMS-MADE X OCCUR					DAMAGE TO RENTED PREMISES (Ea occurrence)	\$100,000
						MED EXP (Any one person)	\$5,000
						PERSONAL & ADV INJURY	\$1,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:					GENERAL AGGREGATE	\$2,000,000
	POLICY PRO- JECT LOC					PRODUCTS - COMP/OP AGG	\$2,000,000
	OTHER:						\$
Α	AUTOMOBILE LIABILITY		CA10000292310	06/01/2025	06/01/2026	COMBINED SINGLE LIMIT (Ea accident)	\$1,000,000
	X ANY AUTO					BODILY INJURY (Per person)	\$
	OWNED SCHEDULED AUTOS					BODILY INJURY (Per accident)	\$
	X HIRED AUTOS ONLY X NON-OWNED AUTOS ONLY					PROPERTY DAMAGE (Per accident)	\$
							\$
Α	X UMBRELLA LIAB X OCCUR		UMB10007771403	06/01/2025	06/01/2026	EACH OCCURRENCE	\$5,000,000
	EXCESS LIAB CLAIMS-MADE					AGGREGATE	\$5,000,000
	DED X RETENTION \$10000						\$
В	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY		WC11019671	06/01/2025	06/01/2026	X PER STATUTE OTH-	
	ANY PROPRIETOR/PARTNER/EXECUTIVE	N/A				E.L. EACH ACCIDENT	\$2,000,000
	(Mandatory in NH)	13/ A				E.L. DISEASE - EA EMPLOYEE	\$2,000,000
	If yes, describe under DESCRIPTION OF OPERATIONS below					E.L. DISEASE - POLICY LIMIT	\$2,000,000
С	C XS over \$5M Umb		EXS0654863	06/01/2025	06/01/2026	\$4,000,000	
Α	Leased/Rent Equi		CPP10010208500	06/01/2025	06/01/2026	\$250,000 Lim;\$1,000) Ded
_							

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
RE: Job #KY-25-00601, TK Stone Middle School - Toilet Accessories , Amount: \$1,866.40 , Stored Location: 7715 National Turnpike, Louisville, KY 40214.

CERTIFICATE HOLDER	
--------------------	--

Elizabethtown Independent Schools %116 East College Street Glasgow, KY 42141

CANCELLATION

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

BHU

© 1988-2015 ACORD CORPORATION. All rights reserved.



Client#: 1411671 64ATLASMET

$ACORD_{\scriptscriptstyle{\mathbb{M}}}$

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY) 10/23/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer any rights to the certificate holder in lieu of such endorsement(s).

and continuate account control any rights to the continuate holder in hear	· cacir criaci comert(c)					
PRODUCER	CONTACT NAME:					
McGriff, a MMA LLC Company	PHONE (A/C, No, Ext): 502 489-5900 FAX (A/C, No): 860					
2600 Eastpoint Parkway	E-MAIL ADDRESS: LouisvilleCL1@McGriff.com					
Louisville, KY 40223	INSURER(S) AFFORDING COVERAGE					
502 489-5900	INSURER A: National Trust Insurance Company	AGE NAIC # 20141 10178				
INSURED	INSURER B : FCCI Insurance Company	10178				
LR Construction Inc.	INSURER C : ClearPath Insurance Company	16273				
dba Atlas Metals	INSURER D: The Cincinnati Insurance Company					
5101 Commerce Crossings Drive	INSURER E:					
Louisville, KY 40229-2100	INSURER F:					

COVERAGES CERTIFICATE NUMBER: REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL SUBR		POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	s
Α	X COMMERCIAL GENERAL LIABILITY		CPP10004709306	06/01/2025	06/01/2026		\$1,000,000
	CLAIMS-MADE X OCCUR					DAMAGE TO RENTED PREMISES (Ea occurrence)	\$100,000
						MED EXP (Any one person)	\$5,000
						PERSONAL & ADV INJURY	\$1,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:					GENERAL AGGREGATE	\$2,000,000
	POLICY PRO- LOC					PRODUCTS - COMP/OP AGG	\$2,000,000
	OTHER:						\$
В	AUTOMOBILE LIABILITY		CA10000292309	06/01/2025	06/01/2026	COMBINED SINGLE LIMIT (Ea accident)	\$1,000,000
	X ANY AUTO					BODILY INJURY (Per person)	\$
	OWNED SCHEDULED AUTOS					BODILY INJURY (Per accident)	\$
	X HIRED AUTOS ONLY X NON-OWNED AUTOS ONLY					PROPERTY DAMAGE (Per accident)	\$
							\$
В	X UMBRELLA LIAB X OCCUR		UMB10007771402	06/01/2025	06/01/2026	EACH OCCURRENCE	\$5,000,000
	EXCESS LIAB CLAIMS-MADE					AGGREGATE	\$5,000,000
	DED X RETENTION \$10000						\$
С	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY		WC11019671	06/01/2025	06/01/2026	X PER STATUTE OTH-	
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED?	N/A				E.L. EACH ACCIDENT	\$2,000,000
	(Mandatory in NH)	N/ A				E.L. DISEASE - EA EMPLOYEE	\$2,000,000
	If yes, describe under DESCRIPTION OF OPERATIONS below					E.L. DISEASE - POLICY LIMIT	\$2,000,000
D	D XS over \$5M Umb		EXS0654863	06/01/2025	06/01/2026	\$4,000,000	
Α	A Leased/Rent Equip		CPP10004709306	06/01/2025	06/01/2026	\$250,000 Lim;\$1,000) De

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)
RE: Job #KY-25-00603, TK Stone Middle School, Closet and Utility Shelving Amount: \$312.27 Stored Location:
7715 National Turnpike, Louisville, KY 40214.

Elizabethtown Independent Schools %116 East College Street Glasgow, KY 42141 SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

CANCELLATION

BHU

© 1988-2015 ACORD CORPORATION. All rights reserved.

CERTIFICATE HOLDER



the AMOUNT CERTIFIED.

APPLICATION AND CERTIFICATE FOR PAYMENT

Work is in accordance with the Contract Documents and the Contractor is entitled to payment of

TO(OWNER):	Elizabethtown Ind Schools 219 Helm St Elizabethtown, KY 42701	PROJECT:	TK Stone Elizabethtown, KY 42701		APPLICATION NO: PERIOD FROM: TO:	7 10/01/25 10/31/25	A
CONTRACTOR	Lusk Mechanical Contractors, Inc 820 S Dixie Hwy	CONTRACT FOR:	Mechanical HVAC and Plumbing	CONTRACT DATE			ALLIANCE
	Muldraugh, KY 40155	BID DIV:	220	JOB#	BP22		выповен в менераго
CONTRACTORS	APPLICATION FOR PAYMENT	***************************************		Application is made for Payment as show			***************************************
CHANGE ORDER				with the Contract Continuation Sheet atta The present status of the this Contract is			
Change Orders a previous months		DEDUCTIONS		ORIGINAL CONTRACT SUM			\$3,173,520.40
TOTAL				Net change by Change Orders			\$0.00
Approved this month				CONTRACT SUM TO DATE			\$3,173,520.40
				TOTAL COMPLETED & STORED TO DA	ATE (Sheet 2)		\$1,126,027.03
				RETAINAGE @ 10%			\$112,602.70
				TOTAL EARNED LESS RETAINAGE			\$1,013,424.33
				LESS PREVIOUS CERTIFICATES (CON	TRACT ONLY)	***************************************	\$914,796.25
Net Change by C	hange Orders \$0.00	\$0.00	\$0.00	CURRENT PAYMENT DUE			\$98,628.08
information and b has been comple amounts have be Payment were iss	contractor certifies that to the best of his is belief the Work covered by this Application ted and in accordance with the Contract Dien paid by him for Work for which previous sued and payments received from the Ownerein is now due.	for Payment ocuments, that all is Certificates for	t	Subscribed and sworn to before me this State of: Notary Public Out Confidence of My Commission expires:	day of	County of:	Meade
By: STATE	di 8 suse	Date:_[6	121/25	ARCHITECT'S CERTIFICATION: By:	Kler		Date:11/10/25
In accordance with the above applica	ERTIFICATE FOR PAYMENT th the Contract Documents, based on on- ation, the Architect certifies to the Owner to hat to the best of his knowledge, information	hat the Work has pr	ogressed to the	Dalton Jackson This certificate is not negotiable. The AN		able only	11/5/202 Date:

This certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or contractor under this Contract.





37

AIA Document G703TM - 1992

Continuation Sheet

AIA Document, G702[™] -1992, Application and Certification for Payment, or G736[™]-2009, Project Application and Project Certificate for Payment, Construction Manager as Adviser Edition, containing Contractor's signed certification is attached. In tabulations below, amounts are in US dollars. APPLICATION NUMBER: APPLICATION DATE: 10/20/2025

10/31/2025 PERIOD TO: djackson@alliancecorporation.com Use Column I on Contracts where variable retainage for line items may apply ARCHITECT'S PROJECT NO: TOTAL BALANCE WORK COMPLETED WORK COMPLETED MATERIALS DESCRIPTION OF WORK SCHEDULED RETAINAGE ITEM TO FINISH PRESENTLY COMPLETED (G/C) FROM PREVIOUS THIS PERIOD Job: TK Stone Middle School VALUE NO. (% of G) (C-G) AND STORED STORED APPLICATION Customer: Etown Ind Schools (NOT IN TO DATE (D+E) **Customer PO#** (D+E+F) DORE) Lusk Job # M25-074 4.735.83 47,358.28 100% 47,358.28 \$ 47.358.28 \$ Bond cost. 3,173.50 31,735.00 100% 31,735.00 \$ 31,735.00 \$ Submittals/ shop drawings (1% of contract) 23,801.25 \$ 793.38 5 25% 1,586.75 \$ 7,933.75 31.735.00 \$ 6,347.00 \$ Clean up (1% of contract) 0% 3,000.00 \$ S 3,000.00 \$ - \$ \$ O&M Manuals \$3,000 0% 1,000.00 \$ \$ 1,000.00 \$ Closeouts & Warranties \$1,000 17,250.00 5 57,500.00 \$ 172,500.00 75% 138.000.00 \$ 34,500.00 \$ \$ 230,000.00 \$ 122,500.00 \$ 6 Area A Material 36,750.00 367,500.00 75% S 73,500.00 \$ 294,000.00 \$ 490.000.00 \$ Area A Labor 92.000.00 \$ 13,800.00 \$ 138,000.00 60% \$ \$ 138,000.00 \$ 230,000.00 \$ Area B Material 8 27,000.00 180,000.00 \$ 270,000.00 60% \$ S 270,000.00 \$ 450.000.00 \$ Area B Labor 9 247.500.00 \$ 2,750.00 27,500.00 10% \$ \$ \$ 275,000.00 \$ 27,500.00 \$ Area C Material 405,000.00 \$ 4,500.00 10 \$ 45,000.00 10% S \$ 450,000.00 \$ 45,000,00 \$ Area C Labor 11 133.000.00 \$ 700.00 \$ \$ 7,000.00 5% 1 \$ 7,000.00 \$ 140,000.00 \$ Area D Material 1,150.00 12 218,500,00 \$ \$ \$ 11,500.00 5% 11,500.00 \$ 230.000.00 Area D Labor 13 112,000,00 \$ 0% \$ \$ 112.000.00 Area E Material 14 184,000.00 \$ 0% \$ \$ \$ 184.000.00 Area E Labor 15 \$ 107,692.13 \$ 0% \$ 107,692.13 Area F Material 16 160,000.00 \$ _ 0% \$ \$ 160,000.00 S Area F Labor 17 #DIV/0! 1\$ \$ \$ 18 \$ #DIV/0! \$ \$ \$ 19 #DIV/0! \$ 18 S 20 #DIV/0! \$ \$ 21 #DIV/0! \$ S 22 #DIV/0! \$ \$ S 23 #DIV/0! \$ \$ S 24 \$ #DIV/0! \$ \$ S 25 S #DIV/0! \$ \$ S 26 S #DIV/0! \$ \$ \$ 27 #DIV/0! \$ \$ \$ \$ 28 #DIV/0! 1 \$ \$ \$ 29 #DIV/0! \$ \$ \$ 30 #DIV/0! \$ \$ \$ 31 #DIV/0! \$ \$ \$ 32 #DIV/0! \$ \$ 33 #DIV/0! \$ \$ 34 #DIV/0! S 35 #DIV/0! \$ \$2,047,493.38 \$112,602.70 36 \$0.00 \$1,126,027.03 35% 3,173,520.41 \$ 1,016,440.28 \$109,586.75

AIA Document G703** - 1992. Copyright © 1963, 1965, 1966, 1967, 1970, 1983, and 1992 by The American Institute of Architects. All rights reserved. WARNING: This AIA * Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA* Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law.

	CONTINUATION SHEET NO. 3 APPLICATION NO.		TK Stone 7 *D*	*E*	*F* INVOICES DUE	ASE ORDERS *G* TOTAL	*H* BALANCE TO	
ITEM #	DESCRIPTION	SUPPLIER	P.O. AMOUNT	PREVIOUS PAYMENTS	THIS MONTH (ATTACHED)	TO DATE (E +F)	FINISH (D - G)	
2			\$18,100.00 \$196,375.00 \$56,722.59 \$1,291,110.00	\$2,100.00 \$1,045.20 \$774,510.09	\$0.00	\$2,100.00 \$0.00 \$1,045.20 \$774,510.09 \$0.00	\$16,000.00 \$196,375.00 \$55,677.39 \$516,599.91 \$0.00	
7 8 9 10								
11 12 13 14								
15 16 17								
18 19 20 21 22	9 0 1 2							
23 24 25 26 27	4 5 6 7							
28 29 30	9					4,000,000,000,000,000,000		
	TOTALS		\$1,562,307.59	\$777,655.29	9 \$0.00	\$777,655.29	\$784,652.30	

POWERING THE FUTURE!

PO Box 36503 Louisville, KY 40233-6503 3312 Gilmore Industrial Blvd., Louisville, KY 40213

10/27/25

ALLIANCE CORPORATION 116 E. COLLEGE STREET GLASGOW, KY 42141

EMAIL: djackson@alliancecorporation.com awilson@alliancecorporation.com INVOICE #: SUBCONTRACT #: AES JOB #: 250150-October BG #20--Electrical

250150

PROJECT DESCRIPTION:

Alliance Corporation - TK Stone Middle School - PA 07 October 2025

TOTAL AMOUNT NOW DUE:

\$207,225.00

PLEASE REMIT TO: ADVANCED ELECTRICAL SYSTEMS, INC. PO BOX 36503 LOUISVILLE, KY 40233-6503

TERMS: DUE UPON RECEIPT. IF YOU WOULD LIKE TO PAY BY CREDIT CARD PLEASE CONTACT BILLING DEPARTMENT AT: 502-962-1102. AFTER 30 DAYS A 1 ½% SERVICE CHARGE WILL APPLY.

APPLICATION AND CERTIFICATE FOR PAYMENT

PROJECT: T K Stone Middle School Renovation TO(OWNER): Elizabethtown Independent District Elizabethtown, KY Board of Education CONTRACT FOR: BP 20 Electrical ATTENTION: **Paul Mullins BP 20** BID DIV: CONTRACTORS APPLICATION FOR PAYMENT CHANGE ORDER SUMMARY Change Orders approved in ADDITIONS **DEDUCTIONS** previous months by Owner TOTAL Approved this month \$0.00 \$0.00 \$0.00 Net Change by Change Orders The undersigned contractor certifies that to the best of his knowledge, information and belief the Work covered by this Application for Payment has been completed and in accordance with the Contract Documents, that all amounts have been paid by him for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due. CONTRACTOR: Advanced Electrical Systems Lea M Santal Date: 10/27/2025

APPLICATION NO: 7 PERIOD FROM: 10/1/2025

22-Jan-25

TO: 10/31/2025



Application is made for Payment as shown below in connection with the Contract Continuation Sheet attached. The present status of the this Contract is as follows:

CONTRACT DATE:

ORIGINAL CONTRACT SUM \$4,683,548.17 \$0.00 Net change by Change Orders \$4,683,548,17 CONTRACT SUM TO DATE TOTAL COMPLETED & STORED TO DATE (Sheet 2) ... \$1,198,250.00 \$119,825.00 RETAINAGE @ 10% \$1,078,425.00 TOTAL EARNED LESS RETAINAGE LESS PREVIOUS CERTIFICATES (CONTRACT ONLY) \$871,200.00 \$207,225.00 **CURRENT PAYMENT DUE**

Subscribed and sworn to before me this 27th day of October 2025

State of: Kentucky,

Notary Public: My Commission exp County of: Jefferson

County of: Jefferson

CM APPROVAL: ALLIANCE CORPORATION

Dalton Jackson

11/5/2025

This certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or contractor under this Contract.

ARCHITECT'S CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on on-site observation and the data comprising the above application, the Architect certifies to the Owner that the Work has progressed to the point indicated: that to the best of his knowledge, information and belief, the quality of the Work is in accordance with the Contract Documents and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

Page 2 of 10

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive

Elizabethtown KY 42701

PROJECT: Alliance Corp-TK Stone 323 Morningside Drive

APPLICATION NO: 7

DISTRIBUTION TO:

Elizabethtown KY 42701

PERIOD TO: 10/31/2025

OWNER CONSTRUCTION MANAGER

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503

3312 Gilmore Industrial Blvd Louisville, KY 40233

ARCHITECT'S

PROJECT NO: AES Job #250150

_ARCHITECT CONTRACTOR

VIA CONSTRUCTION MANAGER:

CONTRACT FOR: BP 20 Electrical

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
1	Permitting	120,000.00	120,000.00	0.00	0.00	120,000.00	100.00	0.00	12,000.00
2	Mobilization	75,000.00	75,000.00	0.00	0.00	75,000.00	100.00	0.00	7,500.00
3	Electrical Shop Drawings & Submittals	25,000.00	25,000.00	0.00	0.00	25,000.00	100.00	0.00	2,500.00
4	Bond	90,000.00	90,000.00	0.00	0.00	90,000.00	100.00	0.00	9,000.00
5	Temporary	125,000.00	50,000.00	12,500.00	0.00	62,500.00	50.00	62,500.00	6,250.00
6	Excavation	80,000.00	0.00	8,000.00	0.00	8,000.00	10.00	72,000.00	800.00
7	Site Lighting - Labor	50,000.00	0.00	2,500.00	0.00	2,500.00	5.00	47,500.00	250.00
8	Lighting Controls Startup	2,500.00	0.00	250.00	0.00	250.00	10.00	2,250.00	25.00
9	Owner Training & Acceptance	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
10	As-Built / Record Drawings & Acceptance	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
11	O&M Manuals & Acceptance	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
12	Warranties	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
13	Demobilization	10,000.00	0.00	0.00	0.00	0.00	0.00	10,000.00	0.00
14	Area A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15	Lighting - Labor	35,000.00	14,000.00	3,500.00	0.00	17,500.00	50.00	17,500.00	1,750.00
16	Lighting Controls - Labor	15,000.00	6,000.00	1,500.00	0.00	7,500.00	50.00	7,500.00	750.00
17	Electrical Distribution - Switchgear - Labor	25,000.00	0.00	12,500.00	0.00	12,500.00	50.00	12,500.00	1,250.00
18	Electrical Distribution - Panelboards - Labor	75,000.00	30,000.00	7,500.00	0.00	37,500.00	50.00	37,500.00	3,750.00
19	Feeders Wire - Labor	95,000.00	0.00	47,500.00	0.00	47,500.00	50.00	47,500.00	4,750.00
20	Feeder Conduit - Labor	145,000.00	58,000.00	14,500.00	0.00	72,500.00	50.00	72,500.00	7,250.00

AIA Type Document Application and Certification for Payment

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive Elizabethtown KY 42701 PROJECT: Alliance Corp-TK Stone 323 Morningside Drive Elizabethtown KY 42701 APPLICATION NO: 7

PERIOD TO: 10/31/2025

DISTRIBUTION TO: OWNER CONSTRUCTION MANAGER

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503 3312 Gilmore Industrial Blvd ARCHITECT'S

PROJECT NO: AES Job #250150

_ARCHITECT _ CONTRACTOR

Louisville, KY 40233

CONTRACT FOR: BP 20 Electrical

VIA ARCHITECT: Ross Tarrant Architects

VIA CONSTRUCTION MANAGER:

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
21	Boxes Whips and support - labor	35,000.00	14,000.00	3,500.00	0.00	17,500.00	50.00	17,500.00	1,750.00
22	Raceways Normal Power - Labor	115,000.00	46,000.00	11,500.00	0.00	57,500.00	50.00	57,500.00	5,750.00
23	Raceways Fire Alarm - Material	60,000.00	24,000.00	36,000.00	0.00	60,000.00	100.00	0.00	6,000.00
24	Raceways Fire Alarm - Labor	60,000.00	24,000.00	6,000.00	0.00	30,000.00	50.00	30,000.00	3,000.00
25	Raceways Data/Voice - Material	7,500.00	3,000.00	750.00	0.00	3,750.00	50.00	3,750.00	375.00
26	Raceways Data/Voice - Labor	7,500.00	3,000.00	750.00	0.00	3,750.00	50.00	3,750.00	375.00
27	Raceways Security - Material	15,000.00	6,000.00	1,500.00	0.00	7,500.00	50.00	7,500.00	750.00
28	Raceways Security - Labor	5,000.00	2,000.00	500.00	0.00	2,500.00	50.00	2,500.00	250.00
29	Raceways Intercom - Material	60,000.00	24,000.00	6,000.00	0.00	30,000.00	50.00	30,000.00	3,000.00
30	Raceways Intercom - Labor	50,000.00	20,000.00	5,000.00	0.00	25,000.00	50.00	25,000.00	2,500.00
31	Branch Circuiting - Material	75,000.00	30,000.00	7,500.00	0.00	37,500.00	50.00	37,500.00	3,750.00
32	Branch Circuiting - Labor	85,000.00	34,000.00	8,500.00	0.00	42,500.00	50.00	42,500.00	4,250.00
33	Access Control Labor	10,000.00	4,000.00	1,000.00	0.00	5,000.00	50.00	5,000.00	500.00
34	Emergency Alert Labor	5,000.00	0.00	2,500.00	0.00	2,500.00	50.00	2,500.00	250.00
35	Electrical Devices - Material	10,000.00	4,000.00	1,000.00	0.00	5,000.00	50.00	5,000.00	500.00
36	Electrical Devices - Labor	10,000.00	4,000.00	1,000.00	0.00	5,000.00	50.00	5,000.00	500.00
37	Cabletrays - Labor	20,000.00	8,000.00	2,000.00	0.00	10,000.00	50.00	10,000.00	1,000.00
38	Fire Alarm System - Labor	20,000.00	0.00	10,000.00	0.00	10,000.00	50.00	10,000.00	1,000.00
39	Low Voltage Data/Voice Cabling - Labor	15,000.00	0.00	7,500.00	0.00	7,500.00	50.00	7,500.00	750.00
40	Intercom Labor	15,000.00	0.00	7,500.00	0.00	7,500.00	50.00	7,500.00	750.00
41	Area B	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00

AIA Type Document Application and Certification for Payment

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive Elizabethtown KY 42701

CONTRACT FOR: BP 20 Electrical

PROJECT: Alliance Corp-TK Stone 323 Morningside Drive Elizabethtown KY 42701

APPLICATION NO: 7 PERIOD TO: 10/31/2025

TO: OWNER CONSTRUCTION

DISTRIBUTION

FROM (CONTRACTOR): Advanced Electrical Systems Inc

ARCHITECT'S

PROJECT NO: AES Job #250150

MANAGER ARCHITECT CONTRACTOR

PO Box 36503

3312 Gilmore Industrial Blvd Louisville, KY 40233

VIA CONSTRUCTION MANAGER:

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
2	Lighting - Labor	35,000.00	15,000.00	0.00	0.00	15,000.00	42.86	20,000.00	1,500.00
3	Lighting Controls - Labor	15,000.00	5,000.00	0.00	0.00	5,000.00	33.33	10,000.00	500.00
4	Electrical Distribution - Switchgear - Labor	25,000.00	5,000.00	0.00	0.00	5,000.00	20.00	20,000.00	500.00
5	Electrical Distribution - Panelboards - Labor	65,000.00	10,000.00	0.00	0.00	10,000.00	15.38	55,000.00	1,000.00
6	Feeders Wire - Labor	75,000.00	0.00	0.00	0.00	0.00	0.00	75,000.00	0.00
7	Feeder Conduit - Labor	75,000.00	15,000.00	0.00	0.00	15,000.00	20.00	60,000.00	1,500.00
8	Boxes Whips and support - labor	15,000.00	7,500.00	0.00	0.00	7,500.00	50.00	7,500.00	750.00
9	Raceways Normal Power - Labor	85,000.00	40,000.00	0.00	0.00	40,000.00	47.06	45,000.00	4,000.00
60	Raceways Fire Alarm - Material	20,000.00	5,000.00	0.00	0.00	5,000.00	25.00	15,000.00	500.00
31	Raceways Fire Alarm - Labor	20,000.00	5,000.00	0.00	0.00	5,000.00	25.00	15,000.00	500.00
2	Raceways Data/Voice - Material	7,500.00	2,000.00	0.00	0.00	2,000.00	26.67	5,500.00	200.00
3	Raceways Data/Voice - Labor	7,500.00	2,000.00	0.00	0.00	2,000.00	26.67	5,500.00	200.00
4	Raceways Security - Material	15,000.00	3,000.00	0.00	0.00	3,000.00	20.00	12,000.00	300.00
5	Raceways Security - Labor	5,000.00	1,500.00	0.00	0.00	1,500.00	30.00	3,500.00	150.00
66	Raceways Intercom - Material	60,000.00	25,000.00	0.00	0.00	25,000.00	41.67	35,000.00	2,500.00
7	Raceways Intercom - Labor	50,000.00	20,000.00	0.00	0.00	20,000.00	40.00	30,000.00	2,000.00
8	Branch Circuiting - Material	75,000.00	25,000.00	0.00	0.00	25,000.00	33.33	50,000.00	2,500.00
9	Branch Circuiting - Labor	85,000.00	25,000.00	0.00	0.00	25,000.00	29.41	60,000.00	2,500.00
0	Access Control Labor	10,000.00	0.00	0.00	0.00	0.00	0.00	10,000.00	0.00
1	Emergency Alert Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
2	Electrical Devices - Material	10,000.00	2,000.00	0.00	0.00	2,000.00	20.00	8,000.00	200.00

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive Elizabethtown KY 42701

CONTRACT FOR: BP 20 Electrical

PROJECT: Alliance Corp-TK Stone 323 Morningside Drive

APPLICATION NO: 7

DISTRIBUTION TO:

Elizabethtown KY 42701

PERIOD TO: 10/31/2025

_ OWNER CONSTRUCTION MANAGER

FROM (CONTRACTOR): Advanced Electrical Systems Inc.

PO Box 36503

3312 Gilmore Industrial Blvd Louisville, KY 40233

ARCHITECT'S

PROJECT NO: AES Job #250150

ARCHITECT CONTRACTOR

VIA CONSTRUCTION MANAGER:

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
63	Electrical Devices - Labor	10,000.00	2,000.00	0.00	0.00	2,000.00	20.00	8,000.00	200.00
64	Cabletrays - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
35	Fire Alarm System - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
56	Low Voltage Data/Voice Cabling - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
67	Intercom Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
38	Area C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
69	Lighting - Labor	35,000.00	0.00	0.00	0.00	0.00	0.00	35,000.00	0.00
70	Lighting Controls - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
71	Electrical Distribution - Switchgear - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
72	Electrical Distribution - Panelboards - Labor	95,000.00	0.00	0.00	0.00	0.00	0.00	95,000.00	0.00
73	Feeders Wire - Labor	100,000.00	0.00	0.00	0.00	0.00	0.00	100,000.00	0.00
74	Feeder Conduit - Labor	145,000.00	35,000.00	0.00	0.00	35,000.00	24.14	110,000.00	3,500.00
75	Boxes Whips and support - labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
76	Raceways Normal Power - Labor	150,000.00	0.00	0.00	0.00	0.00	0.00	150,000.00	0.00
77	Raceways Fire Alarm - Material	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
78	Raceways Fire Alarm - Labor	45,000.00	0.00	0.00	0.00	0.00	0.00	45,000.00	0.00
79	Raceways Data/Voice - Material	7,500.00	0.00	0.00	0.00	0.00	0.00	7,500.00	0.00
30	Raceways Data/Voice - Labor	7,500.00	0.00	0.00	0.00	0.00	0.00	7,500.00	0.00
31	Raceways Security - Material	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
32	Raceways Security - Labor	5,000.00	0.00	0.00	0.00	0,00	0.00	5,000.00	0.00

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive

CONTRACT FOR: BP 20 Electrical

Elizabethtown KY 42701

PROJECT: Alliance Corp-TK Stone

323 Morningside Drive **PERIOD TO: 10/31/2025** Elizabethtown KY 42701

APPLICATION NO: 7

DISTRIBUTION TO:

OWNER CONSTRUCTION

ARCHITECT'S

PROJECT NO: AES Job #250150

MANAGER ARCHITECT

CONTRACTOR

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503

3312 Gilmore Industrial Blvd

Louisville, KY 40233

VIA CONSTRUCTION MANAGER:

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
83	Raceways Intercom - Material	60,000.00	0.00	0.00	0.00	0.00	0.00	60,000.00	0.00
84	Raceways Intercom - Labor	50,000.00	0.00	0.00	0.00	0.00	0.00	50,000.00	0.00
85	Branch Circuiting - Material	75,000.00	0.00	0.00	0.00	0.00	0.00	75,000.00	0.00
86	Branch Circuiting - Labor	85,000.00	0.00	0.00	0.00	0.00	0.00	85,000.00	0.00
87	Access Control Labor	10,000.00	0.00	0.00	0.00	0.00	0.00	10,000.00	0.00
88	Emergency Alert Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
89	Electrical Devices - Material	25,000.00	0.00	0.00	0.00	0.00	0.00	25,000.00	0.00
90	Electrical Devices - Labor	25,000.00	0.00	0.00	0.00	0.00	0.00	25,000.00	0.00
91	Cabletrays - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
92	Fire Alarm System - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
93	Low Voltage Data/Voice Cabling - Labor	65,000.00	0.00	0.00	0.00	0.00	0.00	65,000.00	0.00
94	Intercom Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
95	Area D	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
96	Lighting - Labor	35,000.00	0.00	0.00	0.00	0.00	0.00	35,000.00	0.00
97	Lighting Controls - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
98	Electrical Distribution - Switchgear - Labor	25,000.00	0.00	0.00	0.00	0.00	0.00	25,000.00	0.00
99	Electrical Distribution - Panelboards - Labor	25,000.00	0.00	0.00	0.00	0.00	0.00	25,000.00	0.00
100	Feeders Wire - Labor	50,000.00	0.00	0.00	0.00	0.00	0.00	50,000.00	0.00
101	Feeder Conduit - Labor	50,000.00	0.00	0.00	0.00	0.00	0.00	50,000.00	0.00
102	Boxes Whips and support - labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00

AIA Type Document Application and Certification for Payment

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive Elizabethtown KY 42701 PROJECT: Alliance Corp-TK Stone 323 Morningside Drive Elizabethtown KY 42701

APPLICATION NO: 7

PERIOD TO: 10/31/2025

DISTRIBUTION TO: _ OWNER

CONSTRUCTION
MANAGER
ARCHITECT

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503

3312 Gilmore Industrial Blvd Louisville, KY 40233 **ARCHITECT'S**

PROJECT NO: AES Job #250150

CONTRACTOR

VIA CONSTRUCTION MANAGER:

CONTRACT FOR: BP 20 Electrical

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
103	Raceways Normal Power - Labor	25,000.00	0.00	0.00	0.00	0.00	0.00	25,000.00	0.00
104	Raceways Fire Alarm - Material	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
105	Raceways Fire Alarm - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
106	Raceways Data/Voice - Material	7,500.00	0.00	0.00	0.00	0.00	0.00	7,500.00	0.00
107	Raceways Data/Voice - Labor	7,500.00	0.00	0.00	0.00	0.00	0.00	7,500.00	0.00
108	Raceways Security - Material	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
109	Raceways Security - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
110	Raceways Intercom - Material	60,000.00	0.00	0.00	0.00	0.00	0.00	60,000.00	0.00
111	Raceways Intercom - Labor	50,000.00	0.00	0.00	0.00	0.00	0.00	50,000.00	0.00
112	Branch Circuiting - Material	75,000.00	0 00	0.00	0.00	0.00	0.00	75,000.00	0.00
113	Branch Circuiting - Labor	85,000.00	0.00	0.00	0.00	0.00	0.00	85,000.00	0.00
114	Access Control Labor	10,000.00	0.00	0.00	0.00	0.00	0.00	10,000.00	0.00
115	Emergency Alert Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
116	Electrical Devices - Material	10,000.00	0.00	0.00	0.00	0.00	0.00	10,000.00	0.00
117	Electrical Devices - Labor	10,000.00	0.00	0.00	0.00	0.00	0.00	10,000.00	0.00
118	Cabletrays - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
119	Fire Alarm System - Labor	20,000.00	0.00	0.00	0.00	0.00	0.00	20,000.00	0.00
120	Low Voltage Data/Voice Cabling - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
121	Intercom Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
122	Area E	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
123	Lighting - Labor	35,000.00	0.00	0.00	0.00	0.00	0.00	35,000.00	0.00

AIA Type Document Application and Certification for Payment

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive Elizabethtown KY 42701 PROJECT: Alliance Corp-TK Stone 323 Morningside Drive Elizabethtown KY 42701

APPLICATION NO: 7

PERIOD TO: 10/31/2025

DISTRIBUTION
TO:
OWNER
CONSTRUCTION

MANAGER
_ARCHITECT

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503

3312 Gilmore Industrial Blvd Louisville, KY 40233 ARCHITECT'S

PROJECT NO: AES Job #250150

CONTRACTOR

VIA CONSTRUCTION MANAGER:

CONTRACT FOR: BP 20 Electrical

VIA ARCHITECT: Ross Tarrant Architects

	91	·	APPLICATIONS	THIS PERIOD	MATERIAL	STORED	%	BALANCE	RETAINAGE
124	Lighting Controls - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
125	Electrical Distribution - Switchgear - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
126	Electrical Distribution - Panelboards - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
127	Feeders Wire - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
128	Feeder Conduit - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
129	Boxes Whips and support - labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
130	Raceways Normal Power - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
131	Raceways Fire Alarm - Material	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
132	Raceways Fire Alarm - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
133	Raceways Data/Voice - Material	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
134	Raceways Data/Voice - Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
135	Raceways Security - Material	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
136	Raceways Security - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
137	Raceways Intercom - Material	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
138	Raceways Intercom - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
139	Branch Circuiting - Material	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
140	Branch Circuiting - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
141	Access Control Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
142	Emergency Alert Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
143	Electrical Devices - Material	2,500.00	0.00	0,00	0.00	0.00	0.00	2,500.00	0.00
144	Electrical Devices - Labor	2,500.00	0,00	0.00	0.00	0.00	0.00	2,500,00	0.00

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive

CONTRACT FOR: BP 20 Electrical

Elizabethtown KY 42701

PROJECT: Alliance Corp-TK Stone

323 Morningside Drive Elizabethtown KY 42701 **APPLICATION NO: 7**

PERIOD TO: 10/31/2025

DISTRIBUTION TO:

OWNER

CONSTRUCTION MANAGER ARCHITECT

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503

3312 Gilmore Industrial Blvd

Louisville, KY 40233

ARCHITECT'S

PROJECT NO: AES Job #250150

CONTRACTOR

VIA CONSTRUCTION MANAGER:

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	0/0	BALANCE	RETAINAGE
145	Cabletrays - Labor	1,500.00	0.00	0.00	0.00	0.00	0.00	1,500.00	0.00
146	Fire Alarm System - Labor	1,500.00	0.00	0.00	0.00	0.00	0.00	1,500.00	0.00
147	Low Voltage Data/Voice Cabling - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
148	Intercom Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
149	Gymnasium A/V & Cabling - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
150	Area F	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
151	Lighting - Labor	35,000.00	0.00	0.00	0.00	0.00	0.00	35,000.00	0.00
152	Lighting Controls - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
153	Electrical Distribution - Switchgear - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
154	Electrical Distribution - Panelboards - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
155	Feeders Wire - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
156	Feeder Conduit - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
157	Boxes Whips and support - labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
158	Raceways Normal Power - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
159	Raceways Fire Alarm - Material	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
160	Raceways Fire Alarm - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
161	Raceways Data/Voice - Material	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
162	Raceways Data/Voice - Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
163	Raceways Security - Material	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
164	Raceways Security - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00

AIA Type Document Application and Certification for Payment

TO (OWNER): Elizabethtown Ind BOE 323 Morningside Drive Elizabethtown KY 42701 PROJECT: Alliance Corp-TK Stone 323 Morningside Drive Elizabethtown KY 42701

APPLICATION NO: 7
PERIOD TO: 10/31/2025

DISTRIBUTION TO:

25

OWNER
CONSTRUCTION
MANAGER
ARCHITECT

FROM (CONTRACTOR): Advanced Electrical Systems Inc

PO Box 36503

3312 Gilmore Industrial Blvd Louisville, KY 40233 ARCHITECT'S

PROJECT NO: AES Job #250150

CONTRACTOR

VIA CONSTRUCTION MANAGER:

CONTRACT FOR: BP 20 Electrical

VIA ARCHITECT: Ross Tarrant Architects

ITEM	DESCRIPTION	SCHEDULE VALUE	PREVIOUS APPLICATIONS	COMPLETED THIS PERIOD	STORED MATERIAL	COMPLETED STORED	%	BALANCE	RETAINAGE
165	Raceways Intercom - Material	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
166	Raceways Intercom - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
167	Branch Circuiting - Material	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
168	Branch Circuiting - Labor	15,000.00	0.00	0.00	0.00	0.00	0.00	15,000.00	0.00
169	Access Control Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
170	Emergency Alert Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
171	Electrical Devices - Material	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
172	Electrical Devices - Labor	2,500.00	0.00	0.00	0.00	0.00	0.00	2,500.00	0.00
173	Cabletrays - Labor	1,500.00	0.00	0.00	0.00	0.00	0.00	1,500.00	0.00
174	Fire Alarm System - Labor	1,500.00	0.00	0.00	0.00	0.00	0.00	1,500.00	0.00
175	Low Voltage Data/Voice Cabling - Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
176	Intercom Labor	5,000.00	0.00	0.00	0.00	0.00	0.00	5,000.00	0.00
177	Cafeteria A/V & Cabling - Labor	5,048.17	0.00	0.00	0.00	0.00	0.00	5,048.17	0.00
	REPORT TOTALS	\$4,683,548.17	\$968,000.00	\$230,250.00	\$0.00	\$1,198,250.00	25.58	\$3,485,298.17	\$119,825.00

P.O. Box 36503 • Louisville, KY 40233-6503 PHONE (502) 962-1102 FAX (502) 962-8836 Visit us @ www. aeslou.com

AFFIDAVIT -- WAIVER OF LIEN X PARTIAL OF SINAL

RE:	Project Name/#:	TK Stone Middle School - ELECTRICAL
	Sub-Contractor Name:	ADVANCED ELECTRICAL SYSTEMS, INC.

Representative Name & Title: Lee Saettel- Controller

I, the Advanced Electrical Systems, Inc. representative named above, having been duly sworn, depose and state as follows:

- 1. Advanced Electrical Systems, Inc. has requested partial payment or payment in full, for all materials purchased and/or used to date, and for all labor and/or services rendered, and for all sub-contracts entered into, if any, and for all obligations in connection with the above referenced project supplemented by any and all change orders thereto.
- 2. Upon receipt of partial payment or full payment in the amount of \$207,225.00 Advanced Electrical Systems, Inc. hereby waives and releases its right to file a lien or claim on the above referenced project and improvements thereon, and on the materials, fixtures, apparatus or machinery furnished, and on the monies, funds or other considerations due or to become due from ALLIANCE on account of labor, services, material, fixtures, apparatus or machinery heretofore furnished to this date by Advanced Electrical Systems, Inc.
- 3. Advanced Electrical Systems, Inc. agrees to defend, indemnify and hold harmless including any attorneys' fees and litigation expenses, <u>ALLIANCE</u> for any lien or claim which may be asserted by any subcontractor, supplier, employee, laborer or other person or entity on account of the work, labor or materials furnished by Advanced Electrical Systems, Inc. as described herein. This release does not include any claims for acceleration, compression, and inefficiency not captured in previous change orders caused by scope, growth, and compression.
- 4. Contractor warrants that it has not and will not assign any claim or claims for payment, or any other right to perfect a lien against the above listed project and that the undersigned has the right to execute and deliver this Affidavit.

	Signature of Contractor Representative	
Commonwealth of Kentucky County of Jefferson	o.g.m.	
Subscribed and sworn to before me by	Lee Saettel this 27th day of October 2025	
BASI	Tracsy Breitenstein Notary Public, State at Large	

	CONTINUATION SHEET NO. 3 APPLICATION NO.		RENO *D*	' E*	OWNER PURCH	ASE ORDERS *G* TOTAL	*H* BALANCE TO	
EM #	DESCRIPTION	SUPPLIER	P.O. AMOUNT	PREVIOUS PAYMENTS	THIS MONTH (ATTACHED)	TO DATE (E +F)	FINISH (D - G)	
2	Fire Alarm Football Field Lighting Lighting & Switchgear Sound, Control, Audio-Visual, Pag	Johnson Controlls Musco Sports Lighting LLC Eckert g Everon Solutions	\$83,296.00 \$287,976.00 \$486,314.30 \$613,865.53	\$12,581.04 \$200,538.02 \$275,678.34	\$86,399.34 \$40,692.93 \$116,541.39	\$12,581.04 \$0.00 \$278,867.93 \$392,219.73 \$0.00 \$0.00 \$0.00	\$70,714.96 \$287,976.00 \$287,446.37 \$221,645.80 \$0.00 \$0.00 \$0.00	\$192,468.49 -dj
9 10 11						\$293,84	5.81 -dj	
12 13								
4 5								
6 7								
8 9 0 1								
2 3 4 5								
6 7 8								
9 0 1 2								
3 4 5 6								
7 8 9		5						
	TOTALS		\$1,471,451.83	\$488,797.40	\$165,234.32	\$683,668.70	\$787,783 .13	

\$202,940.73 \$698,646.58 -dj \$772,805.25 -dj

DIRECT VENDOR PO INVOICE TRACKING

JOB NO.:	250150	VPO AMOUNT:	\$256,210.65
JOB NAME:	TK Stone MS Revisions	TOTAL INVS.:	\$174,367.80

GEN. CONTRACTOR: Alliance \$81,842.85

OWNER: Etown BOE

VENDOR: Eckart

VPO NO.: 22-63911

TYPE: LIGHTING

\$256,210.65

INV DATE	INVOICE #	\$ AMT	BAL. REMAIN	Inv. w/ PA	Comments
	S101362733.002	26,202.06	230,008.59		
	S101362733.004	8,370.83	221,637.76		
	S101362733.006	652.67	220,985.09		
06/03/25	S101362733.008	134.67	220,850.42		
06/05/25	S101362733.010	152.61	220,697.81		
	S101374840.004	372.16	220,325.65		
06/09/25	S101374840.002	30,817.86	189,507.79		
	S101362733.012	10,480.00	179,027.79		
06/13/25	S101362733.014	2,113.61	176,914.18		
	S101362733.016	2,818.33	174,095.85		
	S101362733.018	693.33	173,402.52		
	S101362733.020	3,535.33	169,867.19	PA-06	
09/11/25	S101362733.022	1,625.00	168,242.19	PA-06	
9/18/2025	S101362733.002	533.33	167,708.86	PA-07	
9/23/2025	S101362733.026	1268.17	166,440.69	PA-07	
9/23/2025	S101362733.024	792.33	165,648.36	PA-07	
	S101362733.028	611.00	165,037.36	PA-07	
	S101362733.030	37,706.41	127,330.95	PA-07	
9/24/2025	S101362733.032	2,818.33	124,512.62	PA-07	
9/24/2025	S101362733.034	1,339.22	123,173.40	PA-07	
09/25/25	S101362731.004	860.00	122,313.40	PA-07	
09/25/25	S101362733.036	2,258.78	120,054.62	PA-07	
09/30/25	S101362731.006	5,662.24	114,392.38	PA-07	
09/30/25	S101362733.038	301.50	114,090.88	PA-07	
10/03/25	S101362733.040	5,073.00	109,017.88	PA-07	
	S101362733.042	1,690.83	107,327.05	PA-07	
	S101362733.044	5,072.67	102,254.38		
	S101362733.046	2,789.39	99,464.99		
	S101362733.050	607.44	98,857.55	PA-07	
	S101362733.052	8,491.70	90,365.85	PA-07	
10/13/25	S101362733.054	8,523.00	81,842.85	PA-07	

				81,842.85			
	DO NOT USE THIS ROW INSERT NEW ROWS ABOVE THIS LINE						
_		TOTAL	174.367.80				



Fax 502-384-8760

RECEIVED

By Anisha A at 8:11 am, Sep 24, 2025

BILL TO:



INVOICE DATE	INVOICE NUMBER		
09/23/2025	52733.026		
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOME	ER PO NUMBER JOB NAME / RELEASE NUMBER			SALES	SPERSON
40822	40822 22-63911		COREY	SEYMOUR			
,	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSH	AW	DIRECT		Net Due 25th	09/23/2025	05/21/2025
ORDER QTY	SHIP QTY		DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	1ea	1	HONIA E L4-6: SL6L U6 80CRI 40K 600LN	∕IF MI	N10	1268.170/ea	1268.17
Invoice is due by 10/25/2025						Subtotal	1268.17
Past Due in	oices ma	S&H Charges Tax	0.00				
							0.00
						Payments Amount Due	1268.17
nted By: ZSEAN on 9/2	3/2025 7:07:43 P	PM EDT					



RECEIVED

By Anisha A at 8:11 am, Sep 24, 2025 BILL TO:

Invoice

INVOICE DATE	E NUMBER		
09/23/2025	62733.024		
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOME	ER PO NUMBER JOB NAME / RELEASE NUMBER			SALESPERSON		
40822	22-63911			COREY	SEYMOUR			
1	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE	
SHAE	BRADSH	HAW	DIRECT		Net Due 25th	09/23/2025	05/21/2025	
ORDER QTY	SHIP QT	Υ	DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE	
1ea	16	ea LOT: LIT	HONIA E X3: LQC W 1 R	EL N		792.330/ea	792.33	
Invoice is due by 10/25/2025 Past Due invoices may be subject to 2% late charge.						Subtotal S&H Charges Tax	792.33 0.00 0.00	
ed By: 7SEAN on 9/23/2025 7:07:43 PM EDT						Payments Amount Due	0.00 792.33	



RECEIVED

By Anisha A at 8:16 am, Sep 19, 2025

BILL TO:



INVOICE DATE	E NUMBER	
09/18/2025	52731.002	
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	TOMER NUMBER CUSTOMER PO NUMBER JOB NAME / RELEASE NUMBER		SALESPERSON				
40822 22		-63911			COREY	SEYMOUR	
1	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSH	HAW	DIRECT		Net Due 25th	09/18/2025	05/21/2025
ORDER QTY	SHIP QTY	1	DESC	RIPTIC	DN	UNIT PRICE	EXT PRICE
1ea	1e	ea LOT: ISC 2 - TYPE	DLITE E L12: E3U-36			533.330/ea	533.33
Invoice is due l	by 10/25/20)25		Subtotal	533.33		
Past Due inv	oices ma	S&H Charges	0.00				
Additional fre	eight char	ges mav ar	Tax	0.00			
. ida.iioridi ile		555a, a	Payments Amount Due	0.00 533.33			
nted By: ZSEAN on 9/18	3/2025 7:07:33 F	PM EDT					



INVOICE DATE	INVOIC	E NUMBER
09/30/2025	52731.006	
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

BILL TO:

SHIP TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	STOMER NUMBER CUSTOMER PO NUMBER JOB NAME / RELEASE NUMBER		SALES	PERSON				
40822 22		2-63911				COREY	SEYMOUR	
,	WRITER		SHIP VIA			TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSI	HAW	DIRECT			Net Due 25th	09/30/2025	05/21/2025
ORDER QTY	SHIP QT	Υ	DESC	RIPTIC	ON		UNIT PRICE	EXT PRICE
1ea	10	ea LOT: ISO			40		5662.240/ea	5662.24
		14 - TYPE	E L13: E3MINI 375) LC N	VIR.	RECEIVED By Anisha A		Oct 01, 2025
Invoice is due	by 11/25/2	025					Subtotal	5662.24
Past Due invoices may be subject			ject to 2% late ch	arge.			S&H Charges	226.85
and Day 705 AN are 0/20/2025 708/45 DM EDT						Tax	0.00	
						Payments	0.00	
						Amount Due	5889.09	



RECEIVED

By Anisha A at 7:56 am, Sep 25, 2025

INVOICE DATE	E NUMBER		
09/24/2025	52733.028		
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

BILL TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOM	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON
40822		22	2-63911			COREY	SEYMOUR
V	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSH	HAW	DIRECT		Net Due 25th	09/24/2025	05/21/2025
ORDER QTY	SHIP QT	Υ	DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	16		THONIA E A2: STAK 2X2 80CRI 40K COL I	MIN10	O ZT	611.000/ea	611.00
Invoice is due by 10/25/2025 Past Due invoices may be subject to 2% late charge.				Subtotal S&H Charges Tax	611.00 0.00 0.00		
By: 7SEAN on 9/24/2025 7:06:26 PM EDT						Payments Amount Due	0.00 <mark>611.00</mark>



RECEIVED

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

BILL TO:

By Anisha A at 7:56 am, Sep 25, 2025

Invoice

INVOICE DATE	INVOIC	E NUMBER
09/24/2025	S10136	52733.030
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 2

CUSTOMER N	UMBER	CUSTON	MER PO NUMBER	JOB	NAME / RELEASE NUMBER	SAI ESI	PERSON
40822	-		2-63911	002	TO THE STATE OF TH		SEYMOUR
	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSI	HAW	DIRECT		Net Due 25th	09/24/2025 05/21/2025	
ORDER QTY	SHIP QT	Υ	DESC	DESCRIPTION			EXT PRICE
1ea	16	5000LM 4 - TYF 5000LM 13 - TY MVOLT 13 - TY MVOLT 13 - TY LTP SE 39 - TY LTP SE 9 - TYF 22 - TY 3 - TYF 2 - TYF 9 - TYF 7 - TYF LV DX 9 - TYF 8 - TYF 3 - TYF 44 - TY AR RJE	PE C1A: ZL1N L48 If FST MVOLT 40K IF C1C: ZL1N L48 If FST MVOLT 40K IF E D1: LDN6 40/1 IF GZ10 HSG IF D2: LDN6 40/1 IF GZ10 HSG IF D2: LDN6 AR LS IF D2: LDN6 AR LS IF E M1: ELM6L LO IF E EM2: ELM6L LO IF E S1: ABSSS-4G IF E S1: ABSSS-4G IF E S1: ABSSS-4G IF S2PD: NPODMA XX IF S2PD: NPODMA XX IF S1: NPODMA DI IF SNOS: NWSXA IF SNOSD: NWSXA IF SNOSD: NWSXA IF SOS: WSXA PD IF E BH: NBRG 8 KI IF E DS: NCM ADCX IF DS: NCM ADCX IF DS: NCM ADCX IF DS: NCM PD	E 80CF E	RI WH	37706.410/ea	37706.4





INVOICE DATE	INVOICE NUMBER	PAGE NO.
09/24/2025	S101362733.030	2 of 2

ORDER QTY	SHIP QTY	DESCRIPTION	UNIT PRICE	EXT PRICE
		12 - TYPE P: NPP16 EFP		
		5 - TYPE PS: NPS 80		
		2 - TYPE PV: NPP16 EFP SA		
		13 - TYPE PZ: NPP16 D EFP		
		12 - TYPE PZV: NPP16 D EFP SA		
		Missing from		
		summary sheet		
		Updated DPO sheet to includeDJ		
		to includeD3		
Invoice is due	by 10/25/202	5	Subtotal	37706.41
Past Due inv	voices ma	y be subject to 2% late charge.	S&H Charges	0.00
			Tax	0.00
			Payments	Q:Q0
			Amount Due	
ted Bv: ZSEAN on 9/24	4/2025 7:06:26 PN	I FDT	Amount Due	37706.41



Phone 502-426-1476 Fax 502-384-8760

RECEIVED

By Anisha A at 7:56 am, Sep 25, 2025

INVOICE DATE	INVOIC	E NUMBER
09/24/2025	S10136	52733.032
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

BILL TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER NUMBER CUSTOME			ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON
40822 22		2-63911			COREY	SEYMOUR	
1	WRITER		SHIP VIA		TERMS	SHIP DATE ORDER D.	
SHAE	BRADSI	HAW	DIRECT		Net Due 25th	09/24/2025 05/21/202	
ORDER QTY	SHIP QT	Υ	DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	16	1	THONIA PE L1-4: SL6L U4 80CRI 40K 900LN	ЛF MI	N10	2818.330/ea	2818.33
Invoice is due by 10/25/2025						Subtotal	2818.33
Past Due invoices may be subject to 2% late charge.						S&H Charges	0.00
						Tax	0.00
						Payments	0.00
ed By: ZSEAN on 9/24	1/2025 7-06-20	DM EDT				Amount Due	2818.33



Phone 502-426-1476 Fax 502-384-8760

RECEIVED

By Anisha A at 7:56 am, Sep 25, 2025

INVOICE DATE	INVOIC	E NUMBER
09/24/2025	S10136	52733.034
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

BILL TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOME	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON
40822 22			-63911			COREY	SEYMOUR
,	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	SHAE BRADSHAW DIRECT Net Due 25th 09/24/2025 05/2				05/21/2025		
ORDER QTY	SHIP QTY		DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	1ea	4000LM MVOLT	HONIA E A: STAK 2X4 80CRI 40K COL I X2: LHQM LED			1339.220/ea	1339.22
Invoice is due by 10/25/2025						Subtotal	1339.22
Past Due inv	Past Due invoices may be subject to 2% late charge.						0.00
							0.00
						Payments	0.00
nted By: ZSEAN on 9/24	1/2025 7:06:26 F	DM EDT				Amount Due	1339.22



Fax 502-384-8760

RECEIVED

BILL TO:

By Anisha A at 7:55 am, Sep 26, 2025

Invoice

INVOICE DATE	INVOICE NUMBER		
09/25/2025	S10136	52733.036	
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER NUMBER CUSTOME		ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON	
40822 22		-63911			COREY	SEYMOUR	
	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSH	HAW	DIRECT		Net Due 25th	09/25/2025	05/21/2025
ORDER QTY	SHIP QTY	Y	DESC	RIPTIC	N	UNIT PRICE	EXT PRICE
1ea	1e		HONIA NECY1: NECY BAC ENC GFXK			2258.780/ea	2258.78
Invoice is due by 10/25/2025 Past Due invoices may be subject to 2% late charge.						Subtotal S&H Charges Tax	2258.78 0.00 0.00
ited By: ZSEAN on 9/25	5/2025 7:10:55	PM EDT				Payments Amount Due	0.00




Eckart Louisville 1815 PLANTSIDE DR LOUISVILLE, KY 40299-1932

Phone 502-426-147 Fax 502-384-8760

RECEIVED

By Anisha A at 7:55 am, Sep 26, 2025 p.

BILL TO:



09/25/2025 S101362731.004

REMIT TO:
ECKART SUPPLY
426 QUARRY RD NW
CORYDON, IN 47112-6918 1 of 1

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER NUMBER CUSTOME			ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	PERSON
40822 22-		-63911			COREY	SEYMOUR	
1	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSH	AW	DIRECT		Net Due 25th	09/25/2025	05/21/2025
ORDER QTY	SHIP QTY		DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	1ea	a LOT: ISC 3 - TYPE	DLITE E L12: E3U-36			860.000/ea	860.00
Invoice is due by 10/25/2025						Subtotal	860.00
Past Due invoices may be subject to 2% late charge.						S&H Charges Tax	0.00
							0.00
							0.00
ted By: ZSEAN on 9/25/2025 7:10:55 PM EDT						Amount Due	860.00



RECEIVED

By Anisha A

By Anisha A at 7:54 am, Oct 06, 2025

INVOICE DATE	INVOIC	E NUMBER
10/03/2025	S10136	52733.040
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

BILL TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOM	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON
40822		22	2-63911			COREY	SEYMOUR
,	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	SHAE BRADSHAW DIRECT Net Due 25th				Net Due 25th	10/03/2025	05/21/2025
ORDER QTY	SHIP QT	Υ	DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	16		THONIA PE L1-4: SL6L U4 80CRI 40K 900LN	ИF MI	N10	5073.000/ea	5073.00
Invoice is due l	-		ject to 2% late ch	narge.		Subtotal S&H Charges Tax	5073.00 0.00 0.00
						Payments Amount Due	0.00 5073.00



Fax 502-384-8760

RECEIVED

BILL TO:

By Anisha A at 7:54 am, Oct 06, 2025

Invoice

INVOICE DATE	INVOICE NUMBER		
10/03/2025	S10136	52733.042	
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOME	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	PERSON
40822		22	-63911			COREY	SEYMOUR
1	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE BRADSHAW DIRECT				Net Due 25th	10/03/2025	05/21/2025	
ORDER QTY	SHIP QTY	(DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE
1ea	1e:	1	HONIA E L1-8: SL6L U8 80CRI 40K 900LN	ИF MI	N10	1690.830/ea	1690.83
Invoice is due le Past Due inv			ect to 2% late ch	narge.		Subtotal S&H Charges Tax	1690.83 0.00 0.00
nted Rv: 7SFAN on 10/3	N/2025 7-00-27 F	DM EDT				Payments Amount Due	0.00 1690.83



Fax 502-384-8760 **RECEIVED**

BILL TO:

By Anisha A at 7:48 am, Oct 09, 2025

Invoice

INVOICE DATE	INVOICE NUMBER		
10/08/2025	S10136	52733.046	
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOME	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON
40822	40822 22-63911					COREY	SEYMOUR
V	WRITER SHIP VIA				TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSH	IAW	DIRECT		Net Due 25th	10/08/2025	05/21/2025
ORDER QTY	SHIP QTY			RIPTIC	DN	UNIT PRICE	EXT PRICE
1ea	1e:	4000LM MVOLT 7 - TYPE 2500LM 2 - TYPE MVOLT 2 - TYPE 5 - TYPE	HONIA E A2: STAK 2X2 80CRI 40K COL I CC2: ZL1N L24 FST MVOLT 40K D3: LDN6 40/10 GZ10 HSG D3: LW6 AR LSE X3/2: LQC W 2 I E NAR: NAR40	MIN1(80CF S TRI	RI WH	2789.390/ea	2789.39
Invoice is due b			ect to 2% late ch	narge.		Subtotal S&H Charges Tax Payments	2789.39 0.00 0.00 0.00
oted Rv: 7SEAN on 10/8	/2025 7:06:17 5	DM EDT				Amount Due	2789.39



RECEIVED

By Anisha A at 8:00 am, Oct 10, 2025

INVOICE DATE	INVOIC	E NUMBER
10/09/2025	S10136	62733.050
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

BILL TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER NU	IMBER	CUSTOME	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	PERSON
40822	40822 22-63911					COREY SEYMOUR	
W	WRITER SHIP VIA				TERMS	SHIP DATE	ORDER DATE
SHAE BRADSHAW			DIRECT		Net Due 25th	10/09/2025	05/21/2025
ORDER QTY	RDER QTY SHIP QTY DESCRIPTION			RIPTIC	DN	UNIT PRICE	EXT PRICE
1ea	1ea	4000LM MVOLT 4 - TYPE DX CCT	A2: STAK 2X2 80CRI 40K COL I SSCT: NPODMA XX SSCTS: NPODMA	2P) ZT	607.440/ea	607.44
nvoice is due by	y 11/25/202	25				Subtotal	607.44
Past Due invo	oices ma	y be subj	ect to 2% late ch	arge.		S&H Charges Tax	0.00
Additional frei	ght charg	ges may ap	oply.			Payments	0.00



Phone 502-426-1476 Fax 502-384-8760

BILL TO:

RECEIVED

By Anisha A at 7:29 am, Oct 13, 2025

INVOICE DATE	INVOIC	E NUMBER
10/10/2025	S10136	62733.052
REMIT TO:		PAGE NO.
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1

ELIZABETHTOWN INDEP. SCHOOLS

219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOME	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON	
40822	2 22-63911					COREY SEYMOUR		
,	WRITER		SHIP VIA		TERMS	SHIP DATE	ORDER DATE	
SHAE	BRADSH	IAW	DIRECT		Net Due 25th	10/10/2025	05/21/2025	
ORDER QTY	SHIP QTY	<i>,</i>	DESC	RIPTIC	ON	UNIT PRICE	EXT PRICE	
1ea	1e:		THONIA E S1: SSS 25 4G S DDBXD L/AB			8491.700/ea	8491.70	
nvoice is due l	by 11/25/20	25				Subtotal	8491.70	
Past Due inv	voices ma	ay be sub	ject to 2% late ch	arge		S&H Charges	0.00	
Additional fre	eight char	des may ai	nnly			Tax	0.00	
nautional IIE	Jigrit Griar	yes may a	ρριy.			Payments Amount Due	0.00 8491.70	
d By: ZSEAN on 10/1	10/2025 7:05:21	PM EDT				Amount Due	0431.70	



Fax 502-384-8760

RECEIVED

By Anisha A at 7:19 am, Oct 14, 2025

BILL TO:

INVOICE DATE	INVOICE NUMBER		
10/13/2025	S10136	62733.054	
REMIT TO:		PAGE NO.	
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1	

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

WRITER SHIP VIA TERMS SHAE BRADSHAW DIRECT Net Due 2 ORDER QTY SHIP QTY DESCRIPTION 1ea 1ea LOT: LITHONIA 9 - TYPE S1: DSX1 LED P4 40K 70CRI T4M HVOLT SPA NLTAIR2 PIRHN DDBXD	
SHAE BRADSHAW DIRECT Net Due 2 ORDER QTY SHIP QTY DESCRIPTION 1ea 1ea LOT: LITHONIA 9 - TYPE S1: DSX1 LED P4 40K 70CRI T4M HVOLT SPA	25th 10/13/2025 05/21/2025 UNIT PRICE EXT PRICE
ORDER QTY SHIP QTY DESCRIPTION 1ea 1ea LOT: LITHONIA 9 - TYPE S1: DSX1 LED P4 40K 70CRI T4M HVOLT SPA	UNIT PRICE EXT PRICE
1ea 1ea LOT: LITHONIA 9 - TYPE S1: DSX1 LED P4 40K 70CRI T4M HVOLT SPA	
9 - TYPE S1: DSX1 LED P4 40K 70CRI T4M HVOLT SPA	8523.000/ea 8523.0
Invoice is due by 11/25/2025	Subtotal 8523.0
Past Due invoices may be subject to 2% late charge.	S&H Charges 0.0
	Tax 0.0
	Payments 0.0
nted By: ZSEAN on 10/13/2025 7:06:58 PM EDT	Amount Due 8523.0



INVOICE DATE	INVOIC	E NUMBER			
09/30/2025	30/2025 S101362733.03				
REMIT TO:		PAGE NO.			
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1			

BILL TO:

SHIP TO:

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER N	UMBER	CUSTOM	ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	SPERSON
			2-63911			COREY	SEYMOUR
			SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADS	HAW	DIRECT		Net Due 25th	09/30/2025	05/21/2025
ORDER QTY	SHIP QT	ſΥ	DESC	RIPTIC)N	UNIT PRICE	EXT PRICE
1ea	1	ea LOT: LIT	THONIA E DS: NCM ADCX			301.500/ea	301.50
					RECEIV By Anish		am, Oct 01, 2
voice is due b	-					Subtotal	301.50
ast Due inv	oices n	nay be sub	ject to 2% late ch	narge.		S&H Charges	0.00
						Tax	0.00
						Payments	0.00
By: ZSEAN on 9/30		5 D. J. ED. T				Amount Due	301.50



By Anisha A at 7:30 am, Oct 07, 2025

Fax 502-384-8760 RECEIVED BILL TO:

Invoice

INVOICE DATE	INVOIC	E NUMBER		
10/06/2025	/06/2025 S101362733.04			
REMIT TO:		PAGE NO.		
ECKART SUPPLY 426 QUARRY RD NW CORYDON, IN 47112-6918		1 of 1		

ELIZABETHTOWN INDEP. SCHOOLS 219 HELM STREET ELIZABETHTOWN, KY 42701-1511

CUSTOMER NUMBER CUSTOMER			ER PO NUMBER	JOB	NAME / RELEASE NUMBER	SALES	PERSON
40822 22-			2-63911			COREY	SEYMOUR
WRITER			SHIP VIA		TERMS	SHIP DATE	ORDER DATE
SHAE	BRADSHA	ΑW	DIRECT		Net Due 25th	10/06/2025	05/21/2025
ORDER QTY	SHIP QTY		DESC	RIPTIC	N	UNIT PRICE	EXT PRICE
1ea	1ea		HONIA PE L4-6: SL6L U6 80CRI 40K 600LN		N10	5072.670/ea	5072.67
Invoice is due b	Invoice is due by 11/25/2025						5072.67
Past Due inv	Past Due invoices may be subject to 2% late charge. Additional freight charges may apply.						0.00
Additional fre							0.00
ed By: ZSEAN on 10/6/2025 7:06:28 PM EDT						Payments Amount Due	0.00 5072.67

DIRECT VENDOR PO INVOICE TRACKING

JOB NO.:	250150	VPO AMOUNT:	\$613,865.53
JOB NAME:	TK Stone MS Revisions	TOTAL INVS.:	\$392,219.73
GEN. CONTRACTOR:	Alliance	BALANCE:	\$221,645.80

OWNER: Etown BOE

VENDOR: EVERON

VPO NO.: 23-63912

TYPE: SYSTEMS

\$613,865.53

INV DATE	INVOICE #	\$ AMT	BAL. REMAIN	Inv. w/ PA	Comments
06/18/25	159011621	122,192.18	491,673.35		
08/08/25	159424582	153,486.16	338,187.19	PA-05	
10/02/25	159758284	116,541.39	221,645.80	PA-07	
			221,645.80		
			221,645.80		
			221,645.80		
			221,645.80		
			221,645.80		
	DO N	OT USE THIS ROW IN	ISERT NEW ROWS AF	BOVE THIS LINE	-

TOTAL 392,219.73



Elizabethtown Independent C/O AES 3312 Gilmore Industrial Blvd Louisville KY 40213

REMIT PAYMENT TO ▼

EVERON, LLC PO BOX 872987 KANSAS CITY MO 64187-2987

RECEIVED By Anisha A at 8:51 am, Oct 03, 2025

Payment

Invoice 159758284

\$0.00

							everonsolutions.com	
	-		ayment PO ue Date Number		er	Amount Due		
	40073041	9/30/2025	10)/25/2025	23-63912		\$116,541.39	
Item Id	Description		Contract Amount	Completed To Date	Retainage	Less Previous Billings		
1	Material		\$350,608.67	\$350,608.67	\$0.00	\$249,472.2	24 \$101,136.43	
2	Labor		\$226,526.05	\$41,611.06	\$0.00	\$26,206.1	0 \$15,404.96	
		Total	\$577,134.72	\$392,219.73	\$0.00	\$275,678.3	34 \$116,541.39	
		Sub Tota	al				\$116,541.39	
		Sales Ta	ax				\$0.00	
		Retainage Hel	ld				\$0.00	



Invoice Number

159758284

Invoice Date

9/30/2025

Account Number 40073041

Amount due this Invoice

\$116,541.39

Invoice Comments/Scope:

Job Name	Site Location	Job #	Terms
E-Town Ind 27 51 23	T K STONE MIDDLE SCHOOL, 323 MORNINGSIDE DR	300543757	Net 25 Days
Intercommunications and Program	ELIZABETHTOWN KY 42701		
Systems			

Contract Summary

Original amount	Approved changes	Revised Amount	Invoiced amount	Remaining amount	Billed percent	Retainage balance	Deposit amount
\$577,134.72	\$0.00	\$577,134.72	\$392,219.73	\$184,914.99	67.96%	\$0.00	\$0.00

Internal Reference Id	
159758284 - 300543757	E-Town Ind 27 51 23 Intercommunications and Program Systems
159758285 - 300543758	E-Town Ind 27 53 00 Sports Field Sound System
159758286 - 300543759	E-Town Ind 27 53 01 Band Room Sound
159758287 - 300543761	E-Town Ind 28 13 00 Access Control
159758288 - 300543763	E-Town Ind 27 06 10 - Voice/Data Communication System
159758289 - 300543764	E-Town Ind 27 06 10 - Voice/Data Communication System - Football Pressbox

Thank you for choosing Everon

You will be charged a \$25.00 fee for any payment returned. Credit card payments are subject to a credit card surcharge fee. **Make checks payable to Everon and please include your account number.**

Questions?

Call Toll-Free: 844-5-EVERON

Email: ComCare@everonsolutions.com

everonsolutions.com





CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY) 6/20/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

and to mind a trace in the training in grade to the trace in mount in men and	won on wo won (o).	
PRODUCER	CONTACT NAME: AssuredPartners of MO LLC	
AssuredPartners of MO LLC 12645 Olive Blvd, Suite 300	PHONE (A/C, No, Ext): 314-523-8800 FAX (A/C, No): 314-45	3-7555
St Louis MO 63141	E-MAIL ADDRESS: EveronCOI@assuredpartners.com	
	INSURER(S) AFFORDING COVERAGE	NAIC#
	INSURER A: Old Republic Insurance Company	24147
NSURED ADTCOM	INSURER B : ACE Property & Casualty Insurance Co	20699
Everon, LLC 5630 Shepherdsville Rd	INSURER C: HDI Specialty Insurance Company	16131
Louisville, KY 40228	INSURER D: QBE Specialty Insurance Company	11515
	INSURER E: Indian Harbor Insurance Company	36940
	INSURER F:	

COVERAGES CERTIFICATE NUMBER: 195435124 REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR			ADDL	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	S
Α	Х	COMMERCIAL GENERAL LIABILITY	IIIOD	11112	MWZY31801724	10/2/2024	10/2/2025	EACH OCCURRENCE	\$ 1,000,000
С		CLAIMS-MADE X OCCUR			XLXD6212301S	10/2/2024	10/2/2025	DAMAGE TO RENTED PREMISES (Ea occurrence)	\$1,000,000
								MED EXP (Any one person)	\$ 10,000
								PERSONAL & ADV INJURY	\$1,000,000
	GEN	N'L AGGREGATE LIMIT APPLIES PER:						GENERAL AGGREGATE	\$3,000,000
		POLICY X PRO- JECT LOC						PRODUCTS - COMP/OP AGG	\$3,000,000
		OTHER:						Excess GL	\$3,000,000 occ/ag
A	AUT	OMOBILE LIABILITY			MWTB31801624	10/2/2024	10/2/2025	COMBINED SINGLE LIMIT (Ea accident)	\$3,000,000
D	Χ	ANY AUTO			140002059	10/2/2024	10/2/2025	BODILY INJURY (Per person)	\$
		OWNED SCHEDULED AUTOS ONLY						BODILY INJURY (Per accident)	\$
		HIRED NON-OWNED AUTOS ONLY AUTOS ONLY						PROPERTY DAMAGE (Per accident)	\$
								Excess Auto	\$2,000,000 Agg
В	Х	UMBRELLA LIAB X OCCUR			XOOG47427927002	10/2/2024	10/2/2025	EACH OCCURRENCE	\$ 10,000,000
		EXCESS LIAB CLAIMS-MADE						AGGREGATE	\$ 10,000,000
		DED RETENTION\$							\$
Α		RKERS COMPENSATION EMPLOYERS' LIABILITY			MWC31801524	10/2/2024	10/2/2025	X PER OTH- STATUTE ER	
	ANY	PROPRIETOR/PARTNER/EXECUTIVE N	N/A					E.L. EACH ACCIDENT	\$2,000,000
	(Mar	ndatory in NH)	,					E.L. DISEASE - EA EMPLOYEE	\$ 2,000,000
	If yes	s, describe under CRIPTION OF OPERATIONS below						E.L. DISEASE - POLICY LIMIT	\$2,000,000
E	Erro	rs & Omissions			MTP9046829	10/2/2024	10/2/2025	Each Claim Aggregate	10,000,000 10,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Certificate holder, Owner and any other parties as required by written contract are included as Additional Insured. See attached page for automatically included coverage extensions.

Advanced Electrical Systems 3312 Gilmore Industrial Blvd, Louisville, KY 40213 is included as additional insured where required by written contract.

CERTIFICATE HOLDER	CANCELLATION
Elizabethtown IND School 219 Helm Street Elizabethtown KY 42701	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
	AUTHORIZED REPRESENTATIVE

AGENCY CUSTOMER ID:	
LOC #:	



ADDITIONAL REMARKS SCHEDULE

Page 1 of

AGENCY		NAMED INSURED	
AssuredPartners of Missouri, LLC		See Page 1	
POLICY NUMBER			
See Page 1			
CARRIER	NAIC CODE		
See Page 1	See Page 1	EFFECTIVE DATE:	See Page 1

ADDITIONAL REMARKS

THIS ADDITIONAL REMARKS FORM IS A SCHEDULE TO ACORD FORM,

FORM NUMBER: 25 FORM TITLE: Certificate of Liability Insurance

General Liability

- Designated Construction Project(s) General Aggregate Limit per form No. CG2503 (05/09)
- Additional Insured Owners, Lessees or Contractors, where required by written contract per form No. CG2010 (12/19)
- Additional Insured Owners, Lessees or Contractors Completed Operations, where required by written contract per form No. CG2037 (12/19)
- Additional Insured Managers or Lessors of Premises, where required by written contract per form No. CG2011 (12/19)
- Additional Insured Vendor, where required by written contract per form No. CG2044 (12/19)
- Additional Insured Designated Person or Organization, where required by written contract per form No. CG2026 (12/19)
- Additional Insured Lessor of Leased Equipment, where required by written contract per form No. CG2034 (12/19)
- Waiver of Subrogation, where required by written contract per form No. CG2453 (12/19)
- Primary & Non-Contributory, where required by written contract per form No. CG2001 (12/19)
- 30 Day Notice of Cancellation, where required by written contract per form No. PIL029 (10/10)

Auto Liability

- Additional Insured, where required by written contract per form No. PCA048 (09/19)
- Lessor Additional Insured and Loss Payee, where required by written contract per form No. CA2001 (11/20)
- Waiver of Subrogation, where required by written contract per form No. CA0443 (11/20)
- Primary & Non-Contributory, where required by written contract per form No. PCA048 (09/19)
- 30 Day Notice of Cancellation, where required by written contract per form No. PIL029 (10/10)

Workers Compensation / Employers Liability

- · Employers Liability is included for OH and WA
- Waiver of Subrogation, where required by written contract per form No. WC000313, except
 - o California WC040306 (04/84)
 - o Texas WC420304B (06/14)
 - o Utah WC430305
- 30 Day Notice of Cancellation, where required by written contract

\$2M Excess Auto Liability

- Subject to the policy terms & conditions, coverage is follow form and in addition to the scheduled underlying policy:
 - o Auto Liability

\$3M Excess General Liability

- Subject to the policy terms & conditions, coverage is follow form and in addition to the scheduled underlying policy:
 - o General Liability

Umbrella Liability

- Primary & Non-Contributory, where required by written contract per form No. XS-38039 (05/13)
- Subject to the policy terms & conditions, coverage is follow form and in addition to the scheduled underlying policies:
 - o General Liability
 - o Auto Liability
 - o Employers Liability
 - o \$2M Excess Auto Liability
 - o \$3M Excess General Liability

IL 10 (12/06) OLD REPUBLIC INSURANCE COMPANY

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

NOTICE OF CANCELLATION TO CERTIFICATE HOLDERS

This endorsement modifies the notice of cancellation of insurance provided hereunder by adding the following:

- A. In the event this policy is cancelled for any permissible reason, other than for nonpayment of premium, we shall endeavor to provide advance written notice of cancellation to certificate holders set out in the schedule on file with the Company, after notifying the first Named Insured of such cancellation. Notice of cancellation to certificate holders may be made by any commercially reasonable means, including mail, electronic mail, facsimile transmission or courier service.
- **B.** This advance written notification of a cancellation of coverage is intended as a courtesy only. Our failure to provide such advance written notification will not extend the policy cancellation date, nor negate cancellation of the policy.

All other terms and conditions of this policy remain unchanged.

PIL 029 10 10

IL 10 (12/06) OLD REPUBLIC INSURANCE COMPANY

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED AND PRIMARY AND NON-CONTRIBUTORY ENDORSEMENT

This endorsement modifies insurance provided under the following:

BUSINESS AUTO COVERAGE FORM MOTOR CARRIER COVERAGE FORM

SCHEDULE

Designated Person(s) or Organization(s):

All persons or organizations where required by written contract or agreement.

- A. SECTION II COVERED AUTOS LIABILITY COVERAGE, paragraph 1. Who Is An Insured is amended to include the person(s) or organization(s) shown in the above Schedule as an additional "insured", but only with respect to "accidents" arising out of your work while being performed for such person(s) or organization(s).
- **B.** The following is added to the **Other Insurance** Condition in the Business Auto Coverage Form and the **Other Insurance Primary And Excess Insurance Provisions** in the Motor Carrier Coverage Form and supersedes any provision to the contrary:

This policy's Covered Autos Liability Coverage is primary to and will not seek contribution from any other insurance available to the "insured" person(s) or organization(s) shown in the above Schedule provided that:

- 1. Such "insured" is a Named Insured under such other insurance; and
- 2. You have agreed in writing in a contract or agreement that this insurance would be primary and would not seek contribution from any other insurance available to such "insured".

10/02/24 - 10/02/25

PCA 048 09 19 Page 1 of 1

Includes copyrighted material of Insurance Services Office, Inc., with its permission.

MWZY 318017 24 Everon, LLC

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

WAIVER OF TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US (WAIVER OF SUBROGATION) – AUTOMATIC WHEN REQUIRED BY WRITTEN CONTRACT OR AGREEMENT

This endorsement modifies insurance provided under the following:

AUTO DEALERS COVERAGE FORM BUSINESS AUTO COVERAGE FORM MOTOR CARRIER COVERAGE FORM

With respect to coverage provided by this endorsement, the provisions of the Coverage Form apply unless modified by the endorsement.

The Transfer Of Rights Of Recovery Against Others

To Us Condition does not apply to any person(s) or organization(s) for whom you are required to waive subrogation with respect to the coverage provided under this Coverage Form, but only to the extent that subrogation is waived:

- **A.** Under a written contact or agreement with such person(s) or organization(s); and
- B. Prior to the "accident" or the "loss."

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED – OWNERS, LESSEES OR CONTRACTORS – SCHEDULED PERSON OR ORGANIZATION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s)	Location(s) Of Covered Operations	
Any Person(s) or Organization(s) whom you have agreed to include as an Additional Insured under a Written Contract, provided such Contract was executed prior to the date of loss.	All Locations where you perform work for such Additional Insured pursuant to any such Written Contract.	
Information required to complete this Schedule, if not shown above, will be shown in the Declarations.		

- A. Section II Who Is An Insured is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury", "property damage" or "personal and advertising injury" caused, in whole or in part, by:
 - 1. Your acts or omissions; or
 - The acts or omissions of those acting on your behalf;

in the performance of your ongoing operations for the additional insured(s) at the location(s) designated above.

However:

- 1. The insurance afforded to such additional insured only applies to the extent permitted by law; and
- 2. If coverage provided to the additional insured is required by a contract or agreement, the insurance afforded to such additional insured will not be broader than that which you are required by the contract or agreement to provide for such additional insured.

B. With respect to the insurance afforded to these additional insureds, the following additional exclusions apply:

This insurance does not apply to "bodily injury" or "property damage" occurring after:

- All work, including materials, parts or equipment furnished in connection with such work, on the project (other than service, maintenance or repairs) to be performed by or on behalf of the additional insured(s) at the location of the covered operations has been completed; or
- 2. That portion of "your work" out of which the injury or damage arises has been put to its intended use by any person or organization other than another contractor or subcontractor engaged in performing operations for a principal as a part of the same project.

CG 20 10 12 19 © Insurance Serv

C. With respect to the insurance afforded to these additional insureds, the following is added to **Section III – Limits Of Insurance:**

If coverage provided to the additional insured is required by a contract or agreement, the most we will pay on behalf of the additional insured is the amount of insurance:

1. Required by the contract or agreement; or

2. Available under the applicable limits of insurance;

whichever is less.

This endorsement shall not increase the applicable limits of insurance.

© Insurance Services Office, Inc., 2018

10/02/24- 10/02/25

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED – OWNERS, LESSEES OR CONTRACTORS – COMPLETED OPERATIONS

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s)	Location And Description Of Completed Operations
Any Person(s) or Organization(s) whom you have agreed to include as an Additional Insured under a Written Contract, provided such Contract was executed prior to the date of loss.	All Locations where you perform work for such Additional Insured pursuant to any such Written Contract.
Information required to complete this Schedule, if not sho	own above, will be shown in the Declarations

A. Section II – Who Is An Insured is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury" or "property damage" caused, in whole or in part, by "your work" at the location designated and described in the Schedule of this endorsement performed for that additional insured and included in the "products-completed operations hazard".

However:

- The insurance afforded to such additional insured only applies to the extent permitted by law; and
- 2. If coverage provided to the additional insured is required by a contract or agreement, the insurance afforded to such additional insured will not be broader than that which you are required by the contract or agreement to provide for such additional insured.

B. With respect to the insurance afforded to these additional insureds, the following is added to **Section III – Limits Of Insurance:**

If coverage provided to the additional insured is required by a contract or agreement, the most we will pay on behalf of the additional insured is the amount of insurance:

- 1. Required by the contract or agreement; or
- 2. Available under the applicable limits of insurance:

whichever is less.

This endorsement shall not increase the applicable limits of insurance.

IL 10 (12/06) OLD REPUBLIC INSURANCE COMPANY

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

NOTICE OF CANCELLATION TO CERTIFICATE HOLDERS

This endorsement modifies the notice of cancellation of insurance provided hereunder by adding the following:

- A. In the event this policy is cancelled for any permissible reason, other than for nonpayment of premium, we shall endeavor to provide advance written notice of cancellation to certificate holders set out in the schedule on file with the Company, after notifying the first Named Insured of such cancellation. Notice of cancellation to certificate holders may be made by any commercially reasonable means, including mail, electronic mail, facsimile transmission or courier service.
- **B.** This advance written notification of a cancellation of coverage is intended as a courtesy only. Our failure to provide such advance written notification will not extend the policy cancellation date, nor negate cancellation of the policy.

All other terms and conditions of this policy remain unchanged.

PIL 029 10 10

Designated Construction Project(s)

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

DESIGNATED CONSTRUCTION PROJECT(S) GENERAL AGGREGATE LIMIT

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

SCHEDULE

The projects as specified in the written contracts or agreements
Information required to complete this Schedule, if not shown above, will be shown in the Declarations.

- A. For all sums which the insured becomes legally obligated to pay as damages caused by "occurrences" under Section I Coverage A, and for all medical expenses caused by accidents under Section I Coverage C, which can be attributed only to ongoing operations at a single designated construction project shown in the Schedule above:
 - 1. A separate Designated Construction Project General Aggregate Limit applies to each designated construction project, and that limit is equal to the amount of the General Aggregate Limit shown in the Declarations.
 - 2. The Designated Construction Project General Aggregate Limit is the most we will pay for the sum of all damages under Coverage A, except damages because of "bodily injury" or "property damage" included in the "products-completed operations hazard", and for medical expenses under Coverage C regardless of the number of:
 - a. Insureds;
 - b. Claims made or "suits" brought; or
 - **c.** Persons or organizations making claims or bringing "suits".

- 3. Any payments made under Coverage A for damages or under Coverage C for medical expenses shall reduce the Designated Construction Project General Aggregate Limit for that designated construction project. Such payments shall not reduce the General Aggregate Limit shown in the Declarations nor shall they reduce any other Designated Construction Project General Aggregate Limit for any other designated construction project shown in the Schedule above.
- 4. The limits shown in the Declarations for Each Occurrence, Damage To Premises Rented To You and Medical Expense continue to apply. However, instead of being subject to the General Aggregate Limit shown in the Declarations, such limits will be subject to the applicable Designated Construction Project General Aggregate Limit.

CG 25 03 05 09

- B. For all sums which the insured becomes legally obligated to pay as damages caused by "occurrences" under Section I Coverage A, and for all medical expenses caused by accidents under Section I Coverage C, which cannot be attributed only to ongoing operations at a single designated construction project shown in the Schedule above:
 - Any payments made under Coverage A for damages or under Coverage C for medical expenses shall reduce the amount available under the General Aggregate Limit or the Products-completed Operations Aggregate Limit, whichever is applicable; and
 - Such payments shall not reduce any Designated Construction Project General Aggregate Limit.
- C. When coverage for liability arising out of the "products-completed operations hazard" is provided, any payments for damages because of "bodily injury" or "property damage" included in the "products-completed operations hazard" will reduce the Products-completed Operations Aggregate Limit, and not reduce the General Aggregate Limit nor the Designated Construction Project General Aggregate Limit.
- D. If the applicable designated construction project has been abandoned, delayed, or abandoned and then restarted, or if the authorized contracting parties deviate from plans, blueprints, designs, specifications or timetables, the project will still be deemed to be the same construction project.
- **E.** The provisions of Section **III** Limits Of Insurance not otherwise modified by this endorsement shall continue to apply as stipulated.

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

PRIMARY AND NONCONTRIBUTORY – OTHER INSURANCE CONDITION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART LIQUOR LIABILITY COVERAGE PART PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

The following is added to the **Other Insurance** Condition and supersedes any provision to the contrary:

Primary And Noncontributory Insurance

This insurance is primary to and will not seek contribution from any other insurance available to an additional insured under your policy provided that:

(1) The additional insured is a Named Insured under such other insurance; and

(2) You have agreed in writing in a contract or agreement that this insurance would be primary and would not seek contribution from any other insurance available to the additional insured.

WAIVER OF TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US (WAIVER OF SUBROGATION) – AUTOMATIC

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART
ELECTRONIC DATA LIABILITY COVERAGE PART
LIQUOR LIABILITY COVERAGE PART
POLLUTION LIABILITY COVERAGE PART DESIGNATED SITES
POLLUTION LIABILITY LIMITED COVERAGE PART DESIGNATED SITES
PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART
RAILROAD PROTECTIVE LIABILITY COVERAGE PART
UNDERGROUND STORAGE TANK POLICY DESIGNATED TANKS

The following is added to Paragraph 8. Transfer Of Rights Of Recovery Against Others To Us of Section IV – Conditions:

We waive any right of recovery against any person or organization, because of any payment we make under this Coverage Part, to whom the insured has waived its right of recovery in a written contract or agreement. Such waiver by us applies only to the extent that the insured has waived its right of recovery against such person or organization prior to loss.

OLD REPUBLIC INSURANCE COMPANY

WORKERS' COMPENSATION AND EMPLOYERS' LIABILITY POLICY

NOTICE OF CANCELATION TO CERTIFICATE HOLDERS ENDORSEMENT

This endorsement modifies the notice of cancelation of insurance provided hereunder by adding the following:

- A. In the event this policy is canceled for any permissible reason, other than for nonpayment of premium, we shall endeavor to provide advance written notice of cancelation to certificate holders set out in the schedule on file with the Company, after notifying the Insured first named in item 1 of the Information Page of such cancelation. Notice of cancelation to certificate holders may be made by any commercially reasonable means, including mail, electronic mail, facsimile transmission or courier service.
- B. This advance written notification of a cancelation of coverage is intended as a courtesy only. Our failure to provide such advance written notification will not extend the policy cancelation date, nor negate cancelation of the policy.

All other terms and conditions of this policy remain unchanged.

WORKERS' COMPENSATION AND EMPLOYERS' LIABILITY INSURANCE POLICY

WC 124 (4-84)

WC 00 03 13

WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT

This endorsement changes the policy to which it is attached effective on the inception date of the policy unless a different date is indicated below.

(The following "attaching clause" need be completed only when this endorsement is issued subsequent to preparation of the policy.)

This endorsement, effective on

10/02/2024

at 12:01 A.M. standard time, forms a part of

(DATE)

Policy No. MWC31801524

of the

Old Republic Insurance Company
(NAME OF INSURANCE COMPANY)

issued to Everon, LLC

Premium \$ N/A

Authorized Representative

We have the right to recover our payments from anyone liable for an injury covered by this policy. We will not enforce our right against the person or organization named in the Schedule. This agreement applies only to the extent that you perform work under a written contract that requires you to obtain this agreement from us.*

This agreement shall not operate directly or indirectly to benefit any one not named in the Schedule.

Schedule

ANY PERSON OR ORGANIZATION AGAINST WHOM YOU HAVE AGREED TO WAIVE YOUR RIGHTS OF RECOVERY IN A WRITTEN CONTRACT, PROVIDED SUCH CONTRACT IS EXECUTED PRIOR TO THE DATE OF LOSS.

(THIS FORM IS NOT APPLICABLE IN: CA, KY, NJ, TX, UT)

^{*}Typist: strike out third sentence if inapplicable.

APPLICATION AND CERTIFICATE FOR PAYMENT CONSTRUCTION MANAGER-ADVISER EDITION AIA DOCUMENT G702/CMa **PAGE** OF TO: Elizabethtown Independent PROJECT: TK Stone Middle School APPLICATION NO: #3 **DISTRIBUTION TO:** c/o Advanced Electrial Systems Inc. 323 Morningside Dr OWNER 6645 Gilmore Industrial Blvd Elizabethtown, KY 40201 PERIOD TO: 10/31/2025 CONSTRUCTION Louisville, KY 40213 PURCHASE ORDER: 23-63912 MANAGER FROM CONTRACTOR: ARCHITECT CONTRACT DATE: 3/14/2025 CONTRACTOR AES Job # 250150 VIA CONSTRUCTION MANAGER: Inv 159758284 CONTRACT FOR: VIA ARCHITECT: CONTRACTOR'S APPLICATION FOR PAYMENT The undersigned Contractor certifies that to the best of the Contractor Application is made for payment, as shown below, in connection with information and belief the Work covered by this Application for Payment has been the Contract. Continuation Sheet, AIA Document G703, is attached. completed in accordancewith the Contract Documents, that all amounts have been paid by the Contractor for Work which previous Certificates for Payment were ssued and payments received from the Owner, and that current paymentshown berein is now due 1. ORIGINAL CONTRACT SUM 613,865.83 Date: 04/18/2020 2. Net change by Change Orders CONTRACTOR: Everon 3. CONTRACT SUM TO DATE (Line 1+2) 613,865,83 4. TOTAL COMPLETED & STORED TO 10/2/25 DATE (Column G on G703) \$ 376,688.62 5. RETAINAGE: of Work Completed 10% State of: Kentucky (Column D+E on G703) Subscribed and sworn to before me this 2 day of Oct 2025 Notary Public: Lawo 10% of Material Breakout (Column D+E on G703) My Commission expires: April 18, 2026 Total Retainage (Lines 5a + 5b or CERTIFICATE FOR PAYMENT Total in Column 1 of G703) 6. TOTAL EARNED LESS RETAINAGE 376,688.62 In accordance with the Contract Documents, based on on-site obervations and the data (Line 4 less Line 5 Total) comprising this application, the Construction Manager and Architect certify to the 7. LESS PREVIOUS CERTIFICATES FOR Owner that to the best of their knowledge, information and belief the Work has PAYMENT (Line 6 from prior Certificate) 275,678.34 progressed as indicated, the quality of the Work is in sccordance with the Contract 8. CURRENT PAYMENT DUE 116,541,39 Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED. 9. BALANCE TO FINISH, INCLUDING RETAINAGE \$ 237,177.21 (Line 3 less Line 6) **AMOUNT CERTIFIED** CHANGE ORDER SUMMARY **ADDITIONS** DEDUCTIONS (Attach explanation if amount certified differs from the amount applied for. Initial all Total changes approved in previous months by Owner figures on this Application and on the Continuation Sheet that changed to conform Total approved this Month to the amount certified.) TOTALS \$ CONSTRUCTION MANAGER: -NET CHANGES by Change Order By: Dalton Jac 11/6/2025 Date: ARCHITECT: 11/10/25 Date:

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

CONTINUATION SHEET

AIA DOCUMENT G703

PAGE 2 OF

#3

AIA Document G702, APPLICATION AND CERTIFICATION FOR PAYMENT, containing

APPLICATION NO: APPLICATION DATE:

10/2/2025

2

Contractor's signed certification is attached.

10/31/2025

In tabulations below, amounts are stated to the nearest dollar.

PERIOD TO:

Use Column I on Contracts where variable retainage for line items may apply.

ARCHITECT'S PROJECT NO:

Α	В		С		D		E		F		G			Н	I
ITEM NO.	DESCRIPTION OF WORK	S	3.44.1.10			COMPLETED		MATERIALS PRESENTLY		,	TOTAL % COMPLETED (G / C)		BALANCE		RETAINAGE
			VALUE		M PREVIOUS PPLICATION		THIS PERIOD	'	STORED		AND STORED	(G / C)		TO FINISH (C-G)	(IF VARIABLE RATE)
					(D+E)			(NC	OT IN D OR E)		TO DATE (D+E+F)			(· - /	· · · · · -,
1	Intercommunications Materials	\$	47,899.41			\$	47,899.41			\$	47,899.41	100.00%	\$	pa	
2	Intercommunications Labor	\$	56,158.89	\$	14,039.65	\$	-			\$	14,039.65	25.00%	\$	42,119.24	
3	Sports Field Sound Sys Materials	\$	70,623.24			\$	-	\$	70,623.24	\$	70,623.24	100.00%	\$	-	
4	Sports Field Sound Sys Labor	\$	23,376.76			\$	2,337.68			\$	2,337.68	10.00%	\$	21,039.08	
5	Band Room Sound Materials	\$	15,531.11					\$	15,531.11			0.00%	\$	15,531.11	
6	Band Room Sound Labor	\$	9,676.43			\$	967.64			\$	967.64	10.00%	\$	8,708.79	
7	Intrustion Detection Materials	\$	26,784.21			\$	-			\$	-	0.00%	\$	26,784.21	
8	Intrustion Detection Labor	\$	9,946.60			\$	-			\$	-	0.00%	\$	9,946.60	
9	Voice/Data Sys Materials	\$	118,983.37			\$	5,949.17	\$	113,034.20	\$	118,983.37	100.00%	\$	-	
10	Voice/Data Sys Labor	\$	81,109.65	\$	12,166.45	\$	8,110.96			\$	20,277.41	25.00%	\$	60,832.24	
11	ootball Pressbox Voice Data Materials	\$	5,991.70			\$	1,497.93	\$	4,493.77	\$	5,991.70	100.00%			
12	Football Pressbox Voice Data Labor	\$	11,784.46			\$	1,767.67			\$	1,767.67	15.00%	\$	10,016.79	
13	Access Control Materials	\$	91,579.84			\$	45,789.92	\$	45,789.92	\$	91,579.84	100.00%	\$	-	
14		\$	44,420.16			\$	2,221.01			\$	2,221.01	5.00%	\$	42,199.15	
	GRAND TOTALS	\$	613,865.83	\$	26,206.10	\$	116,541.39	\$	249,472.24	\$	376,688.62	61.36%	\$	237,177.21	\$























EVIDENCE OF PROPERTY INSURANCE

DATE (MM/DD/YYYY) 6/20/2025

THIS EVIDENCE OF PROPERTY INSURANCE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE ADDITIONAL INTEREST NAMED BELOW. THIS EVIDENCE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND. EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS EVIDENCE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE ADDITIONAL INTEREST. PHONE (A/C, No, Ext): 314-523-8800 Zurich American Insurance Co. AssuredPartners of MO LLC 1299 Zurich Way 12645 Olive Blvd, Suite 300 Schaumburg, IL 60196 St Louis, MO 63141 E-MAIL ADDRESS FAX (A/C, No): 314-453-7555 CODE: SUB CODE: AGENCY CUSTOMER ID #: INSURED I OAN NUMBER POLICY NUMBER Everon, LLC CPP864309100 5630 Shepherdsville Rd Louisville KY 40228 FFFFCTIVE DATE **EXPIRATION DATE** CONTINUED UNTIL TERMINATED IF CHECKED 10/02/2024 10/02/2025 THIS REPLACES PRIOR EVIDENCE DATED: PROPERTY INFORMATION LOCATION/DESCRIPTION Stored materials located at 5630 Shepherdsville Rd Louisville, KY 40228; in the amount of \$371,401.19 THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS EVIDENCE OF PROPERTY INSURANCE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS. **COVERAGE INFORMATION** PERILS INSURED BASIC BROAD SPECIAL DEDUCTIBLE COVERAGE / PERILS / FORMS AMOUNT OF INSURANCE \$1,000,0000 \$25,000 \$25,000 \$5,000 Personal Property of Others In Transit **REMARKS (Including Special Conditions)** CANCELLATION SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. ADDITIONAL INTEREST NAME AND ADDRESS ADDITIONAL INSURED LENDER'S LOSS PAYABLE LOSS PAYEE MORTGAGEE LOAN # Elizabethtown IND School 219 Helm Street AUTHORIZED REPRESENTATIVE Elizabethtown, KY 42701



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY) 6/20/2025

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

and the mount which the results in give to the terminate method in how the	won on wo or on (o).						
PRODUCER	CONTACT NAME: AssuredPartners of MO LLC						
AssuredPartners of MO LLC 12645 Olive Blvd, Suite 300 St Louis MO 63141 NSURED Everon, LLC 5630 Shepherdsville Rd Louisville, KY 40228	PHONE (A/C, No, Ext): 314-523-8800 FAX (A/C, No): 314-45	3-7555					
	E-MAIL ADDRESS: EveronCOI@assuredpartners.com						
	INSURER(S) AFFORDING COVERAGE	NAIC#					
	INSURER A: Old Republic Insurance Company	24147					
NSURED ADTCOM	INSURER B : ACE Property & Casualty Insurance Co	20699					
Everon, LLC	INSURER C: HDI Specialty Insurance Company	16131					
5630 Shepherdsville Rd	INSURER D: QBE Specialty Insurance Company	11515					
	INSURER E: Indian Harbor Insurance Company	36940					
	INSURER F:						

COVERAGES CERTIFICATE NUMBER: 195435124 REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR		TYPE OF INSURANCE	ADDL	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMIT	S
Α	Х	COMMERCIAL GENERAL LIABILITY	IIIOD	11112	MWZY31801724	10/2/2024	10/2/2025	EACH OCCURRENCE	\$ 1,000,000
С		CLAIMS-MADE X OCCUR			XLXD6212301S	10/2/2024	10/2/2025	DAMAGE TO RENTED PREMISES (Ea occurrence)	\$1,000,000
								MED EXP (Any one person)	\$ 10,000
								PERSONAL & ADV INJURY	\$1,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:							GENERAL AGGREGATE	\$3,000,000
	POLICY X PRO- JECT LOC							PRODUCTS - COMP/OP AGG	\$3,000,000
		OTHER:						Excess GL	\$3,000,000 occ/ag
A	AUT	OMOBILE LIABILITY			MWTB31801624	10/2/2024	10/2/2025	COMBINED SINGLE LIMIT (Ea accident)	\$3,000,000
D	X ANY AUTO				140002059	10/2/2024	10/2/2025	BODILY INJURY (Per person)	\$
		OWNED SCHEDULED AUTOS ONLY						BODILY INJURY (Per accident)	\$
		HIRED NON-OWNED AUTOS ONLY AUTOS ONLY						PROPERTY DAMAGE (Per accident)	\$
								Excess Auto	\$2,000,000 Agg
В	Х	UMBRELLA LIAB X OCCUR			XOOG47427927002	10/2/2024	10/2/2025	EACH OCCURRENCE	\$ 10,000,000
	EXCESS LIAB CLAIMS-MADE							AGGREGATE	\$ 10,000,000
		DED RETENTION\$							\$
Α		RKERS COMPENSATION EMPLOYERS' LIABILITY			MWC31801524	10/2/2024	10/2/2025	X PER OTH- STATUTE ER	
	ANY	PROPRIETOR/PARTNER/EXECUTIVE N	N/A					E.L. EACH ACCIDENT	\$2,000,000
	(Mar	ndatory in NH)	,					E.L. DISEASE - EA EMPLOYEE	\$ 2,000,000
	If yes	s, describe under CRIPTION OF OPERATIONS below						E.L. DISEASE - POLICY LIMIT	\$2,000,000
E	Erro	rs & Omissions			MTP9046829	10/2/2024	10/2/2025	Each Claim Aggregate	10,000,000 10,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Certificate holder, Owner and any other parties as required by written contract are included as Additional Insured. See attached page for automatically included coverage extensions.

Advanced Electrical Systems 3312 Gilmore Industrial Blvd, Louisville, KY 40213 is included as additional insured where required by written contract.

CERTIFICATE HOLDER	CANCELLATION
Elizabethtown IND School	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.
219 Helm Street Elizabethtown KY 42701	AUTHORIZED REPRESENTATIVE

AGENCY CUSTOMER ID:	
LOC #:	



ADDITIONAL REMARKS SCHEDULE

Page 1 of

AGENCY		NAMED INSURED	
AssuredPartners of Missouri, LLC		See Page 1	
POLICY NUMBER			
See Page 1			
CARRIER	NAIC CODE		
See Page 1	See Page 1	EFFECTIVE DATE:	See Page 1

ADDITIONAL REMARKS

THIS ADDITIONAL REMARKS FORM IS A SCHEDULE TO ACORD FORM,

FORM NUMBER: 25 FORM TITLE: Certificate of Liability Insurance

General Liability

- Designated Construction Project(s) General Aggregate Limit per form No. CG2503 (05/09)
- Additional Insured Owners, Lessees or Contractors, where required by written contract per form No. CG2010 (12/19)
- Additional Insured Owners, Lessees or Contractors Completed Operations, where required by written contract per form No. CG2037 (12/19)
- Additional Insured Managers or Lessors of Premises, where required by written contract per form No. CG2011 (12/19)
- Additional Insured Vendor, where required by written contract per form No. CG2044 (12/19)
- Additional Insured Designated Person or Organization, where required by written contract per form No. CG2026 (12/19)
- Additional Insured Lessor of Leased Equipment, where required by written contract per form No. CG2034 (12/19)
- Waiver of Subrogation, where required by written contract per form No. CG2453 (12/19)
- Primary & Non-Contributory, where required by written contract per form No. CG2001 (12/19)
- 30 Day Notice of Cancellation, where required by written contract per form No. PIL029 (10/10)

Auto Liability

- Additional Insured, where required by written contract per form No. PCA048 (09/19)
- Lessor Additional Insured and Loss Payee, where required by written contract per form No. CA2001 (11/20)
- Waiver of Subrogation, where required by written contract per form No. CA0443 (11/20)
- Primary & Non-Contributory, where required by written contract per form No. PCA048 (09/19)
- 30 Day Notice of Cancellation, where required by written contract per form No. PIL029 (10/10)

Workers Compensation / Employers Liability

- · Employers Liability is included for OH and WA
- Waiver of Subrogation, where required by written contract per form No. WC000313, except
 - o California WC040306 (04/84)
 - o Texas WC420304B (06/14)
 - o Utah WC430305
- 30 Day Notice of Cancellation, where required by written contract

\$2M Excess Auto Liability

- Subject to the policy terms & conditions, coverage is follow form and in addition to the scheduled underlying policy:
 - o Auto Liability

\$3M Excess General Liability

- Subject to the policy terms & conditions, coverage is follow form and in addition to the scheduled underlying policy:
 - o General Liability

Umbrella Liability

- Primary & Non-Contributory, where required by written contract per form No. XS-38039 (05/13)
- Subject to the policy terms & conditions, coverage is follow form and in addition to the scheduled underlying policies:
 - o General Liability
 - o Auto Liability
 - o Employers Liability
 - o \$2M Excess Auto Liability
 - o \$3M Excess General Liability

IL 10 (12/06) OLD REPUBLIC INSURANCE COMPANY

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

NOTICE OF CANCELLATION TO CERTIFICATE HOLDERS

This endorsement modifies the notice of cancellation of insurance provided hereunder by adding the following:

- A. In the event this policy is cancelled for any permissible reason, other than for nonpayment of premium, we shall endeavor to provide advance written notice of cancellation to certificate holders set out in the schedule on file with the Company, after notifying the first Named Insured of such cancellation. Notice of cancellation to certificate holders may be made by any commercially reasonable means, including mail, electronic mail, facsimile transmission or courier service.
- **B.** This advance written notification of a cancellation of coverage is intended as a courtesy only. Our failure to provide such advance written notification will not extend the policy cancellation date, nor negate cancellation of the policy.

All other terms and conditions of this policy remain unchanged.

PIL 029 10 10

IL 10 (12/06) OLD REPUBLIC INSURANCE COMPANY

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

ADDITIONAL INSURED AND PRIMARY AND NON-CONTRIBUTORY ENDORSEMENT

This endorsement modifies insurance provided under the following:

BUSINESS AUTO COVERAGE FORM MOTOR CARRIER COVERAGE FORM

SCHEDULE

Designated Person(s) or Organization(s):

All persons or organizations where required by written contract or agreement.

- A. SECTION II COVERED AUTOS LIABILITY COVERAGE, paragraph 1. Who Is An Insured is amended to include the person(s) or organization(s) shown in the above Schedule as an additional "insured", but only with respect to "accidents" arising out of your work while being performed for such person(s) or organization(s).
- **B.** The following is added to the **Other Insurance** Condition in the Business Auto Coverage Form and the **Other Insurance Primary And Excess Insurance Provisions** in the Motor Carrier Coverage Form and supersedes any provision to the contrary:

This policy's Covered Autos Liability Coverage is primary to and will not seek contribution from any other insurance available to the "insured" person(s) or organization(s) shown in the above Schedule provided that:

- 1. Such "insured" is a Named Insured under such other insurance; and
- 2. You have agreed in writing in a contract or agreement that this insurance would be primary and would not seek contribution from any other insurance available to such "insured".

10/02/24 - 10/02/25

PCA 048 09 19 Page 1 of 1

Includes copyrighted material of Insurance Services Office, Inc., with its permission.

MWZY 318017 24 Everon, LLC

WAIVER OF TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US (WAIVER OF SUBROGATION) – AUTOMATIC WHEN REQUIRED BY WRITTEN CONTRACT OR AGREEMENT

This endorsement modifies insurance provided under the following:

AUTO DEALERS COVERAGE FORM BUSINESS AUTO COVERAGE FORM MOTOR CARRIER COVERAGE FORM

With respect to coverage provided by this endorsement, the provisions of the Coverage Form apply unless modified by the endorsement.

The Transfer Of Rights Of Recovery Against Others

To Us Condition does not apply to any person(s) or organization(s) for whom you are required to waive subrogation with respect to the coverage provided under this Coverage Form, but only to the extent that subrogation is waived:

- **A.** Under a written contact or agreement with such person(s) or organization(s); and
- B. Prior to the "accident" or the "loss."

ADDITIONAL INSURED – OWNERS, LESSEES OR CONTRACTORS – SCHEDULED PERSON OR ORGANIZATION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s)	Location(s) Of Covered Operations
Any Person(s) or Organization(s) whom you have agreed to include as an Additional Insured under a Written Contract, provided such Contract was executed prior to the date of loss.	All Locations where you perform work for such Additional Insured pursuant to any such Written Contract.
Information required to complete this Schedule, if not sho	wn above, will be shown in the Declarations.

- A. Section II Who Is An Insured is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury", "property damage" or "personal and advertising injury" caused, in whole or in part, by:
 - 1. Your acts or omissions; or
 - The acts or omissions of those acting on your behalf;

in the performance of your ongoing operations for the additional insured(s) at the location(s) designated above.

However:

- 1. The insurance afforded to such additional insured only applies to the extent permitted by law; and
- 2. If coverage provided to the additional insured is required by a contract or agreement, the insurance afforded to such additional insured will not be broader than that which you are required by the contract or agreement to provide for such additional insured.

B. With respect to the insurance afforded to these additional insureds, the following additional exclusions apply:

This insurance does not apply to "bodily injury" or "property damage" occurring after:

- All work, including materials, parts or equipment furnished in connection with such work, on the project (other than service, maintenance or repairs) to be performed by or on behalf of the additional insured(s) at the location of the covered operations has been completed; or
- 2. That portion of "your work" out of which the injury or damage arises has been put to its intended use by any person or organization other than another contractor or subcontractor engaged in performing operations for a principal as a part of the same project.

CG 20 10 12 19 © Insurance Serv

- **C.** With respect to the insurance afforded to these additional insureds, the following is added to **Section III Limits Of Insurance:**
 - If coverage provided to the additional insured is required by a contract or agreement, the most we will pay on behalf of the additional insured is the amount of insurance:
 - 1. Required by the contract or agreement; or

Available under the applicable limits of insurance;

whichever is less.

This endorsement shall not increase the applicable limits of insurance.

10/02/24- 10/02/25

MWZY 318017 24

ADDITIONAL INSURED – OWNERS, LESSEES OR CONTRACTORS – COMPLETED OPERATIONS

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

SCHEDULE

Name Of Additional Insured Person(s) Or Organization(s)	Location And Description Of Completed Operations
Any Person(s) or Organization(s) whom you have agreed to include as an Additional Insured under a Written Contract, provided such Contract was executed prior to the date of loss.	All Locations where you perform work for such Additional Insured pursuant to any such Written Contract.
Information required to complete this Schedule, if not sho	own above, will be shown in the Declarations

A. Section II – Who Is An Insured is amended to include as an additional insured the person(s) or organization(s) shown in the Schedule, but only with respect to liability for "bodily injury" or "property damage" caused, in whole or in part, by "your work" at the location designated and described in the Schedule of this endorsement performed for that additional insured and included in the "products-completed operations hazard".

However:

- The insurance afforded to such additional insured only applies to the extent permitted by law; and
- 2. If coverage provided to the additional insured is required by a contract or agreement, the insurance afforded to such additional insured will not be broader than that which you are required by the contract or agreement to provide for such additional insured.

B. With respect to the insurance afforded to these additional insureds, the following is added to **Section III – Limits Of Insurance:**

If coverage provided to the additional insured is required by a contract or agreement, the most we will pay on behalf of the additional insured is the amount of insurance:

- 1. Required by the contract or agreement; or
- 2. Available under the applicable limits of insurance:

whichever is less.

This endorsement shall not increase the applicable limits of insurance.

IL 10 (12/06) OLD REPUBLIC INSURANCE COMPANY

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

NOTICE OF CANCELLATION TO CERTIFICATE HOLDERS

This endorsement modifies the notice of cancellation of insurance provided hereunder by adding the following:

- A. In the event this policy is cancelled for any permissible reason, other than for nonpayment of premium, we shall endeavor to provide advance written notice of cancellation to certificate holders set out in the schedule on file with the Company, after notifying the first Named Insured of such cancellation. Notice of cancellation to certificate holders may be made by any commercially reasonable means, including mail, electronic mail, facsimile transmission or courier service.
- **B.** This advance written notification of a cancellation of coverage is intended as a courtesy only. Our failure to provide such advance written notification will not extend the policy cancellation date, nor negate cancellation of the policy.

All other terms and conditions of this policy remain unchanged.

PIL 029 10 10

Designated Construction Project(s)

THIS ENDORSEMENT CHANGES THE POLICY. PLEASE READ IT CAREFULLY.

DESIGNATED CONSTRUCTION PROJECT(S) GENERAL AGGREGATE LIMIT

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART

SCHEDULE

The projects as specified in the written contracts or agreements
Information required to complete this Schedule, if not shown above, will be shown in the Declarations.

- A. For all sums which the insured becomes legally obligated to pay as damages caused by "occurrences" under Section I Coverage A, and for all medical expenses caused by accidents under Section I Coverage C, which can be attributed only to ongoing operations at a single designated construction project shown in the Schedule above:
 - 1. A separate Designated Construction Project General Aggregate Limit applies to each designated construction project, and that limit is equal to the amount of the General Aggregate Limit shown in the Declarations.
 - 2. The Designated Construction Project General Aggregate Limit is the most we will pay for the sum of all damages under Coverage A, except damages because of "bodily injury" or "property damage" included in the "products-completed operations hazard", and for medical expenses under Coverage C regardless of the number of:
 - a. Insureds;
 - b. Claims made or "suits" brought; or
 - **c.** Persons or organizations making claims or bringing "suits".

- 3. Any payments made under Coverage A for damages or under Coverage C for medical expenses shall reduce the Designated Construction Project General Aggregate Limit for that designated construction project. Such payments shall not reduce the General Aggregate Limit shown in the Declarations nor shall they reduce any other Designated Construction Project General Aggregate Limit for any other designated construction project shown in the Schedule above.
- 4. The limits shown in the Declarations for Each Occurrence, Damage To Premises Rented To You and Medical Expense continue to apply. However, instead of being subject to the General Aggregate Limit shown in the Declarations, such limits will be subject to the applicable Designated Construction Project General Aggregate Limit.

CG 25 03 05 09

- B. For all sums which the insured becomes legally obligated to pay as damages caused by "occurrences" under Section I Coverage A, and for all medical expenses caused by accidents under Section I Coverage C, which cannot be attributed only to ongoing operations at a single designated construction project shown in the Schedule above:
 - Any payments made under Coverage A for damages or under Coverage C for medical expenses shall reduce the amount available under the General Aggregate Limit or the Products-completed Operations Aggregate Limit, whichever is applicable; and
 - Such payments shall not reduce any Designated Construction Project General Aggregate Limit.
- C. When coverage for liability arising out of the "products-completed operations hazard" is provided, any payments for damages because of "bodily injury" or "property damage" included in the "products-completed operations hazard" will reduce the Products-completed Operations Aggregate Limit, and not reduce the General Aggregate Limit nor the Designated Construction Project General Aggregate Limit.
- D. If the applicable designated construction project has been abandoned, delayed, or abandoned and then restarted, or if the authorized contracting parties deviate from plans, blueprints, designs, specifications or timetables, the project will still be deemed to be the same construction project.
- **E.** The provisions of Section **III** Limits Of Insurance not otherwise modified by this endorsement shall continue to apply as stipulated.

PRIMARY AND NONCONTRIBUTORY – OTHER INSURANCE CONDITION

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART LIQUOR LIABILITY COVERAGE PART PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART

The following is added to the **Other Insurance** Condition and supersedes any provision to the contrary:

Primary And Noncontributory Insurance

This insurance is primary to and will not seek contribution from any other insurance available to an additional insured under your policy provided that:

(1) The additional insured is a Named Insured under such other insurance; and

(2) You have agreed in writing in a contract or agreement that this insurance would be primary and would not seek contribution from any other insurance available to the additional insured.

WAIVER OF TRANSFER OF RIGHTS OF RECOVERY AGAINST OTHERS TO US (WAIVER OF SUBROGATION) – AUTOMATIC

This endorsement modifies insurance provided under the following:

COMMERCIAL GENERAL LIABILITY COVERAGE PART
ELECTRONIC DATA LIABILITY COVERAGE PART
LIQUOR LIABILITY COVERAGE PART
POLLUTION LIABILITY COVERAGE PART DESIGNATED SITES
POLLUTION LIABILITY LIMITED COVERAGE PART DESIGNATED SITES
PRODUCTS/COMPLETED OPERATIONS LIABILITY COVERAGE PART
RAILROAD PROTECTIVE LIABILITY COVERAGE PART
UNDERGROUND STORAGE TANK POLICY DESIGNATED TANKS

The following is added to Paragraph 8. Transfer Of Rights Of Recovery Against Others To Us of Section IV – Conditions:

We waive any right of recovery against any person or organization, because of any payment we make under this Coverage Part, to whom the insured has waived its right of recovery in a written contract or agreement. Such waiver by us applies only to the extent that the insured has waived its right of recovery against such person or organization prior to loss.

OLD REPUBLIC INSURANCE COMPANY

WORKERS' COMPENSATION AND EMPLOYERS' LIABILITY POLICY

NOTICE OF CANCELATION TO CERTIFICATE HOLDERS ENDORSEMENT

This endorsement modifies the notice of cancelation of insurance provided hereunder by adding the following:

- A. In the event this policy is canceled for any permissible reason, other than for nonpayment of premium, we shall endeavor to provide advance written notice of cancelation to certificate holders set out in the schedule on file with the Company, after notifying the Insured first named in item 1 of the Information Page of such cancelation. Notice of cancelation to certificate holders may be made by any commercially reasonable means, including mail, electronic mail, facsimile transmission or courier service.
- B. This advance written notification of a cancelation of coverage is intended as a courtesy only. Our failure to provide such advance written notification will not extend the policy cancelation date, nor negate cancelation of the policy.

All other terms and conditions of this policy remain unchanged.

WORKERS' COMPENSATION AND EMPLOYERS' LIABILITY INSURANCE POLICY

WC 124 (4-84)

WC 00 03 13

WAIVER OF OUR RIGHT TO RECOVER FROM OTHERS ENDORSEMENT

This endorsement changes the policy to which it is attached effective on the inception date of the policy unless a different date is indicated below.

(The following "attaching clause" need be completed only when this endorsement is issued subsequent to preparation of the policy.)

This endorsement, effective on

10/02/2024

at 12:01 A.M. standard time, forms a part of

(DATE)

Policy No. MWC31801524

of the

Old Republic Insurance Company
(NAME OF INSURANCE COMPANY)

issued to Everon, LLC

Premium \$ N/A

Authorized Representative

We have the right to recover our payments from anyone liable for an injury covered by this policy. We will not enforce our right against the person or organization named in the Schedule. This agreement applies only to the extent that you perform work under a written contract that requires you to obtain this agreement from us.*

This agreement shall not operate directly or indirectly to benefit any one not named in the Schedule.

Schedule

ANY PERSON OR ORGANIZATION AGAINST WHOM YOU HAVE AGREED TO WAIVE YOUR RIGHTS OF RECOVERY IN A WRITTEN CONTRACT, PROVIDED SUCH CONTRACT IS EXECUTED PRIOR TO THE DATE OF LOSS.

(THIS FORM IS NOT APPLICABLE IN: CA, KY, NJ, TX, UT)

^{*}Typist: strike out third sentence if inapplicable.













AES PA 07 - October 2025-250150

Final Audit Report

2025-10-27

Created:

2025-10-27

By:

Tracey Breitenstein (traceyb@aeslou.com)

Status:

Signed

Transaction ID:

CBJCHBCAABAAb2D8XTNKk\$t6F-Frt_S0Z_KlylNKBzdt

"AES PA 07 - October 2025-250150" History

- Document created by Tracey Breitenstein (traceyb@aeslou.com) 2025-10-27 - 5:43:03 PM GMT
- Document emailed to Lee Saettel (lees@aeslou.com) for signature 2025-10-27 5:43:08 PM GMT
- Email viewed by Lee Saettel (lees@aeslou.com)
 2025-10-27 5:59:01 PM GMT
- Document e-signed by Lee Saettel (lees@aeslou.com)
 Signature Date: 2025-10-27 5:59:50 PM GMT Time Source: server
- Agreement completed.
 2025-10-27 5:59:50 PM GMT

APPLICATION AND CERTIFICATE FOR PAYMENT

TO(OWNER):	ELIZABETHTOWN INDEPENDENT DISTRICT BOARD OF EDUCATION	PROJECT:	TK STONE MIDDLE SCHOOL ELIZABETHTOWN, KY		APPLICATION NO PERIOD FROM TO:	: 10/01/25	A	
ATTENTION:		CONTRACT FOR:	Construction Management Services	_ CONTRACT DATE:		8	ALLIANCE CORPORATION uilders & Manage	
CONTRACTORS	S APPLICATION FOR PAYMENT			Application is made for Payment as shown with the Contract Continuation Sheet attac				
CHANGE ORDE		•		The present status of the this Contract is a				
Change Orders a previous months		DEDUCTIONS		ORIGINAL CONTRACT SUM		_	\$814,101.00	
TOTAL				Net change by Change Orders		_	\$0.00	
Approved this month			•	CONTRACT SUM TO DATE		_	\$814,101.00	
				TOTAL COMPLETED & STORED TO DAT	 ΓE (Sheet 2)	· ·····	\$261,375.40	
				RETAINAGE @ 5%		·	\$10,948.27	
				TOTAL EARNED LESS RETAINAGE		<u> </u>	\$250,427.13	
				LESS PREVIOUS CERTIFICATES (CONT	RACT ONLY)		\$224,914.52	
Net Change by C	Change Orders \$0.00	\$0.00	\$0.00	CURRENT PAYMENT DUE		· ·····	\$25,512.61	
	contractor certifies that to the best of his belief the Work covered by this Application							
has been comple amounts have be	eted and in accordance with the Contract Deen paid by him for Work for which previou	Oocuments, that all us Certificates for		Subscribed and sworn to before me this State of: KENTUCKY Notary Public:	day of	County of: BARREN		
Payment were issued and payments received from the Owner, and that curre payment shown herein is now due.			•	My Commission expires: 01/29/2028		County of: BARREN		
CONSTRUCTION	N MANAGER: <u>ALLIANCE CORPOR</u>	ATION						
Bv: Da	Iton Jackson	_{Date:} 1 1	1/5/2025					

#	JATION SHEET NO. 2 T APPLICATION NO. <u>Eight (</u> 8	K STONE MIDDLE SCHOOL		*E* COMPLETED	*F*	*G* TOTAL	*H*	* *
2 CONST 3 MONTH 4 5 6 7 8 9 10 11 12 13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 29 30 31 32 33 34 35	DESCRIPTION OF WORK	SCHEDULED VALUE	FROM PREV. APPLIC.(D+E)	THIS PERIOD	MATERIALS STORED (NOT IN D OR E)	& STORED D+E+F	% G/C	BALANCE TO FINISH C-G
36 37 38	OF WORK CONSTRUCTION SERVICES STRUCTION SERVICES THLY REIMBURSABLES	\$42,410.10 \$381,690.90 \$390,000.00	\$42,410.10 \$101,109.92 \$91,000.00	\$13,855.38 \$13,000.00	IN D OR E)		100% 30%	C-G \$0.00 \$266,725.60 \$286,000.00
39 40 TOTAL			 \$234,520.02	 \$26,855.38	\$0.00	 \$261,375.40		 \$552,725.60
