

Update on FCPS Construction / Renovation Projects

February 23, 2026

Rise STEM Academy for Girls



Rise STEM Academy for Girls




➤ Architect:	Ross Tarrant Architects
➤ General Contractor:	D.W. Wilburn, Inc.
➤ GC Contract Sum:	\$48,800,100.00
➤ Total Project Cost:	\$58,460,689.35
➤ Change Orders to Date (4):	\$682,270.19
➤ Scheduled Contract Completion Date:	June 2026
➤ % of Contract Completed:	79%
➤ Revised Completion Date per GC:	N/A
➤ Weekly Construction Updates:	www.fcps.net/risestem

Rise STEM Academy for Girls



- **Completed/Work in Progress:**
 - Above ceiling and lighting installation work.
 - Floor prep for more terrazzo.
 - Ceramic tile installation.
 - Elevator work.
 - Mechanical rooms.
 - KU completed permanent power.

- **Upcoming Work/Look Ahead:**
 - Storm system work will continue.
 - Above ceiling work continues.
 - Gyp. board installation will continue.
 - Tile installation will continue.
 - Terrazzo installation will continue.
 - Mechanical room work will continue.
 - Metal panel installation will continue.

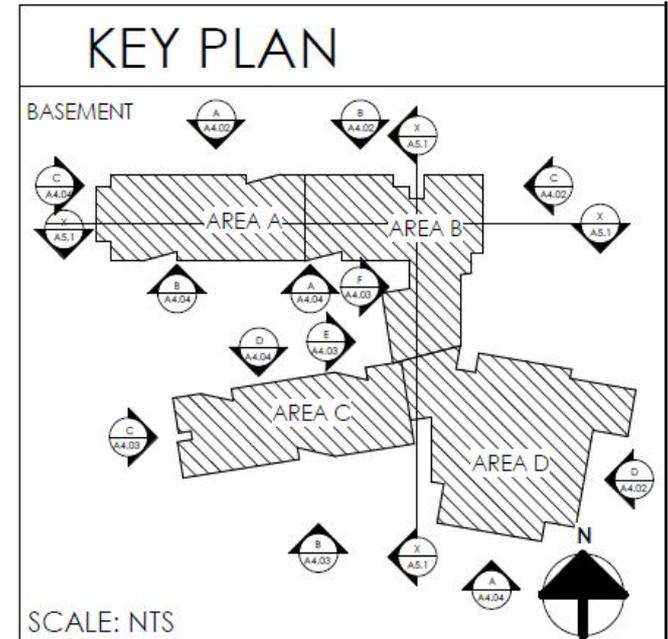

Rise STEM Academy for Girls



Paint and Terrazzo Work In Progress



Week Ending January 9, 2026

Rise STEM Academy for Girls



White Board Installation In Progress



Rise STEM Academy for Girls



Lighting Installation In Progress



Week Ending January 9, 2026

Rise STEM Academy for Girls



Acoustical Spray Foam Installation In Progress



Rise STEM Academy for Girls



Drywall Installation in Progress



Week Ending January 9, 2026

Rise STEM Academy for Girls



Exterior Window Shades Installation In Progress



Week Ending January 9, 2026

Rise STEM Academy for Girls



Metal Panel Wall Installation In Progress



Week Ending January 9, 2026

Rise STEM Academy for Girls



Spray Foam Insulation Work In Progress



Week Ending January 9, 2026

Henry Clay High (New)



Henry Clay High (New)




- Architect: Tate Hill Jacobs Architects
- General Contractor: D.W. Wilburn, Inc.
- GC Contract Sum: \$153,218,800.00
- Total Project Cost: \$178,900,227.60
- Change Orders to Date (3): \$791,550.89
- Scheduled Contract Completion Date: June 2028 (Building)
June 2029 (Site/Athletics)
- % of Contract Completed: 31%
- Revised Completion Date per GC: N/A
- Weekly Construction Updates: www.fcps.net/HCconstruction



Henry Clay High (New)

- **Completed/Work in Progress:**
 - Geothermal well field drilling at the south end of the site is complete.
 - KAWC installation of main waterline is complete.
 - ICF and CIP concrete formwork placing and pouring, & the installation of IFAs at ICF walls is in progress.
 - Laying of CMU walls and the installation of hollow metal frames is underway.
 - Under-slab plumbing/electrical and concrete slabs are in progress.
 - Steel erection is underway in areas A, B and C.
 - Area D hollowcore and joist erection is complete.
 - Above ceiling MEP installation is in progress at areas A, B & C.
 - Stair A installation is complete and Stair B installation is in progress.

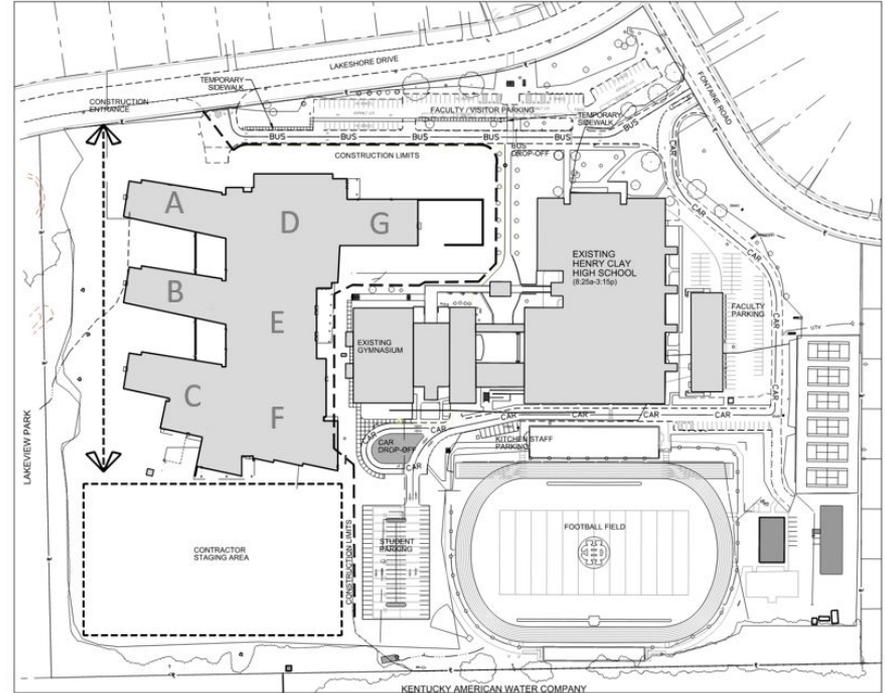


B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

Henry Clay High (New)



➤ Upcoming Work/Look Ahead:

- Continue hauling in fill materials and continue site grading.
- Continue sanitary piping and manholes.
- Continue with ICF and CIP concrete walls.
- Continue laying CMU walls.
- Continue with under-slab plumbing and electrical.
- Continue pouring concrete slabs on grade.
- Continue installing IFAs and hollow metal frames.
- Continue with steel erection.
- Continue with above ceiling MEP installation.
- Begin retaining wall construction.

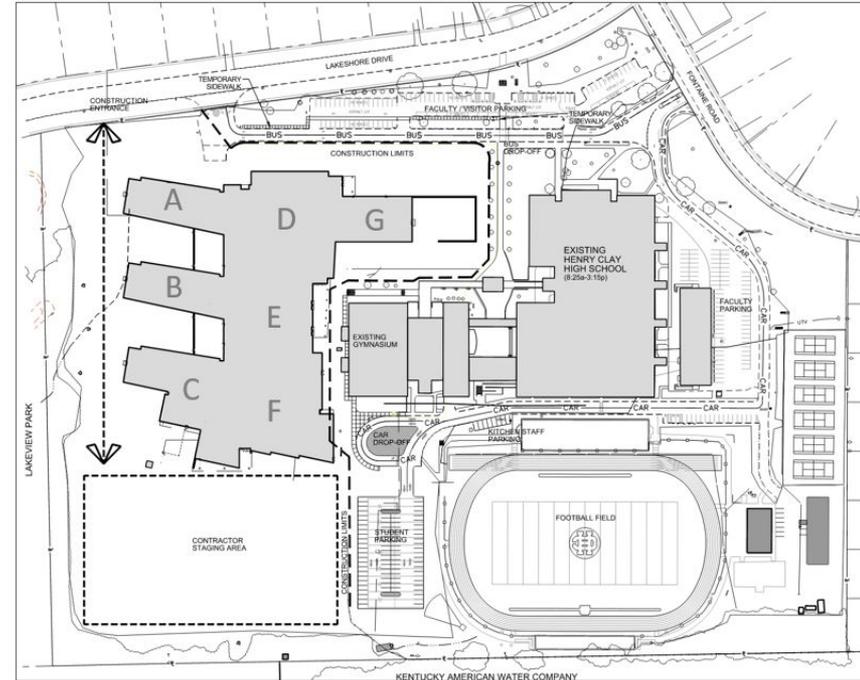

B PHASE 1 - BUILDING CONSTRUCTION CIRCULATION
SCALE: N.T.S.

Henry Clay High (New)

Area D (Storm Shelter): Steel Joist Erection Complete & Installation of Metal Decking in Progress



Henry Clay High (New)



Area D (Storm Shelter): Steel Joist Erection Complete & Installation of Metal Decking in Progress



Week Ending January 9, 2026

Henry Clay High (New)




Area B (Classroom Wing) at North-South Corridor: ICF, CMU and Hollow Metal Frame Installation



Week Ending January 9, 2026

Henry Clay High (New)

Area B (Classroom Wing): Stair B Installation in Progress

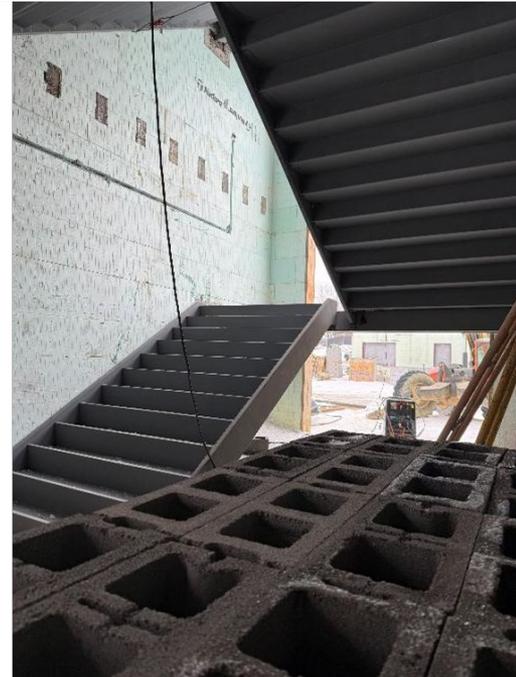

Henry Clay High (New)

Area B (Classroom Wing): Ductwork and Cable Tray Installation in Progress at Level 1





Henry Clay High (New)

Area C (Classroom Wing): Level 2 Steel Erection Complete; Cable Tray & Ductwork Installation



Week Ending January 9, 2026

Henry Clay High (New)



Area A (Classroom Wing): Level 2 Above Ceiling Mechanical, Electrical, and Plumbing



New Elementary on Greendale Rd



New Elementary on Greendale Rd



- Architect: Sherman Carter Barnhart Architects
- Construction Manager (CM): Codell Construction
- Construction Contract Cost: \$41,446,729.12
- Total Project Cost: \$50,569,587.60
- Change Orders to Date (7): \$54,942.00
- Scheduled Contract Completion Date: July 2027
- % of Contract Completed: 22.87%
- Revised Completion Date per CM: N/A
- Weekly Construction Updates: www.fcps.net/GreendaleES

New Elementary on Greendale Rd




➤ Completed/Work in Progress::

- The site was covered in snow and ice. Not all site items could be observed.
- Laying of interior CMU masonry is in progress in Women's 169 and Men's 170. The area has been tented to keep heat.
- A few locations of CMU appear to have been damaged from the cold temperature.
- Installation of above grade MEP is in progress.
- The retention pond is frozen over but appears to be operating properly. Water was not observed in the lower pond.
- Temporary electric is connected to the building.

➤ Upcoming Work/Look Ahead:

- Continue setting and filling the ICF forms.
- Continue placing concrete floor slabs.
- Continue laying of masonry in the kitchen area.
- Continue placement of the hollow core planks.

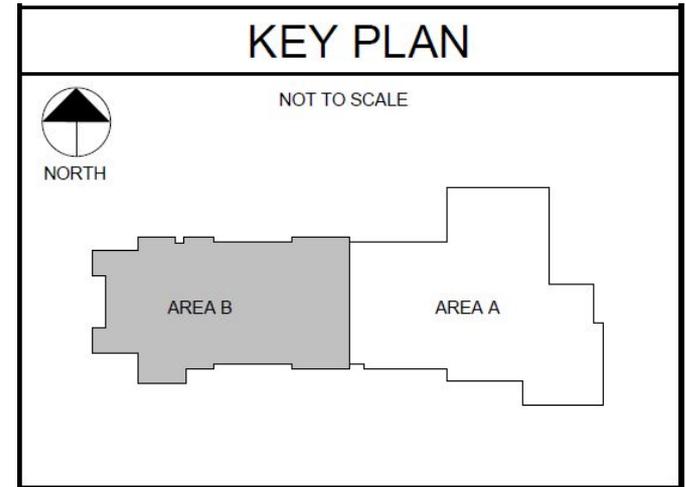

New Elementary on Greendale Rd




Snow Covered Site at the Geothermal



New Elementary on Greendale Rd



Laying of Interior CMU at Women's 169

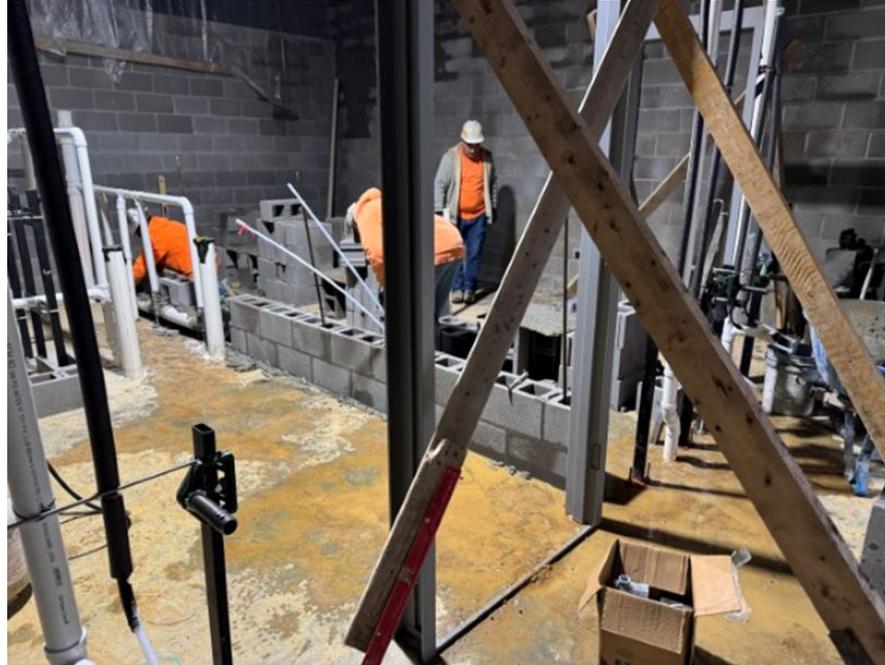

Week Ending January 9, 2026

New Elementary on Greendale Rd



Copper Piping Installation at Corridor C02



New Elementary on Greendale Rd



Plumbing Stub Ups in Restroom 170A



Week Ending January 9, 2026

New Elementary on Greendale Rd



Duct Openings are installed in the CMU Corridor Wall (C02)



New Elementary on Greendale Rd



Upper Retention Pond



New Elementary on Greendale Rd



Lower Retention Pond





Thank you!
