



Cecilia Valley Elementary



Construction Update

December 8, 2017

Original Construction Cost:	\$15,510,000.00
Present Construction Cost:	\$15,493,286.52 (Including Change Orders 1-10)

Original Completion Dates	
Substantial Completion:	September 1, 2017
Final Completion:	October 1, 2017

Anticipated Completion Dates	
Substantial Completion:	October 14, 2017 (Per Change Order 9)
Final Completion:	November 14, 2017 (Per Change Order 9)



Change Order Summary

<u>Change Order</u>	<u>Amount</u>	<u>Status</u>	<u>Rvsd. Contract Amount</u>
Change Order No. 01	\$3,765.00	BOE Approved	\$15,513,765.00
Change Order No. 02	\$0.00	BOE Approved	\$15,513,765.00
Change Order No. 03	\$3,839.00	BOE Approved	\$15,517,604.00
Change Order No. 04	\$33,737.00	BOE Approved	\$15,551,341.00
Change Order No. 05	(\$53,691.75)	BOE Approved	\$15,497,649.25
Change Order No. 06	(\$5,232.53)	BOE Approved	\$15,492,416.72
Change Order No. 07	\$7,768.00	BOE Approved	\$15,500,184.72
Change Order No. 08	(\$2,400.00)	BOE Approved	\$15,497,784.72
Change Order No. 09	(\$5,000.00)	BOE Approved	\$15,492,784.72
Change Order No. 10	\$501.80	BOE Approved	\$15,493,286.52

Summary

Schedule

Contract Substantial Completion is October 14, 2017.

Greg Potter (Isaac Tatum Construction) has indicated that the building will now be completed by November 27, 2017 for occupancy permit. John Stith has indicated that the school will be occupied December 2, 2017 and students will start classes in school on December 3, 2017.

Sherman Carter Barnhart has finalized all on site punch list reviews.



Image 1

Exterior Building Entry / Entry Canopy



Image 2

Entry Canopy looking South



Image 3

Building Exterior (Rear) / Gymnasium



Image 4

Rear Exterior Canopy / Media Center Beyond



Image 5

Rear Exterior Canopy



Image 6

Playground



Image 7

Exterior Building Entry



Image 8

Building Entry / Vestibule



Image 9

Entry / Reception

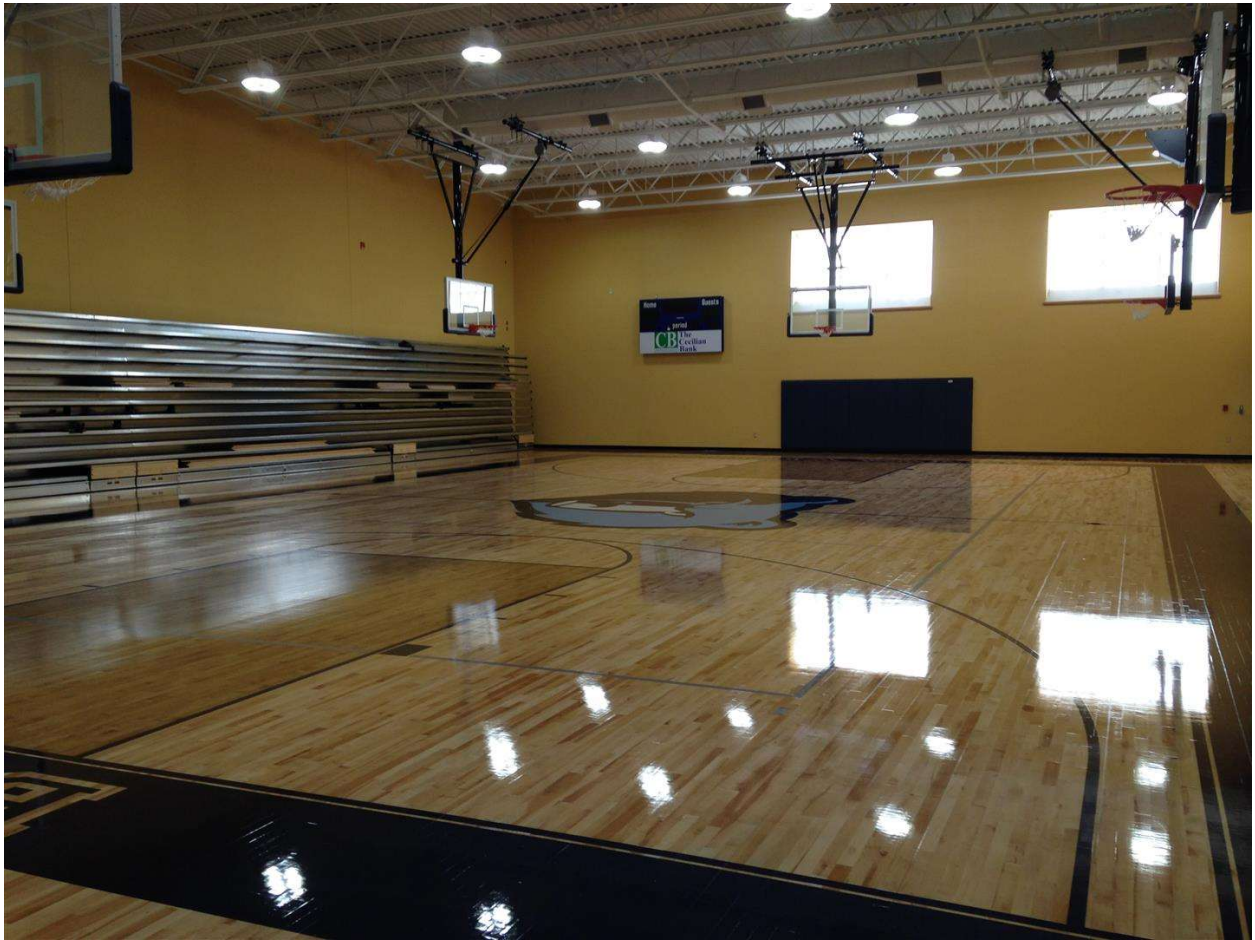


Image 10

Gymnasium



Image 11

Upper Lobby / Clerestory



Image 12

Restroom



Image 13

Media Center



Image 14

First floor corridor
