





Bullitt County Public Schools

1040 Highway 44 East
Shepherdsville, Kentucky 40165

502-869-8000
Fax 502-543-3608
www.bullittschools.org

MEMO:

TO: Mr. Jesse Bacon 

FROM: Bret Highley 

DATE: October 9, 2018

RE: Construction Update
Bullitt Lick Middle School Addition/Renovation BG 17-14

Please find the monthly construction update for Bullitt Lick Middle School as submitted by Cate Ward, Studio Kremer Architects.

If you have any questions, please call me at 502-921-3659.

Attachments:

- October Construction Update





CONSTRUCTION UPDATE

From October 2, 2018 Progress Meeting

Bullitt Lick Middle School – Renovation and Gym Addition
555 W Blue Lick Road
Shepherdsville, KY 40165

SKA #: 2016-86

BG #: 17-148

CONSTRUCTION SUMMARY

This construction summary shows photos of the building the day we had our bi-weekly progress meeting and conducted a punch walk through of the kitchen and ceilings above the 8th grade classrooms. The kitchen is up and running and staff have moved into the space. Kitchen punch list items included finish items and areas where staff have requested modifications to the equipment layout. The above ceiling space in the 8th grade classroom was in good shape with a few exceptions of adding more ceiling support cables as well as demolition of abandoned wiring. The ceiling subcontractor was on site that day to address the ceiling work as the A/E team noted it.


Exterior work to complete includes finishing the new brick cornice that replaced the metal fascia panels at the roof line – this work will continue around the eastern portion of the building. EH Construction's goal is to wrap up the roof abatement and recoating work by the end of October – the dry weather is helping them meet this goal. The exterior bus canopy will be painted and cleaned up as well.

Aside from work noted on the last punch list, Area B & C interior work is complete. Punch list items are being addressed by EH and their subcontractors while they continue to renovate the classrooms. You'll see on the phasing plan included with this memo that the first 8th grade classrooms are being turned over to the school after fall break. EH will continue phasing the classrooms until January. There will be five more classroom phases and EH expects to finish those every two to three weeks. The A/E team will plan to punch those classroom spaces after every progress meeting to keep on schedule and note any areas of repair prior to students and staff moving back in.

Photos included in this memo include rooms that have been renovated as well as in-progress renovated classroom images.

PHASING DIAGRAM & AREAS OF CONSTRUCTION

Areas noted in green are nearing completion or are complete. The areas currently under construction are noted in red. Yellow indicates areas left to complete.

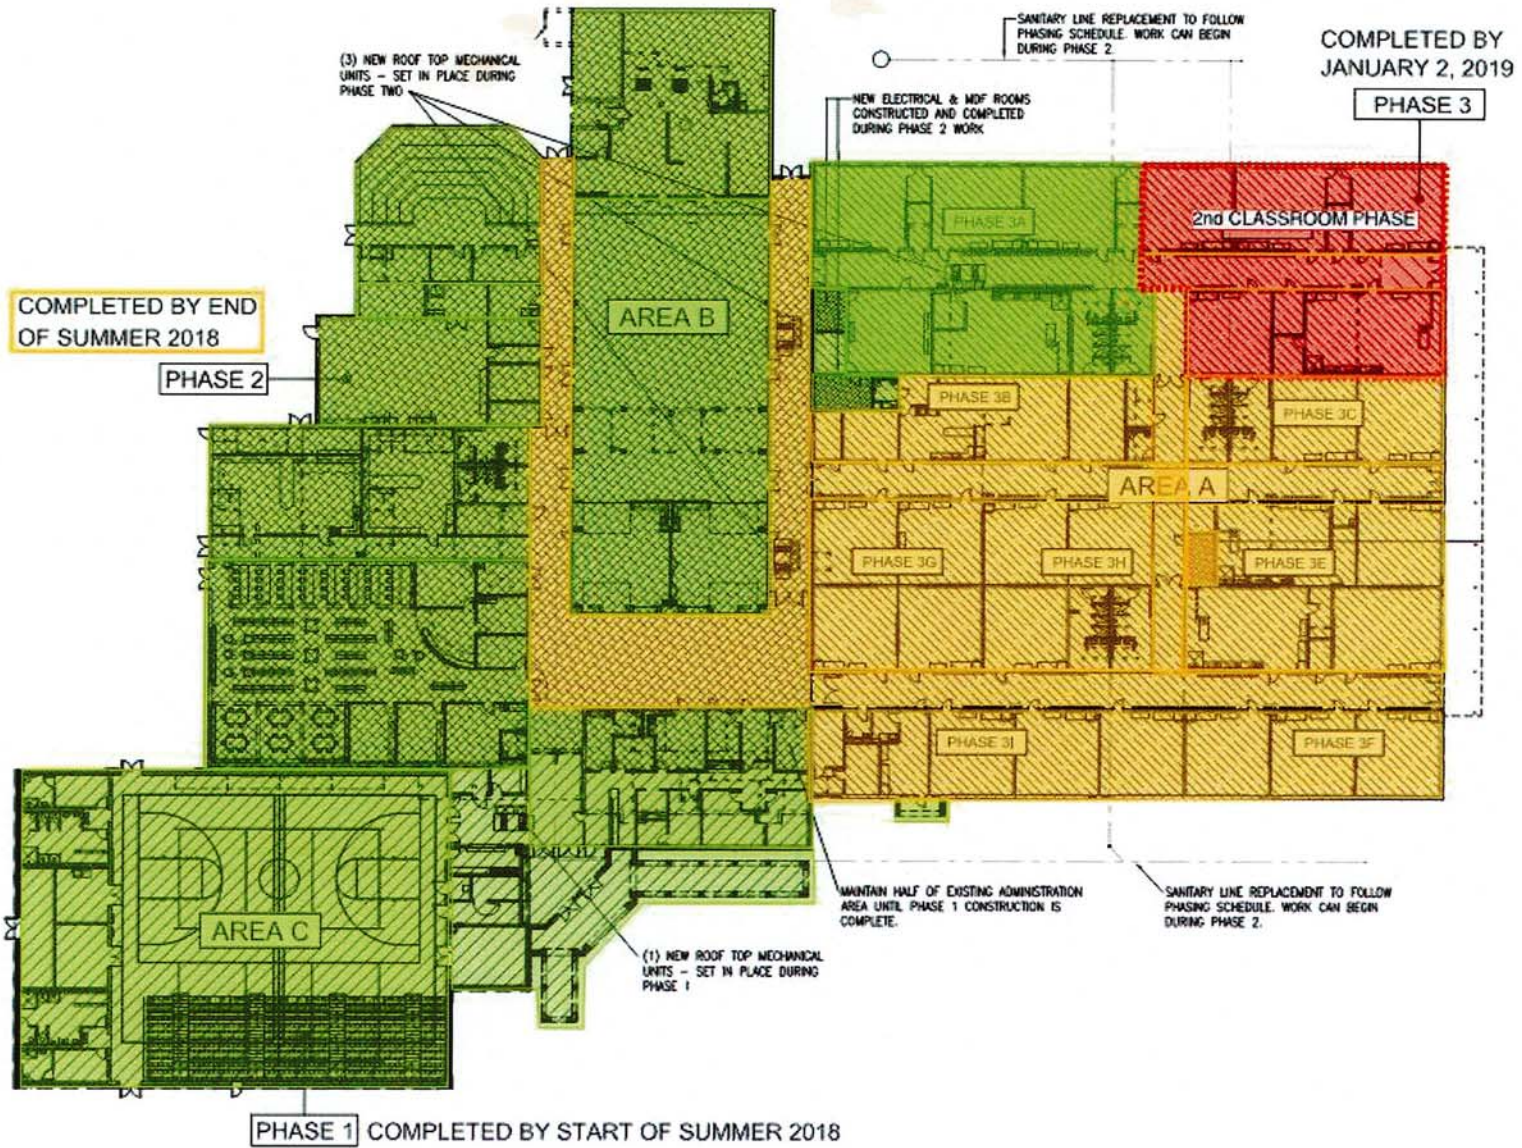

CONSTRUCTION PROGRESS PHOTOS




View of Exterior. (10-2-2018)



View of Exterior – New brick cornice work continues around remainder of the building. (10-2-2018)



View of renovated classroom in progress – Teacher's Desk and Student Charging Station. (10-2-2018)

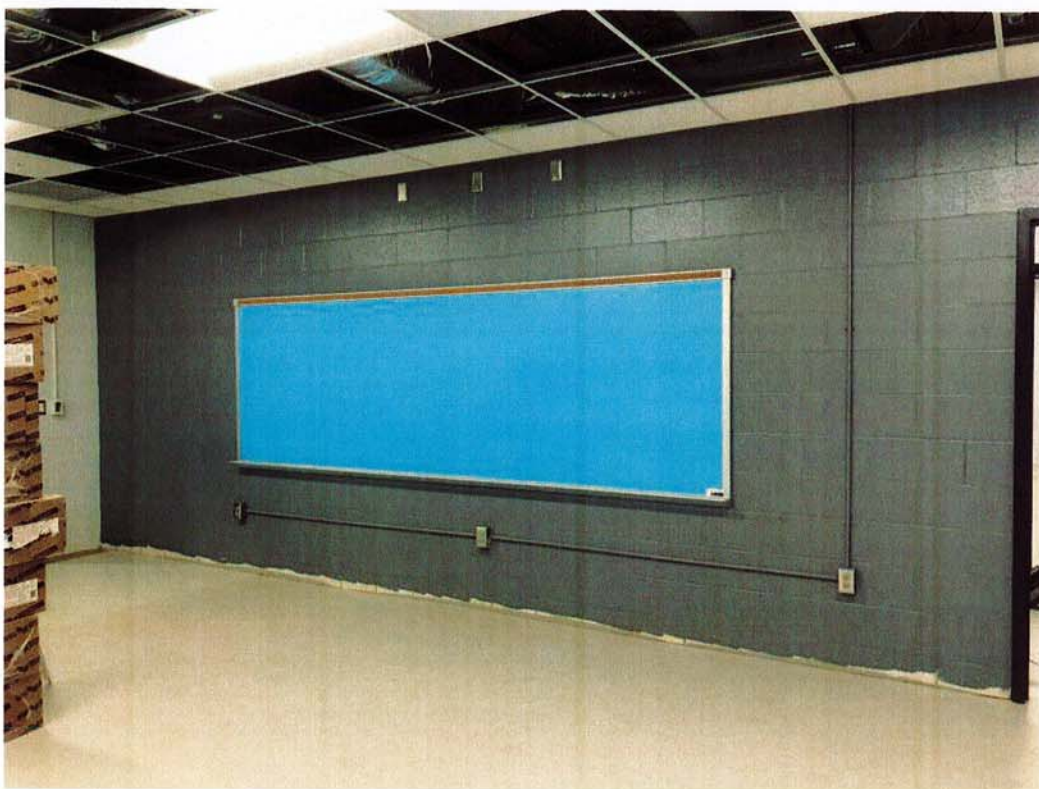

View of renovated classroom in progress – Teaching Wall. (10-2-2018)




Painting touch-ups in progress at Commons Space. (10-2-2018)



View of Commons Space. (10-2-2018)



View of Renovated Media Center. (10-2-2018)

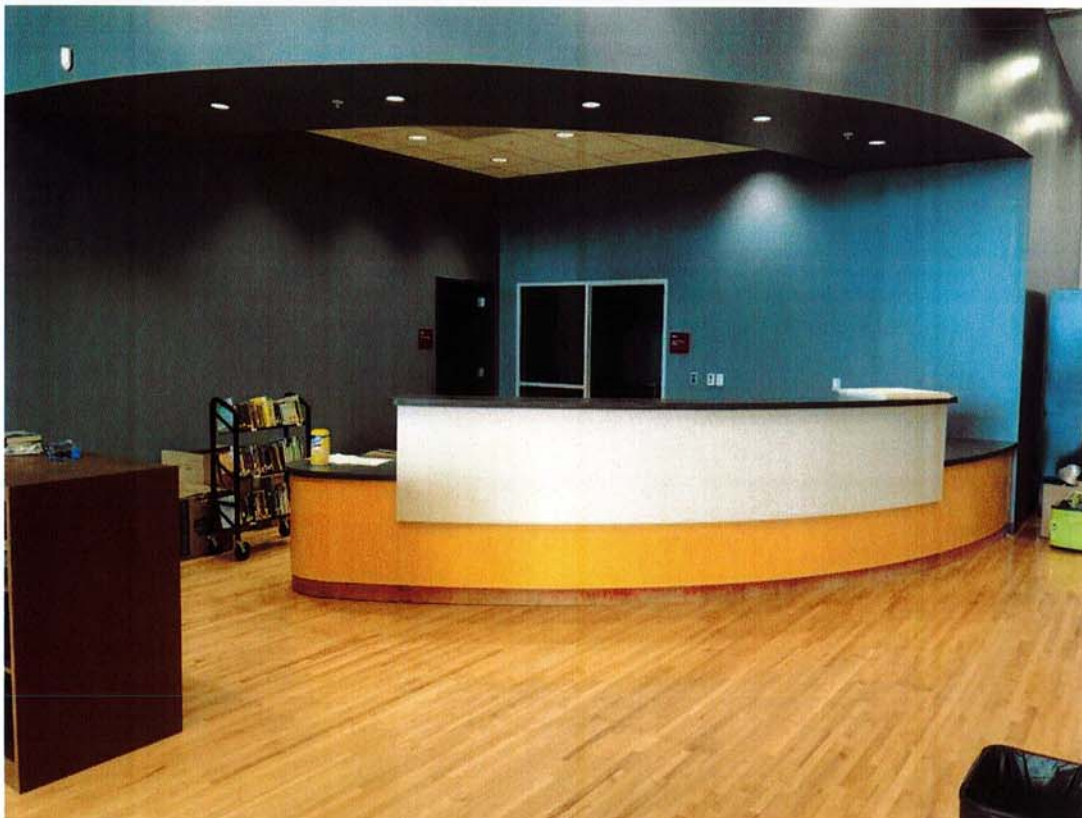

View of Renovated Media Center Check-Out Desk. (10-2-2018)




View of Renovated Art Room. (10-2-2018)



View of Renovated Art Room – Chromebook storage cubbies. (10-2-2018)



View of Renovated Cafeteria Serving Line. (10-2-2018)

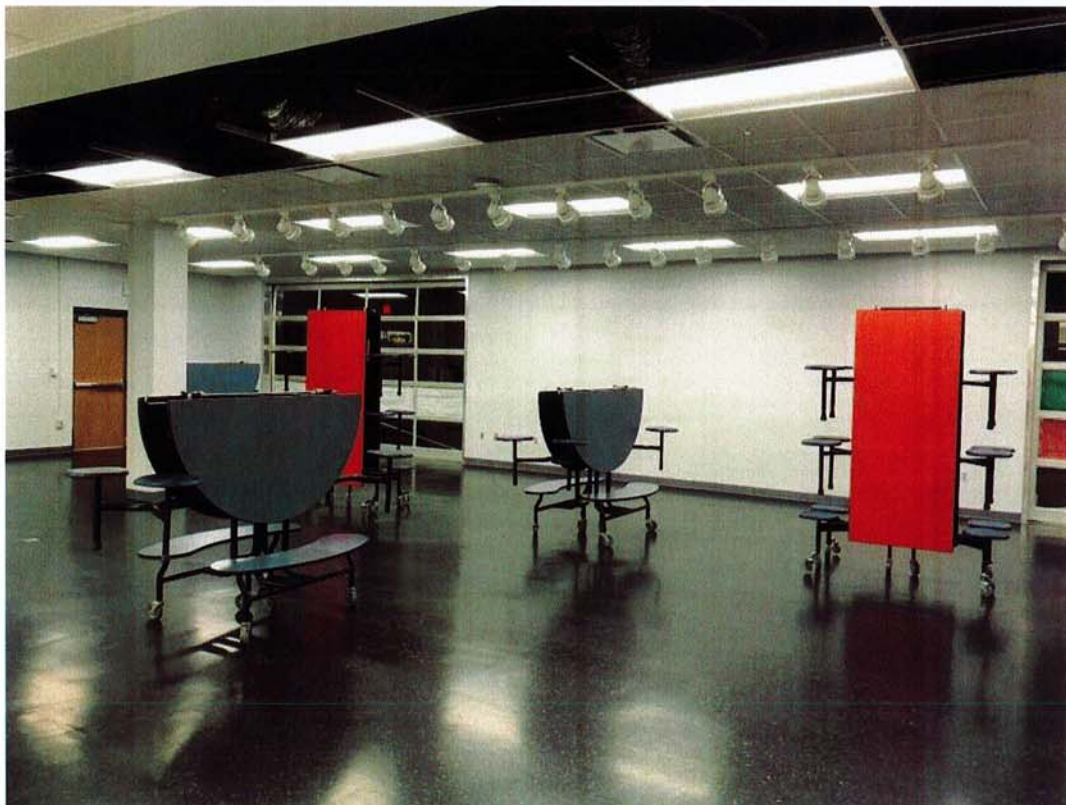

View of Renovated Cafeteria Presentation Area – Ceiling Work in Progress. (10-2-2018)



View of Renovated Band Room. (10-2-2018)
