




Bullitt County Public Schools

1040 Highway 44 East
Shepherdsville, Kentucky 40165

502-869-8000
Fax 502-543-3608
www.bullittschools.org

MEMO:

TO: Mr. Jesse Bacon 

FROM: Bret Highley

DATE: November 13, 2018

RE: Construction update: Bullitt Lick Middle School Addition/Renovation BG 17-14

Please find the monthly construction update for Bullitt Lick Middle School as submitted by Cate Ward, Studio Kremer Architects.

If you have any questions, please call me at 502-921-3659.

Attachments:

- November Construction Update





CONSTRUCTION UPDATE

From November 6th, 2018 Punch Walk Through & October 30th Progress Meeting

Bullitt Lick Middle School – Renovation and Gym Addition

555 W Blue Lick Road

Shepherdsville, KY 40165

SKA #: 2016-86

BG #: 17-148

CONSTRUCTION SUMMARY

This construction summary shows photos of the building the day we conducted a punch walk through of the 8th grade classrooms as well as work being done in the 7th grade corridor during our October 30th progress meeting.

The 8th grade corridor and adjacent classrooms are now fully occupied. The punch list contained items related to finishes, mostly painting, and wrapping up installation of casework components. EH Construction is currently working on the next classroom phase in the 7th grade corridor. Work to be completed in occupied areas of the school (Areas B & C) is being done during 2nd shift.


The exterior masonry work is now complete with the new brick cornice fully installed. EH Construction has roughly 5,000 square feet of new roofing left to install as of October 30th. The design team is on call to verify work has been completed on the roof during the month of November.

EH is currently working on the third classroom wing phase – they have three phases left to complete before January. EH is keeping to a two to three-week schedule on the phases because most of the infrastructural work was done during the summer which allows them to focus on the remaining selective demolition and installation of finishes at the classrooms and corridors. The floor slab moisture mitigation occurs concurrently with each classroom phase. The final classroom phase to be finished will be along the west side of the 7th grade corridor at the FMD and EBD classrooms – the school asked for these students not to be displaced during the rest of the fall semester. Work at these specialized classrooms is scheduled to be completed during Winter Break.

SKA and EH will be working through a final punch schedule for the remainder of the project. The substantial completion date is set for January 2nd, 2019.

PHASING DIAGRAM & AREAS OF CONSTRUCTION

Areas noted in green are nearing completion or are complete. The areas currently under construction are noted in red. Yellow indicates areas left to complete.

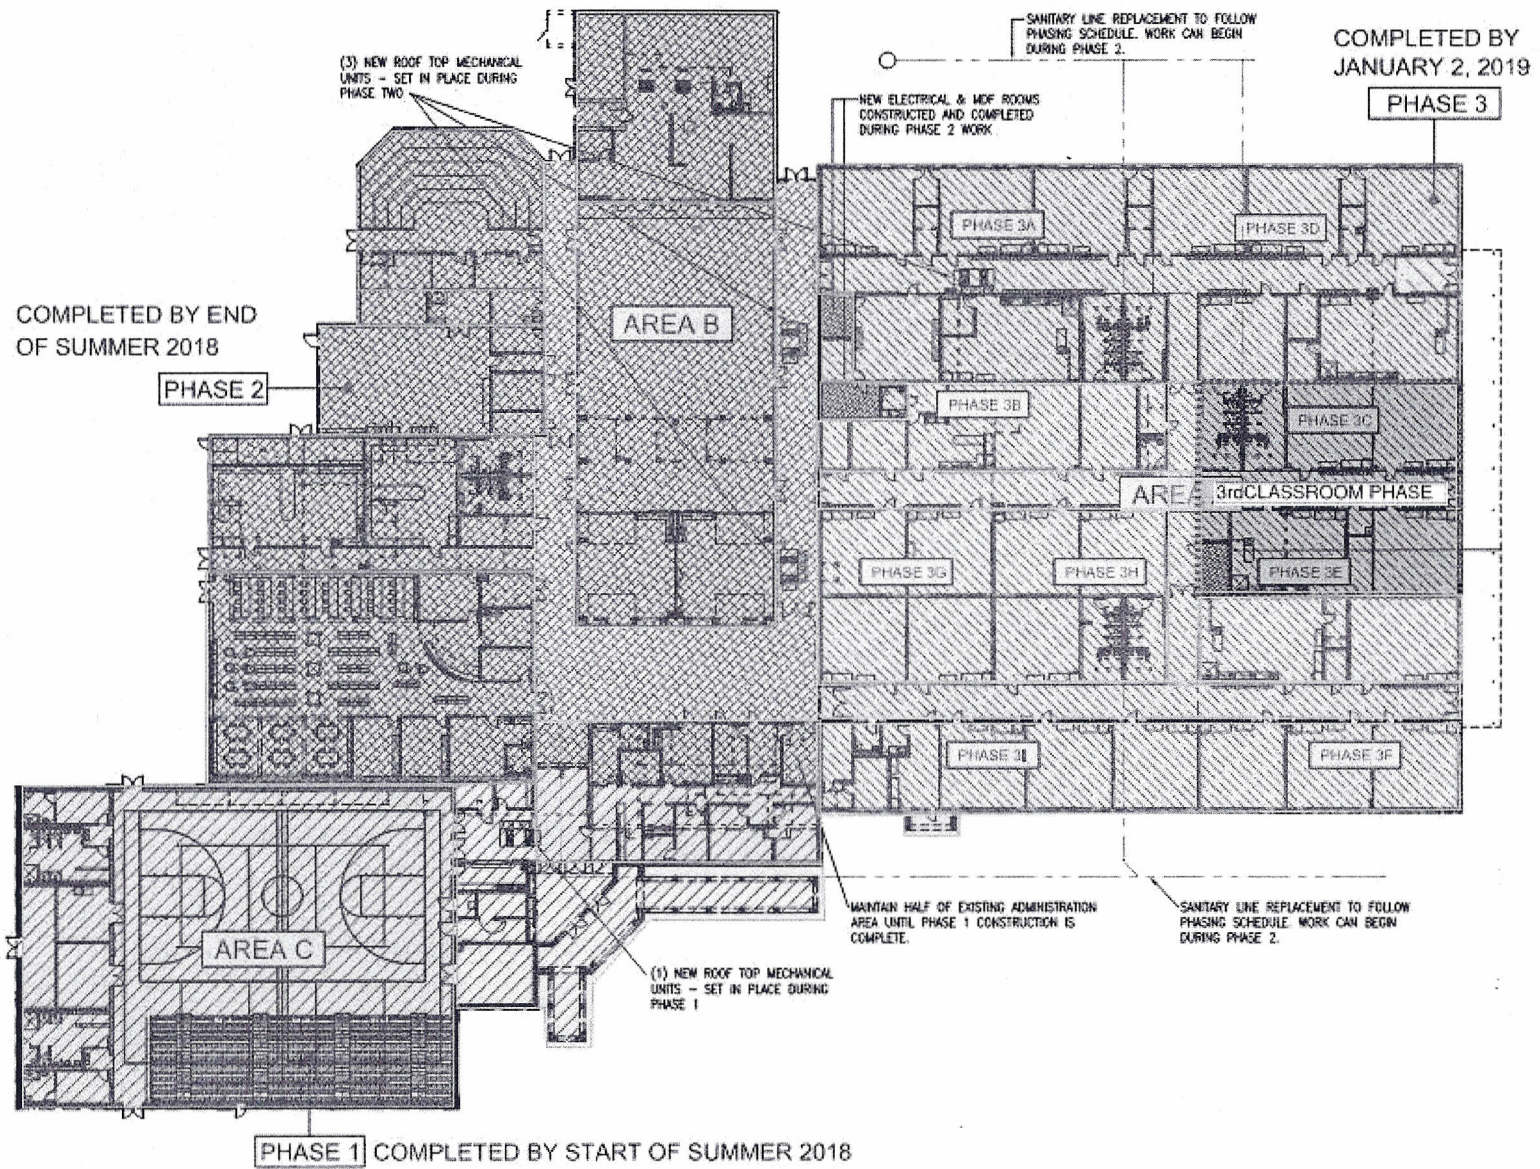


CONSTRUCTION PROGRESS PHOTOS



View of Demolition in 7th Grade Classroom. (10-30-2018)



View of Demolition in 7th Grade Corridor. (10-30-2018)

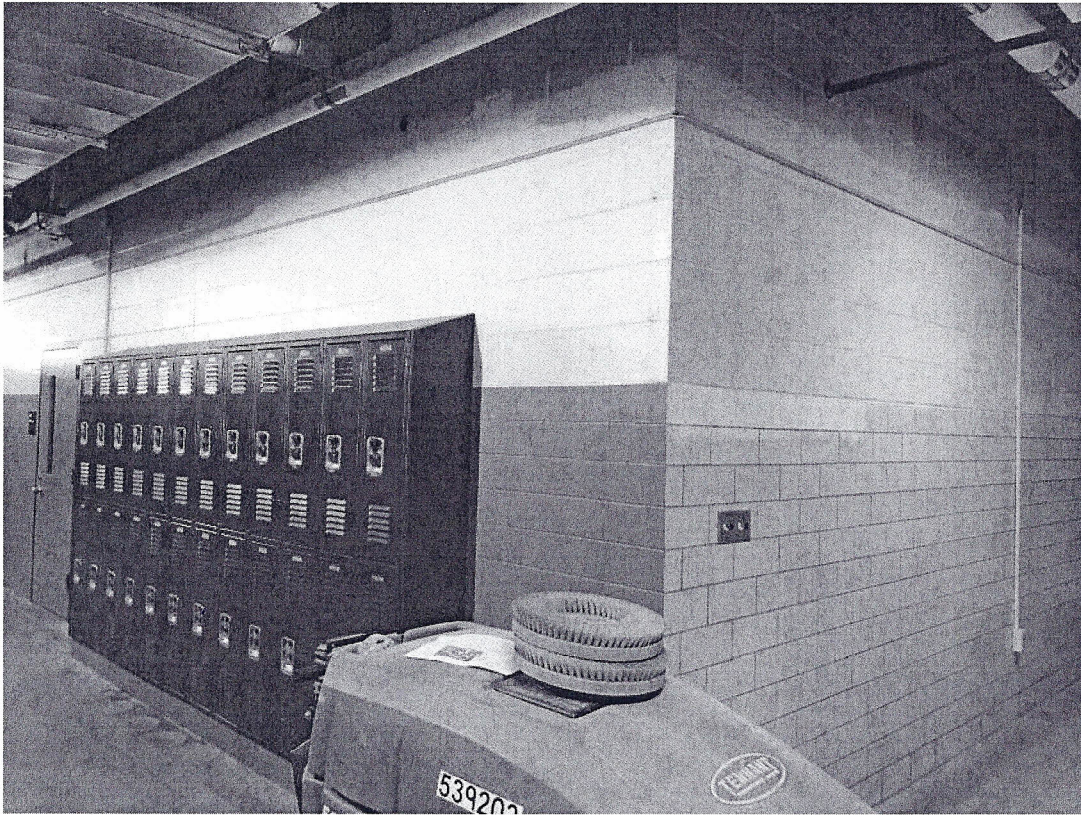

View of newly renovated 8th grade corridor extending to 7th grade wing. (11-06-2018)



View of new science lab cabinetry – work in progress. (11-06-2018)
