

## Bullitt County Public Schools

---

1040 Highway 44 East  
Shepherdsville, Kentucky 40165

502-869-8000  
Fax 502-543-3608  
[www.bullittschools.org](http://www.bullittschools.org)

### MEMO:

TO: Mr. Jesse Bacon *JB*

FROM: Bret Highley

DATE: March 13, 2019

RE: Construction Update:  
Bullitt Lick Middle School Addition/Renovation  
BG 17-14

Find attached the monthly construction update for Bullitt Lick Middle School as submitted by Scott Kremer, Studio Kremer Architects.

If you have any questions, please call me at 502-921-3659.

### Attachments:

- March Construction Update



## CONSTRUCTION UPDATE

Bullitt Lick Middle School – Renovation and Gym Addition  
555 W Blue Lick Road  
Shepherdsville, KY 40165

**SKA #: 2016-86**

**BG #: 17-148**

### CONSTRUCTION SUMMARY 3/11/19


All spaces are occupied and EH Construction is working on getting all new mechanical equipment up and running while working on completing previous punch list items. A follow-up final punch inspection has been delayed until the week following Spring Break to allow the contractor to do a full stripping and waxing of all V.C.T. flooring while the students and staff are on break and now that damaged and discolored tiles have been replaced. All interior work should be substantially complete following the punch inspection the second week of April. Work to be completed in occupied areas of the school is being done during 2<sup>nd</sup> shift.

Completed work since the last construction update are seen below. These pictures show the progress and completed work approved in Change Order #15 to address the infiltration of water to the brick masonry above the roof between corridor C502 and the Media Center. This work entailed power washing away all dirt and debris, applying spray foam to entire length of wall, and applying a cover of 2 coats of silicone sealant.



Work to repair the parking lots approved in Change Order #13 is estimated to begin the week prior to Spring Break for students. With the added parking lot repair scope, the site portion of the construction contract has been extended by 95 days so as to complete paving work under

appropriate weather conditions. The areas, shown in red below, will receive repairs and an asphalt overlay. The schedule for this work is for the West parking lot to be carried out the week prior to Spring Break and the East parking lot (bus drop off area) to be carried out the week of Spring Break so as not to interfere with student activity.

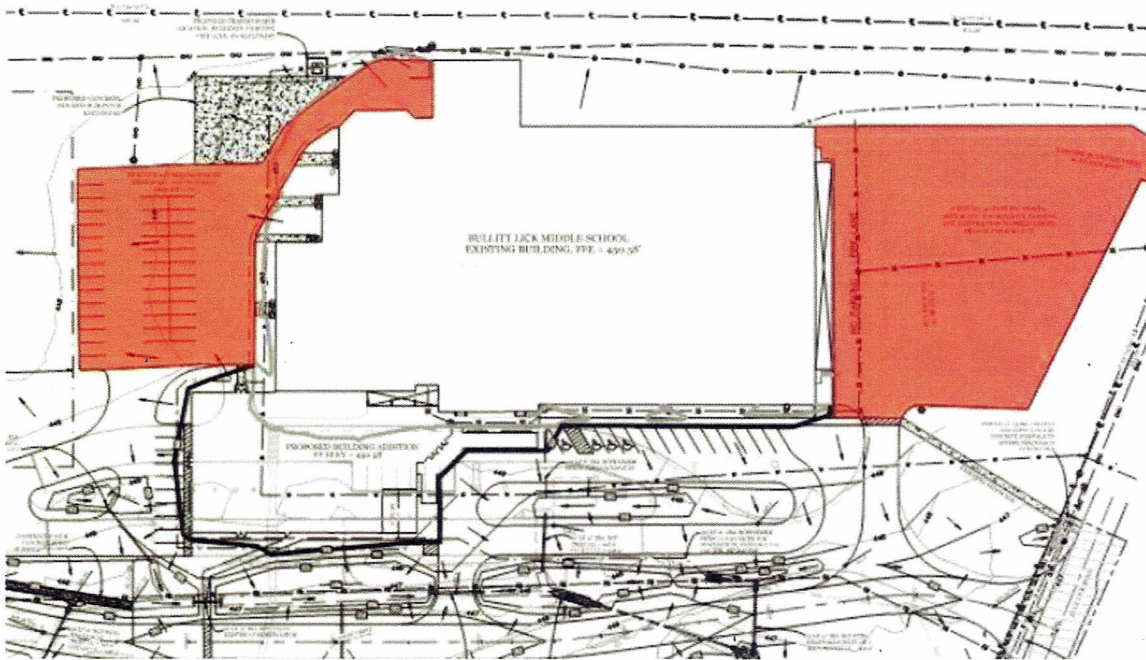

End of Construction Summary 3/11/19
