

**FIELD OBSERVATION REPORT****2018-06 (Scott HS)**

■ TO:	Kenton County Board of Education 1055 Eaton Drive Ft. Wright, KY 41017	■ DATE:	2018.06.20
ATTENTION:	Mr. Rob Haney		
■ FROM:	Mark Perry mperry@pca-arch.com 1881 Dixie Highway, Suite 130 Fort Wright, KY 41011 V: 859.431.8612 • F: 859.431.8611	■ PROJECT:	Kenton County School District Scott High School – Phase IV
COPIES TO:	Mr. Danny Mann	PROJECT NO.:	2016-124

## ■ WE TRANSMIT THE ATTACHED ITEMS VIA: EMAIL

## PURPOSE

- ☐ For your use
- ☐ As requested
- ☐ For review and comment
- ☐ For information
- ☒ For record
- ☐ For approval
- ☐

## DISPOSITION

- ☐ No exceptions noted
- ☐ Exceptions noted,  
Revise as indicated.
- ☐ REJECTED:  
REVISE AND RESUBMIT
- ☐

COPIES	DATE	DESCRIPTION	PAGES
1	2018-06	Field Observation Report	6

**Division 01: General Requirements**

01.01: 2018.06.12 – Temporary protection was installed at wall mounted utilities to remain near the former loading dock.

01.02: 2018.06.19 – Floor protection was in place in the gymnasium in advance of installing structural steel and ductwork for the new roof top units.

**Division 02: Existing Conditions**

02.01: 2018.06.12 – Demolition activities were occurring at both the lower level and upper level simultaneously with multiple crews working. Selective demolition of classroom walls and ceilings at the upper level, selective demolition of lower level fascia in the commons, and selective demolition along the lower level wall common with the auditorium were all taking place. All ceilings had already been removed.

02.02: 2018.06.19 – Roof and exterior skin had been removed at the former commons. A crew was actively removing flooring in that area. Some saw cuts had been made in the former kitchen area in preparation for underground plumbing, though no slabs had been removed for trenching. Ceiling tiles had been removed at the corridor outside the gymnasium. Openings for the portal frames at the main level firewall had been created.

02.03: 2018.06.19 – Demolition crews were actively removing the south exterior wall skin at the upper level and removing interior upper level debris. Half of the brick guard rail in the former commons had been removed.

**Division 03: Concrete**

03.01: 2018.06.19 – The new concrete footing at the firewall along the gymnasium had been poured up to the existing corridor doors.



PCA ARCHITECTURE

**Division 04: Masonry**

*04.01: 2018.06.19 – The mason was actively working on the first portion of firewall, starting at the Phase 3 end of the wall.*

**Division 20-28: MEP**

*20-28.01: 2018.06.19 – The geothermal subcontractor was actively installing circuit piping in the well field.*

*20-28.02: 2018.06.19 – Plumbing supply piping was actively being installed above the gym corridor ceiling.*

*20-28.03: 2018.06.19 – Assorted trapeze hangers had been installed at the underside of the upper level slab.*


**CONSTRUCTION PHOTOS**



2018.06.12 – Former commons space.



2018.06.12 – Electrical demolition in existing fire pump room

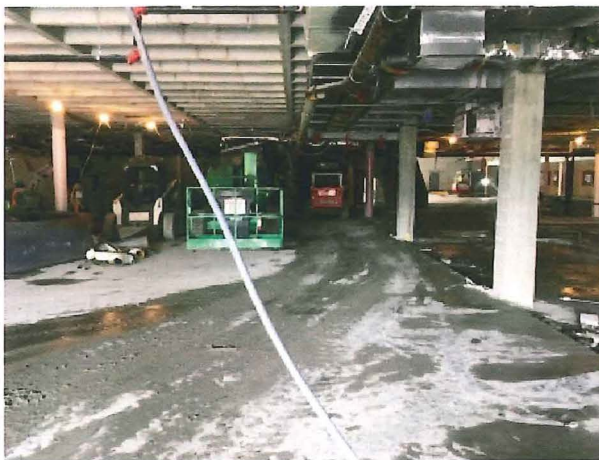

2018.06.12 – Lower level demolition



2018.06.12 – Lower level demolition





PCA ARCHITECTURE



2018.06.12 – Lower level demolition



2018.06.12 – Dumping debris out a wall opening at the upper level



2018.06.12 – Protection at utilities to remain



2018.06.19 – Circuit piping installation at well field



2018.06.19 – Circuit piping installation at well field



2018.06.19 – Former commons





2018.06.19 – New footing at firewall



2018.06.19 – Footing at firewall portal frame



2018.06.19 – New hangers along east end of firewall



2018.06.19 – Opening for doors at future scene shop



2018.06.19 – Saw cut for plumbing trench



2018.06.19 – Removing flooring in former commons





PCA ARCHITECTURE



2018.06.19 – Exposed existing structure at courtyard



2018.06.19 – Exposed structure at courtyard



2018.06.19 – Masonry firewall started



2018.06.19 – Floor protection in the gym



2018.06.19 – work in gym corridor



2018.06.19 – Looking down at former commons





PCA ARCHITECTURE



2018.06.19 – Upper level demolition



2018.06.19 – Upper level demolition



2018.06.19 – Upper level demolition



2018.06.19 – Upper level demolition

- ☐ Please acknowledge receipt of transmitted items.
- ☐ Return transmitted items to PCA ARCHITECTURE <sup>PSC</sup>.

END

If enclosures are not as noted, please notify PCA ARCHITECTURE immediately.  
Scott HS FieldRpt-201806
