



FIELD OBSERVATION REPORT

2018.07

| | | | |
|------------|---|--------------|--|
| ■ TO: | Kenton County Board of Education 1055 Eaton Drive Ft. Wright, KY 41017 | ■ DATE: | 2018.07.24 |
| ATTENTION: | Mr. Rob Haney | | |
| ■ FROM: | Ralph Cooper rcooper@pca-arch.com 1881 Dixie Highway, Suite 130 Fort Wright, KY 41011 V: 859.431.8612 • F: 859.431.8611 | ■ PROJECT: | Kenton County School District Hinsdale Elementary |
| COPIES TO: | Mr. Danny Mann | PROJECT NO.: | 2017-074 |

■ WE TRANSMIT THE ATTACHED ITEMS VIA: EMAIL

| | | | |
|----------------|---|--------------------|--|
| PURPOSE | <input type="checkbox"/> For your use | DISPOSITION | <input type="checkbox"/> No exceptions noted |
| | <input type="checkbox"/> As requested | | <input type="checkbox"/> Exceptions noted, Revise as indicated. |
| | <input type="checkbox"/> For review and comment | | <input type="checkbox"/> REJECTED: REVISE AND RESUBMIT |
| | <input type="checkbox"/> For information | | |
| | <input checked="" type="checkbox"/> For record | | |
| | <input type="checkbox"/> For approval | | |
| | <input type="checkbox"/> | | |

| COPIES | DATE | DESCRIPTION | PAGES |
|--------|---------|--------------------------|-------|
| 1 | 2018.07 | Field Observation Report | 10 |

Division 02: Site Work and Demolition

02.01: 2018.07.23 – Foundation walls have been back-filled with self-draining granular fill.

02.02: 2018.07.23 – Granular base has been installed for new exterior stairs.

02.03: 2018.07.23 – Site walls have been backfilled with self-draining granular fill.

Division 03: Concrete

03.01: 2018.06.28 – Excavation and forming of the footings and foundation walls continues. West foundation stem wall has been poured. Footings have been poured for the south wall. A portion of the east foundation stem wall has been poured. The remainder are being formed.

03.02: 2018.06.28 – Underpinning of the existing building wall has been completed at the location between the new and existing building.

03.03: 2018.07.16 – Installation of the footing and foundation walls has been completed.

03.04: 2018.07.16 – Installation of the granular backfill under the floor slab has started.

03.05: 2018.07.23 – Concrete slab has been poured. Workers were in the process of finishing the slab.

Division 04: Masonry

04.01: 2018.06.28 – The mason has begun laying the base course in the area of the new Lobby.

04.02: 2018.07.16 – Construction of the masonry wall between the new and existing building has begun.



04.03: 2018.07.23 – Masonry work continues. Portion of wall between new and existing building is at full height. A portion of the east wall has been constructed. Masonry work is on hold until the slab pour is finished.

Division 07: Thermal and Moisture Protection

07.01: 2018.07.16 – Foundation insulation has been installed in most areas. The top still needs to be trimmed to permit the concrete slab to meet the exterior wall.

07.02: 2018.07.16 – Foundation waterproofing has been installed along the south wall of the new addition.

07.03: 2018.07.16 – The excess foundation waterproofing is being ground off the site walls near the new concrete stairs.

Division 08: Doors and Frames

08.01: – No items noted.

Division 15: Plumbing

15.01: 2018.06.28 – The installation of the underground sanitary piping continues.

15.02: 2018.07.16 – Installation of the under-slab sanitary for the new office toilet rooms is in progress.

15.03: 2018.07.16 – Floor drain has been installed in the mechanical room.

Division 16: Electric

16.01: 2018.06.28 – The electrician is preparing conduit and electrical boxes for roughing in the masonry walls.

16.02: 2018.07.16 – The under-slab electrical conduits have been installed for the floor outlet in the Conference Room.


CONSTRUCTION PHOTOS



2018.06.28 – Construction of the foundation stem walls are in progress.



2018.06.28 – Formwork is being installed for the foundation stem walls.

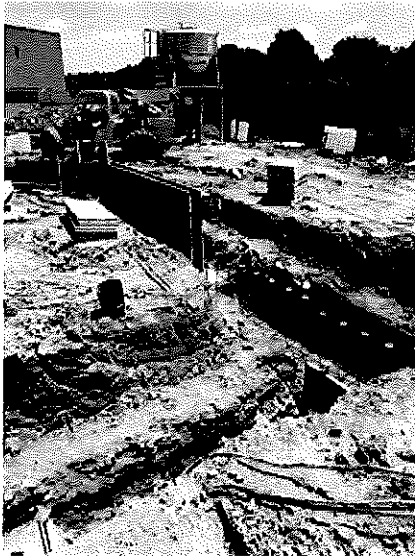

2018.06.28 – Formwork is being installed for the foundation stem walls..



2018.06.28 – Foundation stems walls have been installed at the main entry.




2018.06.28 – Site walls for the ADA ramp from the new building.




2018.06.28 – Masonry is being stocked on site for construction of the new walls.




2018.06.28 – Installation of the concrete masonry walls has begun.

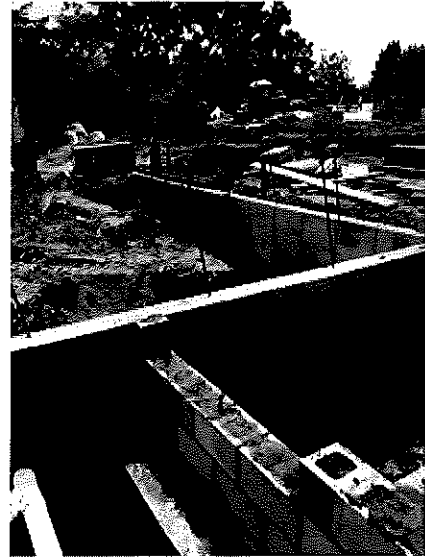


2018.06.28 – Installation of the concrete masonry walls has begun.

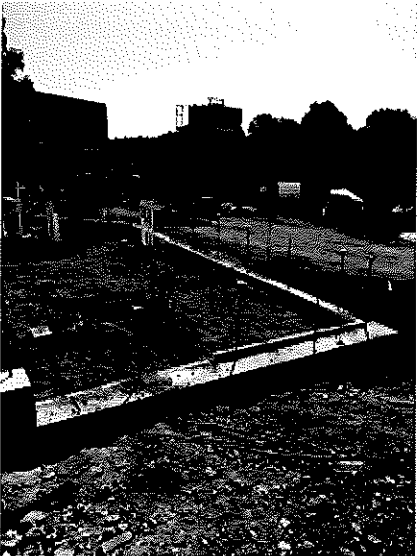

2018.07.16 – Installation of the perimeter slab insulation and granular base for the new floor is in progress.

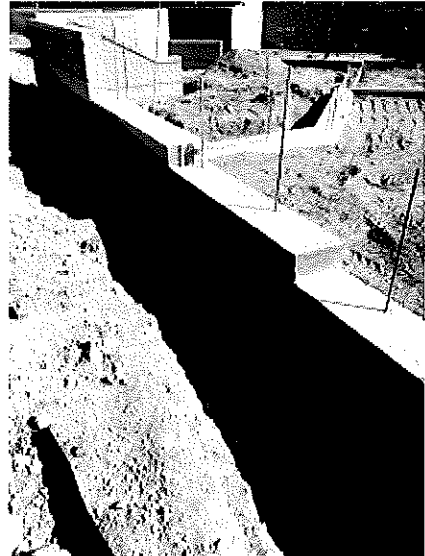


2018.07.16 – The south foundation wall of the new building has been waterproofed..

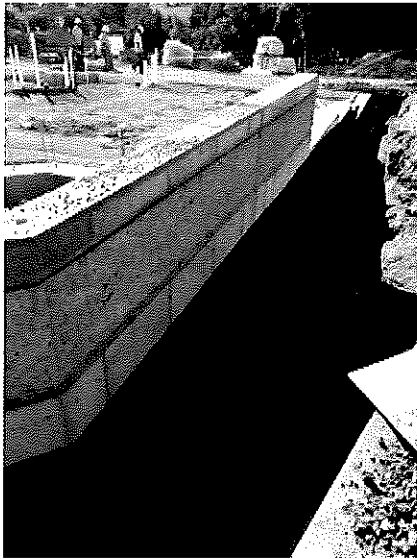


2018.07.16 – Waterproofing and protection board has been placed over the site walls.




2018.07.16 – A worker is removing the waterproofing overspray from the site walls.

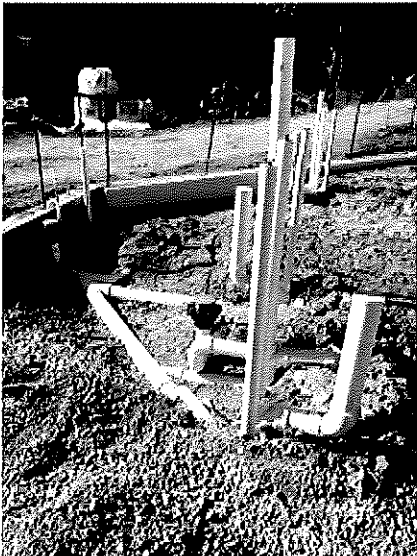


2018.07.16 – Installation of the under-slab plumbing is in progress.

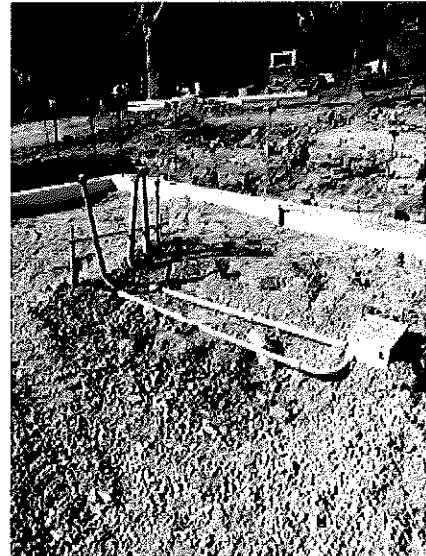

2018.07.16 – Installation of the under-slab electric is in progress.

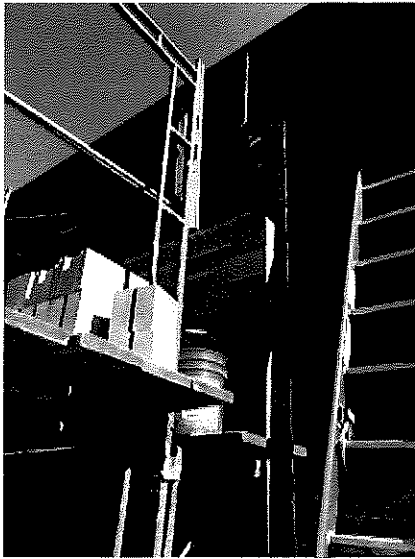

2018.07.16 – Construction of the concrete masonry wall adjacent the existing building has started.

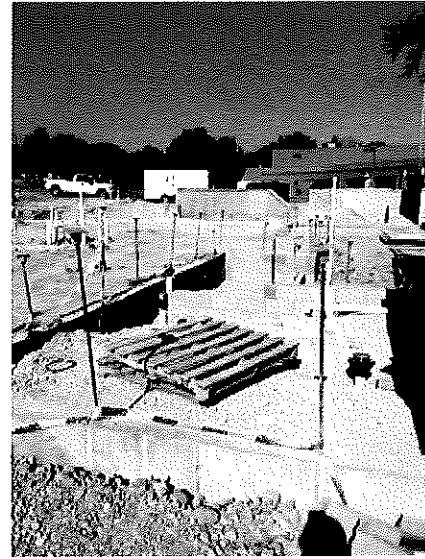


2018.07.16 – Installation of the under-slab plumbing in the mechanical room is in progress.



2018.07.16 – Installation of the under-slab plumbing in the mechanical room is in progress.



2018.07.16 – Installation of the under-slab plumbing in the mechanical room is in progress.

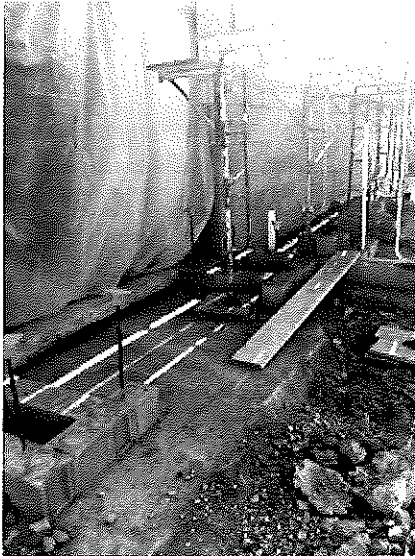


2018.07.16 – Construction of the concrete masonry wall adjacent the existing building has started.




2018.07.16 – Construction of the concrete masonry wall adjacent the existing building has started.



2018.07.23 – The slab-on-grade has been poured and is being finished.

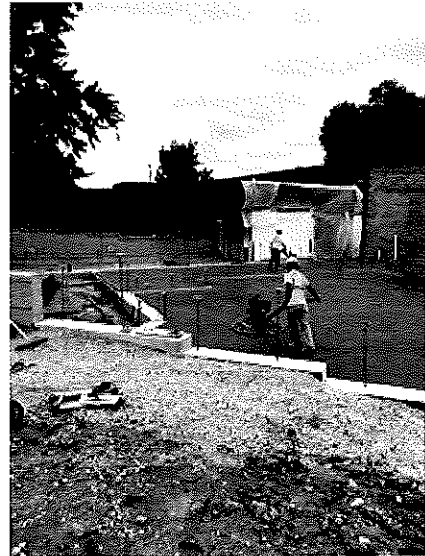


2018.07.23 – The slab-on-grade has been poured and is being finished.

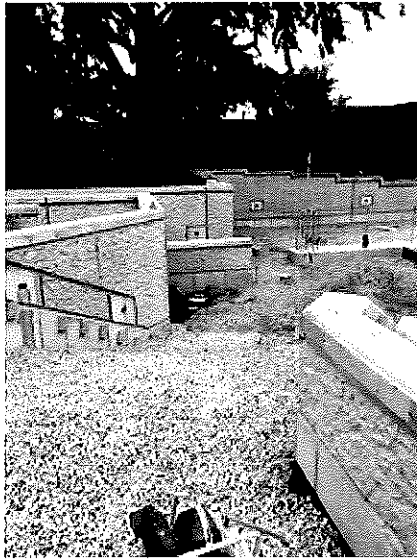


2018.07.23 – Granular backfill has been installed for the new concrete stairs.



2018.07.23 – The slab-on-grade has been poured and is being finished.

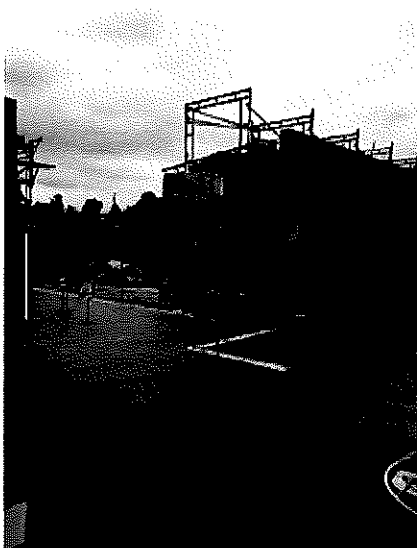

2018.07.23 – The slab-on-grade has been poured and is being finished. The installation of the concrete masonry walls continues.

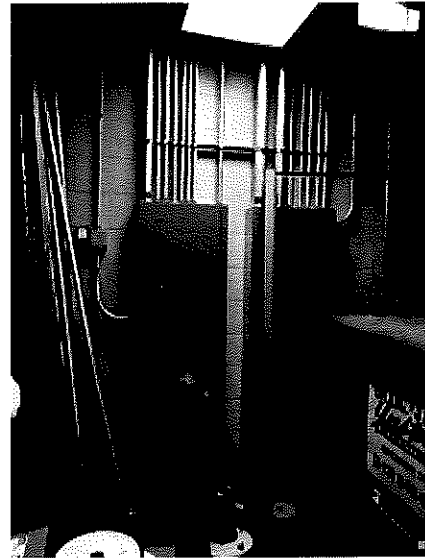

2018.07.23 – Work continues on installation of the electrical panels.



2018.07.23 – The installation of the concrete masonry walls continues.



2018.07.23 – The installation of the concrete masonry walls continues.




2018.07.23 – The installation of the concrete masonry walls continues.




2018.07.23 – The installation of the concrete masonry walls continues.



PCA ARCHITECTURE

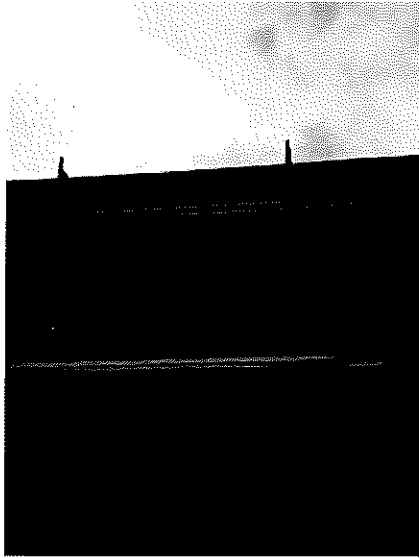


2018.07.23 – The installation of the concrete masonry walls continues.

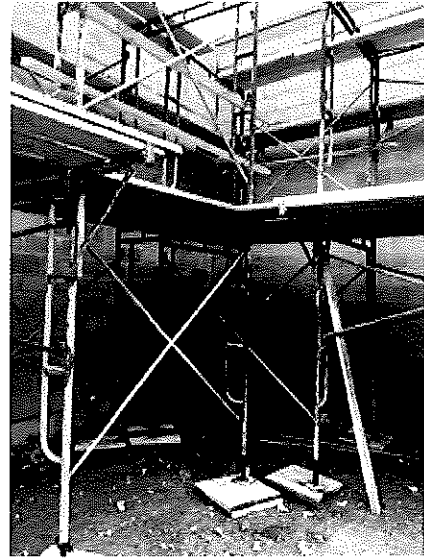

2018.07.23 – The installation of the concrete masonry walls continues.



2018.07.23 – The site walls have been backfilled with self-draining granular fill.

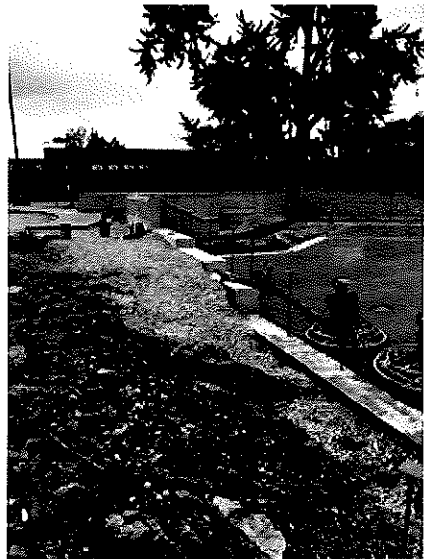

2018.07.23 – The foundation walls have been backfilled with self-draining granular fill.

- ☐ Please acknowledge receipt of transmitted items.
- ☐ Return transmitted items to PCA ARCHITECTURE ^{PSC}.

END
