

Peck Flannery Gream Warren Architects, LLC

112 North Main St.

Elizabethtown, Kentucky 42701

Phone: 270-765-2147

Fax: 270-765-2148

Email: lgream@pfgw.org

Website: www.pfgw.net

November 10, 2009

Ms. Nannette Johnston Hardin County Board of Education 65 W.A. Jenkins Rd. Elizabethtown, KY 42701

RE:

November 2009

Hardin County Schools

(Report of Projects in Progress)

Dear Nannette:

Please consider the following as a report on projects which our firm is presently providing Architecture/Engineering services.

I have two action items to present this month.

1. RINEYVILLE ELEMENTARY SCHOOL: WHITTENBERG CONSTRUCTION

Building Bid Package "A": Remaining work on this project consists of completion of year end maintenance items.

One year end maintenance item remains unresolved; that being staining of asphalt paving at three locations by what appears to be iron oxide. We are reviewing this item with Whittenberg Construction and Scotty's Paving at this time and will report solution in near future.

HEARTLAND ELEMENTARY SCHOOL: MOREL CONSTRUCTION COMPANY

Building Bid Package "A": Remaining work on this project consists of completion of site punch list and year end items. (verification of grass growth, erosion control).

Civil Engineer Mike Billings is preparing documents to obtain a proposal from Morel Construction to extend Nelson Drive to the East property line.

3. NORTH HARDIN HIGH SCHOOL PHASE TWO and THREE RENOVATIONS (2008- 2009) - MCNUTT CONSTRUCTION:

Work is progressing on phase three portions of the project. Charlie Jones will present construction progress during the November 19th Board meeting.

Board Action Item:

The following change order item is presented to the board for consideration.

3.1 Masonry work was performed on time and material basis at various locations.

ADD OF \$13,278.00

Reason For Change: Additional time and material work was authorized to hide existing exposed piping, repair walls resulting from eliminating existing abandoned mechanical chases and thereby freeing space for classrooms, etc.

4. 2009- ROOFING PROJECTS- SWIFT ROOFING

Attached is a November 9 letter from Swift Roofing giving a status report of Parkway Elementary, Mulberry-Helm and North Hardin roofing projects.

5. BUS GARAGE - JENKINS-ESSEX CONSTRUCTION

The building is occupied by mechanics and office personnel. A site punch list is scheduled for Friday, November 13.

Board Action Item:

The following change order item is presented to the board for consideration.

5.1 Add 6' high chain link fence approximately 1,349 feet long at the rear property line and portions of each side property line near the rear of the site.

ADD OF \$22,785.70

Reason For Change: There was fencing at the above referenced areas, it however was determined to be unsuitable for the new Bus Facility and that new fencing would be required at this location.

6. RECORDS/STORAGE BUILDING - KLEINHOLTER CONSTRUCTION

A review of the installed roof is presently being made. A final report will be made shortly.

Please give me a call if you have questions regarding this report.

Sincerely,

Larry Gream

c: Gary Milby David Wyatt

Change Order 3.1 Masonry work performed on time and material basis North Hardin.

Recommended Motion:

I move the Hardin County Board approve Change Order #3.1 Masonry work performed on time and material basis on Phase 2&3 renovation at North Hardin High School.

Change Order 5.1 Additional Fence at new bus garage.

Recommended Motion:

I move the Hardin County Board approve Change Order #5.1 adding 6' high chain link fence approximately 1349 feet long at the rear of the property line and portions of each side property line near the rear of the site.

September 29, 2009

Peck, Flannery, Gream, Warren, Inc.
112 N. Main Street

Elizabethtown, KY 42701

ATTN: Larry Gream


Re:

Phase 2 & 3 Renovations

North Hardin High School

Radcliff, Kentucky

Dear Larry:



COST BREAKDOWN

Sub-Contract cost per attached	\$9,071.00
Bond 1%	91.00
Overhead and Profit 15%	<u>1,374.00</u>
Total	\$10,536.00

If you should have any question or need further information please contact me at our office.

Sincerely,

Mark McNutt; President

MM:je

10: MC NOTE CONSTIUCTION

JOB Jork Harden High School Phase II III.

CONTRACT JOB NO. 823

PREPARED BY RECEIVED SEP 2 2 2009

WORK TO BEGIN BY

WORK TO BE COMPLETED BY


Repair Door 212B

1 Labor " 18.86 277.76

MATERIA 12.10

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Communications are the covered by this order shall be performed under the same terms and conditions as that included in the Original Communications are the covered by this order shall be performed under the same terms and conditions as that included in the Original Communications are the covered by this order shall be performed under the same terms and conditions as that included in the Original Communications are the covered by this order shall be performed under the same terms and conditions as that included in the Original Communications are the covered by the covered by this order shall be performed under the same terms and conditions are that included in the Original Communication of the covered by the covered by

CHANGES APPROVED



PREVIOUS CONTRACT AMOUNT	\$
AMOUNT OF THIS ORDER	\$ 289.86
TOTAL CONTRACT AND EXTRAS	\$

NC3814

3v:___

	110	•		•.	•,,•		
--	-----	---	--	----	------	--	--

JOB CONTRACT J	Hardin High School Phase II + II)
PREPARED B	823
WORK TO BEGIN BY	RECEIVED SEP 2 2 2009
WORK TO BE	10.000

Grand & Tuck pointing Libery & Old Locker Wall


Imason 79.46

Total His. 71

5640.95

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Contract

CHANGES APPROVED



PREVIOUS CONTRACT AMOUNT	\$
AMOUNT OF THIS ORDER	\$5640.95
TOTAL CONTRACT AND EXTRAS	\$

NC3814

1	1 /1000	1371	UCT	100	一个汽车的40分	1.
,			3.04	••		. •-

DATE

JOB OTT HAID H. 9h School Phase II 4 TII

CONTRACT JOB NO.

823

PREPARED BY RECEIVED SEP 2 2 2009

WORK TO BEGIN BY


WORK TO BE
COMPLETED BY

Room 1418+142 Repar Block Wall I MASON 36, 238.35
1 Labor 178.29
416.64

MATERIAL 82.40

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Contract

CHANGES APPROVED



499.04
<u> </u>

NC3814

		* * *		• 4**	
--	--	-------	--	-------	--

Phase II + TI CONTRACT JOB NO. PREPARED BY RECEIVED SEP 2 2 2009

WORK TO **BEGIN BY**


WORK TO BE COMPLETED BY

Repair Wall-

/ mason 1 Labor

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Contract

CHANGES APPROVED



PREVIOUS CONTRACT AMOUNT \$ AMOUNT OF THIS ORDER TOTAL CONTRACT AND EXTRAS

NC3814

By:.

Garry R. Grubbs
302 Presidential Boulevard
Hodgenville, KY 42748

		10.00	<	8,7 8,	11.77		0.072413	
--	--	-------	---	--------	-------	--	----------	--

DATE

JOB No. Hardin High School Phase II 4700

CONTRACT JOB NO. 823

PREPARED BY

WORK TO BEGIN BY


WORK TO BE COMPLETED BY

ROOMS 135 ROPAIN Block WALL

1 Labor " 475.44 1111.04

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Contract

CHANGES APPROVED



. . •

PREVIOUS CONTRACT AMOUNT	\$
AMOUNT OF THIS ORDER	\$////. 04
TOTAL CONTRACT AND EXTRAS	\$

NC3814

/11 × /16	77 CO	ASTIO	OTION	er lage (AP)	10 22 2
	• •		· figur	-	N. 34.

JOB North Hardin High School Phase II III
CONTRACT JOB NO. 823
PREPARED BY RECEIVED SEP 2 2 2009


WORK TO BEGIN BY WORK TO BE COMPLETED BY

Repaire Door 129B.

1 Mason 3 Hrs 238.35 1 Labor " 178.25 416.60

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Committee or the conditions are that included in the Original Committee or the covered by this order shall be performed under the same terms and conditions as that included in the Original Committee or the covered by this order shall be performed under the same terms and conditions as that included in the Original Committee or the covered by this order shall be performed under the same terms and conditions as that included in the Original Committee or the covered by this order shall be performed under the same terms and conditions as that included in the Original Committee or the covered by the cover

CHANGES APPROVED



PREVIOUS CONTRACT AMOUNT	\$
AMOUNT OF THIS ORDER	\$ 4/6. 60
TOTAL CONTRACT AND EXTRAS	S

NC3814

Bv:

JOB Jork Hardin High School Phase II III
CONTRACT JOB NO. 823

PREPARED BY RECEIVED SEP 2 2 2009

WORK TO BEGIN BY

WORK TO BE COMPLETED BY


Room 215 Repair Block WAY

1 MASON 2H1 158.90 1 Labor " 118.86 277.76

MATERIAL 18.20

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Dans and

CHANGES APPROVED



....

PREVIOUS CONTRACT AMOUNT	S
AMOUNT OF THIS ORDER	\$ 295.94
TOTAL CONTRACT AND EXTRAS	S
	rest in south and a

NC3814

,

TO Me Nort Constitution

DATE

JOB

North Hard of High School Phase II III

CONTRACT JOB NO.

823

PREPARED BY RECEIVED SEP 2 2 2009

WORK TO BEGIN BY

WORK TO BE

Room 212C Block Wall to Hide P.pe

1 Mason 4H1 317.80 1 Labor " <u>237.72</u> 555.5%


MATERIAL

COMPLETED BY

53.25

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Computation

CHANGES APPROVED



PREVIOUS CONTRACT AMOUNT	\$
AMOUNT OF THIS ORDER	\$ 608. 77
TOTAL CONTRACT AND EXTRAS	\$

NC3814

September 23, 2009

Peck, Flannery, Gream, Warren, Inc. 112 N. Main Street Elizabethtown, KY 42701

ATTN: Larry Gream

Phase 2 & 3 Renovations

North Hardin High School

Radcliff, Kentucky



3.18

Dear Larry:

Re:

We propose to furnish all necessary labor, material and equipment to lay block around electric box in Room #238 for the sum of \$957.00.

Cost Breakdown

Sub-Contract per attached	\$824.00
Bond Premium 1%	8.00
Overhead and Profit 15%	125.00
TOTAL	\$957.00

If you should have any questions or need any further information please contact me at our office.

Sincerely,

Mark McNutt; President

MM:je

CONT ACT CHANGE ORDER

Commonwealth Masonry, Inc. Garry R. Grubbs 302 Presidential Boulevard Hodgenville, KY 42748

•	 0571	 		
100			4	

DATE

JOB

MOTT HAID High School Phase II 4 III

CONTRACT JOB NO.

823

PREPARED BY

WORK TO BEGIN BY

WORK TO BE
WORK TO BE

Parm 238 LAG Block Around Elec. Box

COMPLETED BY

1 MASON 52 436.98 1 Labor 52 326.87 763.85

MATERIAL: 60.45


The work covered by this order shall be performed under the same terms and conditions as that included in the Original Contract

CHANGES APPROVED

a se adjunction of the second	80 to •••
15	***

PREVIOUS CONTRACT AMOUNT	\$
AMOUNT OF THIS ORDER	\$824.30
TOTAL CONTRACT AND EXTRAS	\$
14	***************************************

NC3814

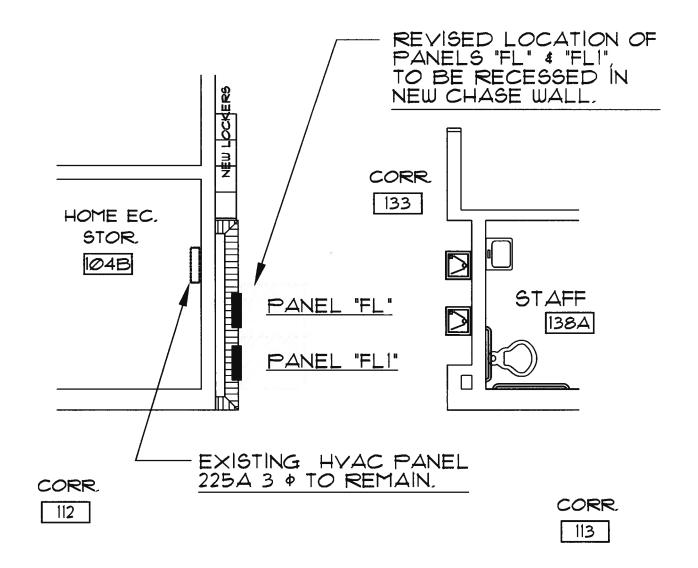

NEW CMU ELECTRICAL PANEL CHASE

SCALE: 1/4" = 1'-0"

NHHS RENOVATION PHASE 2 -3	JOB NO. Ø7Ø1B
Peck Flannery Gream Warren Inc.	10-16-08
Peck Flannery Gream Warren Inc. architects 12 North Man Etaboliton, Kontucty 42701	MOD, 3

www.mcnutt-construction.com

September 23, 2009

Peck, Flannery, Gream, Warren, Inc. 112 N. Main Street

Elizabethtown, KY 42701

ATTN: Larry Gream

3.10

Re:

Phase 2 & 3 Renovations

North Hardin High School

Radcliff, Kentucky

Dear Larry:

We propose to furnish all necessary labor, material and equipment to make repairs to the east wall of PE Office 144A for the sum of \$1,785.00.

Cost Breakdown

Sub-Contractor per attached	\$1,537.00
Bond Premium 1%	15.00
Overhead and Profit 15%	233.00
TOTAL	\$1,785.00

Should you have any questions please contact our office.

Sincerely,

Mark McNutt; President

MM:je

		9 . 2 ₁₀ .	• 4	1 100	
--	--	-----------------------	-----	-------	--

North HArdin High School Phase II + III CONTRACT JOB NO. PREPARED BY WORK TO

BEGIN BY WORK TO BE COMPLETED BY

2 MASONS 2 Labors

794.50 594.30 1388.80


MASON RATE 79.45 Labor Rive 59,43

MATERIAL

148.40

The work covered by this order shall be performed under the same terms and conditions as that included in the Original Contract

CHANGES APPROVED



\$
\$1537.20
\$

NC3814





SWIFT ROOFING OF E'TOWN, INC P.O. BOX 502

ELIZABETHTOWN, KY 42702

PEONE: (270) 737-2224 FAX: (270) 737-5307

Attn.: Phil Moyers 11/10/09

Peck Flannery Gream Warren

Re.: Hardin County Schools

Progress Report

Parkway Elementary:

All roofing, flashing and sheet metal work are now complete.

Final manufacturers punch list items are being completed today, close out documents will soon follow and the warranty shall be issued for this project.

North Hardin HS:

The lower roof sections are now complete with additional roof drains installed. The white gravel surfacing is completed and awaiting sheet metal work.

The tear off, new insulation, base and cap sheet along with all base flashing over the Library / Gym roof is 100% complete and awaiting cure period (White surfacing may begin 11/18/09). Sheet metal work will follow the application of white gravel surfacing.

Mulberry Helm:

This project also is complete with all roofing, flashing and sheet metal. The installation of white gravel surfacing has been completed on all sections along with debris clean up. Architect punch list job inspection has been completed all roofing items have been corrected and awaiting masonry repairs, the manufacturer inspection shall follow. Installation of the third canopy is now complete, final clean up and close out documents will soon follow.

Thank You,

Brian Delk Project Manager

esterday's Success



Building Tomorrow's Dreams...

09 November 2009

Peck Flannery Gream Warren Architects, LLC Attn: Larry Gream 112 North Main Street Elizabethtown, KY 42701

Dear Sir,

Jenkins-Essex Construction proposes to provide all labor, materials, and equipment necessary for installation of new chain link fencing. I have attached our subcontractor's quote for this work to assist you in your review. Please advise on acceptance of this proposal.

Please find listed below a summary of the costs associated with this change:

CONSTRUCTION

K&D Fence Markup Total Estimated Cost

\$ 21,196.00 \$ 1,589.70 \$ 22,785.70

Thank you for your attention to these matters, if you require any additional information feel free to contact me in our office.

Very guly yours,

larrod Benningfield Project Manager

Shop
~~~~

# K & D FENCING, INC.

BENNING FIELD ATTN JARRETT CHAINLINK-WOOD-VINYL-AGRICULTURAL-ORNAMENTALIRON


Kyle R. Toy 634 Stovall Road Elizabethtown, KY 42701

**FREE ESTIMATES FULLY INSURED** 

Phone/Fax 270-737-8970 Cellular

270-735-2388

<u>PROPOSAJ</u> OWNER TENKINS 653 EX HOME PHONE: **ADDRESS** WORK PHONE: 765-6413 FAX: 765-7767 CELLULAR: **CHAINLINK SPECIFICATIONS** WOOD SPECIFICATIONS VINYLSPECIFICATIONS HEIGHT: 6'+ B. WIRE HEIGHT: HEIGHT: FINISH: GALUBRIZES STYLE: STYLE FRAMEWORK: 5340 WOOD TYPE: COLOR: FABRIC: 9 64. ALUMINIZED PICKET STYLE:

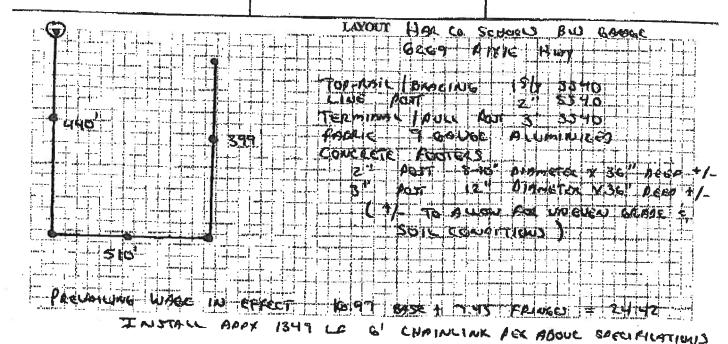

21,196.00 ESTIMATOR Authorized and Accepted By PAYMENT TERMS DATE MATERING DAAW REGUILED FIN

UTILITIES ABOVE/BELOW GROUND PROPERTY LINE LOCATED (Y) N ELECTRIC/WATER ON SITE ON FENCE ON OFF PROPERTY LINE APPX C" 1 -

ESTIMATE GOOD 30 DAYS APPROXIMATE START TIME

CUSTOMER SOLELY RESPONSIBLE FOR LOCATION OF FENCE LINE!

CUSTOMER SOLELY RESPONSIBLE TO BE IN COMPLIANCE WITH ANY/ALL SUBDIVISION, LOCAL, STATE & PEDERAL RESTRICTIONS AND/OR REGULATIONS.

K & 1) FENCE NOT RESPONSIBLE FOR DAMAGE TO SEPTIC SYSTEMS, GUTTERS, DRAINS OR FOUNDATION DRAINS.
