

PROJECT  
Woodford Co. HS Emergency Structural Rep  
RTA 2133

VISIT NAME  
FOR220412

AUTHOR  
FAYE BAHRAMI

DATE  
5/11/2022

REPORT NO  
01

STATUS  
FINAL

---

**VISIT DETAILS**

IN ATTENDANCE  
Faye Bahrami - RossTarrant Architects

WEATHER

**Sunny, 80 degrees**

GENERAL COMMENTS

Two people were working on fastening the channels during the site visit.

**OBSERVATIONS**

ITEM: 001-001

REMARKS: South Locker Room: The footings are completed and the structural steel framing is underway. The supporting beams have been installed. The columns are in place. The channel installation is nearly complete. Fasteners were not completed at the time of site visit.








ITEM: 001-002

REMARKS: North Locker Room: The footings are completed and the structural steel framing is underway. The supporting beams have been installed. The columns are in place. The channel installation is nearly complete. Fasteners were completed. The reinforcing steel and steel plates are in place and still require final welds. Concrete placement from above has not begun.

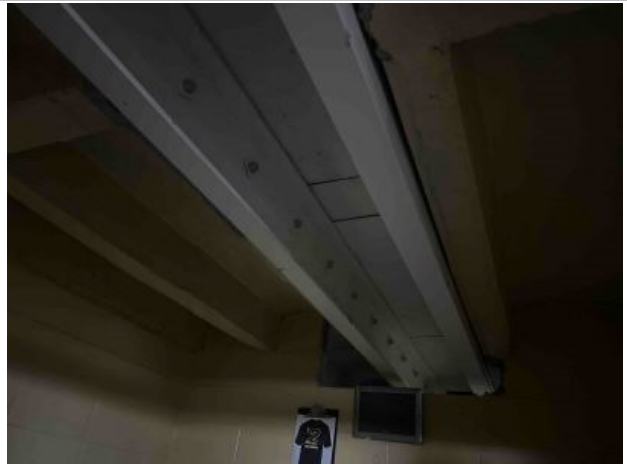





RossTarrant Architects  
101 old lafayette avenue  
lexington, kentucky 40502  
p 859.254.4018  
f 859.231.5046  
[www.rosstarrant.com](http://www.rosstarrant.com)
