



Critical Dates for School Opening:

**November 29th** – Temporary Certificate of Occupancy / Certificate of Occupancy – State Building Inspector will be on site tomorrow to issue a TCO/CO if work meets his approval.

**December 2<sup>nd</sup>** – Substantial Completion – Main Building  
- SKA will perform a walk through that day to determine Substantial Completion.

**December 12<sup>th</sup>, 13<sup>th</sup>, 14<sup>th</sup>** – Student/Teacher Field Trips

**December 15<sup>th</sup>** – Teachers set up Classrooms

**December 23<sup>rd</sup>** – Substantial Completion - Gym




NEW OLD MILL ELEMENTARY SCHOOL – CONSTRUCTION UPDATE









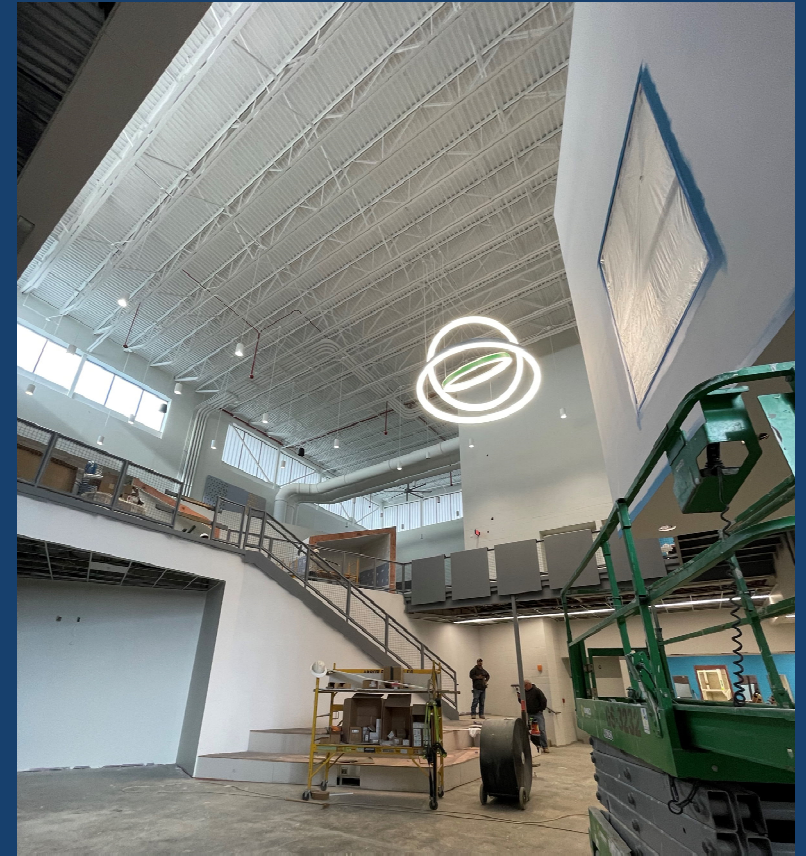

























Change Orders:

Change Order #22 - Door Mullion

Add a removeable mullion as exterior door: \$1,186.80

Change Order #23 - Commons Pipe Chase

Add chase to obscure piping at Commons: \$3,444.25

Change Order #24 – Domestic Water Pump

Add water pump to address water pressure: \$45,385.44

Use of Construction Allowances to Date:

**No Billing towards these allowances.**

**Balances:**

Soil Allowance Balance: \$142,683.04

Site Electrical: \$20,000

Haul Unsuitable Material: \$50,000

Total anticipated Allowance refund to project: \$212,683.04

