



FIELD OBSERVATION REPORT

Food Service Building, 202276 -CA8

Date: 4/8/2025 Time: 1:00 PM

Observed by: Joseph Jones, AIA

Trades Observed on Site: Carpenters, Excavators

Weather: 40s/Sunny

Report No: 3

1. Work observed in Progress

- a) The site had recovered well from the recent flooding rains to the point that excavations and earth moving were proceeding normally.
- b) Excavating and earth moving was ongoing.
- c) Preparing areas for the next footing pour.
- d) Preparing steel reinforcing for footings.

2. General Observations

- a) The building pad had dried due to sunny/breezy conditions after the flooding rains that occurred the week before.
- b) Some mud was washed onto the footings from the rains. The mud will need to be removed before the stem walls are added.



- c) The footing on the southeast corner drops significantly to bear on suitable soils. The reinforcement that was in place reflects that. The footing bottoms appeared to be firm.




- d) Steel reinforcement was in place at the northeast corner.



- e) The footing steps to the southeast. Steel reinforcing was placed on concrete block risers.



- f) Soils were being removed to reach plan bottoms.

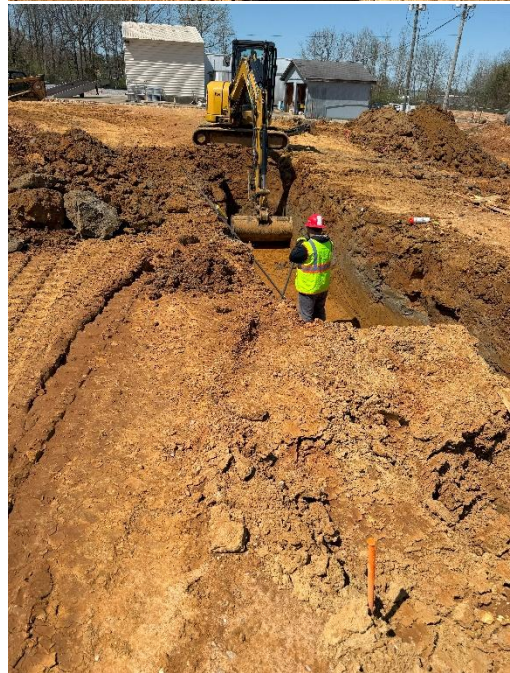

- g) Once soils were excavated, it was removed to the area in front of the facilities building for loading onto dump trucks.



- h) The excess soils were being loading into dump trucks for disposal off site.



3. Stored Material Observed:

- a) Concrete accessories.
- b) Geothermal piping.

4. Follow up items:

- a) Note any changes to the plans on the As-Built Drawings.

Follow up by:

☐ Architect, ☐ Owner, ☐ MEP Engineer, ☐ Structural Engineer,
☐ Civil Engineer ☐ Construction Manager, ☐ Other

Respectfully submitted,

JRA Architects
Joseph Jones, AIA,
Construction Contract Administrator

cc: 202276, CA8, HCS, Wehr, B+K, CMTA, JRA
