



PROGRESS REPORT

**HARDIN COUNTY SCHOOLS
JHHS ATHLETIC FACILITIES
NEW LINCOLN TRAIL ELEMENTARY SCHOOL
NEW EAST MIDDLE SCHOOL
HARDIN COUNTY 2018 DISTRICT FACILITIES PLAN (DFP)**

Project No: 2016133, 201752, 2016110
Date: February 15, 2018
Time: 6:00 PM
Location: Hardin County Board of Education

JHHS ATHLETIC IMPROVEMENTS (BG# 17-111)

The last regular construction progress meeting was held on February 6th. A report of the meeting activities is attached to this report. The contractor is working to complete the limited remaining work items. The recent sub-freezing temperatures have impacted the ability to perform some of the final work.

Payment application #6 has been submitted by JRA to HCS for processing.

Action items tonight include Approval of Change Order #3, which results in a credit of (\$15,600.22)

The current contract milestones are as follows:

Substantial Completion (all work):	January 14, 2018 (unchanged)
Contract Amount:	\$2,364,699.78 (decreased by \$15,600.22)

NEW LINCOLN TRAIL ELEMENTARY SCHOOL (BG# 18-098)

No items to report.

NEW EAST MIDDLE SCHOOL (BG# 18-098)

No items to report.


DISTRICT FACILITY PLAN UPDATE

State Board Meeting to approve the updated DFP at the February 7, 2018 meeting.

**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 2

Progress Report
February 15, 2018

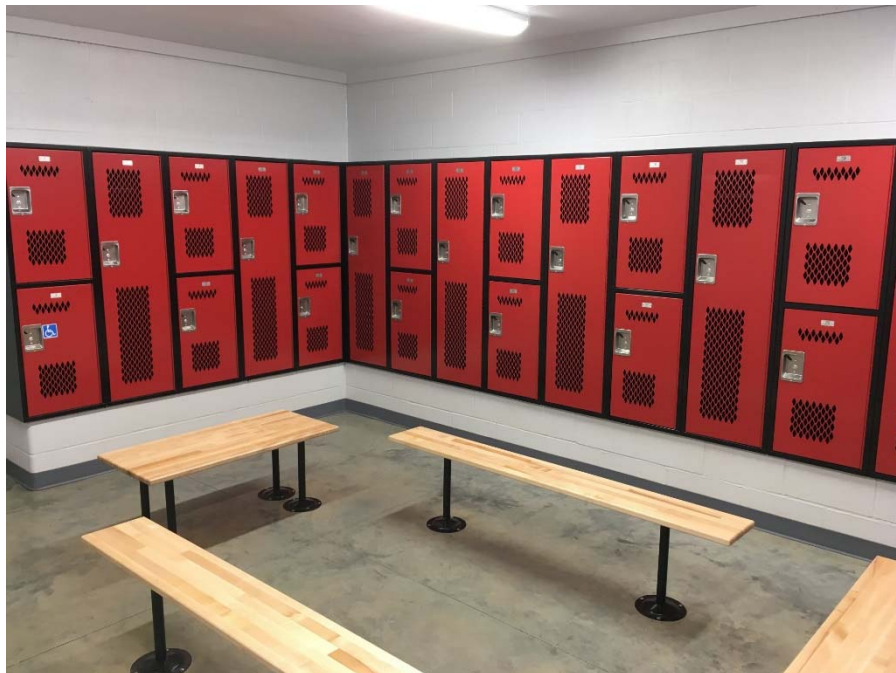

**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 3

Progress Report
February 15, 2018



**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 4

Progress Report
February 15, 2018



**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 5

Progress Report
February 15, 2018



**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 6

Progress Report
February 15, 2018



**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 7

Progress Report
February 15, 2018



**HARDIN COUNTY SCHOOLS
JT ALTON MIDDLE SCHOOL – RE-ROOF PROJECT
DISTRICT FACILITY PLAN UPDATE
JHHS ATHLETIC FACILITIES**

Page 8

Progress Report
February 15, 2018

