



August 28, 2023 Design and Construction Update











# Football Stadiums - Opening





### **Board Consent Items**

Change Orders #13
BEHS Sidewalk - Connects Home
Side grandstand to endzone
concrete.


Change Order #14
Added Gate for Player Access at
BCHS Field

Change Order #15
Existing Press Box Demolition at Visitor Bleachers.



Football Stadiums - Opening



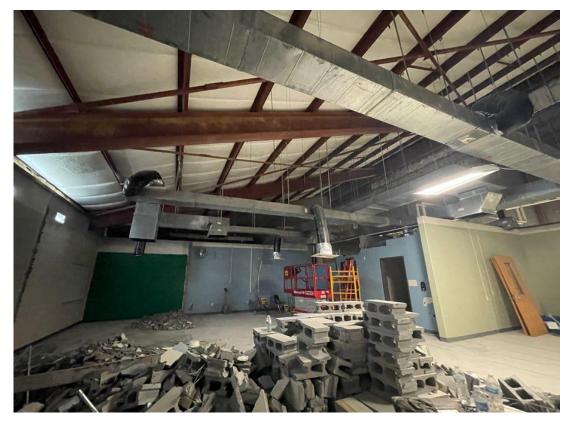





**Bernheim Middle School - Construction** 






studio kremer architects

















## **Bernheim Middle School - Construction**

#### **Board Consent Items**

#### **Revised BG-1**

#### Accounts for Bid Results, Bond Sale and V/E Effort.

- A/E Fee Reduced by \$13,000 and added to Construction Contingency Reduction in fee reflects the Value Engineering (V/E) Effort
- Bond Sale Revisions Include:
  - o Bond Discount Reduced, revised amount shown.
  - Cost of Issuance fee Reduced
  - Additional Proceeds and Bond Rounding Line Item added.
  - Bond Sale SFCC and FSPK amounts revised
  - Bond Premium added to Funds Available
- Total Project Cost reduced by \$450,928.95 due to an Advantageous Bond Sale and A/E Fee Reduction due to V/E Effort.

Please note, additional Project Savings will be submitted through a Change Order Credit to the General Construction Contract that reflect results of the V/E Effort around \$280,000 that will be added to Construction Contingency. Total project savings are around \$730,000 from original post-bid assumptions.




**Bernheim Middle School - Construction** 








MOVING FORWARD

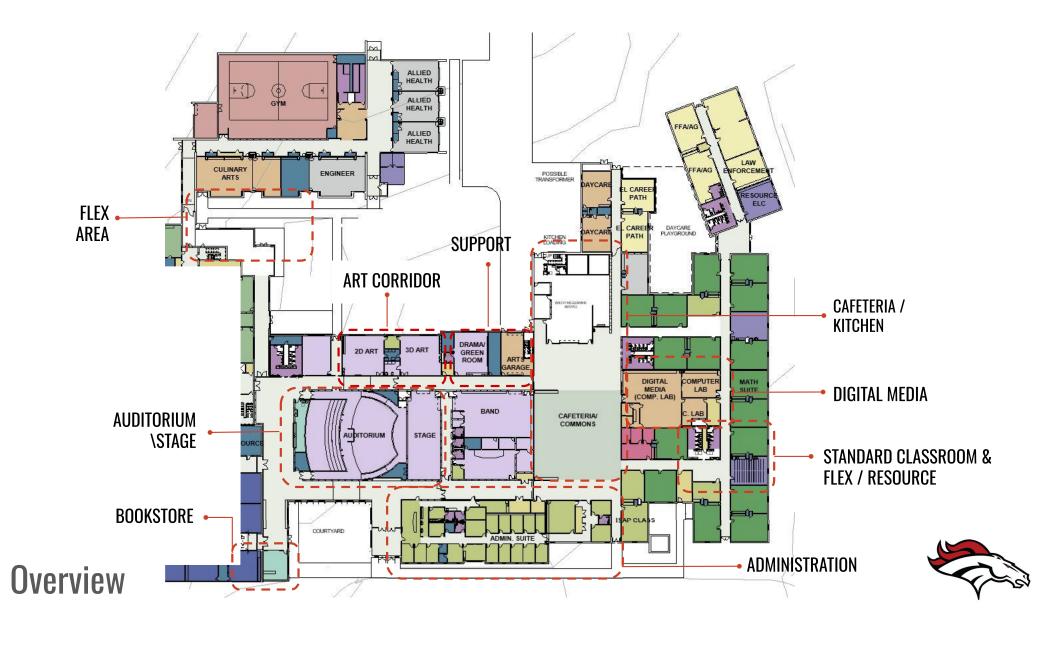

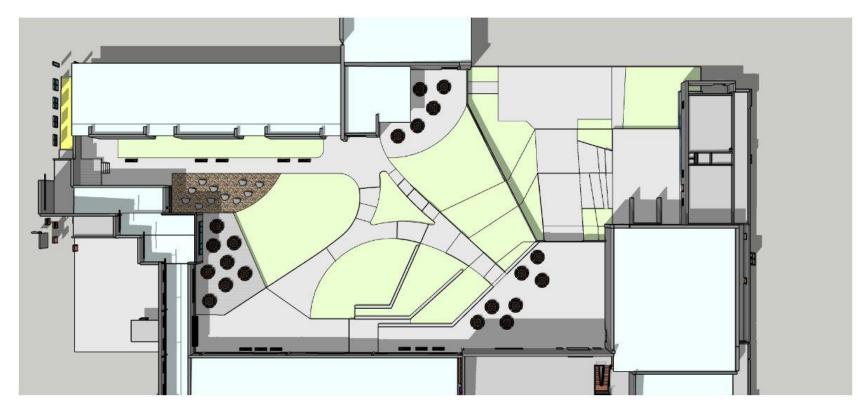























### **Board Consent Items**

## **Design Development Drawings**

**BG-2 - Outline Specifications** 

**BG-3 - Probable Cost** 

\$38,130,000 Construction \$7,535,000 Soft Costs

Total Cost - \$45,665,000.00





### Recommendation for Upcoming Projects

#### BOND SALE 1 - Proceed with BEHS Fine Arts Phase 1 - Bid prior to End of Year

- BEHS Phase 1 Fine Arts and Campus Master Planning | Probable BG-1 Post Bid Cost \$46,000,000 (Reflected on BG-3 submitted with DD Package)
  - 1. Release for Bid mid-October | Bid Date November 15<sup>th</sup> | Starte Construction December 1, 2023 (or December 12<sup>th</sup> based on Board Schedule) | Bond Sale December 2023

#### BOND SALE 2 – May 2024 (Combine All Athletics and Life Safety)

- Phase 2 Athletics and Field Houses All Campuses
  - 1. Release for Bid March 2024 | Bid Date April | April 15, 2024 | Bond Sale May 2024
- 2. **Life Safety Projects -** Probable BG-1 Post Bid Cost \$4,505,000 (There is an active BG-1)
  - 1. Release for Bid late March 2024 | Bid Date April 2024 (different contractors of this work, I am not worried bidding this at same time as Athletics) | Construction April 15, 2024 | Bond Sale May 2024



# **Next Steps and Project Recommendations**



### Recommendation for Upcoming Projects

#### BOND SALE 3 - High School Interior Building Renovations Pushed to End of Design Effort

- 1.) Priority wise I think we should assume HB 678 will expire in July, we should have Athletics under contract should that happen to leverage the use of Restricted Funding.
- 2.) Opening facilities pulls a lot of District Support staggering opening dates will not over stretch District personnel and right now we have these openings planned/assumed:
  - a. Bernheim Opens January 2025 at earliest/July 2025 at latest
  - b. BEHS Fine Arts Opens January 2026 at earliest/July 2026 at latest
  - c. Sport Facilities I would assume Field House Construction would take from 12 to 18-months if starting Construction April 2024 Potential Field House Openings are April 2025 at earliest or October 2025 at latest.



# **Next Steps and Project Recommendations**



### Recommendation for Upcoming Projects

#### **BOND SALE 3 – TBD – High School Interior Building Renovations**

- 3.) I think with the design of the Field Houses, programming space will become available inside each High School we could leverage that open space for more classroom spaces or other needed programs.
- 4.) Our design assumptions for the high school renovations were based on September 2022 visions I think we need to revisit each to gain a better understanding of scope and school needs.
- 5.) Holding off on Renovations can allow for bonding capacity to replenish and we can more appropriately recommend project scope based on available funding.
- 6.) I still think the bidding climate is volatile I am not sure WHERE it will go, but I would like to space out bids to get better understanding of unit costs and see where we can strategically reduce scope.



# **Next Steps and Project Recommendations**

