

FACPAC Contract Change Order

Supplemental Information Form (Ref# 63910)

Form Status: Saved

Tier 1 Project: CHHS Phase 2

BG Number: 23-403

Status: Active

District: Hardin County (HB678) (231)

Phase: Project Initiation (View Checklist)

Contract: Bailey's Masonry, Inc., 0003, Masonry

Type: CM Bid Package

Proposed

Change Order Number

3-4

Time Extension Required

No

Date Of Change Order

12/12/2025

Change Order Amount To Date

Increase

Construction Contingency

Calculations below are project wide. Remaining negative Construction Contingency may require the submission of a revised BG1.

Current Approved Amount	\$2,026,223.39
Net Approved COs	\$77,164.09
Remaining After Approved COs	\$1,949,059.30
Net All COs	\$311,732.15
Remaining After All COs	\$1,714,491.24

This Requested Change Order Amount \$2,400.00

+/-

Change In A/E Fee This Change Order \$112.80

+/-

Change In CM Fee This Change Order \$38.40

+/-

Remaining Construction Contingency Balance

Contract Change Requested By

Architect/Engineer; Local Board of Education

Contract Change Reason Code

Expansion of Scope

Change Order Description And Justification

In accordance with PR #029 and the attached contractor pricing, contractor shall provide all required labor material and equipment required to complete this work as it relates to their particular scope.

Cost Benefit To Owner

Contract unit prices have been utilized No

to support the cost associated with this

change order.

Detailed Cost Breakdown

Contract unit prices have not been utilized, provide a detailed cost breakdown which separates labor, material, profit and overhead.

Detail Item	Amount	Percent of Total
Labor		0.00%
Materials		0.00%
Profit and Overhead		
Bond Insurance		0.00%
Cost Breakdown Total:	\$0.00	
Cost for this Change Order supported by an alternate bid or competitive price quote		
Explain Why		

Change Order Supplemental Information Form Signature
Page (Online Form Ref# 63910)



D. Robert Deal
2025.12.15 10:56:15-05'00'

Architect

Date



12/15/25

Construction Manager

Date

Finance Officer

Date

Local Board of Education Designee

Date



AIA[®] Document G701/CMa[™] – 1992

Change Order - Construction Manager-Adviser Edition

OWNER ☒
 CONSTRUCTION MANAGER ☐
 ARCHITECT ☐
 CONTRACTOR ☐
 FIELD ☐
 OTHER ☐

PROJECT (Name and Address)
 CENTRAL HARDIN HS PHASE II
 3040 LEITCHFIELD ROAD
 CECILIA, KY 42724

CHANGE ORDER NUMBER: 3-4
INITIATION DATE: 12/12/2025

TO CONTRACTOR (Name and Address)
 BAILEY'S MASONRY

PROJECT NUMBERS: 000826
CONTRACT DATE: 1/29/2024
CONTRACT FOR: BID PACKAGE #03 MASONRY

THE CONTRACT IS CHANGED AS FOLLOWS: In accordance with PR #029 and the attached contractor pricing, contractor shall provide all required labor material and equipment required to complete this work as it relates to their particular scope.

The original Contract Sum was	2,140,441.00
Net change by previously authorized Change Orders	10,400.00
The Contract Sum prior to this Change Order was	2,150,841.00
The Contract Sum will be Increased by this Change Order in the amount of	2,400.00
The new Contract Sum including this Change Order will be	2,153,241.00

The Contract Time will be adjusted by 0 days.
 The date of Substantial Completion as of the date of this Change Order therefore is 12/1/2026.

NOT VALID UNTIL SIGNED BY THE CONSTRUCTION MANAGER, ARCHITECT, CONTRACTOR AND OWNER.

CODELL CONSTRUCTION COMPANY

CONSTRUCTION MANAGER (Firm Name)
 4475 ROCKWELL ROAD WINCHESTER, KY 40391

ADDRESS

BY (Signature)

(Typed Name)

DATE:

BAILEY'S MASONRY

CONTRACTOR (Firm Name)

ADDRESS

BY (Signature)

(Typed Name)

DATE:

JRA ARCHITECTS

ARCHITECT (Firm Name)
 301 EAST VINE STREET LEXINGTON, KY 40507

ADDRESS

D. Robert Deal
 2025.12.15 10:56:29-05'00'

BY (Signature)

(Typed Name)

DATE:

HARDIN COUNTY BOARD OF EDUCATION

OWNER (Firm Name)
 65 W. A. JENKINS ROAD ELIZABETHTOWN, KY 42701

ADDRESS

BY (Signature)

(Typed Name)

DATE:

**AIA**[®]**Document G709[™] – 2018****Proposal Request**

PROJECT: *(name and address)*
Central Hardin High School Phase 2
Elizabethtown, KY

CONTRACT INFORMATION:
Contract For:
General Construction
Date:
10-17-2022

Architect's Project Number: 2019111 Ph 2
Proposal Request Number: 29
Proposal Request Date: 10-29-2025

OWNER: *(name and address)*
Hardin County Board of Education
65 W. A. Jenkins Road
Elizabethtown, KY 42701

ARCHITECT: *(name and address)*
JRA Architects
301 E. Vine Street
Lexington, KY 40507

CONTRACTOR: *(name and address)*
Codell Construction Company
4475 Rockwell Rd.
Winchester, KY 40391

The Owner requests an itemized proposal for changes to the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. The Contractor shall submit this proposal within (0) days or notify the Architect in writing of the anticipated date of submission.

(Insert a detailed description of the proposed modifications to the Contract Documents and, if applicable, attach or reference specific exhibits.)

The owner would like to remove 2 display cases and turn them into closets.

Provide pricing for demolition of the sliding window, CMU below and bottom of display case. Provide a 3'-0" by 7'-2" single "Type F" wood door with hollow metal frame.

Match door hardware on H215A door. Infill with CMU as required.

Match adjacent finishes and paint interior of room P-1, add B-1 rubber base, RT-1 rubber flooring and add light fixture.

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE, OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

REQUESTED BY THE ARCHITECT



ARCHITECT *(Signature)*

BY: D. Robert Deal, AIA, President

(Printed name, title, and license number if required)

DOIO

H116

H114


EMR


H114

H111

EVATOR

EL-3

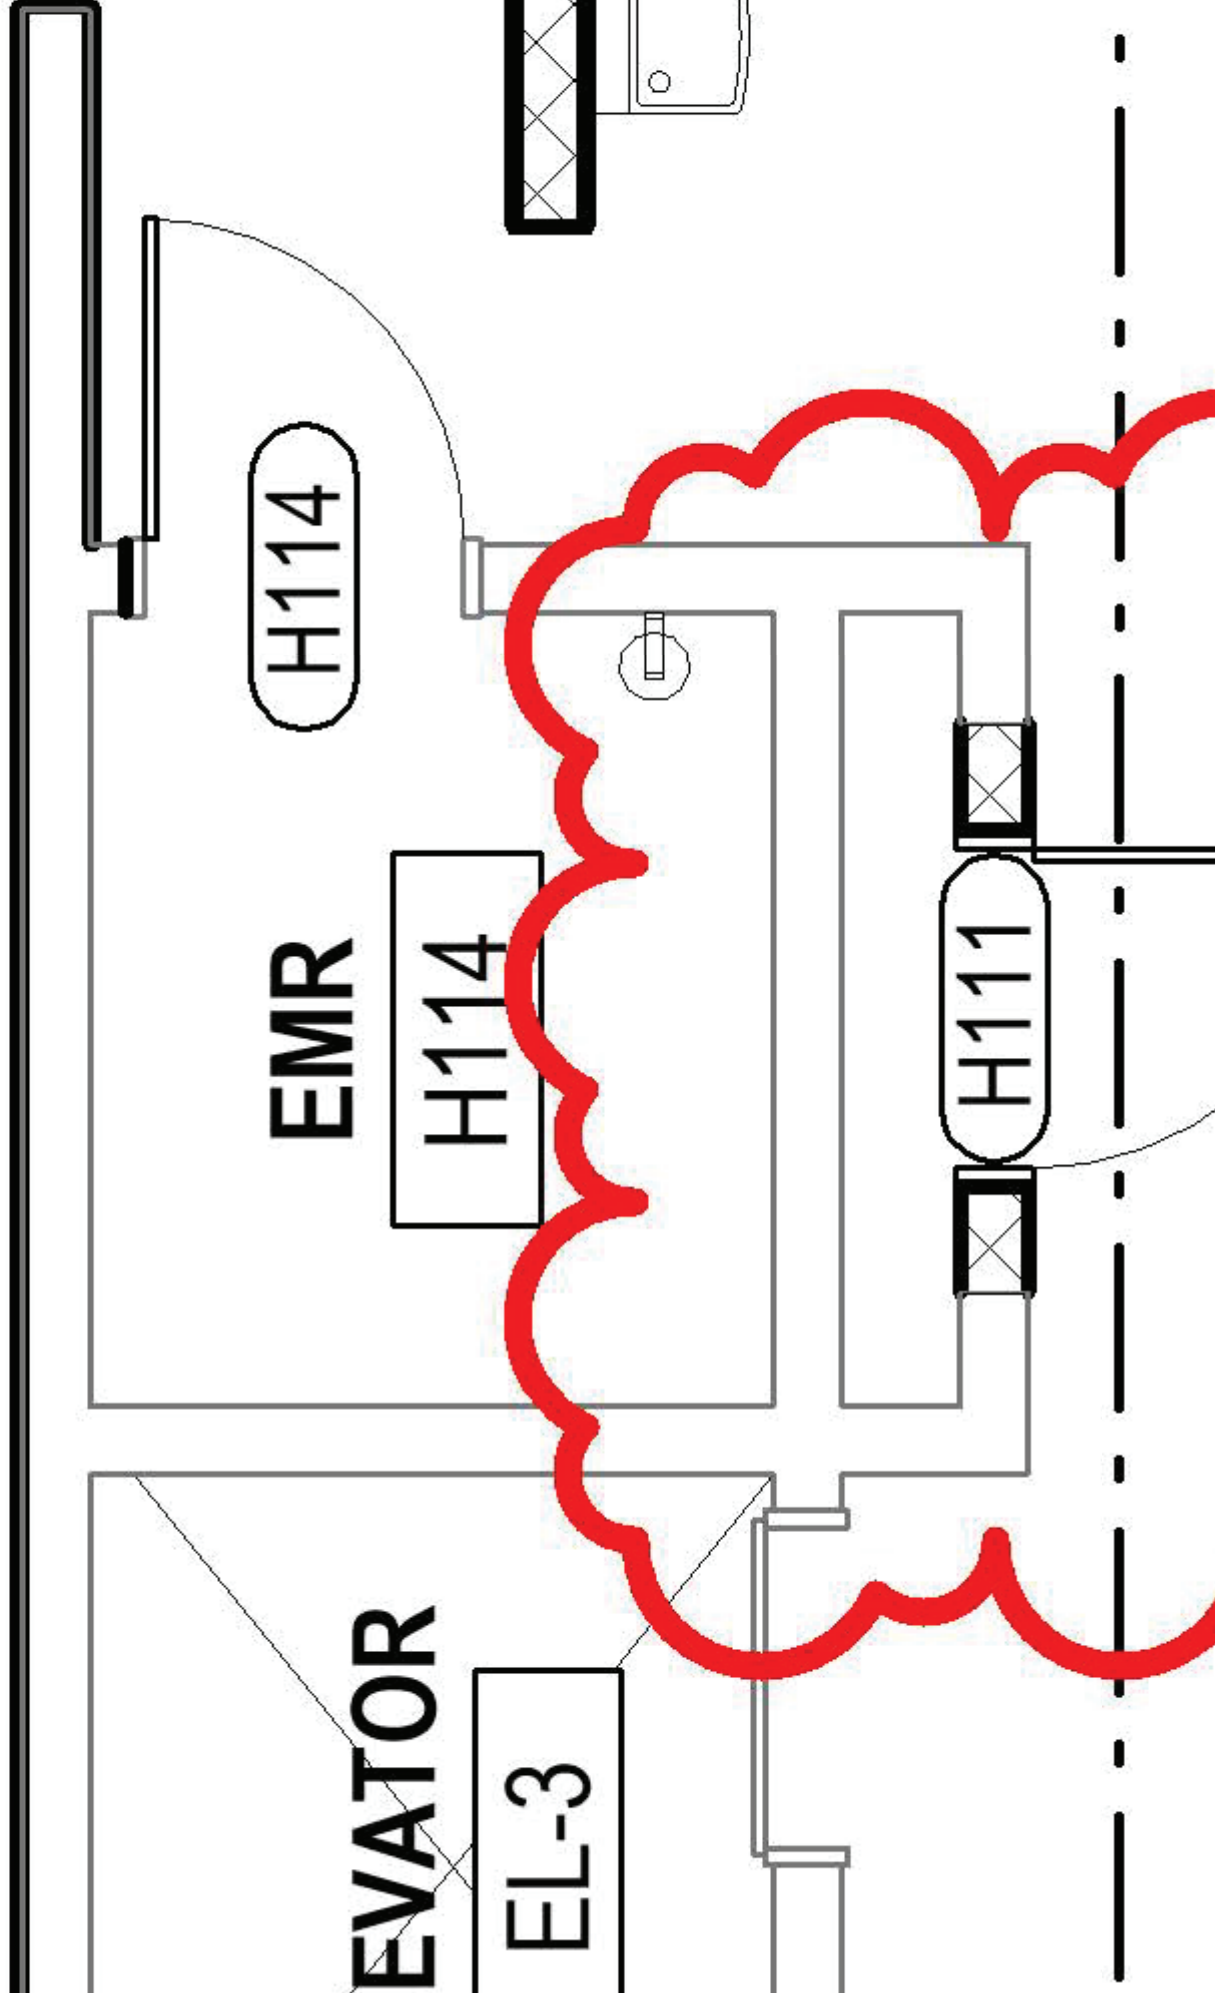

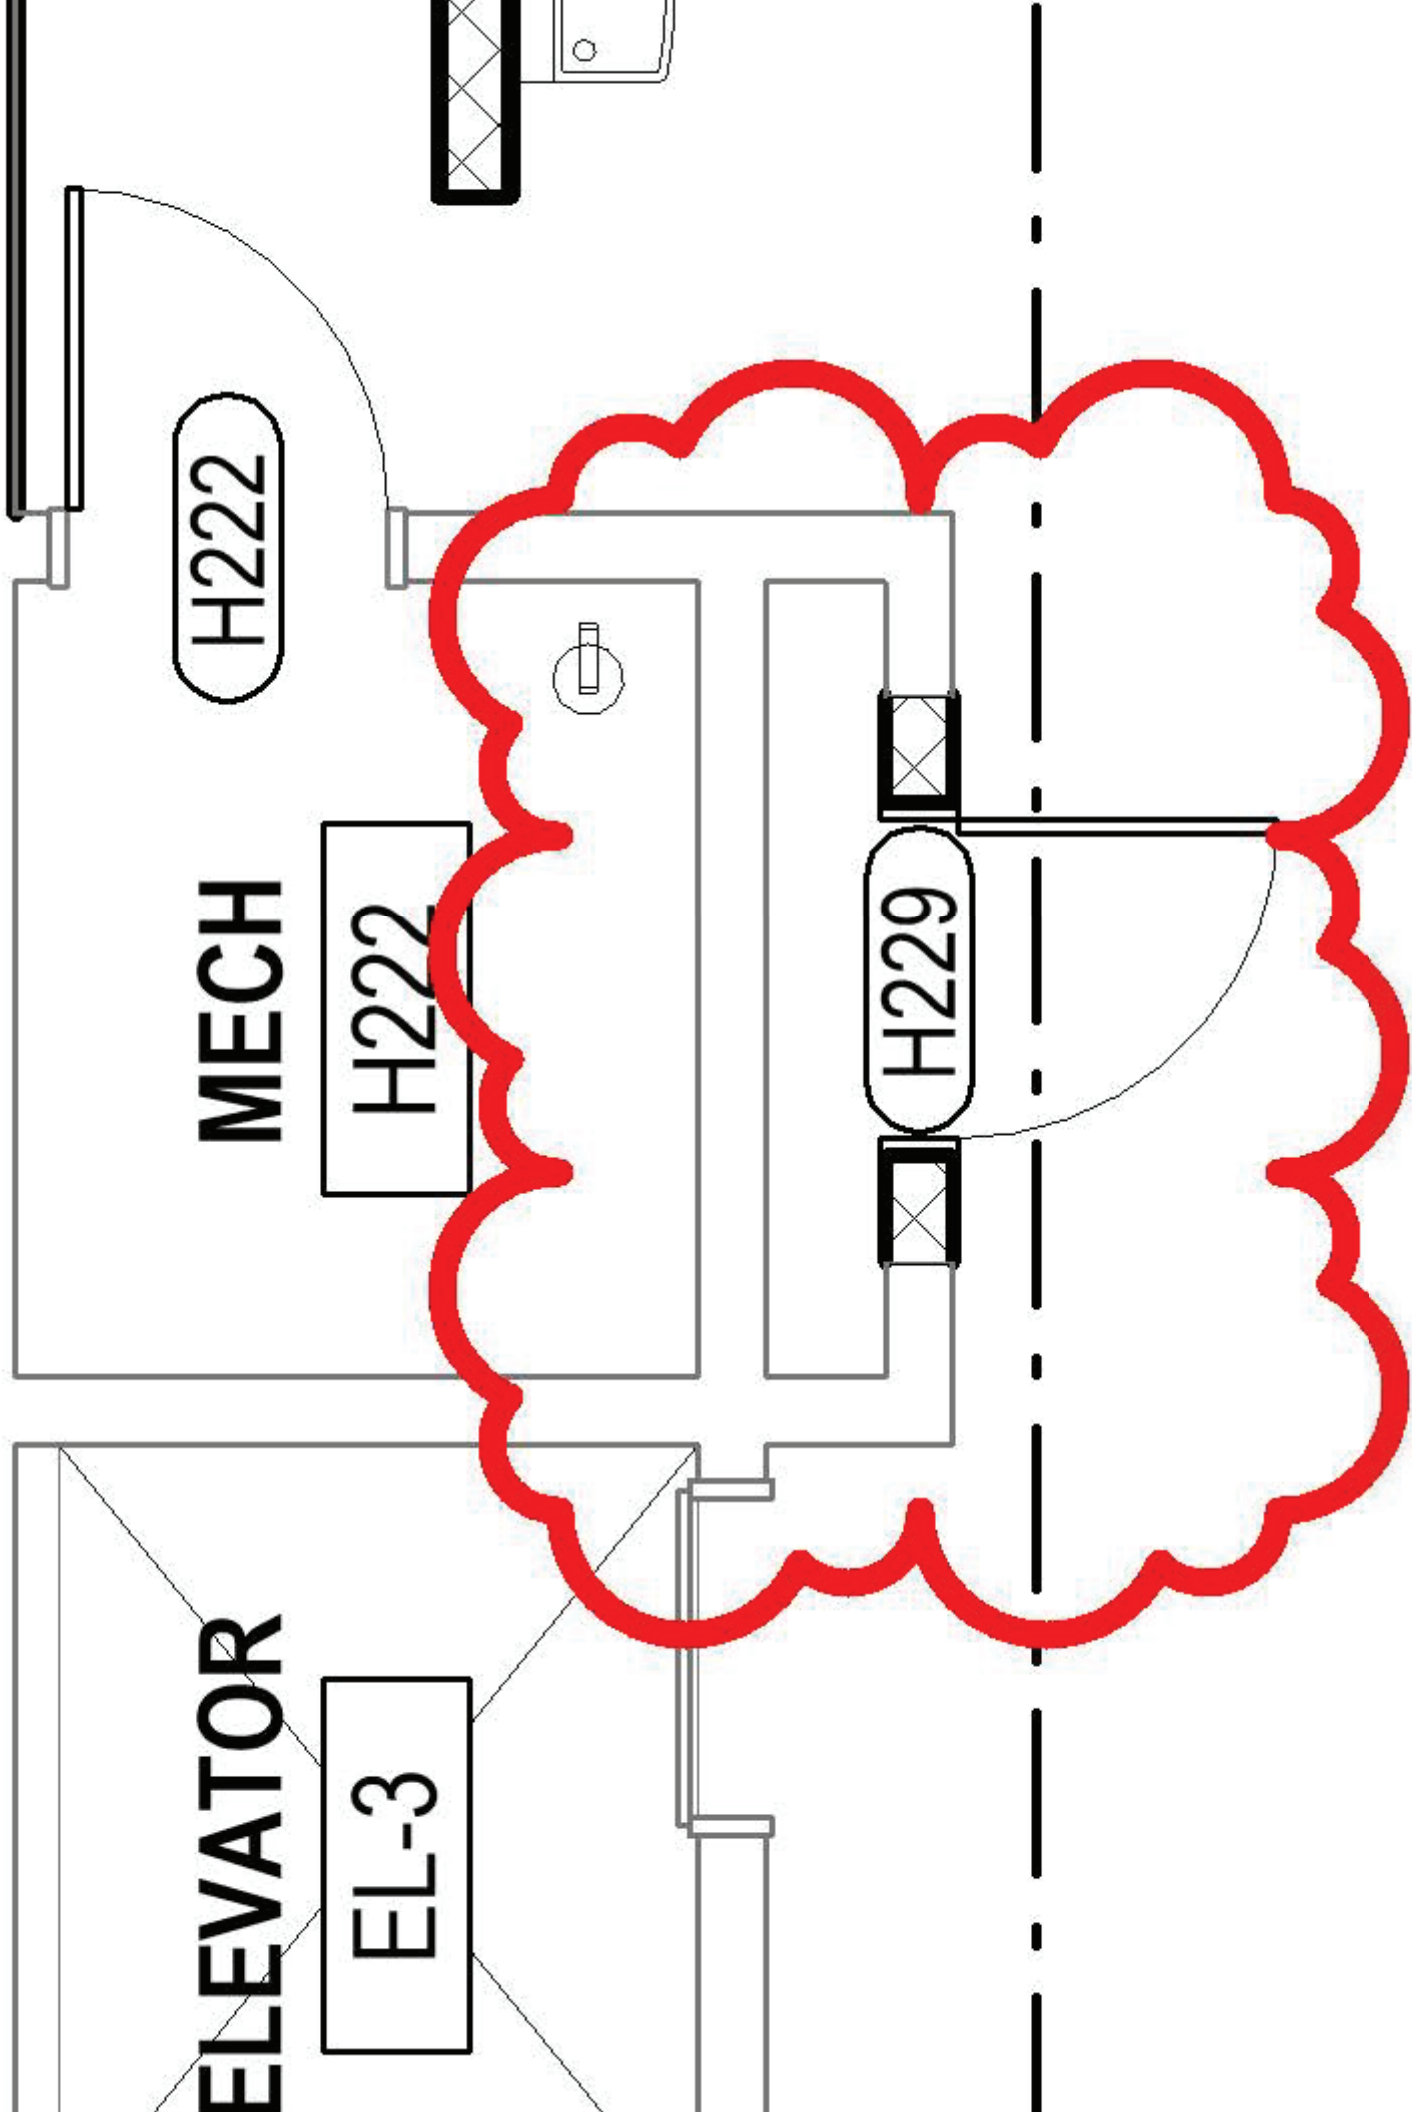



1331 Battle Training Road
Elizabethtown, KY 42701
Phone (270) 765-0969
info@baileysmasonry.com

Proposal Request

Project
Central Hardin High School - Phase 2
Cecilia, KY

12/2/2025

Qty	Description	Unit Price	Total
	PR #29 - Display Case - Closets Infill 2 display cases with CMU to convert to closets Labor and materials Demo to be performed by others		
TOTAL			\$2,400.00



Commercial



Brick & Block



Industrial
