

#### Change Order

PROJECT (Name and address):	CHANGE ORDER NUMBER: 006	OWNER: 🛛
Cecilia Valley Elem School Elizabethtown, KY	<b>DATE:</b> July 12, 2017	ARCHITECT: ⊠
TO CONTRACTOR (Name and address):	ARCHITECT'S PROJECT NUMBER: 1429 / BG 13-017	CONTRACTOR: 🖂
Isaac Tatum Construction, Inc.	CONTRACT DATE: May 27, 2016	FIELD:
PO Box 665 85 Sulfur Springs Road	CONTRACT FOR: General Construction	File 1429 B/CO (Ecopy):
Lebanon, KY 40033		

#### THE CONTRACT IS CHANGED AS FOLLOWS:

(Include, where applicable, any undisputed amount attributable to previously executed Construction Change Directives)

- 1. Omit eight (8) student reading tables and 32 student chairs per Proposal Request #15 in the Media Center. Credit (\$6,762.80).
- 2. Project schedule has been affected by rain weather delays for May 2017 by four (4) days. The date of substantial completion will be changed from September 19, 2017 to September 23, 2017.
- 3. Change sidewalk configuration, delete 20 l.f. of fence and add two trees at the Pre-School playground per Proposal Request #11. Cost \$1,480.90.
- Delete epoxy paint and paint with latex. Provide stainless steel wall panels on north kitchen wall per Proposal Request #8. Cost \$49.37

The original Contract Sum was	\$ .	10,904,515.00
The net change by previously authorized Change Orders	\$	-12,350.75
The Contract Sum prior to this Change Order was	\$	10,892,164.25
The Contract Sum will be decreased by this Change Order in the amount of	\$	5,232.53
The new Contract Sum including this Change Order will be	\$	10,886,931.72

The Contract Time will be increased by Four (4) days.

The date of Substantial Completion as of the date of this Change Order therefore is September 23, 2017

**NOTE:** This Change Order does not include changes in the Contract Sum, Contract Time or Guaranteed Maximum Price which have been authorized by Construction Change Directive until the cost and time have been agreed upon by both the Owner and Contractor, in which case a Change Order is executed to supersede the Construction Change Directive.

#### NOT VALID UNTIL SIGNED BY THE ARCHITECT, CONTRACTOR AND OWNER.

July 12, 2017 DATE	DATE	DATE
Jim Pearcy, Construction Admin. (Typed name)	(Typed name)	(Typed name)
BY (Signature)	BY (Signature)	BY (Signature)
2405 Harrodsburg Road, Lexington, KY 40504 ADDRESS	PO Box 665, 85 Sulfur Springs Road , Lebanon, KY 40033 ADDRESS	65 W. A. Jenkins Rd Elizabethtown, KY 42701 ADDRESS
Sherman Carter Barnhart Architects PLLC ARCHITECT (Firm name)	Isaac Tatum Construction, Inc.  CONTRACTOR (Firm name)	OWNER (Firm name)

## **KENTUCKY DEPARTMENT OF EDUCATION** 702 KAR 4:160

# CHANGE ORDER SUPPLEMENTAL INFORMATION FORM

BG #:13-017 Change Order No.: _006							
District Facility District: Hardin County Code: 231 Name: Cecilia Valley Elementary  Project Cecilia Valley Elementary School Extension Required: ☐ Yes ☑ No		chool Code: <u>030</u> Four (4) day(s)					
Date of Change Order: <u>July 12, 2017</u> Change Order Amount: ☐ Increase ☐ De	ecrease	☐ Unchanged					
Contractor / Vendor Name: <u>Isaac Tatum Construction, Inc.</u> Bid Package No.	:						
1. This Requested Change Order Amount + / -	\$	(5,232.53)					
2. Remaining Construction Contingency Balance: (including line 1 above)	\$						
3. Change in A/E Fee for this Change Order +/-	\$	78.04					
4. Change in CM Fee for this Change Order +/-	\$						
Note: Change Orders equal to or greater than \$25,000 shall be submitted to KDE was Attach additional pages if necessary.	ith detai	I cost breakdown.					
Contract change requested by: 🔀 Local Board of Education 🔲 General Contractor	☐ Ar	chitect/Engineer					
☐ Construction Manager ☐ Code Enforcement Official ☐ Other:							
Contract change reason code:  ☐ Reduction of Scope ☐ Expansion of Scope ☐ Other:							
Change Order Description and Justification: Cost Benefit to Owner:							
Omit eight (8) student reading tables and 32 student chairs. Add four days to the substantial completion date for weather. Change sidewalk, fence & landscaping at Pre-school playground. Delete epoxy paint and stainless steel wall panels in kitchen.							
Have contract unit prices been utilized to support the cost associated with this change order?  Yes No If no, provide a detailed cost breakdown which separates labor, material, profit and overhead.							
Cost Breakdown Refer to attachment.  Total Change Order Amt.: Labor Materials Profit & Over	erhead*	Bond & Insurance					
\$(5,232.53) \$ \$ \$		\$					
% of Total Change Order Amt.: % %	%	%					
*Profit & Overhead shall not exceed 15% of net cost of change order							
Is the cost for this change order supported by an alternate bid or competitive price quote(  Yes No If no, explain why  Board of Education Designee's Signature  Date  Architect's Signature		dr 7/12/17 Date					
Finance Officer's Signature Date Construction Manager's Signature	gnature	Date					



P.O. Box 665 215 N. Depot St. Lebanon, KY 40033

Tel (270) 692-4045 Fax (270) 692-2324 www.isaactatumconstruction.com

June 12, 2017

Sherman Carter Barnhart Architects 2405 Harrodsburg Rd. Lexington, KY 40504

Attn: Jim Piercy

Reference: Cecilia Valley Elementary Change Order – Request for additional days added

to contract.

It rained 16 days in May. The average days for rainfall in May is 12.

We are requesting an extension in contract time of 4 day.

Backup information is available.

Thanks,

Isaac Tatum

Isaac Tatum Construction, Inc.

National Environmental Satellite, Data, and Information Service National Oceanic & Atmospheric Administration Elev; 715 ft. Lat: 37,687\* N Lon: 85,845" W U.S. Department of Commerce

Station: ELIZABETHTOWN 1.8 SE, KY US GHCND:US1KYHD0005

Record of Climatological Observations These data are quality controlled and may not be identical to the original observations. Generalish on 06/02/2017

16 28 X

151 Patton Avenue Asheville, North Carolina 28801 Observation Time Temperature: Unknown Observation Time Precipitation:

National Centers for Environmental Information

	-	1		emperature (r.)	Ţ.		ı	ucommical			Evaporation	nonz	***************************************	*	Soli l'emperature (r.)	(u) ame		
	***************************************		24 hi at ob	24 hrs. ending at observation time	<b>⇔</b> ○ #	24	Hour Arm at observe	24 Hour Amounts ending at observation time		At Obs Time	<u> </u>		-	4 in depth			8 in depth	
> & @ :	<b>∑</b> 0 c +-	∠ ∞ ۵			<b>ω φ ⊾ &gt;</b>	Rain, melled	u.	Snow, ice		Snow, ice pellets,		Amount of Evap.	Ground			Ground		
***	£		Мах.	Min.	w ○ c	snow, etc. (in)	- m co	pellets. hail (m)	- m O	do do (in)	εÊ		Cover (see *)	Max.	Ę	Cover (see *)	Max.	M.
	2	1	******************		-	0.37												
2017 5						00.0		0.0										
	3				***************************************	0.00		0.0		<b></b>								
2017 5	4					90'0			-									
2017   5	5				***************************************	0.83												
						0.37												
						0.39			<u> </u>									
	8				***************************************	0,00		0.0										
						0.00		0.0										
		6				00.0		0.0										
2017   5		1			A THE TAXABLE PROPERTY OF THE	0.02												
		2				0.29												
		-				0.26												
		4				00.0		0.0	<b></b>									
		5				00.0		0.0										
		9				0.00		0.0										
		7				0.00		0.0										
		80				0.00		0.0										
2017 5		<b>о</b>				00.0		0.0										
		0				20'0												
		***				0.54				<b></b>								
2017 5		2				0.24												
		9				0.00		0.0	-									
2017 5		*				0.02												
		S				1,22												
		9				0.05												
		7				0.00		0.0										
	5 2	28				1.23												
		ō				0.01												
		0				0.00		0.0										
2017 5		<del></del>				00.0		0.0	<b></b>									
						00 4		4 4	<u> </u>									

Empty, or Itlank, cells indicate that a data observation was not reported.

\*\*Ground Cover: T-efrass; 2\*\*Fallow; 3\*\*Bare Ground; 4\*\*Broine grass; 5\*\*Sod; 6\*\*Straw mulch; 7\*\*Grass muck; 8\*\*Bare muck; 0\*\*Linknown

\*\*s\*\*This data value failed one of NGD's quality control tests.

\*Takes in the Precipitation category above indicate a TRACE value was recorded.

\*A\*\* values in the Precipitation Flag or this Strow Flag column indicate a multiday total, accumulated since last measurement, is being used.

\*A\*\* values in the Precipitation Flag or this Strow Flag column indicate a multiday total, accumulated since last measurement, is being used.

Data value inconsistency may be present due to rounding calculations during the conversion process from SI metric units to standard impedial units.

U.S. Department of Commerce
National Oceanic & Atmospheric Administration
National Environmental Satellite, Data, and Information Service Elev: 690 ft. Lat: 37.680° N Lon: 85.876° W

> Monthly Normals Summary of

Generated on 06/02/2017

1981-2010

National Centers for Environmental Information 151 Patton Avenue Asheville, North Carolina 28801

Station: ELIZABETHTOWN, KY US GHCND: USC00152512 Summary Month N ---> ---> ೆ 4.59 4.23 5.82 4.35 4.91 3.67 3.14 4.02 4.02 5.82 Mean 3.83 Totals 3.79 >= 0.01 11.3 9.3 12.5 111.4 12.2 10.5 8.8 7.8 7.8 9.5 11.4 120.5 6.8 6.8 5.7 8.3 8.5 5.7 6.7 7.9 Mean Number of Days Daily Precipitation Precipitation (in.) >= 0.50 3.1 3.0 3.0 3.3 3.3 3.3 3.3 3.6 3.6 3.6 3.6 2.7 >= 1.00 1.0 0.9 1.1 16 1 18 10 14 0.9 Precipitation Probabilities
Probability that precipitation will be
equal to or less than
the indicated amount Monthly Precipitation vs. Probability Levels 3.48 2.56 3.25 3.63 4.21 47.11 3.83 3.08 4.19 5.33 4.24 4.74 8 5.67 5.05 4.68 3.82 5.34 6.17 5.41 4.45 5.87 5.06 .75 5.03

@ Denotes mean number of days greater than 0 but less than 0.05.
 -7777: a non-zero value that would round to zero
 Empty or blank cells indicate data is missing or insufficient occurrences to compute value.



### Work Changes Proposal Request

WOLK Changes Fropusair	request	
PROJECT (Name and address):	PROPOSAL REQUEST NUMBER	:: 015 OWNER: ⊠
Cecilia Valley Elem School Elizabethtown, KY	DATE OF ISSUANCE: June 22, 2	2017 ARCHITECT: ⊠ CONSULTANT: ⊠
OWNER (Name and address):	CONTRACT FOR: General Cons	
Hardin County Schools 65 W. A. Jenkins Rd Elizabethtown, KY 42701	CONTRACT DATE: May 27, 201	.6 FIELD:  File 1429X:
FROM ARCHITECT (Name and address): Sherman Carter Barnhart Arch PLLC 2405 Harrodsburg Road Lexington, KY 40504	ARCHITECT'S PROJECT NUMBE BG 13-017	ER: 1429 /
TO CONTRACTOR (Name and address): Isaac Tatum Construction, Inc. PO Box 665 85 Sulfur Springs Road Lebanon, KY 40033		
Please submit an itemized proposal for the Contract Documents described here: Architect, in writing, of the date on whi	<ul> <li>n. Within ten (10) days, the Contrac</li> </ul>	ontract Time for proposed modifications to ctor must submit this proposal or notify the ed.
THIS IS NOT A CHANGE ORDER, A CON WORK DESCRIBED IN THE PROPOSED I	STRUCTION CHANGE DIRECTIVE OF MODIFICATIONS.	R A DIRECTION TO PROCEED WITH THE
DESCRIPTION (Insert a written descript	ion of the Work):	
Omit 8 student reading tables and 32 stu	ident chairs within the Media Cente	er.
ATTACHMENTS (List attached documen	ts that support description):	
None		•
REQUESTED BY THE ARCHITECT		L. ATA
(0)	Tom Smith	h, AIA ame and title)
(Signature)	(Frinteu n	ume um mue)



Mike K. Bell Phone: 502.779.2100 Fax: 502.810.2257 Mike.bell@atlas-co.com

# CHANGE ORDER June 27, 2017

To: Attention: Project: Ref doc: Atlas #:	Isaac Tatum Construction, Inc. Tim Tatum Cecilia Valley Elementary School ACO#10 PR#15 Deduct Library Material 65374 — Library Furniture	
Thank you for referenced p	or bringing to our attention the need for an adjustmen project:	t to the above
Deduct 8 stu	ident tables and 32 student chairs within the Media Ce	enter
Atlas Break	Down	
	t amount (\$6,380.00)	
Price include Price exclude Pricing good	es installation.	
	rder approved – no official change order required. rder rejected.	
Signature		Date



#### Work Changes Proposal Request

PR	OJECT	(Name	and address):	
			- 1/19 C	
		2.7	5 % t	

Cecilia Valley Elem School Elizabethtown, KY

OWNER (Name and address): Hardin County Schools 65 W. A. Jenkins Rd Elizabethtown, KY 42701

FROM ARCHITECT (Name and address): Sherman Carter Barnhart Arch PLLC 2405 Harrodsburg Road Lexington, KY 40504

TO CONTRACTOR (Name and address): Isaac Tatum Construction, Inc. PO Box 665 85 Sulfur Springs Road Lebanon, KY 40033

PROPOSAL REQUEST NUMBER: 011 -Revised

DATE OF ISSUANCE: June 2, 2017

**CONTRACT FOR:** General Construction

CONTRACT DATE: May 27, 2016

BG 13-017

ARCHITECT: 🛛

OWNER: 🛛

CONSULTANT: X

CONTRACTOR:

File 1429X, CA Copy: X

FIELD:

ARCHITECT'S PROJECT NUMBER: 1429 /

Please submit an itemized proposal for changes in the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. Within ten (10) days, the Contractor must submit this proposal or notify the Architect, in writing, of the date on which proposal submission is anticipated.

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

**DESCRIPTION** (Insert a written description of the Work):

Contractor to provide revised pricing based on attached revised PR#11 drawing.

ATTACHMENTS (List attached documents that support description):


PR #11 Revised - SD1.2

REQUESTED BY THE ARCHITECT:

(Stenature)

Ben Sorrell, Landscape Architect

(Printed name and title)

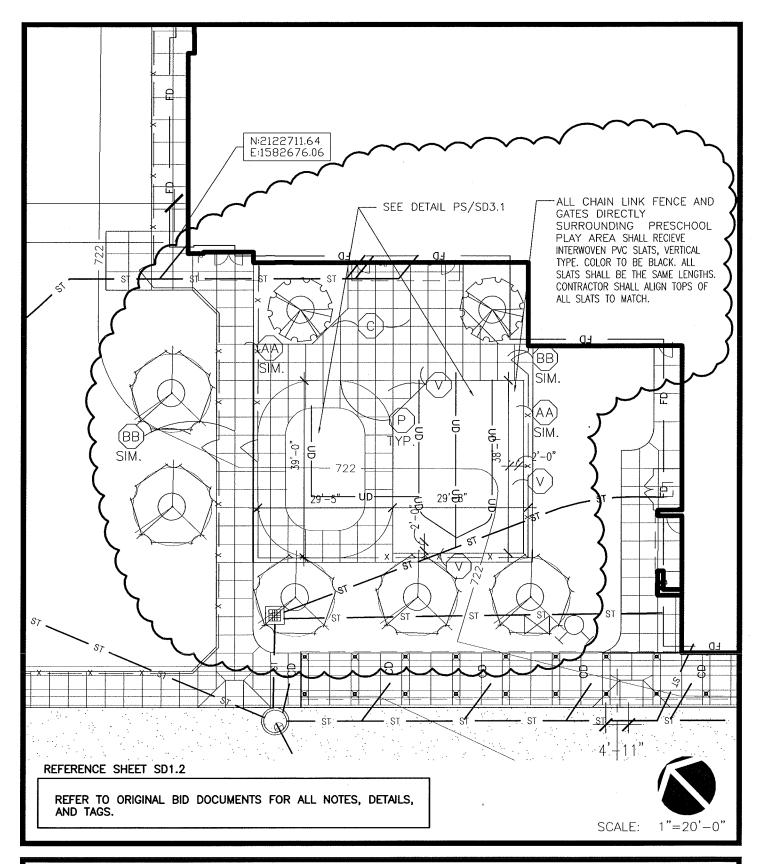

#### REVISED PROPOSAL REQUEST #11 - SD1.2 REVISED PRE-SCHOOL PLAYGROUND 1429 SHEET NO. SD1.2 JOB NO. SHERMAN CARTER BARNHART **COPYRIGHT © 2017** PROJECT NAME **CECILIA VALLEY ELEMENTARY** DATE 6/2/17 SHERMAN CARTER ARCHITECTS **BARNHART** ARCHITECTS, PLLC PROJECT LOCATION HARDIN COUNTY, KENTUCKY DRAWN **KRP**





P.O. Box 665 215 N. Depot St. Lebanon, KY 40033 Tet (270) 692-4045 Fax (270) 692-2324 www.isaactatumconstruction.com

March 7, 2017

SCB Architects
Attn: Jim Pearcy

Reference: CVES PR#11

Additional Sidewalk	
206SqFt @ \$6.50 SqFt unit price	\$1,339.00
Additional Trees	
1 flowering dogwood	\$200;00
1 Japanese Zelkova	\$250.00
Reduction in Chain link fence	
20 LFT @ \$18.78LFt	-\$375.60
158/ Bush & Quantized on your strift price	\$67.50
15% Profit & Overhead on non unit price	307.30

Total:

\$1,480.90

Thank you,

Isaac Tatum

Isaac Tatum Construction, Inc.



### Work Changes Proposal Request

PROJECT (Name and address): Cecilia Valley Elem School Elizabethtown, KY

OWNER (Name and address): Hardin County Schools 65 W. A. Jenkins Rd Elizabethtown, KY 42701

FROM ARCHITECT (Name and address):
Sherman Carter Barnhart Architects PLLC
2405 Harrodsburg Road
Lexington, KY 40504

TO CONTRACTOR (Name and address):
Isaac Tatum Construction, Inc. PO Box 665
85 Sulfur Springs Road
Lebanon, KY 40033

PROPOSAL REQUEST NUMBER: 008

DATE OF ISSUANCE: January 26, 2017

**CONTRACT FOR:** General Construction

CONTRACT DATE: May 27, 2016

ARCHITECT'S PROJECT NUMBER: 1429 /

BG 13-017

OWNER: 🖂

ARCHITECT: ⊠

CONSULTANT:

CONTRACTOR: ⊠

FIELD:

File 1429X (Efile): 🗵

Please submit an itemized proposal for changes in the Contract Sum and Contract Time for proposed modifications to the Contract Documents described herein. Within ten (10) days, the Contractor must submit this proposal or notify the Architect, in writing, of the date on which proposal submission is anticipated.

THIS IS NOT A CHANGE ORDER, A CONSTRUCTION CHANGE DIRECTIVE OR A DIRECTION TO PROCEED WITH THE WORK DESCRIBED IN THE PROPOSED MODIFICATIONS.

**DESCRIPTION** (Insert a written description of the Work):

Add 4' tall stainless steel wall panel the full length of the north wall of Kitchen 145 (from interior corner near opening 145L and NE corner of walk-in freezer.

Also, delete epoxy component of all wall painting. Paint using standard, specified latex.

ATTACHMENTS (List attached documents that support description):

N/A

REQUESTED BY THE ARCHITECT:

(Signature)

Tom Smith, AIA

(Printed name and title)



P.O. Box 665 215 N. Depot St. Lebanon, KY 40033 Tet (270) 692-4045 Fax (270) 692-2324 www.isaactatumconstruction.com

June 12, 2017

SCB Architects
Attn: Jim Pearcy

Reference: CVES PR#8

Add 4'x 36' of Stainless Steel Panels	\$3,103.8
UNIT PRICES	
Delete 3520 Sqft of Epoxy Paint	
3520 sqft@\$2.50 sqft unit price	-\$8,800.0
Add 3520 Sqft of Latex Paint	
3520 Sqft @ \$1.50 sqft unit price	\$5,280.0
TOUR CORD OF THE LEADING	\$465.5
15% Profit & Overhead on non unit price	<u> </u>
ral:	\$49.3

Thank you,

Isaac Tatum

Isaac Tatum Construction, Inc.



### **C&T Design and Equipment Co., Inc.**

Commercial and Industrial Food Service Equipment 6315 Midland Industrial Drive Shelbyville, KY 40065 Phone: 502-633-8030 • 800-240-4188 • Fax: 502-633-8031

6/12/2017

#### **CHANGE ORDER**

Location
Cecilia Valley Elementary
East Main Street
Cecilia, KY. 40033

Isaac Tatum Construction P.O. Box 665, Lebanon, KY 40033 Tim Tatum

#### Option #1

Provide and Install (4) sheets 20 ga.S/S to go on wall \$2,956.00 + Tax if applies.

(36' X 4' Installed)

Option #2

Provide and Install (9) sheets 20 ga.S/S to go on wall \$6361.00 + Tax if applies.

(36' X 9'-6" Installed)

Χ			
Tim Tatur	n		
